



## Executive Program Summary July 2025

---

This report outlines, at an executive review level, the progress planned by the Construction Program Supervisor through July 2025 and key activities planned for August 2025.

### OVERVIEW

Safety Security & Police Building – Lee Lewis's Construction GMP was Board approved in June. The permit process has had some challenges with City of Mansfield due to a revised Deed and a delayed Plat permit. New expectation for permit is August 2025.

Early Learning Center 2.0 – Bids were received by Core Construction and are being reviewed for Board approval in August 2025. The permit process has had some challenges with City of Mansfield due to some drainage issues and a delayed Plat permit. New expectation for permit is August 2025.

Middle Schools Fine Arts Additions – The early flooring and demolition packages have begun and are on track to be complete for start of school in August. The GMP for the main scope is being presented for Board approval in July. The permit process is ongoing and is in the first round of comments from the City of Mansfield and expected to be complete in August 2025.

Ben Barber Innovation Academy and Frontier HS Addition & Renovations - Core Construction's GMP was Board approved in June. The permit process has had some challenges with City of Mansfield due to some drainage issues and a delayed Plat permit. New expectation for permit is August 2025.

High School Baseball & Softball Turf & Batting Cages – Permits have been issued for MHS, LHS and LRHS and construction has begun. Huckabee got some unexpected comments from the City of Arlington permit review and are revising and responding for an expedited Permit for SHS and THS.

6<sup>th</sup> Avenue & Main Transportation – In Design Development, we have a good design for the 6<sup>th</sup> Avenue facility presented in June. The CIP and renovation scope at the Main Transportation and Danny Griffin Operations Complex is. DD deliverable will be in August and issue for Permit and Bid in September and October, respectively.

Early Roofing – Bids have been Board approved and Purchase Orders issued. Construction ongoing with a completion of the IS campuses by school start and the ES campuses just after the start of school.

Busses - Purchase Orders for 95 of the 77 passenger buses and 26 of 54 passenger buses. 66 of the 77 passenger buses, and 26 of the 54 passenger buses have been delivered. Several of the out of commission buses have been sold in auction.

The Technology Department has issued purchase orders for Proposition A infrastructure equipment. The equipment purchases include network switches and wireless access points for auxiliary buildings.

Technology has also issued purchase orders for Proposition B capital equipment purchases. Interactive panels have been shipped and will begin arriving soon. Digital displays have been ordered and should arrive in October. Fiber Ring proposal was approved in March and will start this summer.

The 2024 Bond Program website is complete with progress updates, information, and photos. The website will be consistently updated with project information.

### SCHEDULE:

The Report for each project is attached herewith.

### BUDGET:


The Program Report Summary of expenditures is attached herewith.

# Bond 2024 Funding Summary

• Bond Allocation	\$ 588,500,000	
• Issuance Savings	<u>2,054,800</u>	
Total	\$ 590,554,800	
• Expended	\$ 49,736,354	
• Encumbered	<u>108,660,442</u>	
•      Total	\$ 158,396,796	
• Unassigned Funds	\$ 432,158,004	(Includes Program Contingency)
• Current Year Interest	<u>7,881,512</u>	
Total Unassigned	\$ 440,039,516	

## Safety Operations Center & Police Department

### Schedule Summary

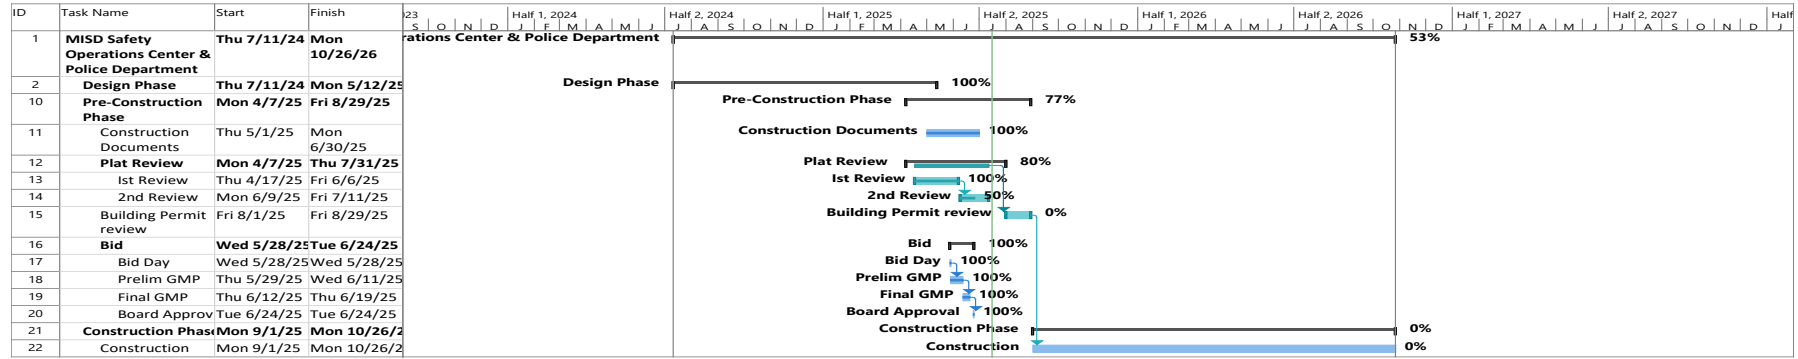

### Cost Summary

Budget Amount \$ 26,000,000.00

Contract Award Amount: \$25,220,899.00

Change Order:

New Contract Amount

### Scope of Work


1. The new building to serve the Mansfield Independent School District needs a new Safety, Security, and Police Department.
2. The new facility will include an Emergency Operations Center (EOC).
3. Provide adequate space for all departments and staff.
4. Virtual Training Simulator for officer training.

### Status Summary

1. The Architect and design committee members have had several preliminary meetings to develop the building design based on the specialized requirements.
2. The Design Team is working on scheduling visits to tour other EOC facilities. A topographical survey has been ordered to begin the site design. As soon as the RFQ for Geotechnical & Materials Testing is complete, the Bond Department will order the Geotechnical study to begin.
3. Lee Lewis Construction has started the pre-construction phase of the project.
4. 100% Construction Documents budget estimates are in line.
5. Received COI and P&P Bonds on July 11.
6. Still working on plat.

## MISD New Early Learners Academy

### Schedule Summary

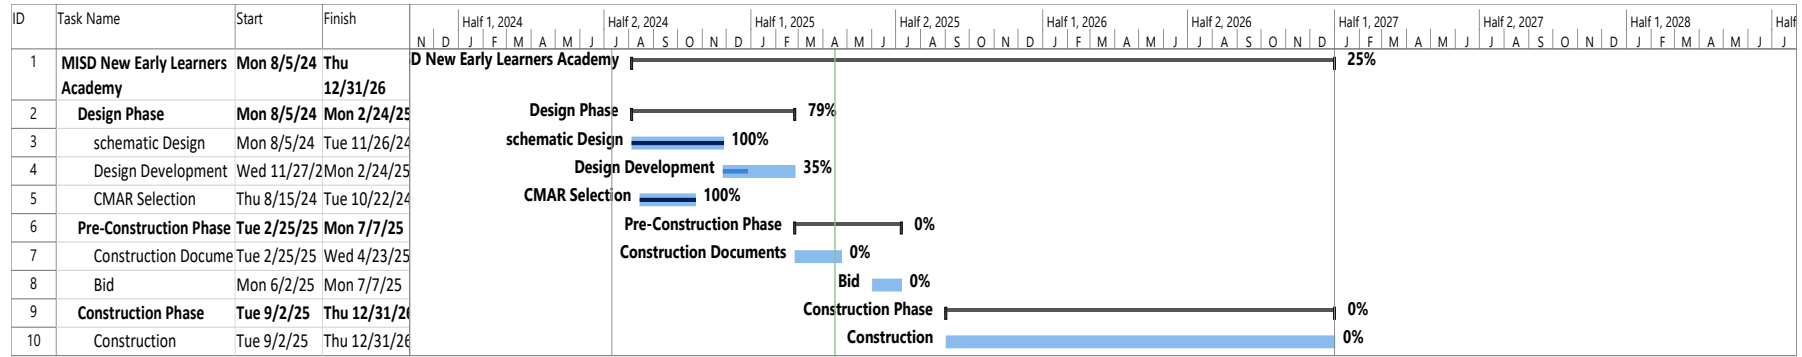

### Budget

\$46,803,188.00

### Cost Summary

Pre-Construction Fee: \$ 65,000.00

Contract Award Amount:

Change Order:

New Contract Amount

### Scope of Work


1. Build a New Early Learners Academy

### Status Summary

1. Mansfield ISD, Huckabee Architects, and Herbert Beasley Land Surveyors are coordinating with the City to finalize the plat and tree survey in preparation for permit issuance upon GMP approval.
2. Signed and sealed construction documents were issued, Bid Opening was held at Core Construction on Thursday, July 10<sup>th</sup>, with the final GMP to be presented at the August Board meeting.
3. Mansfield ISD, Huckabee Architects, and the Jandrucko Administration and Curriculum & Instruction teams have finalized experience plans in collaboration with Exhibit Concepts.

## Phase 1 Package 1 Jobe & Worley MS Fine Arts Addition & CIP Package

### Schedule Summary

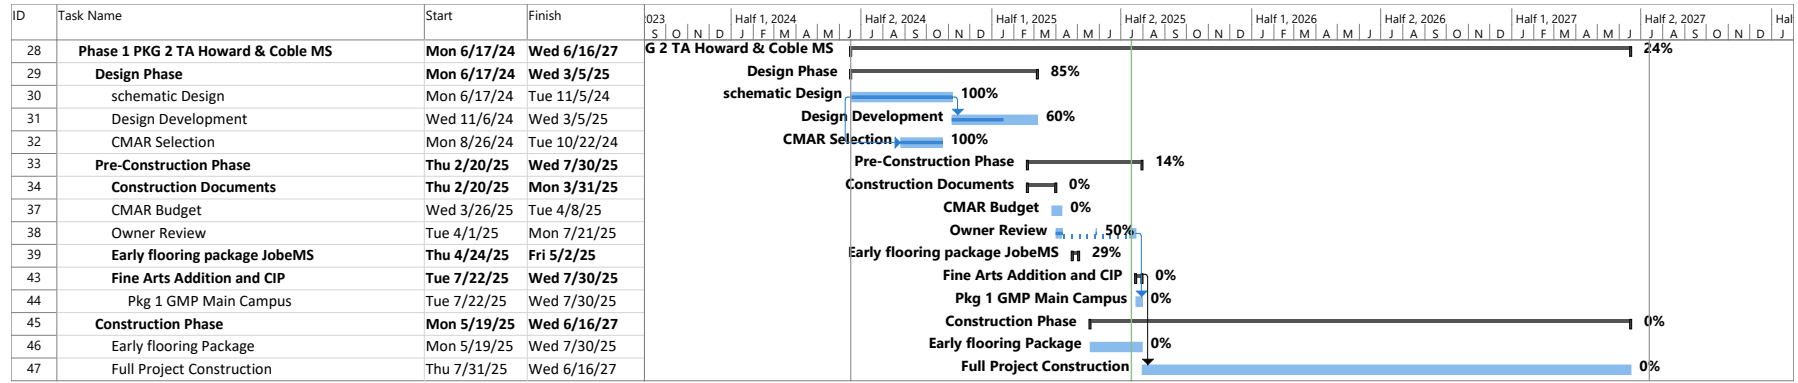

### Cost Summary

Budget Amount: \$ 34,232,820.00

Change Order:

Contract Award Amount: \$31,608,506.00

Pre-Con Fee: \$40,000.00

New Contract Amount: Early Flooring Jobe: \$914,345.00

New Contract Amount: Jobe GMP#2 \$15,767,159.00 New Contract Amount: Worley GMP#2 \$14,927,003.00

### Scope of Work


1. New Fine Arts additions to for Jobe & Worley Middle Schools
2. Replace the running tracks, bleachers, and scoreboards at both schools,
3. Renovate weightrooms.
4. Life cycle replacements on air conditioning, flooring as required.
5. Linda Jobe will get new serving lines.

### Status Summary

1. Huckabee Architects have completed the signed and sealed construction documents. GMP has been finalized and will be presented at July board meeting.
2. Early flooring installation at Jobe Middle School will begin this month, with substantial completion anticipated by August 6<sup>th</sup>. Flooring project is on schedule to be completed and prepped for technology and furniture put back before students return to school. Rubber flooring is scheduled for installation over the winter break with substantial completion anticipated by January 6<sup>th</sup>.
3. Proposed phasing plans have been developed and review with campus principals.

## Middle School Fine Arts Additions PKG 2 T A Howard & James Coble Middle School with Life Cycle Replacement

### Schedule Summary

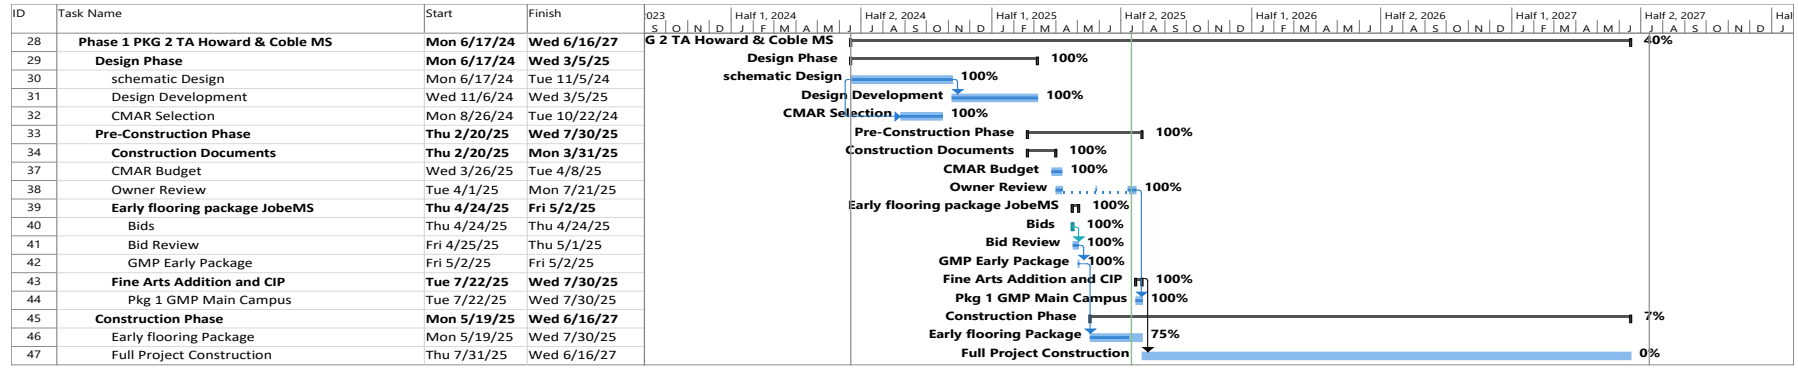

### Cost Summary

Budget Amount: \$ 34,600,000.00

Change Order:

Contract Award Amount: \$ 29,785,236

Pre-Con Fee: \$80,000.00

New Contract Amount: Early Flooring Coble: \$967,084.00

New Contract Amount: Coble GMP#2 \$16,380,462.00

New Contract Amount: Howard GMP#2 \$12,432,560.00

### Scope of Work


1. Construct Fine Arts additions.
2. Safety & Security Upgrades including weapons detection systems.
3. Technology infrastructure & life cycle replacements.
4. MEP life cycle replacements.
5. New serving lines in the cafeteria.
6. Civil work, track, bleacher, and scoreboard replacements.
7. Proposition B, interactive panels in classrooms and common spaces and digital signage.

### Status Summary

1. Huckabee Architects have completed the signed and sealed construction documents. Lewis Construction Inc. to finalize the GMP for the July board meeting.
2. Early flooring admin area completion 7/12, early flooring project deadline August 1, 2025
3. Rubber flooring in Choir and Band is scheduled for installation over the winter break.

## Middle School Fine Arts Addition PKG 3 Jones & Wester with Life Cycle Replacement

### Schedule Summary

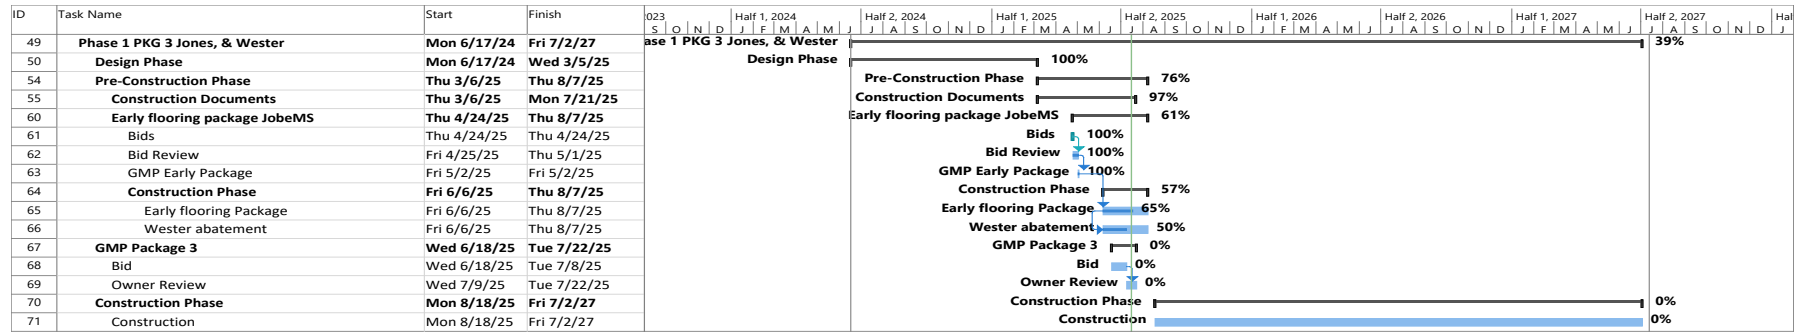

### Cost Summary

Pre – Construction Fee: \$40,000.00

Estimated Budget Amount: \$49,399,156

New Contract Amount: \$39,630,477.00

Jones Early Flooring Package: \$910,702.00

Change Order:

Wester Early Package (Abatement/Demo): \$1,215,207.00,

### Scope of Work

1. Construct Fine Arts additions.
2. Safety & Security Upgrades including weapons detection systems.
3. Technology infrastructure & life cycle replacements.
4. MEP life cycle replacements, including lighting upgrades at Brooks Wester MS.
5. New serving lines in the cafeteria at Danny Jones MS.
6. Proposition B, interactive panels in classrooms and common spaces and digital signage


### Status Summary

1. Huckabee Architects have completed the signed and sealed construction documents. GMP has been finalized and will be presented at July board meeting.
2. Early flooring installation at Jobe Middle School will begin this month, with substantial completion anticipated by August 6<sup>th</sup>. Flooring project is on schedule to be completed and prepped for technology and furniture put back before students return to school. Rubber flooring is scheduled for installation over the winter break with substantial completion anticipated by January 6<sup>th</sup>.
3. Proposed phasing plans have been developed and review with campus principals.

4. Early site demolition & abatement is underway at Wester Middle School with substantial completion anticipated by August 6<sup>th</sup>.



**Ben Barber Innovation Academy / Frontier STEM Academy CTE Addition & Life Cycle Replacement Phoenix Academy**  
Schedule Summary

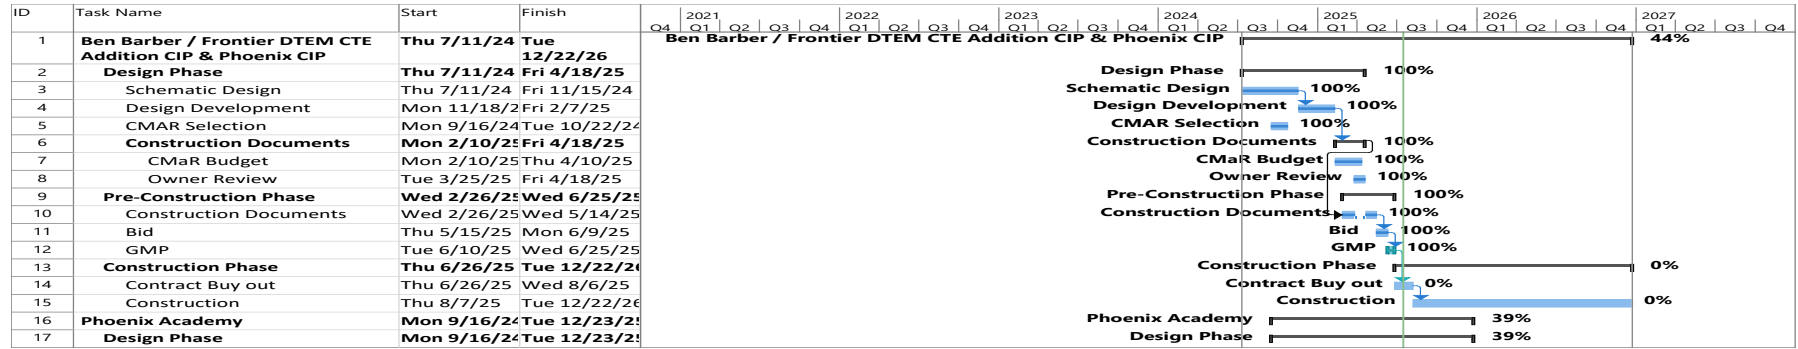

Cost Summary

Proposed Budget: Ben Barber CTE \$18,319,424.00

Pre – Construction Fee: \$40,000.00

Contract Award Amount: \$21,728,789.00

Change Order:

New Contract Amount

Scope of Work

1. Ben Barber CTE Addition & CIP
  - a. New CTE Addition
  - b. Roof Top Unit R-22 replacement, life safety & security upgrades, Day Care play surface replacement.
  - c. Paving repairs
2. Phoenix Academy
  - a. Life safety & security upgrades, Interior Lighting replacement
  - b. Paving repairs

Status Summary

1. New programs to be included are Robotics and Automation Technology, Biomedical Sciences, Aviation Maintenance, and HVAC.
2. Huckabee Architects, Mansfield ISD, and Herbert Beasley Land Surveyors are coordinating to finalize the plat required for permit issuance.
3. We will proceed with the NTP, bonding, insurance, and contract documents to ensure construction can begin promptly once permits are secured.
4. Now receiving new equipment.
5. Core Construction will erect fence by August 8<sup>th</sup>.

### A-1 Mansfield High School Baseball & Softball Field Turf Upgrades, Batting Cages & Bull Pens

#### Schedule Summary

ID	Task Name	Start	Finish	2022				2023				2024				2025				2026
				Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	
1	A-1 Mansfield High School Baseball, Softball Turf Projects, Batting Cages & Bullpens	Tue 9/3/24	Tue 12/30/25	h School Baseball, Softball Turf Projects, Batting Cages & Bullpens																60%
2	Design Phase	Tue 9/3/24	Mon 1/20/25	Design Phase																100%
5	Pre-Construction Phase	Tue 1/21/25	Tue 5/27/25	Pre-Construction Phase																99%
11	Construction Phase	Tue 5/27/25	Tue 12/30/25	Construction Phase																4%
12	NTP	Mon 6/2/25	Mon 6/2/25	NTP																100%
13	Contract Buy Out	Tue 5/27/25	Thu 6/19/25	Contract Buy Out																25%
14	Construction	Mon 6/30/25	Tue 12/30/25	Construction																0%

#### Cost Summary

Pre – Construction Fee: \$10,000.00

Budget Amount: \$6,508,530

Contract Award Amount: \$5,976,120.00

Change Order:

New Contract Amount


#### Scope of Work

1. New Turf for Baseball & Softball fields at the 5 High Schools.
2. New batting cages for baseball & softball at each campus.

#### Status Summary

1. Construction began with substantial completion targeted for December 31, 2025.
2. Demolition of existing structures is underway, the installation of storm sewer has begun, and subgrade preparation and drainage work has started at the baseball and softball fields.
3. The Athletics Department has finalized color selections of batting cages


### Schedule Summary

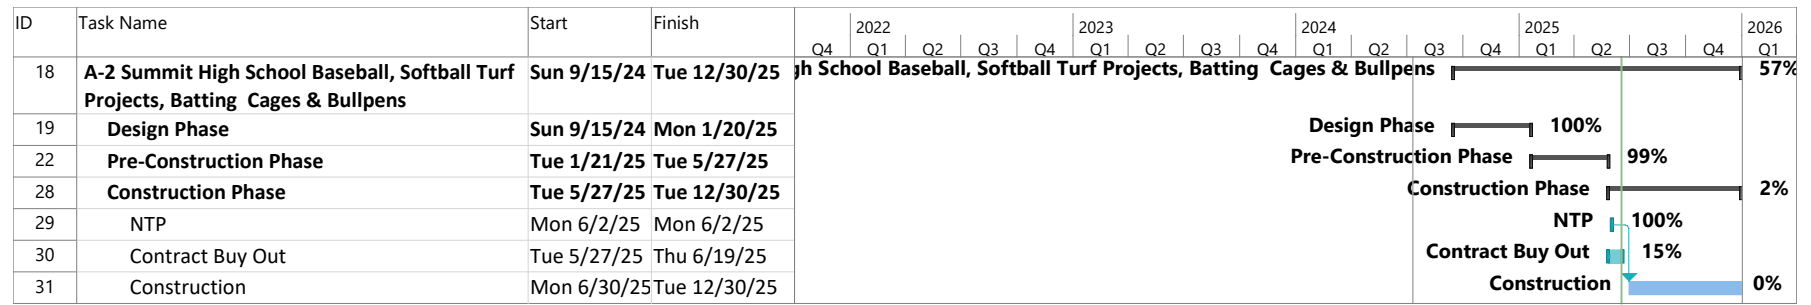

### A-3 Legacy High School Baseball, Softball Turf Project, Batting Cages & Bullpens

#### Schedule Summary

ID	Task Name	Start	Finish	2022				2023				2024				2025				2026
				Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
33	A-3 Legacy High School Baseball, Softball Turf Projects, Batting Cages & Bullpens	Sun 9/15/24	Tue 12/30/25	h School Baseball, Softball Turf Projects, Batting Cages & Bullpens																59%
34	Design Phase	Sun 9/15/24	Mon 1/20/25	Design Phase												100%				
37	Pre-Construction Phase	Tue 1/21/25	Tue 5/27/25	Pre-Construction Phase												99%				
43	Construction Phase	Tue 5/27/25	Tue 12/30/25	Construction Phase												7%				
44	NTP	Mon 6/2/25	Mon 6/2/25	NTP												100%				
45	Contract Buy Out	Tue 5/27/25	Thu 6/19/25	Contract Buy Out												50%				
46	Construction	Mon 6/30/25	Tue 12/30/25	Construction												0%				



#### Cost Summary

Pre -Construction Fee: \$ 10,000.00

Budget Amount: \$6,135,302.00

Contract Award Amount: \$5,563,466.00

Change Order:

New Contract Amount

#### Scope of Work

1. New Turf for Baseball & Softball fields at the 5 High Schools.
2. New batting cages for baseball & softball at each campus.

#### Status Summary

1. Construction has begun with substantial completion targeted for December 31, 2025.
2. OAC meetings occurred with Crossland Construction, Huckabee Architects, and Mansfield ISD last week.
3. Construction company is working on completion of demolition of paving sidewalks, and existing batting cages. They are removing existing scoreboards and proof rolling and placing a 6" select fill cap on the fields in preparation for turf. They are also working on underground utility locates, utility demolition, and storm drainage re-work.

### A-4 Lake Ridge High School Baseball, Softball Turf Project, Batting Cages & Bullpens

#### Schedule Summary

ID	Task Name	Start	Finish	Timeline																			
				2022				2023				2024				2025				2026			
				Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1		
48	A-4 Lake Ridge High School Baseball, Softball Turf Projects, Batting Cages & Bullpens	Tue 9/3/24	Wed 12/31/25	h School Baseball, Softball Turf Projects, Batting Cages & Bullpens																		59%	
49	Design Phase	Tue 9/3/24	Mon 1/20/25	Design Phase																		100%	
52	Pre-Construction Phase	Tue 1/21/25	Tue 5/27/25	Pre-Construction Phase																		99%	
58	Construction Phase	Tue 5/27/25	Wed 12/31/25	Construction Phase																		3%	
59	NTP	Mon 6/2/25	Mon 6/2/25	NTP																		100%	
60	Contract Buy Out	Tue 5/27/25	Mon 6/30/25	Contract Buy Out																		15%	
61	Construction	Mon 6/30/25	Wed 12/31/25	Construction																		0%	

#### Cost Summary

Pre -Construction Fee: \$ 10,000.00

Budget Amount: \$5,937,467.00

Contract Award Amount: \$5,812,794.00

Change Order:

New Contract Amount

#### Scope of Work

1. New Turf for Baseball & Softball fields at the 5 High Schools.
2. New batting cages for baseball & softball at each campus.

#### Status Summary

1. Construction has begun with substantial completion targeted for December 31, 2025.
2. OAC meetings occurred with Crossland Construction, Huckabee Architects, and Mansfield ISD last week.
3. Crossland Construction has begun on removal of existing fencing, batting cages, mow strip, and concrete. The have installed their seal fence and began dirt work. They are removing existing scoreboards and will demo the storm drain according to drawings.

## Timberview High School Baseball & Softball Field Turf Upgrades, Batting Cages & Bull Pens

### Schedule Summary

ID	Task Name	Start	Finish	2022				2023				2024				2025				2026 Q1
				Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	
63	A-5 Timberview High School Baseball, Softball Turf Projects, Batting Cages & Bullpens	Tue 9/3/24	Tue 12/30/25	h School Baseball, Softball Turf Projects, Batting Cages & Bullpens																61%
64	Design Phase	Tue 9/3/24	Mon 1/20/25	Design Phase 100%																
67	Pre-Construction Phase	Tue 1/21/25	Tue 5/27/25	Pre-Construction Phase 99%																
73	Construction Phase	Tue 5/27/25	Tue 12/30/25	Construction Phase 7%																
74	NTP	Mon 6/2/25	Mon 6/2/25	NTP 100%																
75	Contract Buy Out	Tue 5/27/25	Thu 6/19/25	Contract Buy Out 50%																
76	Construction	Mon 6/30/25	Tue 12/30/25	Construction 0%																

### Cost Summary

Pre -Construction Fee: \$ 10,000.00

Budget Amount: \$6,229,786.00

Contract Award Amount: \$5,652,763.00

Change Order:

New Contract Amount

### Scope of Work


1. New Turf for Baseball & Softball fields at the 5 High Schools.
2. New batting cages for baseball & softball at each campus.

### Status Summary

1. Construction is scheduled to begin this month with substantial completion targeted for December 31, 2025. Awaiting permit from the City of Arlington.
2. Site plan has been approved by the City and Building plan comments were addressed by Huckabee Architects last week.
3. Contractor is pursuing early site grading permit with the City of Arlington.
4. Minor site preparation activities have begun.

## 6<sup>th</sup> Ave Transportation Building Main Transportation, Danny Griffin OPS

### Schedule Summary

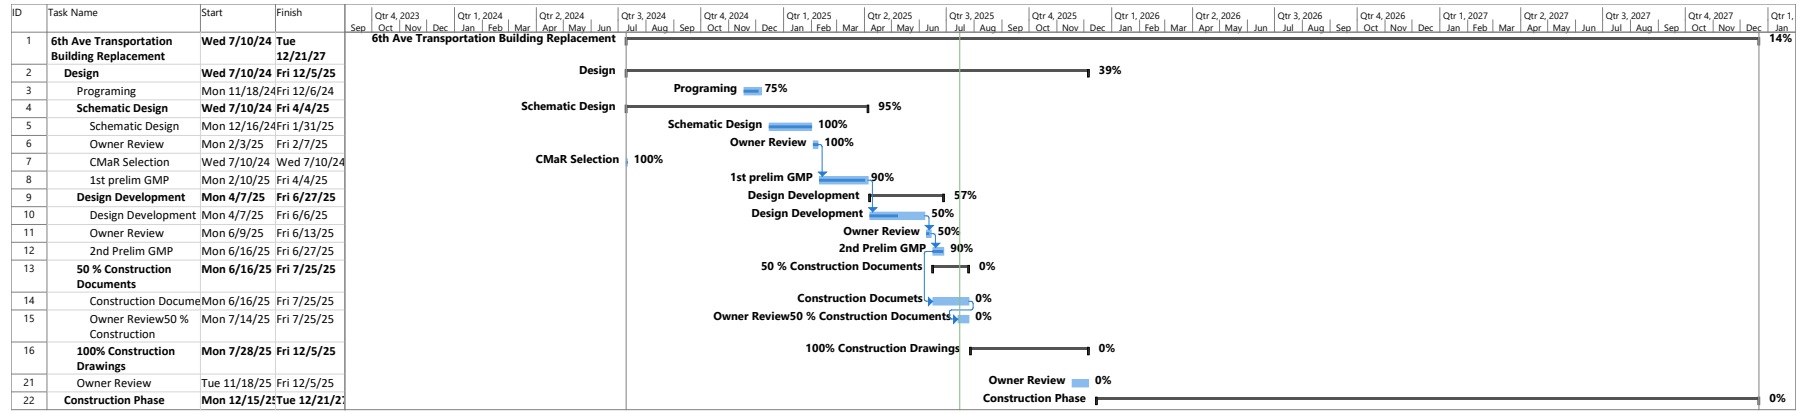

### Cost Summary

Revised Budget Amount: \$25,330,120.00

Change Order:

New Contract Amount

### Scope of Work:


1. New transportation offices with enough office space for staff, increased space for technology closet. Provide adequate space for training the 6<sup>th</sup> Avenue transportation department.
2. A new bus mechanic repair shop, so mechanics can safely work on buses out of the weather.
3. Additional bus parking for up to 150 buses, and the staff parking to accommodate the additional buses.
4. The design now will have a 10,000 gal unleaded and 20,000-gal diesel tanks with enough pumps to meet the future needs of the district.

### Status Summary:

1. Smith & Co. will be working with Huckabee as the architect.
2. Currently working on site plan, floor plan layout and the schematic design.
3. Authers Building Group is the selected CMAr.
4. CMAr is almost complete with the SD Estimate.
5. Smith & Co. Presented to the June Board meeting the DD presentation.
6. Authers Building Group provided preliminary 50 % DD pricing that was inline with proposed budget amounts.

## Cross Timbers Intermediate School Life Cycle Roof Overlay Project

### Schedule Summary

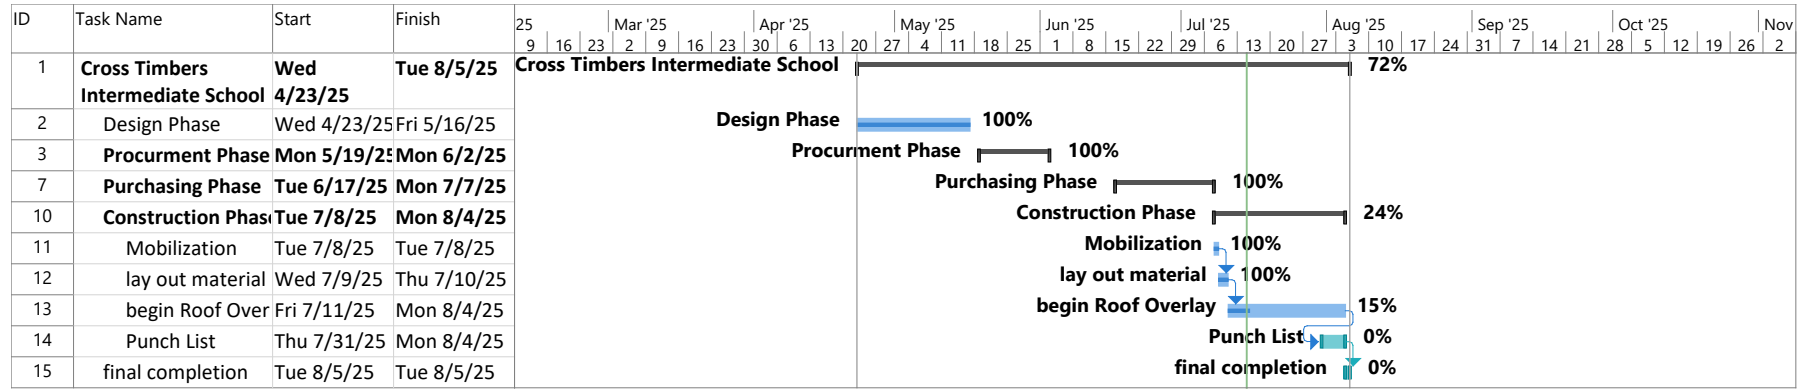

### Cost Summary

Contract Award Amount: \$ 858,619.73

Change Order:

New Contract Amount

### Scope of Work

1. Original roof had reached the end of life and warranty expired.
2. Overlay 80 mil Duro – Last Single Ply PVC roof membrane with Rock-board over vacuumed gravel roof.
3. Extend roofing materials under roof top units and new metal coping.
4. As part of the Proposition A Capitol Improvement Scope, MISD, Huckabee, and RAM USA inspected the existing roof for water damage and determined it would be acceptable to provide a new single ply roof membrane over ½” Duro-Guard Dexcell Roof Board.


### Status Summary:

1. Design Phase began in April of 2025 and completed in May 2025.
2. Bidding was held through the TIPS Procurement coop to the Roofing Manufacturer Duro-Last. Utilizing only current qualified Platinum Level roof installers. Merit Roofing was the best overall value and the lowest bidder.
3. Contractor has mobilized on site and is beginning to install the roof overlay.



## Donna Shepard Intermediate School Life Cycle Roof Overlay Project

### Schedule Summary

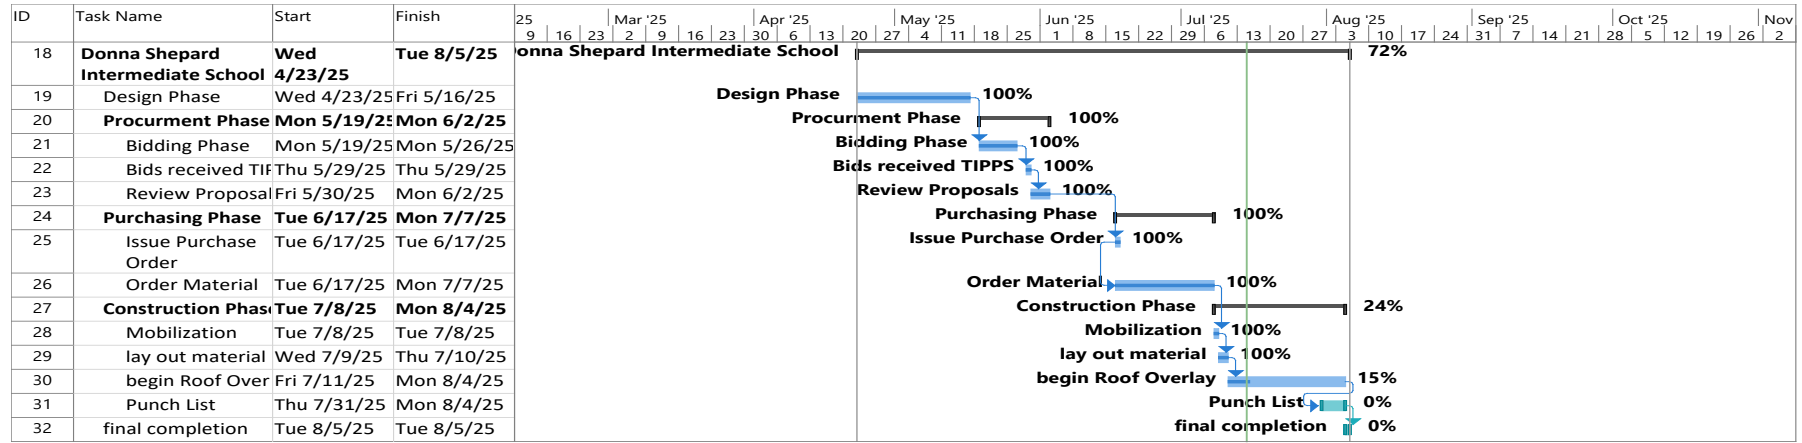

### Cost Summary

Contract Award Amount: \$ 974,816.30

Change Order:

New Contract Amount

### Scope of Work


1. Original roof had reached the end of life and warranty expired.
2. Overlay 80 mil Duro – Last Single Ply PVC roof membrane with Rock-board over vacuumed gravel roof.
3. Extend roofing materials under roof top units and new metal coping.
4. As part of the Proposition A Capitol Improvement Scope, MISD, Huckabee, and RAM USA inspected the existing roof for water damage and determined it would be acceptable to provide a new single ply roof membrane over ½” Duro-Guard Dexcel Roof Board.

### Status Summary:

1. Design Phase began in April of 2025 and completed in May 2025.
2. Bidding was held through the TIPS Procurement coop to the Roofing Manufacturer Duro-Last. Utilizing only current qualified Platinum Level roof installers. Prime Source Roofing was the best overall value and the lowest bidder.
3. Contractor has mobilized on site and is beginning to install the roof overlay.

### D.P. Morris Elementary School Life Cycle Roof Overlay Project

#### Schedule Summary

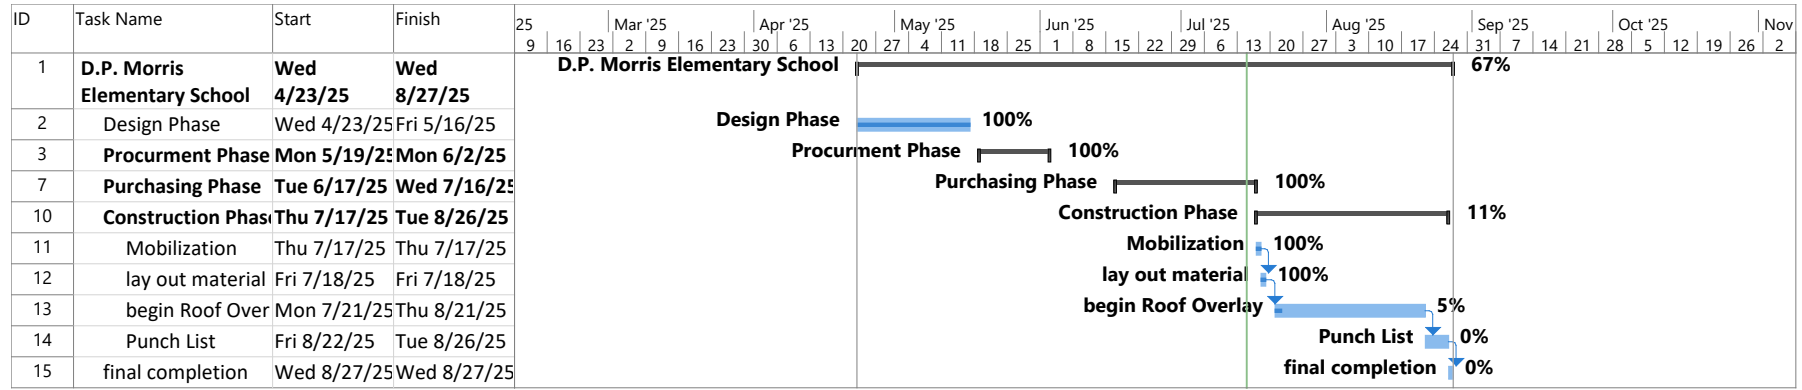

#### Cost Summary

Contract Award Amount: \$ 823,677.26

Change Order:

New Contract Amount

#### Scope of Work


1. Original roof had reached the end of life and warranty expired.
2. Overlay 80 mil Duro – Last Single Ply PVC roof membrane with Rock-board over vacuumed gravel roof.
3. Extend roofing materials under roof top units and new metal coping.
4. As part of the Proposition A Capitol Improvement Scope, MISD, Huckabee, and RAM USA inspected the existing roof for water damage and determined it would be acceptable to provide a new single ply roof membrane over ½” Duro-Guard Dexcell Roof Board.

#### Status Summary:

1. Design Phase began in April of 2025 and completed in May 2025.
2. Bidding was held through the TIPS Procurement coop to the Roofing Manufacturer Duro-Last. Utilizing only current qualified Platinum Level roof installers. Prime Source Roofing was the best overall value and the lowest bidder.
3. Contractor has mobilized on site and is beginning to install the roof overlay.

## Willie Brown Elementary School Life Cycle Roof Overlay Project

### Schedule Summary

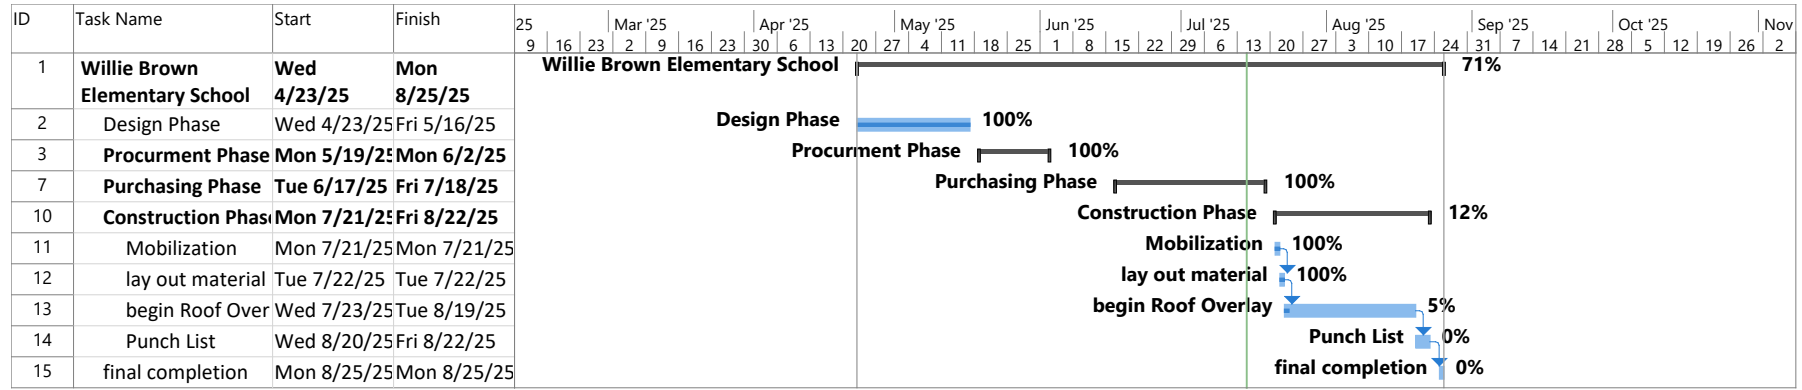

### Cost Summary

Contract Award Amount: \$ 820,209.17

Change Order:

New Contract Amount

### Scope of Work


1. Original roof had reached the end of life and warranty expired.
2. Overlay 80 mil Duro – Last Single Ply PVC roof membrane with Rock-board over vacuumed gravel roof.
3. Extend roofing materials under roof top units and new metal coping.
4. As part of the Proposition A Capitol Improvement Scope, MISD, Huckabee, and RAM USA inspected the existing roof for water damage and determined it would be acceptable to provide a new single ply roof membrane over ½” Duro-Guard Dexcell Roof Board.

### Status Summary:

1. Design Phase began in April of 2025 and completed in May 2025.
2. Bidding was held through the TIPS Procurement coop to the Roofing Manufacturer Duro-Last. Utilizing only current qualified Platinum Level roof installers. Prime Source Roofing was the best overall value and the lowest bidder.
3. Contractor has mobilized on site and is beginning to install the roof overlay.

## Transportation Bus Purchases

### Schedule Summary

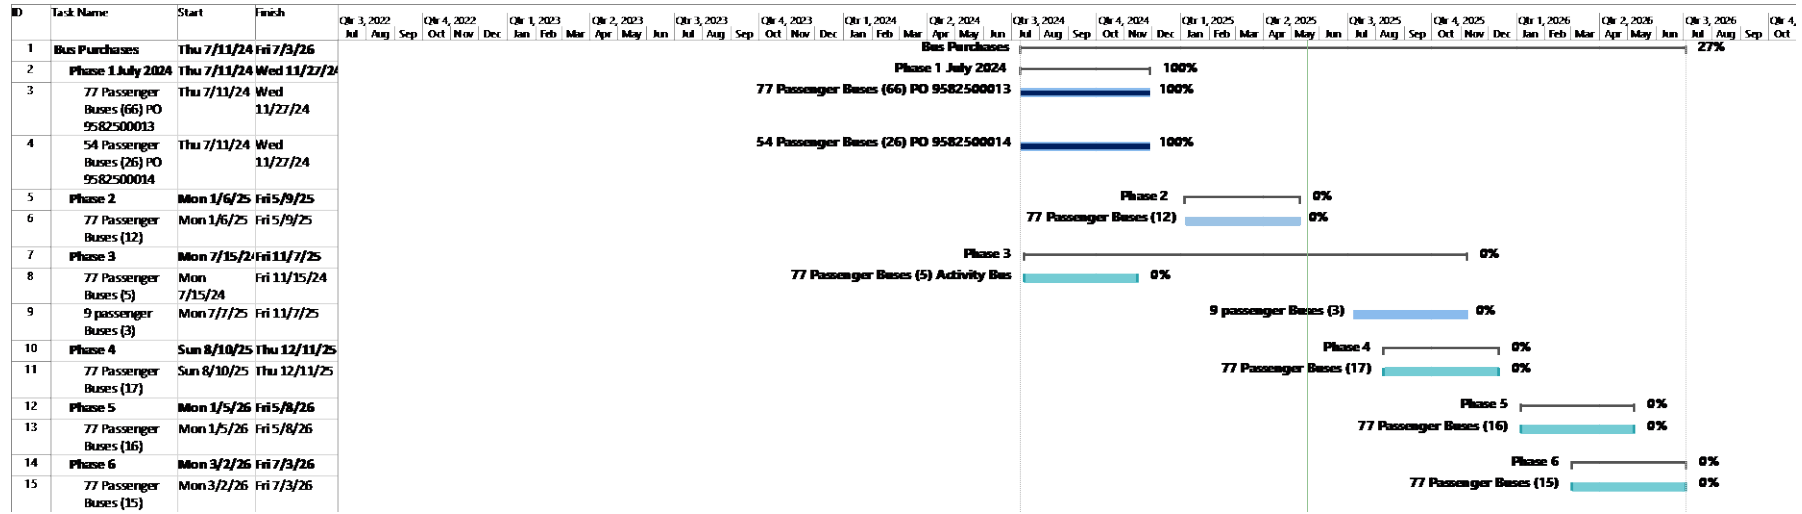

### Cost Summary

Contract Award Amount: 14,581,228

### Scope of Work


1. Purchase 165 replacement buses.

### Status Summary

1. July 15 – Purchased 66 ea., 77 passenger buses. All have been received.
2. July 15 – Purchased 26 ea., 54 passenger buses. All have been received.
3. The second round of bus orders are in process.

## Technology Infrastructure Proposition A and Proposition B Interactive Panels and Digital Displays

### Schedule Summary

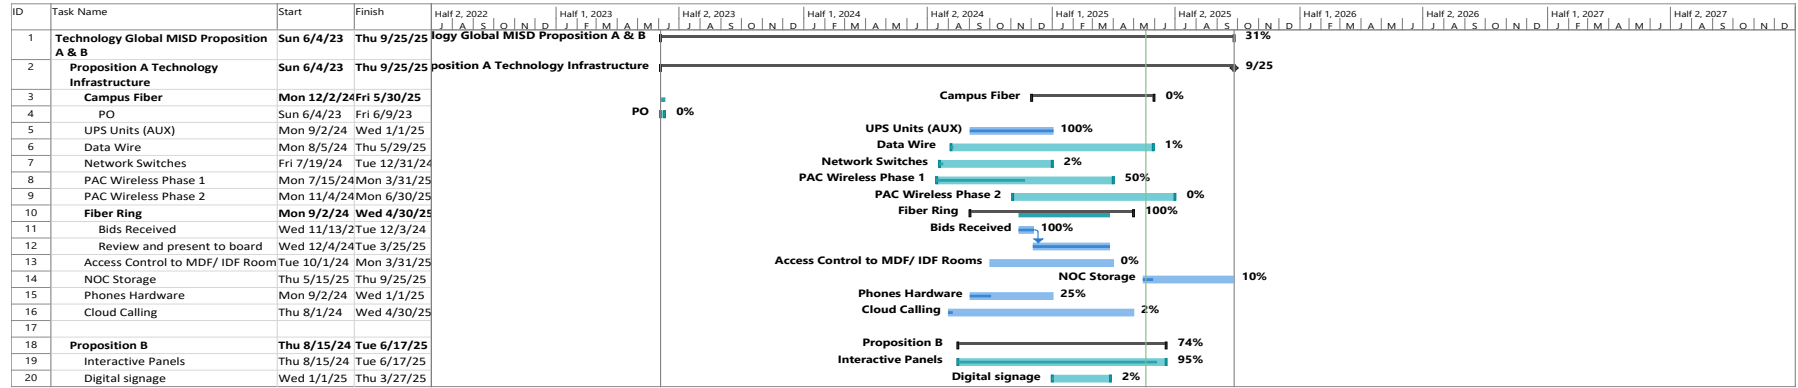

### Cost Summary

Contract Award Amount:

Change Order:

New Contract Amount

### Scope of Work


1. Proposition A.
  - a. Network switches throughout the district.
  - b. New fiber ring.
  - c. UPS Units
  - d. NOC Storage
2. Proposition B
  - a. Interactive Panels for classrooms
  - b. Digital signage for common areas, libraries

### Status Summary

1. The Technology Department will start issuing Purchase Orders for Proposition A infrastructure by the end of July and into August for switches, fiber ring, and other components.
2. Proposition B's interactive panels and digital signage will be issued as well.
3. Switches & WAP PO provided to vendors. Technology Department meeting with vendor & installer to go over schedule to begin installs.
4. Phone refresh meetings was held this month to work on product configuration.
5. Contera was selected as the best overall bidder for the fiber ring.
6. Interactive panel install is almost complete.

## Proposition A Safety & Security Infrastructure District Wide S-2

### Schedule Summary

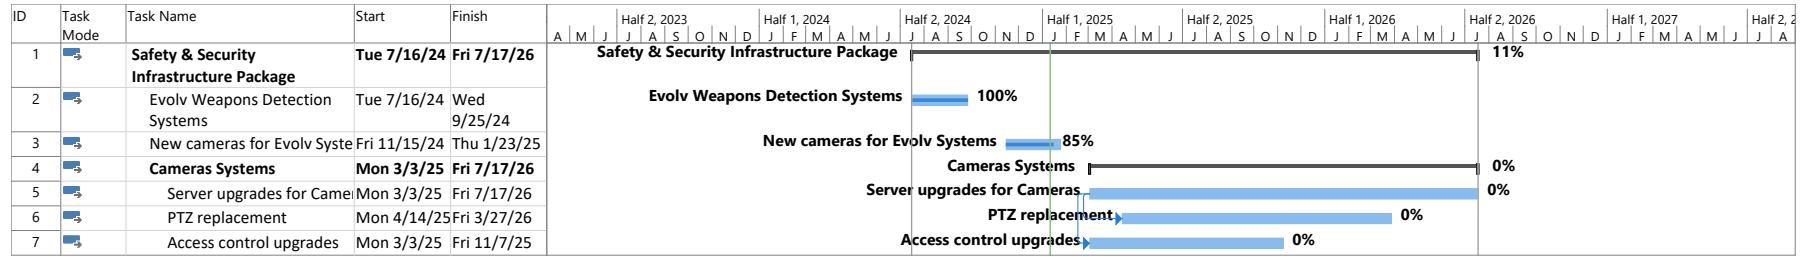

### Cost Summary

Budget Amount: \$7,200,000.00

Change Order:

New Contract Amount

### Scope of Work

1. Installation of Weapons detection systems
2. Upgrading PTZ cameras throughout the district, camera servers and access control

### Status Summary

1. Safety and Security has issued PO for the capital lease Evolv Weapons Detection systems. Much of the material is on hand and installations have begun for middle schools, high school competition gyms, and stadiums. Installation should be completed mid-September.
2. Cameras & access control will begin later this year.
3. Meeting was held with a design consultant to review our camera and access control district wide.
4. Evron was selected to install additional cameras at the Evolv Weapons Detection.
5. Several presentations with camera manufacture and software companies were attended by the Bond, Safety & Security Departments, and the MISD PD. Further evaluations are forthcoming over the next couple of months.
