



Collin College

2017 Capital Improvement Program
Monthly Report
May 2021

Collin County Community College District

Project Reference: 60541060
Project Number: 60541060

June 07, 2021

Quality information

Prepared by



Nuria Cortes
Program Controls Manager

Reviewed by



Jeff Hagerich
Deputy Program Director

Approved By



Adrian Grimes
Program Director

Revision History

Revision	Revision date	Details	Authorized	Name	Position
First Publication	June 07, 2021	May '21 Report	Yes	Adrian Grimes	Program Director

Distribution List

# Hard Copies	PDF Required	Association / Company Name
	1	Dr. Neil Matkin / Collin College
	1	Chris Eyle / Collin College

Prepared for:

Collin County Community College District
3452 Spur 399
Suite 327
McKinney, TX 75069

Prepared by:

Nuria Cortes
Program Controls Manager
E: ncortes.aecom@collin.edu

AECOM
13355 Noel Road
4th Floor
Dallas TX, 75240
aecom.com

Copyright © 2020 by AECOM

All rights reserved. No part of this copyrighted work may be reproduced, distributed, or transmitted in any form or by any means without the prior written permission of AECOM.

Table of Contents

1.	Introduction	5
2.	Executive Summary	5
3.	Scope	7
3.1	Phase 1	7
3.2	Phase 2	7
3.3	Phase 3	8
4.	Community	8
4.1	Project Teams	8
4.1.1	Phase 1	8
4.1.2	Phase 2	9
4.1.3	Phase 3	10
4.2	Current Personnel Estimate	11
4.3	Community Outreach	11
5.	Schedule	12
5.1	Program	12
5.2	Phase 1	12
5.3	Phase 2	13
5.4	Phase 3	15
6.	Budget	16
6.1	Program Summary	16
6.2	Phase 1	16
6.3	Phase 2	17
6.4	Phase 3	18
6.5	Phase A	19
6.6	Additional Program Budgets	20
7.	Completed Items	20
7.1	General Program	20
7.2	Procurement	20
7.3	Design	20
7.4	Pre-Construction	20
7.5	Construction	20
7.6	Acceptance and Close-Out	21
8.	Pending Items	21
8.1	General Program	21
8.2	Procurement	21
8.3	Design	21
8.4	Pre-Construction	21
8.5	Construction	21
8.6	Acceptance and Close-Out	21
	Appendix A – Construction Progress Photos	22

1. Introduction

On May 6, 2017, voters approved Collin College's \$600 million bond proposal to facilitate a long-range plan to accommodate the projected population growth in Collin County over the next two decades. The program consists of 4 new campuses and 2 new facilities.

On May 16, 2017, in a special session, the Board of Trustees granted the District President authority to enter and negotiate into contract with AECOM Technical Services, Inc. (AECOM) to provide Program Management Services to the Collin College 2017 Capital Improvement Program. On May 25, 2017, Collin College issued a Notice to Proceed to AECOM. As part of these services, AECOM will deliver a monthly report to provide status and progress of key aspects of the Program.

2. Executive Summary

The Program is progressing as planned with no major issues to report at this time.

Completed and Pending Items

- [Technical Campus – Received the Certificate of Occupancy from City of Allen on May 10th](#)
- [Wylie Campus – The installation of scuppers at the Conference Center is completed. Signage updates were approved by the Provost and are in production. The 11-month project walk with Collin College, AECOM, Page Southerland Page, and Skanska was done on May 27th.](#)
- [Celina Campus – Irrigation and landscaping is on-going at the campus. Interior finishes work is in final stages throughout the building. Punchlist items are being worked on.](#)
- [Farmersville Campus – Additional flag poles have been installed. Additional infrastructure for the Barnes and Noble bookstore has been completed. Construction of the City's Collin Parkway road project is on-going.](#)
- [IT Center – Overhead MEP is near completion in Area B. Door hardware and lighting controls programming is in progress. Finishing of the bridges, monumental stairs, and terrazzo flooring is on-going. Restroom finishes and fixtures are on-going. Priming, painting, and floor installation is nearing completion. At the Quad area, light fixtures and pavers are being installed, irrigation and planting is on-going, and the water feature installation is complete. Architect/Owner punchlist walks are on-going.](#)
- [Frisco Campus \(Addition and Renovations\) – Building permits for Lawler Hall, Heritage Hall and Founders Hall interior renovations have been issued. Engineering drawings for Lawler Hall and Alumni Hall have been approved by the City. Installation of the fire water line is complete for the firelane. Hydronic pipe has been delivered and area is being prepped for installation. Landscape is complete at the loop road and parking lot.](#)
- [McKinney Campus \(Welcome Center and Renovations\) – Site Upgrades: Installation of underground storm piping, storm inlets and water lines is on-going. Welcome Center: foundation work is on-going. Renovations: Demo work in the kitchen is on-going. Demolition in the dental offices is ongoing.](#)

Items of close attention

- [Completion of the new outer loop access road in Celina by Collin County/NTTA](#)
- [Monitoring the progress of the new road the City of Farmersville is installing along the west entrance of the Farmersville Campus](#)
- [Monitoring the progress of the Celina Campus and the IT Center to ensure they are completed in time for Fall 2021 classes.](#)

Budget Summary

- \$554,362,207 of the \$600,000,000 has been committed to-date in the form of contracts with various vendors. This represents 92.39% of the overall program budget committed.
- \$505,311,661 of the \$554,362,207 committed amount has been expended to-date. This represents 91.15% of the commitments to date and 84.22% of the program budget.

3. Scope

3.1 Phase 1

- Wylie Campus
 - Construction of a campus on a new approximately 97-acre site
 - The campus includes:
 - Campus Commons
 - Library
 - Student Center/Conference Center
 - Central Utility Plant
- Technical Campus
 - Construction of a Technical Campus on a new 32-acre site in Allen, Texas
 - The campus includes:
 - 450 space underground parking garage
 - Academic Building (includes space for dual credit students)
 - 3 Trade Bar Buildings to support CTE programs

3.2 Phase 2

- Celina Campus
 - Construction of a campus on a new approximately 75-acre site
 - The campus includes:
 - Student Union / Workforce / Instructional Building
- Farmersville Campus
 - Construction of a campus on a new approximately 76-acre site
 - The campus includes:
 - Student Union / Workforce / Instructional Building
- Frisco Campus
 - Construction of a new IT Center building on the existing campus

3.3 Phase 3

- Additions and Renovations at Frisco Campus
 - Alumni Hall Renovations and Additions
 - Lawler Hall Renovations
 - Heritage Hall Upgrades
 - Founders Hall Renovations
 - Wayfinding
- Additional Frisco Campus Projects
 - Construction of a new fire lane, parking lot, and loop road on the existing campus
 - Trane Upgrades
- Additions and Renovations at McKinney Campus
 - Construction of a new Welcome Center on the existing campus
 - New Entry Drive and Parking
 - Pistol Range Demo
 - Kitchen and Dining Renovations in Main Building
 - Dental Hygiene Renovations
 - Wayfinding
- Additional McKinney Campus Projects
 - Trane Upgrades
- Additional Plano Campus Projects
 - Trane Upgrades
 - Wayfinding
- Additional Courtyard Center Projects
 - Trane Upgrades
- Additional CHEC Projects
 - Trane Upgrades

4. Community

4.1 Project Teams

4.1.1 Phase 1

- Wylie Campus
 - Program Manager: AECOM Technical Services, Inc.
 - A/E: Page Southerland Page, Inc.
 - MEP: Reed, Wells, Benson & Co.
 - Civil Engineer: Pacheco Koch Consulting Engineers, Inc.

- Cost Consulting: Vermeulens
- Construction Manager-at-Risk: Skanska USA Building, Inc.
- Commissioning Agent: Bath Group, Inc.
- Technical Campus
 - Program Manager: AECOM Technical Services, Inc.
 - A/E: Perkins+Will, Inc.
 - Associate Architect: Hoefer Wysocki Architecture
 - MEP: Purdy McGuire
 - Civil Engineer: Pacheco Koch Consulting Engineers, Inc.
 - Structural Engineer: L.A. Fuess Partners, Inc.
 - Cost Consulting: Vermeulens
 - Construction Manager-at-Risk: McCarthy Building Companies, Inc.
 - Commissioning Agent: Farnsworth


4.1.2 Phase 2

- Celina Campus
 - Program Manager: AECOM
 - A/E: Beck Architecture, LLC
 - Structural Engineer: L.A. Fuess Partners, Inc.
 - MEP: Reed, Wells, Benson & Co.
 - Civil Engineer: RLK Engineering
 - Construction Manager-at-Risk: JT Vaughn Construction
- Farmersville Campus
 - Program Manager: AECOM
 - A/E: Beck Architecture, LLC
 - Structural Engineer: L.A. Fuess Partners, Inc.
 - MEP: Reed, Wells, Benson & Co.
 - Civil Engineer: RLK Engineering
 - Construction Manager-at-Risk: JT Vaughn Construction
- IT Center
 - Program Manager: AECOM
 - A/E: Beck Architecture, LLC
 - Structural Engineer: L.A. Fuess Partners, Inc.
 - MEP: ME Engineers
 - Civil Engineer: RLK Engineering
 - Construction Manager-at-Risk: JE Dunn Construction

4.1.3 Phase 3

- Welcome Center at the McKinney Campus
 - Program Manager: AECOM Technical Service, Inc.
 - A/E: PBK
 - Construction Manager-at-Risk: Skanska USA Building, Inc.
 - Commissioning Agent: Bath Group, Inc.
- Loop Road/Parking at Frisco Campus
 - Program Manager: AECOM Technical Service, Inc.
 - Civil Engineer: RLK Engineering
 - Construction Manager-at-Risk: JE Dunn Construction
- Fire Lane at Frisco Campus
 - Program Manager: AECOM Technical Service, Inc.
 - Civil Engineer: RLK Engineering
 - Construction Manager-at-Risk: Skanska USA Building, Inc.
- Additional Projects at Frisco Campus
 - Program Manager: AECOM Technical Service, Inc.
 - A/E: Page Southerland Page, Inc.
 - Construction Manager-at-Risk: Skanska USA Building, Inc.
- Additional Projects at McKinney Campus
 - Program Manager: AECOM Technical Service, Inc.
 - A/E: PBK
 - Construction Manager-at-Risk: Skanska USA Building, Inc.
- Trane Upgrades at 5 Existing Campuses
 - Program Manager: AECOM Technical Service, Inc
 - Design – Builder: Trane Companies, Inc.
- Additional Projects at Plano Campus (Wayfinding)
 - Program Manager: AECOM Technical Service, Inc
 - A/E: IN2 Architects
 - Construction Manager-at-Risk: TBD

4.2 Current Personnel Estimate

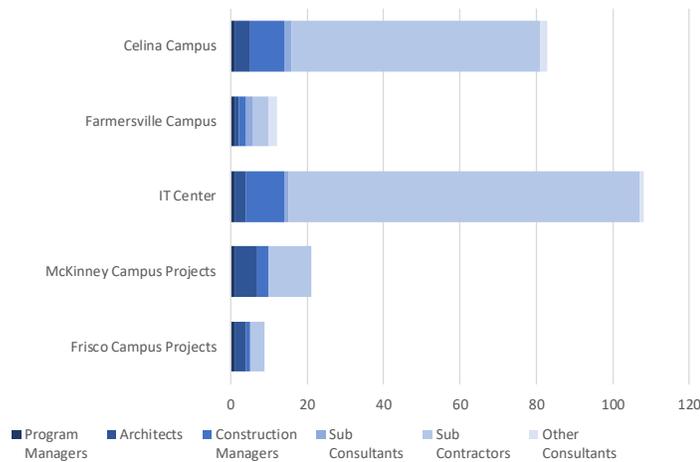


It is estimated that the Program Managers, Architects, Construction Managers, Sub-Consultants, and Sub-Contractors, under contract with Collin College for the 2017 Capital Improvement Program, have 233 employees contributing to the program's progress.

4.3 Community Outreach

- Collin College 2017 Capital Improvement Program Website
 - <https://CollinCollege2017CIP.com>
 - Includes the following features:
 - Program Overview
 - Project Scopes
 - Project Schedules
 - Project Budgets
 - Progress Photos/Renderings
 - Live On-Site Camera Feeds

5. Schedule

5.1 Program

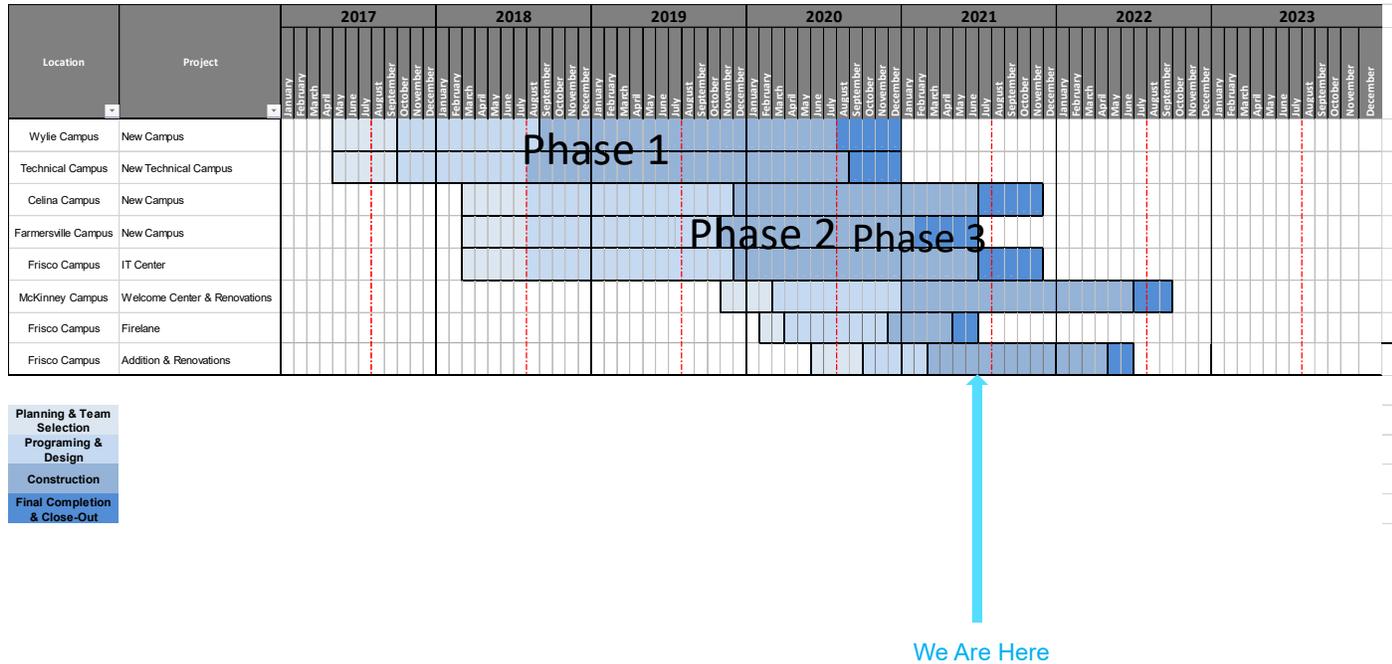

5.2 Phase 1

Wylie Campus

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	May 16, 2017	May 16, 2017	👍	May 16, 2017	👍
BOT Approval of A/E Procurement Method	May 23, 2017	May 23, 2017	👍	May 23, 2017	👍
BOT Approval of Construction Delivery Method	May 23, 2017	May 23, 2017	👍	May 23, 2017	👍
BOT Approval of Recommended Firms	August 22, 2017	August 22, 2017	👍	August 22, 2017	👍
Architect Mobilized	September 12, 2017	September 29, 2017	👎	September 28, 2017	👍
GMP Construction Documents Submittal	June 26, 2018	June 26, 2018	👍	June 26, 2018	👍
BOT Approval of GMP	August 28, 2018	August 28, 2018	👍	August 28, 2018	👍
Contractor Mobilized	September 10, 2018	September 12, 2018	👎	September 12, 2018	👍
Foundations Complete	May 18, 2019	April 30, 2019	👍	April 23, 2019	👍
Structures Complete	June 28, 2019	June 28, 2019	👍	May 23, 2019	👍
Dry-In of Buildings Complete	October 26, 2019	October 26, 2019	👍	October 29, 2019	👍
Permanent Power Complete	September 17, 2019	September 17, 2019	👍	September 21, 2019	👍
Interior Finish-Out Complete	May 1, 2020	June 10, 2020	👎	July 1, 2020	👍
Substantial Completion	June 25, 2020	June 25, 2020	👍	June 30, 2020	👍
Final Completion	August 23, 2020	July 2021	👎	-	
Student Occupancy	August 2020	August 2020	👍	August 1, 2020	👍

Technical Campus

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	May 16, 2017	May 16, 2017	↑	May 16, 2017	✓
BOT Approval of A/E Procurement Method	May 23, 2017	May 23, 2017	↑	May 23, 2017	✓
BOT Approval of Construction Delivery Method	May 23, 2017	May 23, 2017	↑	May 23, 2017	✓
BOT Approval of Recommended Firms	August 22, 2017	August 22, 2017	↑	August 22, 2017	✓
Architect Mobilized	September 12, 2017	September 29, 2017	↓	September 28, 2017	✓
GMP Construction Documents Submittal	April 16, 2018	April 16, 2018	↑	April 19, 2018	✓
BOT Approval of GMP	June 26, 2018	June 26, 2018	↑	June 26, 2018	✓
Contractor Mobilized	July 6, 2018	July 20, 2018	👉	July 26, 2018	✓
Foundations Complete	September 23, 2019	September 23, 2019	↑	July 29, 2019	✓
Structures Complete	November 18, 2019	November 18, 2019	↑	November 13, 2019	✓
Roofing of Buildings Complete	December 20, 2019	December 20, 2019	↑	December 20, 2019	✓
Permanent Power Complete	December 15, 2019	January 10, 2020	↓	January 15, 2020	✓
Building A Punchlist Generated	June 5, 2020	June 12, 2020	👉	June 12, 2020	✓
Building B Punchlist Generated	June 12, 2020	June 19, 2020	👉	June 19, 2020	✓
Building C Punchlist Generated	June 30, 2020	July 6, 2020	👉	July 9, 2020	✓
Building D Punchlist Generated	July 6, 2020	July 20, 2020	👉	July 15, 2020	✓
Substantial Completion	July 6, 2020	August 10, 2020	↓	August 10, 2020	✓
Final Completion	September 4, 2020	May 10, 2021	↓	May 10, 2021	✓
Student Occupancy	August 2020	August 2020	↑	August 8, 2020	✓

5.3 Phase 2

Celina Campus

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	September 25, 2018	February 14, 2018	↑	February 14, 2018	✓
BOT Approval of A/E Procurement Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Construction Delivery Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Recommended A/E Firm	June 26, 2018	June 26, 2018	↑	June 26, 2018	✓
BOT Approval of Recommended CM Firm	August 2018	August 2018	↑	August 28, 2018	✓
Architect Mobilized	July 24, 2018	July 24, 2018	↑	July 31, 2018	✓
Schematic Design Submittal	January 8, 2019	January 15, 2019	👉	January 16, 2019	✓
Design Development Submittal	April 30, 2019	April 30, 2019	↑	April 26, 2019	✓
Construction Document Submittal	September 20, 2019	September 20, 2019	↑	September 3, 2019	✓
Contractor Mobilized	December 2019	December 2019	↑	November 25, 2019	✓
Foundations Complete	April 9, 2020	April 14, 2020	👉	April 21, 2020	✓
Structures Complete	July 7, 2020	July 7, 2020	↑	June 9, 2020	✓
Roofing of Buildings Complete	December 2, 2020	December 2, 2020	↑	November 13, 2020	✓
Permanent Power Complete	October 7, 2020	October 7, 2020	↑	May 28, 2020	✓
Interior Finish-Out Complete	May 18, 2021	May 18, 2021	↑	May 28, 2021	✓
Substantial Completion	July 15, 2021	June 30, 2021	↑	-	
Final Completion	August 12, 2021	August 30, 2021	↓	-	
Student Occupancy	August 2021	August 2021	↑	-	

Farmersville Campus

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	September 25, 2018	February 14, 2018	↑	February 14, 2018	✓
BOT Approval of A/E Procurement Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Construction Delivery Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Recommended A/E Firm	June 26, 2018	June 26, 2018	↑	June 26, 2018	✓
BOT Approval of Recommended CM Firm	August 2018	August 2018	↑	August 28, 2018	✓
Architect Mobilized	July 24, 2018	July 24, 2018	↑	July 31, 2018	✓
Schematic Design Submittal	December 20, 2018	December 18, 2018	↑	December 18, 2018	✓
Design Development Submittal	April 2, 2019	April 19, 2019	↓	April 26, 2019	✓
Construction Document Submittal	July 25, 2019	August 9, 2019	↓	August 9, 2019	✓
Contractor Mobilized	November 2019	November 2019	↑	October 21, 2019	✓
Foundations Complete	March 5, 2020	March 13, 2020	👉	April 2, 2020	✓
Structures Complete	April 13, 2020	April 13, 2020	↑	April 30, 2020	✓
Roofing of Buildings Complete	June 29, 2020	June 29, 2020	↑	June 30, 2020	✓
Permanent Power Complete	June 30, 2020	July 7, 2020	👉	May 4, 2020	✓
Interior Finish-Out Complete	November 30, 2020	November 30, 2020	↑	December 11, 2020	✓
Substantial Completion	January 5, 2021	January 5, 2021	↑	December 21, 2020	✓
Final Completion	February 2, 2021	July 2021	↓	-	
Student Occupancy	August 2021	March 2021	↑	March 12, 2021	✓

IT Center

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	September 25, 2018	February 14, 2018	↑	February 14, 2018	✓
BOT Approval of A/E Procurement Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Construction Delivery Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Recommended A/E Firm	June 26, 2018	June 26, 2018	↑	June 26, 2018	✓
BOT Approval of Recommended CM Firm	August 2018	August 2018	↑	August 28, 2018	✓
Architect Mobilized	July 24, 2018	July 24, 2018	↑	July 31, 2018	✓
Schematic Design Submittal	May 24, 2019	May 24, 2019	↑	May 24, 2019	✓
Design Development Submittal	August 23, 2019	August 23, 2019	↑	August 23, 2019	✓
Construction Document Submittal	December 9, 2019	December 9, 2019	↑	December 9, 2019	✓
Contractor Mobilized	December 2019	January 6, 2020	↓	January 20, 2020	✓
Construction Start for Loop Road/Parking	June 1, 2020	July 13, 2020	↓	July 27, 2020	✓
Foundations Complete	June 22, 2020	June 22, 2020	↑	May 2, 2020	✓
Structures Complete	August 14, 2020	August 14, 2020	↑	July 14, 2020	✓
Phase 1 Construction Complete for Loop Road/Parking	August 15, 2020	August 15, 2020	↑	August 22, 2020	✓
Phase 2 Construction Complete for Loop Road/Parking	October 31, 2020	March 15, 2021	↓	March 15, 2021	✓
Roofing of Buildings Complete	November 3, 2020	November 23, 2020	↓	October 23, 2020	✓
Permanent Power Complete	January 4, 2021	January 4, 2021	↑	January 29, 2021	✓
Interior Finish-Out Complete	May 13, 2021	June 30, 2021	↓	-	
Substantial Completion	June 30, 2021	July 7, 2021	👉	-	
Final Completion	August 26, 2021	August 26, 2021	↑	-	
Student Occupancy	August 2021	August 2021	↑	-	

* Phase 3 (Loop Road and Parking Lot) at Frisco Campus is included in this schedule

5.4 Phase 3

McKinney Campus (Welcome Center and Renovations)

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	August 27, 2019	August 27, 2019		August 27, 2019	
BOT Approval of A/E Procurement Method	October 22, 2019	October 22, 2019		October 22, 2019	
BOT Approval of Construction Delivery Method	February 2020	February 2020		October 22, 2019	
BOT Approval of Recommended A/E Firm	March 24, 2020	March 24, 2020		April 28, 2020	
BOT Approval of Recommended CM Firm	March 24, 2020	March 24, 2020		April 28, 2020	
Architect NTP	April 14, 2020	April 14, 2020		April 8, 2020	
Schematic Design Submittal	August 1, 2020	August 1, 2020		August 1, 2020	
Site Construction Document Submittal	October 2, 2020	October 2, 2020		October 2, 2020	
Welcome Center Construction Document Submittal	November 20, 2020	November 20, 2020		October 30, 2020	
GMP #1 * Board Approval	December 8, 2020	December 8, 2020		December 8, 2021	
GMP #2 ** Board Approval	January 26, 2021	February 23, 2021		January 26, 2021	
GMP #1 * Construction Start	January 18, 2021	January 18, 2021		January 28, 2021	
GMP #2 ** Construction Start	March 1, 2021	March 1, 2021		March 15, 2021	
Substantial Completion	May 2022	May 2022		-	
Student Occupancy	July 2022	July 2022		-	

* GMP #1 Site, Civil, and Demolition for Renovation Work

** GMP #2 Construction of New Welcome Center and Renovation

Frisco Campus (Addition and Renovations)

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	August 27, 2019	August 27, 2019		August 27, 2019	
BOT Approval of Recommended AE Firm	June 23, 2020	June 23, 2020		June 23, 2020	
BOT Approval of Recommended CM Firm	August 25, 2020	August 25, 2020		August 25, 2020	
GMP #1 * Board Approval	October 27, 2020	October 27, 2020		October 27, 2020	
GMP #1 * Construction Start	December 15, 2020	December 15, 2020		December 2, 2020	
GMP #2 ** Board Approval	March 2021	April 2021		April 25, 2021	
GMP #2 ** Construction Start	April 2021	June 2021		-	
Substantial Completion	March 25, 2022	April 2022		-	

* GMP #1 Fire Lane

** GMP #2 Alumni Hall Remaining Work, Renovations and Foundation Work

6. Budget

6.1 Program Summary

Program Wide Budget Summary

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$47,226,570	\$43,165,457	\$43,039,100	\$40,479,559	100%	94%
Investigation, Testing & Verification	\$8,185,410	\$7,004,680	\$5,563,925	\$4,316,120	79%	78%
Construction, Equipment & Furnishings	\$486,561,069	\$511,592,603	\$505,351,389	\$460,120,165	99%	91%
Misc.	\$394,411	\$392,348	\$141,294	\$135,618	36%	96%
Contingency	\$61,621,273	\$12,459,833	\$0	\$0	0%	0%
Total Program Budget	\$600,000,000	\$600,000,000	\$554,362,207	\$505,311,661		
% of Total Program Budget Committed	92.39%					
% of Total Commitments Expended	91.15%					
% of Total Program Budget Expended	84.22%					

6.2 Phase 1

Wylie Campus

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$15,051,440	\$13,460,383	\$13,442,958	\$13,434,860	100%	100%
Investigation, Testing & Verification	\$2,679,247	\$2,084,678	\$1,770,108	\$1,580,489	85%	89%
Construction, Equipment & Furnishings	\$133,174,284	\$150,289,548	\$150,276,391	\$149,012,706	100%	99%
Misc.	\$126,082	\$176,483	\$61,361	\$61,361	35%	100%
Contingency	\$6,571,649	\$19,153	\$0	\$0	0%	0%
Total Project Budget	\$157,602,702	\$166,030,244	\$165,550,818	\$164,089,416		
% of Total Project Budget Committed	99.71%					
% of Total Commitments Expended	99.12%					
% of Total Project Budget Expended	98.83%					

Technical Campus

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$14,713,206	\$13,833,223	\$13,830,223	\$13,729,376	100%	99%
Investigation, Testing & Verification	\$2,619,039	\$1,694,355	\$1,544,626	\$1,261,690	91%	82%
* Construction, Equipment & Furnishings	\$130,181,602	\$161,588,160	\$161,525,434	\$160,079,816	100%	99%
Misc.	\$123,249	\$39,091	\$38,397	\$38,397	98%	100%
Contingency	\$6,423,972	\$22,523	\$0	\$0	0%	0%
Total Project Budget	\$154,061,068	\$177,177,352	\$176,938,680	\$175,109,279		
Allen ISD Reimbursement	-	(\$12,000,000)	(\$12,000,000)	-		
Allen EDC Grant	-	(\$400,000)	(\$400,000)	-		
% of Total Project Budget Committed	99.87%					
% of Total Commitments Expended	98.97%					
% of Total Project Budget Expended	98.83%					

* Actual Budget from bond funds is \$149,188,160 (\$161,588,160 less \$12,000,000 Allen ISD Reimbursement and \$400,000 Allen EDC Grant)

6.3 Phase 2

Celina Campus

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$5,078,807	\$4,011,464	\$3,980,605	\$3,601,426	99%	90%
Investigation, Testing & Verification	\$936,908	\$936,908	\$585,520	\$451,501	62%	77%
Construction, Equipment & Furnishings	\$46,569,862	\$49,120,075	\$47,274,895	\$39,446,415	96%	83%
Misc.	\$44,090	\$64,229	\$22,096	\$21,260	34%	96%
Contingency	\$2,482,596	\$979,587	\$0	\$0	0%	0%
Total Project Budget	\$55,112,263	\$55,112,263	\$51,863,116	\$43,520,603		
% of Total Project Budget Committed	94.10%					
% of Total Commitments Expended	83.91%					
% of Total Project Budget Expended	78.97%					

Farmersville Campus

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$2,539,404	\$2,185,319	\$2,171,319	\$2,022,651	99%	93%
Investigation, Testing & Verification	\$468,453	\$540,867	\$444,545	\$329,175	82%	74%
Construction, Equipment & Furnishings	\$23,284,932	\$25,523,763	\$25,336,847	\$20,574,563	99%	81%
Misc.	\$22,045	\$26,912	\$6,107	\$6,107	23%	100%
Contingency	\$1,241,298	\$229,272	\$0	\$0	0%	0%
Total Project Budget	\$27,556,132	\$28,506,132	\$27,958,817	\$22,932,496		
% of Total Project Budget Committed	98.08%					
% of Total Commitments Expended	82.02%					
% of Total Project Budget Expended	80.45%					

IT Center

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$5,472,853	\$4,884,249	\$4,850,347	\$4,213,383	99%	87%
Investigation, Testing & Verification	\$1,009,600	\$1,193,900	\$867,038	\$646,782	73%	75%
Construction, Equipment & Furnishings	\$50,183,042	\$46,223,400	\$44,974,015	\$33,803,091	97%	75%
Misc.	\$47,510	\$53,157	\$10,487	\$5,647	20%	54%
Contingency	\$2,675,210	\$4,814,688	\$0	\$0	0%	0%
Total Project Budget	\$59,388,215	\$57,169,393	\$50,701,887	\$38,668,904		

% of Total Project Budget Committed **88.69%**

% of Total Commitments Expended **76.27%**

% of Total Project Budget Expended **67.64%**

* Project Budget contains funds for Phase 3 (Loop Road and Parking Lot) at Frisco Campus

6.4 Phase 3**McKinney Campus (Welcome Center and Renovations)**

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$4,370,860	\$4,420,820	\$4,393,648	\$3,126,363	99%	71%
Investigation, Testing & Verification	\$472,163	\$553,973	\$352,088	\$46,483	64%	13%
Construction, Equipment & Furnishings	\$30,179,816	\$38,342,104	\$35,458,255	\$4,530,200	92%	13%
Misc.	\$31,435	\$32,476	\$2,845	\$2,845	9%	100%
Contingency	\$2,833,454	\$3,180,222	\$0	\$0	0%	0%
Total Project Budget	\$37,887,728	\$46,529,595	\$40,206,835	\$7,705,891		

% of Total Project Budget Committed **86.41%**

% of Total Commitments Expended **19.17%**

% of Total Project Budget Expended **16.56%**

Frisco Campus (Addition and Renovations)

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$2,883,468	\$1,942,048	\$1,826,404	\$1,183,754	94%	65%
Investigation, Testing & Verification	\$347,015	\$347,015	\$79,219	\$26,233	23%	33%
Construction, Equipment & Furnishings	\$16,724,000	\$16,869,367	\$15,687,890	\$696,711	93%	4%
Misc.	\$70,820	\$77,677	\$44,463	\$8,661	57%	19%
Contingency	\$1,094,995	\$3,704,931	\$0	\$0	0%	0%
Total Project Budget	\$21,120,298	\$22,941,038	\$17,637,975	\$1,915,358		

% of Total Project Budget Committed **76.88%**

% of Total Commitments Expended **10.86%**

% of Total Project Budget Expended **8.35%**

Plano Campus (Additional Projects)

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Total Project Budget	\$0	\$2,177,541	\$13,625	\$6,125		
% of Total Project Budget Committed	0.63%					
% of Total Commitments Expended	44.95%					
% of Total Project Budget Expended	0.28%					

6.5 Phase A**Public Safety Training Center**

Budget Group	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Construction Costs	\$31,068,022	\$31,068,022	\$31,068,022	100%	100%
Total Project Budget	\$31,068,022	\$31,068,022	\$31,068,022		

Trane Energy PACT

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Frisco Campus	\$9,725,336	\$9,725,336	\$9,725,336	\$9,493,156	100%	98%
Plano Campus	\$6,797,834	\$6,797,834	\$6,797,834	\$6,797,834	100%	100%
McKinney Campus	\$4,044,983	\$4,044,983	\$4,044,983	\$4,044,983	100%	100%
Courtyard Center	\$548,720	\$548,720	\$548,720	\$548,720	100%	100%
Collin Higher Education Center	\$720,659	\$720,659	\$720,659	\$720,659	100%	100%
Total Program Budget	\$21,837,531	\$21,837,531	\$21,837,531	\$21,605,351		
% of Total Project Budget Committed	100.00%					
% of Total Commitments Expended	98.94%					
% of Total Project Budget Expended	98.94%					

6.6 Additional Program Budgets

Program Level

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Building Fund Reimbursement	\$51,150,000	\$0	\$0	\$0	0%	0%
Program Wide Traffic Study	\$0	\$370,000	\$370,000	\$351,500	100%	95%
Program Contingency	\$39,393,094	\$3,214,389	\$0	\$0	0%	0%
Trane PACT Program Management		\$99,500	\$99,500	\$99,500	100%	100%
Bond Fees		\$9,500	\$9,500	\$9,500	100%	100%
District Wide Air Cleaning		\$140,000	\$140,000	\$133,700	100%	96%
District Wide Commissioning		\$17,500	\$17,500	\$17,500	100%	100%
Total Project Budget	\$90,543,094	\$3,850,889	\$636,500	\$611,700		

7. Completed Items

7.1 General Program

- AECOM issued the Monthly Program Report for April '21 to Collin College on May 7th
- AECOM conducted coordination meetings with the Executive Committee on May 17th

7.2 Procurement

- No Procurement Items have been completed at this time

7.3 Design

- No Design Items have been completed at this time

7.4 Pre-Construction

- No Pre-Construction Items have been completed at this time

7.5 Construction

- Collin College, AECOM, Beck Architecture, LLC, and JT Vaughn Construction conducted Weekly OAC meetings on May 5th, 12th, 19th, and 26th for the Celina Campus
- Collin College, AECOM, Page Southerland Page, Inc., and Skanska USA Building, Inc. conducted Weekly OAC meetings on May 5th, 12th, 19th, and 26th for the Frisco Campus
- Collin College, AECOM, Beck Architecture, LLC, and JE Dunn Construction conducted Weekly OAC meetings on May 4th, 11th, 18th, and 25th for the IT Center at the Frisco Campus
- Collin College, AECOM, Page Southerland Page, Inc. and Skanska USA Building, Inc. conducted Weekly OAC meetings on May 4th, 11th, 18th, and 25th for the McKinney Campus Addition and Renovations
- JE Dunn Construction held an FF&E/IT Coordination meeting with Collin College, AECOM, and Beck Architecture, LLC on May 13th for the IT Center at the Frisco Campus
- AECOM held a Network Ops Center IT Requirements meeting with Collin College and Page Southerland Page, Inc. on May 14th for the Heritage Hall at the Frisco Campus

- AECOM held a Move Out walkthrough meeting with Collin College and Skanska USA Building, Inc. on May 19th for the Alumni Hall Dining at the Frisco Campus
- JE Dunn Construction held a punch walkthrough for Area A (West Wing) with Collin College, AECOM, and Beck Architecture, LLC on May 24th and 25th for the IT Center at the Frisco Campus
- AECOM held a Move Out walkthrough meeting with Collin College and Skanska USA Building, Inc. on May 26th for Heritage Hall at the Frisco Campus
- Collin College, AECOM, Page Southerland Page, Inc. and Skanska USA Building, Inc. met for an 11 Month Project Review meeting on May 27th at the Wylie Campus

See Appendix A for Construction Progress Photos

7.6 Acceptance and Close-Out

- No Acceptance and Close-Out Phase Items have been completed at this time

8. Pending Items

8.1 General Program

- No General Program items are pending at this time

8.2 Procurement

- [Execution of Skanska USA Building, Inc. GMP for the Frisco Campus Additions and Renovations](#)

8.3 Design

- No Design items are pending at this time

8.4 Pre-Construction

- [Coordination with the City of Frisco on the permitting/zoning requirements for the work on the Frisco Campus](#)
- [Coordination with the City of McKinney on the permitting/zoning requirements for the Welcome Center at the McKinney Campus](#)

8.5 Construction

- [Punch list at the Farmersville Campus and IT Center at Frisco Campus](#)

See Appendix A for Construction Progress Photos

8.6 Acceptance and Close-Out

- [Wylie and Technical Campuses achieved Substantial Completion and were accepted by the College in preparation for the Fall 2020 semester. Final close-out activities are nearing completion on both projects.](#)

Appendix A – Construction Progress Photos

Celina Campus



May '21 Aerial



Landscape at North Building, NW View



Landscape at West Side of Building



Campus Signage at Main Entrance



Anthony Peterson Center of Academic Assistance



LVN/CAN Lab



Mechanical Room

IT Center at Frisco Campus



May '21 Aerial



Quad Area



Carpet Install on 3rd Floor




Water Feature Installed



Signage Installed at Atrium Stairs



Women's Restroom on 3rd Floor

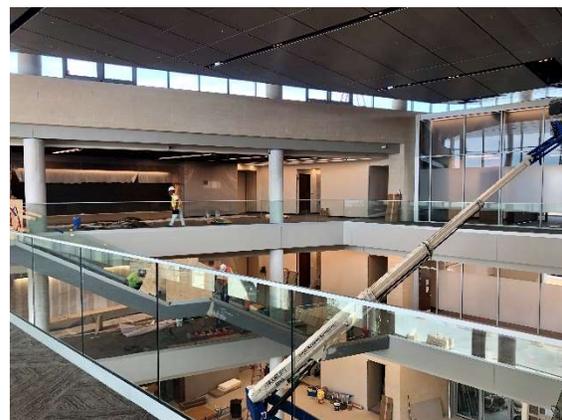

NE View of Atrium from 3rd Floor

Fire Lane at Frisco Campus



North to South View of Fire Lane

Welcome Center and Parking Lot at McKinney Campus



May Aerial



Parking Lot Prepped for Pour
