

Crosby ISD Construction Update



September 21, 2026

Administration Building

Completion: Summer 2027

Architect: Stantec

General Contractor: TBD

Current Status:

- Building Permit Approved
- Contractor Bid Date September 24, 2026

Upcoming Milestones:

- Bid Date Evaluation and Award September 25- October 9, 2026
- Recommendation to Board October 19, 2026



Red Barn

Completion: Summer 2027

Architect: Pfluger


General Contractor: TBD December 2026

Current Status:

- 100% Design Development
- Defined Scope to include Red Barn and White Barn

Upcoming Milestones:

- 50% Construction Documents September 30, 2026

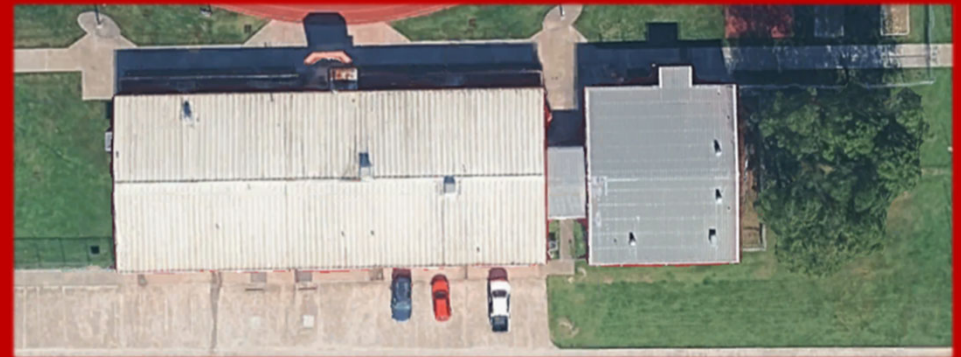

Crosby Sixth Grade Campus

Completion: June 18, 2027

Architect: Stantec

General Contractor: Gamma

Current Status :

- Mock Up is complete
- Steel Delivery and Erection this Week
- 95% Complete on Detention Pond

Upcoming Milestones:

- Final Slab Pour October 20, 2026
- Steel Erection and Decking through October and Early November



Crosby Sixth Grade Campus

