




2026 BOND PROJECT UPDATE

October 20, 2026

MIDWAY HS ADDITIONS & RENOVATIONS

- Pier Drilling Complete
- Grade Beam Construction 50%
- Underground Plumbing Starting 10/19
- Submittals are coming in and under review
- Project is on schedule with a completion date of 7/31/27
 - 2 days lost to rain, but still on-schedule

Midway HS	GMP1	GMP2
Total GMP	\$1,327,908	\$12,131,859
Billed To Date	\$733,859	\$116,748
Balance To Finish	\$594,048	\$12,015,110
Remaining Contingency	\$194,860	\$1,395,000

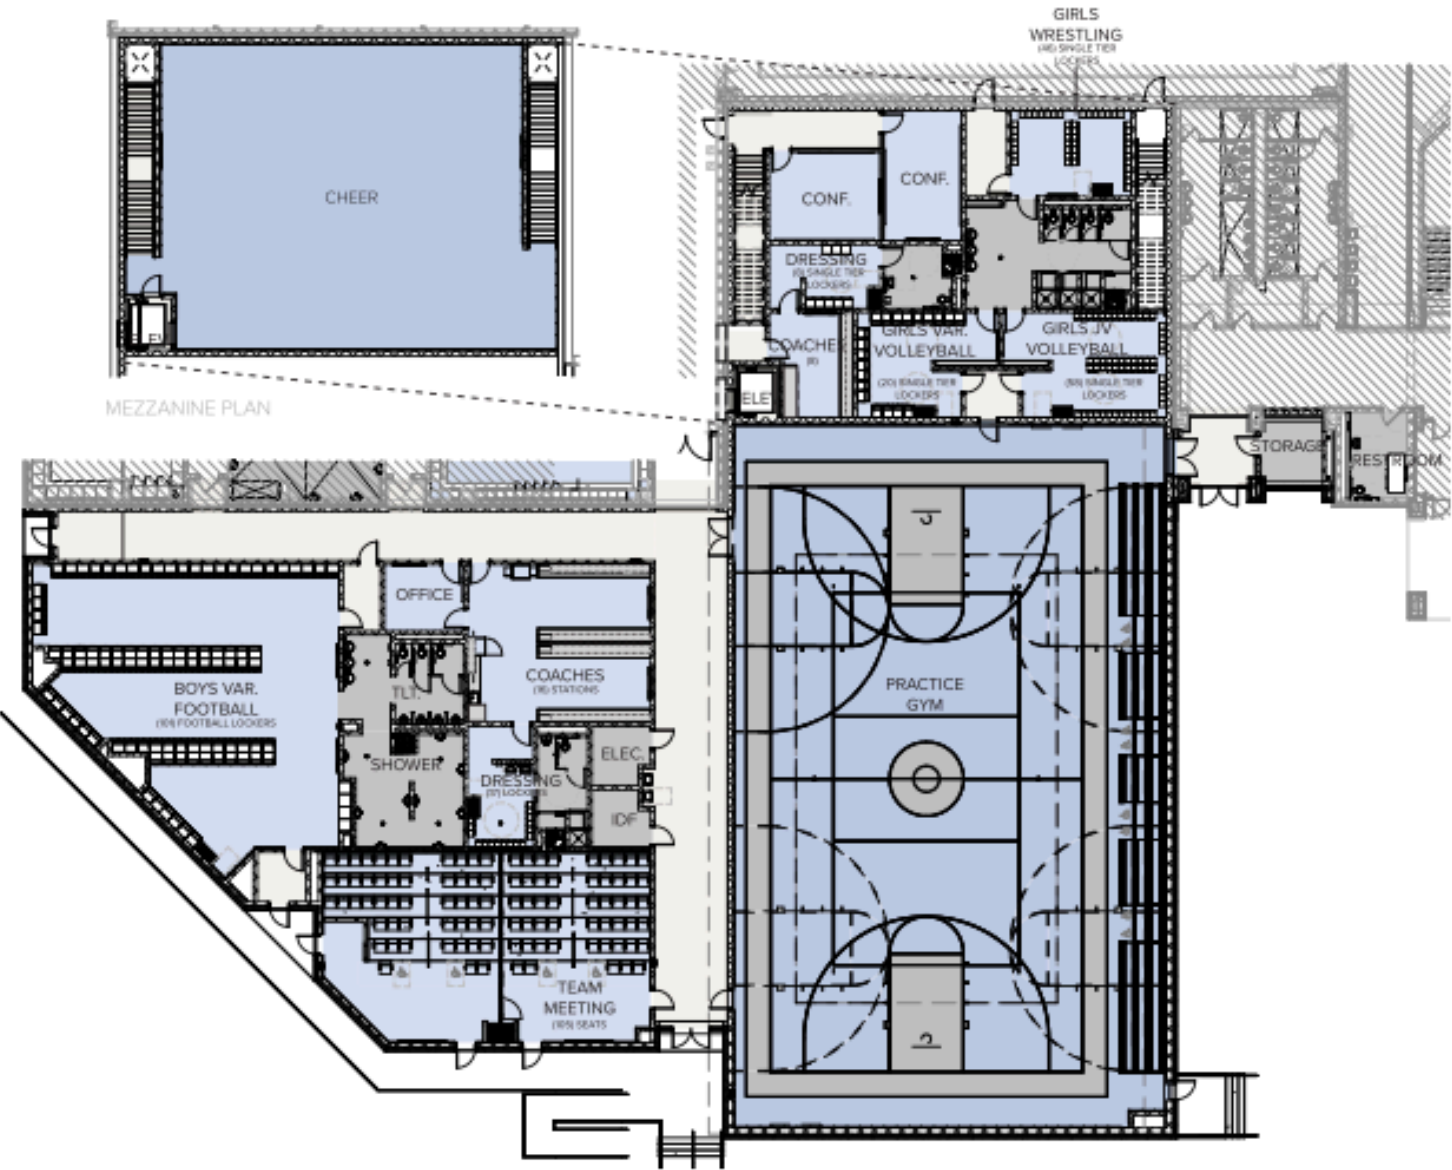

MIDWAY HS ADDITIONS & RENOVATIONS



Drilling Piers



Pouring Piers



Peirs Complete

MIDWAY HS ADDITIONS & RENOVATIONS



Forming Up
Grade Beams



Completed
Grade Beams



Elevator Pit

DEFERRED MAINTENANCE

Up-Coming Projects

- Castleman Creek
 - HVAC - Offices/Classrooms
 - This will complete CCE HVAC Update
 - Work will happen over Thanksgiving/Christmas Breaks
- Administration Building
 - Generator Install and Electrical Upgrades for Technology
 - Work is tentatively scheduled for Christmas Break
 - Equipment leadtimes driving project schedule

QUESTIONS



Ken Wolf, Director of Operations
