



Collin College

2017 Capital Improvement Program
Monthly Report
July 2020


Collin County Community College District

Project Reference: 60541060
Project Number: 60541060

August 7, 2020

Quality information

Prepared by _____



Nuria Cortes
Program Documents Manager

Checked by _____



Nick Fiehler
Program Controls Manager

Approved By _____



Adrian Grimes
Program Director

Revision History

Revision	Revision date	Details	Authorized	Name	Position
First Publication	August 07, 2020	July '20 Report	Yes	Adrian Grimes	Program Director

Distribution List

# Hard Copies	PDF Required	Association / Company Name
	1	Dr. Neil Matkin / Collin College
	1	Chris Eyle / Collin College

Prepared for:

Collin County Community College District
3452 Spur 399
Suite 327
McKinney, TX 75069

Prepared by:

Nuria Cortes
Program Documents Manager
E: ncortes.aecom@collin.edu

AECOM
13355 Noel Road
4th Floor
Dallas TX, 75240
aecom.com

Copyright © 2019 by AECOM

All rights reserved. No part of this copyrighted work may be reproduced, distributed, or transmitted in any form or by any means without the prior written permission of AECOM.

Table of Contents

1.	Introduction.....	5
2.	Executive Summary	5
3.	Scope.....	6
	3.1 Phase 1	6
	3.2 Phase 2	6
	3.3 Phase 3	7
4.	Community	7
	4.1 Project Teams	7
	4.1.1 Phase 1	7
	4.1.2 Phase 2	8
	4.1.3 Phase 3	9
	4.2 Current Personnel Estimate.....	9
	4.3 Community Outreach.....	10
5.	Schedule	10
	5.1 Program.....	10
	5.2 Phase 1	11
	5.3 Phase 2	12
	5.4 Phase 3	13
6.	Budget.....	14
	6.1 Program Summary	14
	6.2 Phase 1	14
	6.3 Phase 2	15
	6.4 Phase 3	16
	6.5 Phase A	17
	6.6 Additional Program Budgets	18
7.	Completed Items.....	18
	7.1 General Program.....	18
	7.2 Procurement	18
	7.3 Design	18
	7.4 Pre-Construction	18
	7.5 Construction.....	18
	7.6 Acceptance and Close-Out.....	19
8.	Pending Items.....	19
	8.1 General Program.....	19
	8.2 Procurement	19
	8.3 Design	19
	8.4 Pre-Construction	19
	8.5 Construction.....	19
	8.6 Acceptance and Close-Out.....	20
	Appendix A – Construction Progress Photos	21

1. Introduction

On May 6, 2017, voters approved Collin College's \$600 million bond proposal to facilitate a long-range plan to accommodate the projected population growth in Collin County over the next two decades. The program consists of 4 new campuses and 2 new facilities.

On May 16, 2017, in a special session, the Board of Trustees granted the District President authority to enter and negotiate into contract with AECOM Technical Services, Inc. (AECOM) to provide Program Management Services to the Collin College 2017 Capital Improvement Program. On May 25, 2017, Collin College issued a Notice to Proceed to AECOM. As part of these services, AECOM will deliver a monthly report to provide status and progress of key aspects of the Program.

2. Executive Summary

The Program is progressing as planned with no major issues to report at this time.

Completed and Pending Items

- Technical Campus – TCO's for staff occupancy have been received for Buildings A, B, and C. MEP finals have been received for entire campus. Fire alarm and sprinkler inspections are pending for the garage and Building D. Punchlist items are on-going in all buildings. FF&E delivery and installation is on-going for all buildings. Commissioning and Test & Balance is on-going for throughout the campus. Installation of monument signs was completed 07/31 and installation of site signage is on-going.
- Wylie Campus Landscaping finalization and cleanup is ongoing. Landscape furniture has been set and anchored. All subs are correcting any final punch list items at Campus Commons, Student Center, and Conference Center. Furniture install is on-going at the Campus Commons, Student Center, and Conference Center, with weekly install schedule updates due to issues with COVID.

Items of close attention

- Installation of FF&E and IT infrastructure are being closely monitored to ensure completion of the Wylie and Technical Campus projects by Fall 2020.
- Receipt of Student Occupancy approval from the City of Allen for the Technical Campus

Budget Summary

- \$503,381,573 of the \$600,000,000 has been committed to-date in the form of contracts with various vendors. This represents 83.90% of the overall program budget committed.
- \$406,220,677 of the \$503,381,573 committed amount has been expended to-date. This represents 80.70% of the commitments to date and 67.70% of the program budget.

3. Scope

3.1 Phase 1

- Wylie Campus
 - Construction of a campus on a new approximately 97-acre site
 - The campus includes:
 - Campus Commons
 - Learning Resource Center / Library
 - Student Center/Conference Center
 - Central Utility Plant
- Technical Campus
 - Construction of a Technical Campus on a new 32-acre site in Allen, Texas
 - The campus includes:
 - 500 space underground parking garage
 - Academic Building (includes space for dual credit students)
 - 3 Trade Bar Buildings to support CTE programs
 - Programs planned for inclusion include:
 - Advanced Manufacturing, Automotive, Construction, and Health Science

3.2 Phase 2

- Celina Campus
 - Construction of a campus on a new approximately 75-acre site
 - The campus includes:
 - Student Union / Workforce / Instructional Building
- Farmersville Campus
 - Construction of a campus on a new approximately 76-acre site
 - The campus includes:
 - Student Union / Workforce / Instructional Building
- Frisco Campus
 - Construction of a new IT Center building on the existing campus

3.3 Phase 3

- Frisco Campus
 - Construction of a new fire lane, parking lot, and loop road on the existing campus
- McKinney Campus
 - Construction of a new Welcome Center on the existing campus
- Additional McKinney Campus Projects
 - Trane Upgrades
 - New Entry Drive and Parking
 - Pistol Range Demo
 - Classroom Building and Dining Renovations
 - Dental Hygiene Renovations
 - Wayfinding
- Additional Frisco Campus Projects
 - Trane Upgrades
 - Alumni Hall Renovations and Additions
 - Lawler Hall Renovations
 - Heritage Hall Upgrades
 - Founders Hall Renovations
 - Wayfinding
- Additional Plano Campus Projects
 - Trane Upgrades
 - Wayfinding
- Additional Courtyard Center Projects
 - Trane Upgrades
- Additional CHEC Projects
 - Trane Upgrades

4. Community

4.1 Project Teams

4.1.1 Phase 1

- Wylie Campus
 - Program Manager: AECOM Technical Services, Inc. (under contract)
 - A/E: Page Southerland Page, Inc. (under contract)
 - MEP: Reed, Wells, Benson & Co.
 - Civil Engineer: Pacheco Koch Consulting Engineers, Inc.

- Cost Consulting: Vermeulens
- Construction Manager-at-Risk: Skanska USA Building, Inc. (under contract)
- Commissioning Agent: Bath Group, Inc. (under contract)
- Technical Campus
 - Program Manager: AECOM Technical Services, Inc. (under contract)
 - A/E: Perkins+Will, Inc. (under contract)
 - Associate Architect: Hoefer Wysocki Architecture
 - MEP: Purdy McGuire
 - Civil Engineer: Pacheco Koch Consulting Engineers, Inc.
 - Structural Engineer: L.A. Fuess Partners, Inc.
 - Cost Consulting: Vermeulens
 - Construction Manager-at-Risk: McCarthy Building Companies, Inc. (under contract)
 - Commissioning Agent: Farnsworth (under contract)


4.1.2 Phase 2

- Celina Campus
 - Program Manager: AECOM (under contract)
 - A/E: Beck Architecture, LLC (under contract)
 - Structural Engineer: L.A. Fuess Partners, Inc.
 - MEP: Reed, Wells, Benson & Co.
 - Civil Engineer: RLK Engineering
 - Construction Manager-at-Risk: JT Vaughn Construction (under contract)
- Farmersville Campus
 - Program Manager: AECOM (under contract)
 - A/E: Beck Architecture, LLC (under contract)
 - Structural Engineer: L.A. Fuess Partners, Inc.
 - MEP: Reed, Wells, Benson & Co.
 - Civil Engineer: RLK Engineering
 - Construction Manager-at-Risk: JT Vaughn Construction (under contract)
- IT Center
 - Program Manager: AECOM (under contract)
 - A/E: Beck Architecture, LLC (under contract)
 - Structural Engineer: L.A. Fuess Partners, Inc.
 - MEP: ME Engineers
 - Civil Engineer: RLK Engineering
 - Construction Manager-at-Risk: JE Dunn Construction (under contract)

4.1.3 Phase 3

- Welcome Center at the McKinney Campus
 - Program Manager: AECOM Technical Service, Inc. (under contract)
 - A/E: PBK (under contract)
 - Construction Manager-at-Risk: Skanska (under contract)
- Fire Lane and Loop Road/Parking at Frisco Campus
 - Program Manager: AECOM Technical Service, Inc. (under contract)
 - Civil Engineer: RLK Engineering (under contract)
 - Construction Manager-at-Risk: JE Dunn (under contract)
- Additional Projects at Frisco Campus
 - Program Manager: AECOM Technical Service, Inc. (under contract)
 - A/E: Page Southerland Page, Inc. (contract pending)
 - Construction Manager-at-Risk: (RFQ Process has started)
- Additional Projects at McKinney Campus
 - Program Manager: AECOM Technical Service, Inc. (under contract)
 - A/E: PBK (under contract)
 - Construction Manager-at-Risk: Skanska (under contract)

4.2 Current Personnel Estimate

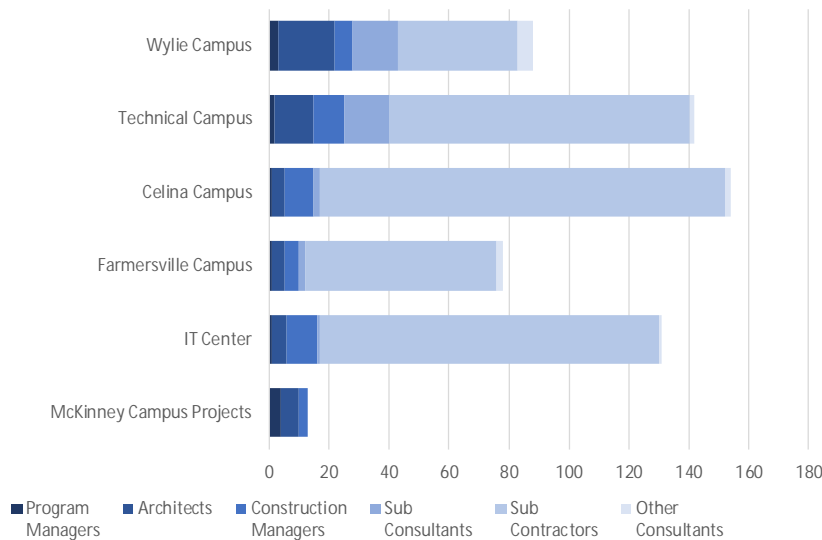


It is estimated that the Program Managers, Architects, Construction Managers, Sub-Consultants, and Sub-Contractors, under contract with Collin College for the 2017 Capital Improvement Program, have 593 employees contributing to the program's progress.

4.3 Community Outreach

- Collin College 2017 Capital Improvement Program Website
 - o <https://CollinCollege2017CIP.com>
 - o Includes the following features:
 - Program Overview
 - Project Scopes
 - Project Schedules
 - Project Budgets
 - Progress Photos/Renderings
 - Live On-Site Camera Feeds

5. Schedule

5.1 Program

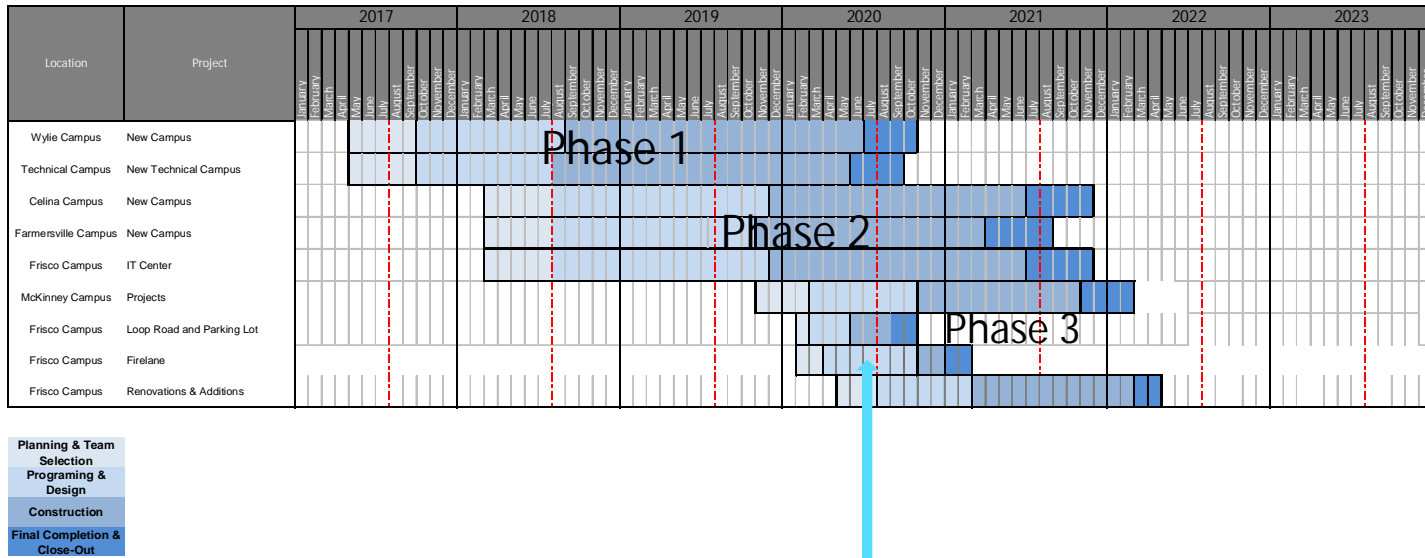

5.2 Phase 1

Wylie Campus

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	May 16, 2017	May 16, 2017	↑	May 16, 2017	✓
BOT Approval of A/E Procurement Method	May 23, 2017	May 23, 2017	↑	May 23, 2017	✓
BOT Approval of Construction Delivery Method	May 23, 2017	May 23, 2017	↑	May 23, 2017	✓
BOT Approval of Recommended Firms	August 22, 2017	August 22, 2017	↑	August 22, 2017	✓
Architect Mobilized	September 12, 2017	September 29, 2017	↓	September 28, 2017	✓
GMP Construction Documents Submittal	June 26, 2018	June 26, 2018	↑	June 26, 2018	✓
BOT Approval of GMP	August 28, 2018	August 28, 2018	↑	August 28, 2018	✓
Contractor Mobilized	September 10, 2018	September 12, 2018	↔	September 12, 2018	✓
Foundations Complete	May 18, 2019	April 30, 2019	↑	April 23, 2019	✓
Structures Complete	June 28, 2019	June 28, 2019	↑	May 23, 2019	✓
Dry-In of Buildings Complete	October 26, 2019	October 26, 2019	↑	October 29, 2019	✓
Permanent Power Complete	September 17, 2019	September 17, 2019	↑	September 21, 2019	✓
Interior Finish-Out Complete	May 1, 2020	June 10, 2020	↓	July 1, 2020	✓
Substantial Completion	June 25, 2020	June 25, 2020	↑	July 1, 2020	✓
Final Completion	August 23, 2020	August 23, 2020	↑	-	
Student Occupancy	August 2020	August 2020	↑	-	

Technical Campus

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	May 16, 2017	May 16, 2017	↑	May 16, 2017	✓
BOT Approval of A/E Procurement Method	May 23, 2017	May 23, 2017	↑	May 23, 2017	✓
BOT Approval of Construction Delivery Method	May 23, 2017	May 23, 2017	↑	May 23, 2017	✓
BOT Approval of Recommended Firms	August 22, 2017	August 22, 2017	↑	August 22, 2017	✓
Architect Mobilized	September 12, 2017	September 29, 2017	↓	September 28, 2017	✓
GMP Construction Documents Submittal	April 16, 2018	April 16, 2018	↑	April 19, 2018	✓
BOT Approval of GMP	June 26, 2018	June 26, 2018	↑	June 26, 2018	✓
Contractor Mobilized	July 6, 2018	July 20, 2018	↔	July 26, 2018	✓
Foundations Complete	September 23, 2019	September 23, 2019	↑	July 29, 2019	✓
Structures Complete	November 18, 2019	November 18, 2019	↑	November 13, 2019	✓
Roofing of Buildings Complete	December 20, 2019	December 20, 2019	↑	December 20, 2019	✓
Permanent Power Complete	December 15, 2019	January 10, 2020	↓	January 15, 2020	✓
Building A Punchlist Generated	June 5, 2020	June 12, 2020	↔	June 12, 2020	✓
Building B Punchlist Generated	June 12, 2020	June 19, 2020	↔	June 19, 2020	✓
Building C Punchlist Generated	June 30, 2020	July 6, 2020	↔	July 9, 2020	✓
Building D Punchlist Generated	July 6, 2020	July 20, 2020	↔	July 15, 2020	✓
Substantial Completion	July 6, 2020	August 10, 2020	↓	-	
Final Completion	September 4, 2020	September 10, 2020	↔	-	
Student Occupancy	August 2020	August 2020	↑	-	

5.3 Phase 2

Celina Campus

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	September 25, 2018	February 14, 2018	↑	February 14, 2018	✓
BOT Approval of A/E Procurement Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Construction Delivery Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Recommended A/E Firm	June 26, 2018	June 26, 2018	↑	June 26, 2018	✓
BOT Approval of Recommended CM Firm	August 2018	August 2018	↑	August 28, 2018	✓
Architect Mobilized	July 24, 2018	July 24, 2018	↑	July 31, 2018	✓
Schematic Design Submittal	January 8, 2019	January 15, 2019	↘	January 16, 2019	✓
Design Development Submittal	April 30, 2019	April 30, 2019	↑	April 26, 2019	✓
Construction Document Submittal	September 20, 2019	September 20, 2019	↑	September 3, 2019	✓
Contractor Mobilized	December 2019	December 2019	↑	November 25, 2019	✓
Foundations Complete	April 9, 2020	April 14, 2020	↘	April 21, 2020	✓
Structures Complete	July 7, 2020	July 7, 2020	↑	June 9, 2020	✓
Roofing of Buildings Complete	December 2, 2020	December 2, 2020	↑	-	
Permanent Power Complete	October 7, 2020	October 7, 2020	↑	-	
Interior Finish-Out Complete	May 18, 2021	May 18, 2021	↑	-	
Substantial Completion	July 15, 2021	June 30, 2021	↑	-	
Final Completion	August 12, 2021	July 29, 2021	↑	-	
Student Occupancy	August 2021	August 2021	↑	-	

Farmersville Campus

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	September 25, 2018	February 14, 2018	↑	February 14, 2018	✓
BOT Approval of A/E Procurement Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Construction Delivery Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Recommended A/E Firm	June 26, 2018	June 26, 2018	↑	June 26, 2018	✓
BOT Approval of Recommended CM Firm	August 2018	August 2018	↑	August 28, 2018	✓
Architect Mobilized	July 24, 2018	July 24, 2018	↑	July 31, 2018	✓
Schematic Design Submittal	December 20, 2018	December 18, 2018	↑	December 18, 2018	✓
Design Development Submittal	April 2, 2019	April 19, 2019	↓	April 26, 2019	✓
Construction Document Submittal	July 25, 2019	August 9, 2019	↓	August 9, 2019	✓
Contractor Mobilized	November 2019	November 2019	↑	October 21, 2019	✓
Foundations Complete	March 5, 2020	March 13, 2020	↘	April 2, 2020	✓
Structures Complete	April 13, 2020	April 13, 2020	↑	April 30, 2020	✓
Roofing of Buildings Complete	June 29, 2020	June 29, 2020	↑	June 30, 2020	✓
Permanent Power Complete	June 30, 2020	July 7, 2020	↘	May 4, 2020	✓
Interior Finish-Out Complete	November 30, 2020	November 30, 2020	↑	-	
Substantial Completion	January 5, 2021	January 5, 2021	↑	-	
Final Completion	February 2, 2021	February 2, 2021	↑	-	
Student Occupancy	August 2021	August 2021	↑	-	

IT Center

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	September 25, 2018	February 14, 2018	↑	February 14, 2018	✓
BOT Approval of A/E Procurement Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Construction Delivery Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Recommended A/E Firm	June 26, 2018	June 26, 2018	↑	June 26, 2018	✓
BOT Approval of Recommended CM Firm	August 2018	August 2018	↑	August 28, 2018	✓
Architect Mobilized	July 24, 2018	July 24, 2018	↑	July 31, 2018	✓
Schematic Design Submittal	May 24, 2019	May 24, 2019	↑	May 24, 2019	✓
Design Development Submittal	August 23, 2019	August 23, 2019	↑	August 23, 2019	✓
Construction Document Submittal	December 9, 2019	December 9, 2019	↑	December 9, 2019	✓
Contractor Mobilized	December 2019	January 6, 2020	↓	January 20, 2020	✓
Construction Start for Loop Road/Parking	June 1, 2020	July 13, 2020	↓	July 27, 2020	✓
Foundations Complete	June 22, 2020	June 22, 2020	↑	May 2, 2020	✓
Structures Complete	August 14, 2020	August 14, 2020	↑	July 14, 2020	✓
Construction Complete for Loop Road/Parking	August 15, 2020	August 15, 2020	↑	-	
Roofing of Buildings Complete	November 3, 2020	November 3, 2020	↑	-	
Permanent Power Complete	January 4, 2021	January 4, 2021	↑	-	
Interior Finish-Out Complete	May 13, 2021	May 13, 2021	↑	-	
Substantial Completion	June 30, 2021	July 7, 2021	↔	-	
Final Completion	August 26, 2021	August 26, 2021	↑	-	
Student Occupancy	August 2021	August 2021	↑	-	

* Phase 3 (Loop Road, Fire Lane, and Parking Lot) at Frisco Campus is included in this schedule

5.4 Phase 3

McKinney Campus Projects

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	August 27, 2019	August 27, 2019	↑	August 27, 2019	✓
BOT Approval of A/E Procurement Method	October 22, 2019	October 22, 2019	↑	October 22, 2019	✓
BOT Approval of Construction Delivery Method	February 2020	February 2020	↑	October 22, 2019	✓
BOT Approval of Recommended A/E Firm	March 24, 2020	March 24, 2020	↑	April 28, 2020	✓
BOT Approval of Recommended CM Firm	March 24, 2020	March 24, 2020	↑	April 28, 2020	✓
Architect NTP	April 14, 2020	April 14, 2020	↑	April 8, 2020	✓
Schematic Design Submittal	August 1, 2020	August 1, 2020	↑	August 1, 2020	✓
Design Development Submittal	September 5, 2020	September 5, 2020	↑	-	
Student Occupancy	January 2022	January 2022	↑	-	

Frisco Campus Renovations and Additions Projects

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	August 27, 2019	August 27, 2019	↑	August 27, 2019	✓
BOT Approval of Recommended AE Firm	June 23, 2020	June 23, 2020	↑	June 23, 2020	✓
BOT Approval of Recommended CM Firm	August 25, 2020	August 25, 2020	↑	-	

6. Budget

6.1 Program Summary

Program Wide Budget Summary

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$47,226,570	\$43,074,730	\$41,828,656	\$34,706,394	97%	83%
Investigation, Testing & Verification	\$8,185,410	\$6,921,670	\$5,327,959	\$3,252,978	77%	61%
Construction, Equipment & Furnishings	\$486,561,069	\$504,969,349	\$456,094,425	\$368,145,127	90%	81%
Misc.	\$394,411	\$388,166	\$130,533	\$116,177	34%	89%
Contingency	\$61,621,273	\$18,508,746	\$0	\$0	0%	0%
Total Program Budget	\$600,000,000	\$600,000,000	\$503,381,573	\$406,220,677		
% of Total Program Budget Committed	83.90%					
% of Total Commitments Expended	80.70%					
% of Total Program Budget Expended	67.70%					

6.2 Phase 1

Wylie Campus

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$15,051,440	\$13,504,128	\$13,504,128	\$12,903,414	100%	96%
Investigation, Testing & Verification	\$2,679,247	\$2,084,678	\$1,792,096	\$1,498,654	86%	84%
Construction, Equipment & Furnishings	\$133,174,284	\$150,257,310	\$150,256,427	\$139,437,358	100%	93%
Misc.	\$126,082	\$175,999	\$60,878	\$59,328	35%	97%
Contingency	\$6,571,649	\$62,674	\$0	\$0	0%	0%
Total Project Budget	\$157,602,702	\$166,084,789	\$165,613,528	\$153,898,753		
% of Total Project Budget Committed	99.72%					
% of Total Commitments Expended	92.93%					
% of Total Project Budget Expended	92.66%					

Technical Campus

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$14,713,206	\$13,792,895	\$13,740,617	\$13,178,258	100%	96%
Investigation, Testing & Verification	\$2,619,039	\$1,694,355	\$1,633,265	\$1,019,015	96%	62%
* Construction, Equipment & Furnishings	\$130,181,602	\$161,016,861	\$160,163,695	\$144,304,790	99%	90%
Misc.	\$123,249	\$38,767	\$38,073	\$25,267	98%	66%
Contingency	\$6,423,972	\$579,929	\$0	\$0	0%	0%
Allen ISD Reimbursement	-	(\$12,000,000)	(\$12,000,000)	-		
Allen EDC Grant	-	(\$400,000)	(\$400,000)	-		
Total Project Budget	\$154,061,068	\$164,722,807	\$163,175,650	\$158,527,330		
% of Total Project Budget Committed	99.06%					
% of Total Commitments Expended	97.15%					
% of Total Project Budget Expended	96.24%					

* Actual Budget from bond funds is \$148,616,861 (\$161,016,861 less \$12,000,000 Allen ISD Reimbursement and \$400,000 Allen EDC Grant)

6.3 Phase 2

Celina Campus

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$5,078,807	\$3,988,794	\$3,956,435	\$2,853,820	99%	72%
Investigation, Testing & Verification	\$936,908	\$936,908	\$588,490	\$238,747	63%	41%
Construction, Equipment & Furnishings	\$46,569,862	\$47,510,609	\$42,279,249	\$17,902,038	89%	42%
Misc.	\$44,090	\$62,092	\$19,124	\$19,124	31%	100%
Contingency	\$2,482,596	\$2,613,860	\$0	\$0	0%	0%
Total Project Budget	\$55,112,263	\$55,112,263	\$46,843,297	\$21,013,728		
% of Total Project Budget Committed	85.00%					
% of Total Commitments Expended	44.86%					
% of Total Project Budget Expended	38.13%					

Farmersville Campus

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$2,539,404	\$2,185,319	\$2,171,319	\$1,682,802	99%	78%
Investigation, Testing & Verification	\$468,453	\$540,867	\$448,095	\$176,548	83%	39%
Construction, Equipment & Furnishings	\$23,284,932	\$25,178,752	\$23,052,211	\$12,921,580	92%	56%
Misc.	\$22,045	\$26,716	\$5,911	\$5,911	22%	100%
Contingency	\$1,241,298	\$574,479	\$0	\$0	0%	0%
Total Project Budget	\$27,556,132	\$28,506,132	\$25,677,536	\$14,786,841		
% of Total Project Budget Committed	90.08%					
% of Total Commitments Expended	57.59%					
% of Total Project Budget Expended	51.87%					

IT Center

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$5,472,853	\$4,858,074	\$4,823,265	\$3,147,020	99%	65%
Investigation, Testing & Verification	\$1,009,600	\$1,192,700	\$856,813	\$320,015	72%	37%
Construction, Equipment & Furnishings	\$50,183,042	\$50,320,449	\$39,837,291	\$7,153,348	79%	18%
Misc.	\$47,510	\$53,157	\$5,647	\$5,647	11%	100%
Contingency	\$2,675,210	\$8,030,624	\$0	\$0	0%	0%
Total Project Budget	\$59,388,215	\$64,455,003	\$45,523,016	\$10,626,029		
% of Total Project Budget Committed	70.63%					
% of Total Commitments Expended	23.34%					
% of Total Project Budget Expended	16.49%					

* Project Budget contains funds for Phase 3 (Loop Road, Fire Lane, and Parking Lot) at Frisco Campus

6.4 Phase 3

McKinney Campus Projects

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$4,370,860	\$4,375,520	\$3,262,892	\$589,580	75%	18%
Investigation, Testing & Verification	\$472,163	\$472,163	\$9,200	\$0	2%	0%
Construction, Equipment & Furnishings	\$30,179,816	\$30,179,816	\$0	\$0	0%	0%
Misc.	\$31,435	\$31,435	\$901	\$901	3%	100%
Contingency	\$2,833,454	\$3,505,791	\$0	\$0	0%	0%
Total Project Budget	\$37,887,728	\$38,564,725	\$3,272,993	\$590,481		
% of Total Project Budget Committed	8.49%					
% of Total Commitments Expended	18.04%					
% of Total Project Budget Expended	1.53%					

Frisco Campus (Additional Projects)

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$2,883,468	\$2,883,468	\$528,468	\$36,000	18%	7%
Investigation, Testing & Verification	\$347,015	\$347,015	\$0	\$0	0%	0%
Construction, Equipment & Furnishings	\$16,724,000	\$16,724,000	\$0	\$0	0%	0%
Misc.	\$70,820	\$70,820	\$0	\$0	0%	0%
Contingency	\$1,094,995	\$1,094,995	\$0	\$0	0%	0%
Total Project Budget	\$21,120,298	\$21,120,298	\$528,468	\$36,000		
% of Total Project Budget Committed	2.50%					
% of Total Commitments Expended	6.81%					
% of Total Project Budget Expended	0.17%					

Plano Campus (Additional Projects)

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Total Project Budget	\$0	\$4,677,541	\$0	\$0		
% of Total Project Budget Committed	0.00%					
% of Total Commitments Expended	0.00%					
% of Total Project Budget Expended	0.00%					

6.5 Phase A

Public Safety Training Center

Budget Group	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Construction Costs	\$31,068,022	\$31,068,022	\$31,068,022	100%	100%
Total Project Budget	\$31,068,022	\$31,068,022	\$31,068,022		

* This project was not managed by AECOM. However, it is included in the report to make a complete report of Bond costs.

Trane Energy PACT

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Frisco Campus	\$9,725,336	\$9,725,336	\$9,725,336	\$6,491,655	100%	67%
Plano Campus	\$6,797,834	\$6,797,834	\$6,797,834	\$4,770,037	100%	70%
McKinney Campus	\$4,044,983	\$4,044,983	\$4,044,983	\$2,866,213	100%	71%
Courtyard Center	\$548,720	\$548,720	\$548,720	\$536,634	100%	98%
Collin Higher Education Center	\$720,659	\$720,659	\$720,659	\$693,453	100%	96%
Total Program Budget	\$21,837,531	\$21,837,531	\$21,837,531	\$15,357,992		
% of Total Project Budget Committed	100.00%					
% of Total Commitments Expended	70.33%					
% of Total Project Budget Expended	70.33%					

6.6 Additional Program Budgets

Program Level

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Building Fund Reimbursement	\$51,150,000	\$0	\$0	\$0	0%	0%
Program Wide Traffic Study	\$0	\$370,000	\$370,000	\$351,500	100%	95%
Program Contingency	\$39,393,094	\$3,141,389	\$0	\$0	0%	0%
Trane PACT Program Management		\$99,500	\$99,500	\$36,000	100%	36%
District Wide Air Cleaning		\$140,000	\$140,000	\$3,150	100%	2%
District Wide Commissioning		\$100,000	\$19,850	\$2,625	20%	13%
Total Project Budget	\$90,543,094	\$3,850,889	\$370,000	\$351,500		

* Building Fund Reimbursements for Wylie Campus land, Technical Campus land, and Public Safety Training Center construction costs were completed in August '18. Budgets, Commitments and Expenditures for these costs are reflected in each project.

** Program Contingency Original Budget is the result of the balance from the original Phase 3 & 4 projects less the funding for the Frisco Campus Parking Garage, McKinney Campus Welcome Center & Trane Energy PACT projects.

* Additional Phase 3 projects to be funded from Program Contingency

7. Completed Items

7.1 General Program

- [AECOM issued the Monthly Program Report for June '20 to Collin College on July 7th](#)
- [AECOM conducted coordination meetings with the Executive Committee on July 13th, 20th, and 27th](#)

7.2 Procurement

- [PBK Contract for the McKinney Campus Welcome Center was executed and PO was issued on July 23rd](#)

7.3 Design

- [PBK held a Plan Review Meeting with Collin College and AECOM for the McKinney Campus Welcome Center on July 20th](#)
- [PBK held a Plan Review Meeting with Collin College and AECOM for the McKinney Campus Welcome Center on July 22nd](#)
- [PBK held a meeting with Collin College and AECOM for the Dental Hygiene Renovations at the McKinney Campus on July 31st](#)

7.4 Pre-Construction

- No Pre-Construction Items have been completed at this time

7.5 Construction

- [Collin College, AECOM, Perkins+Will, Inc. and McCarthy Building Companies, Inc. conducted Weekly OAC meetings on July 1st, 8th, 15th, 22nd, and 29th for the Technical Campus](#)
- [Collin College, AECOM, Page Southerland Page, Inc. and Skanska USA Building, Inc. conducted Weekly OAC meetings on July 2nd, 9th, 16th, 23rd, and 30th for the Wylie Campus](#)

- Collin College, AECOM, Page Southerland Page, Inc., Skanska USA Building, Inc. and Bath Commissioning conducted Weekly MEP/Commissioning meetings on July 1st, 8th, 15th, 22nd, and 29th for the Wylie Campus
- Collin College, AECOM, Beck Architecture, LLC, and JT Vaughn Construction conducted Weekly OAC meetings on July 1st, 8th, 15th, 22nd, and 29th for the Celina Campus
- Collin College, AECOM, Beck Architecture, LLC, and JT Vaughn Construction conducted Weekly OAC meetings on July 2nd, 9th, 16th, 23rd, and 30th for the Farmersville Campus
- Collin College, AECOM, Beck Architecture, LLC, and JE Dunn Construction conducted an OAC meeting on July 7th, 14th, 21st, and 28th for the IT Center at the Frisco Campus
- McCarthy Building Companies, Inc. held the Trade Bar C Part 1 Punchlist Walk with AECOM, Perkins & Will, Inc., and Hoefer Wysocki on July 1st for the Technical Campus
- Collin College, AECOM, and Beck Architecture, LLC met to discuss skunkworks on July 6th for the IT Center
- Collin College, AECOM, and Beck Architecture, LLC met to discuss Windows Labs on July 7th for the IT Center
- McCarthy Building Companies, Inc. held the Trade Bar C Part 2 Punchlist Walk with AECOM, Perkins & Will, Inc., and Hoefer Wysocki on July 9th for the Technical Campus
- McCarthy Building Companies, Inc. held the Trade Bar D Punchlist Walk with AECOM, Perkins & Will, Inc., and Hoefer Wysocki on July 15th for the Technical Campus
- McCarthy Building Companies, Inc. held the Site and Exterior Punchlist Walk with AECOM, Perkins & Will, Inc., and Hoefer Wysocki on July 29th for the Technical Campus

See Appendix A for Construction Progress Photos

7.6 Acceptance and Close-Out

- No Acceptance and Close-Out Phase Items have been completed at this time

8. Pending Items

8.1 General Program

- No General Program items are pending at this time

8.2 Procurement

- [CMAR Short-list Interviews for the Frisco Campus projects](#)

8.3 Design

- [Revised easement locations at Celina Campus due to changes in new roadway alignment](#)

8.4 Pre-Construction

- [Coordination with the City of Frisco on the permitting/zoning requirements for the work on the Frisco Campus](#)

8.5 Construction

- [FF&E deliveries, city inspections, and interior and exterior finishes in the Trade Bars, at the Technical Campus](#)
- [FF&E deliveries, IT installation, and punch list at the Wylie Campus](#)

- [Student Occupancy approval from City of Allen](#)
See Appendix A for Construction Progress Photos

8.6 Acceptance and Close-Out

- No Acceptance and Close-Out activities are underway at this time

Appendix A – Construction Progress Photos

Technical Campus



July '20 Aerial



South View of Academic Building




Southern Monument Sign



Alignment Lifts in Trade Bar D




Shared Building Lab at Trade Bar C

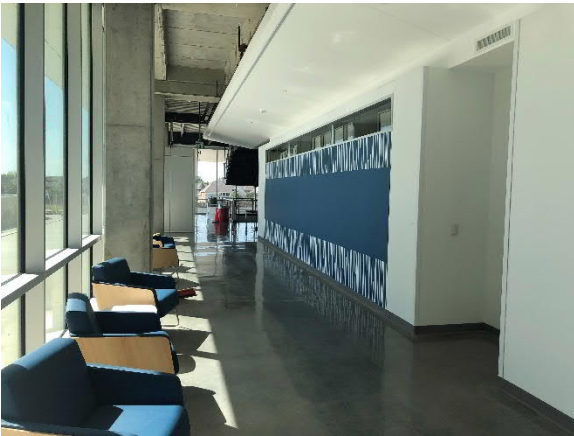


Graphic Install at Main Entrance of Academic Building



Kiosks at One-Stop Shop in Academic Building

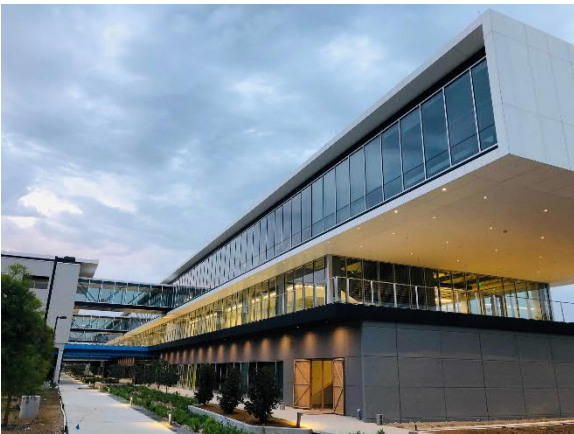

North End View of Academic Building

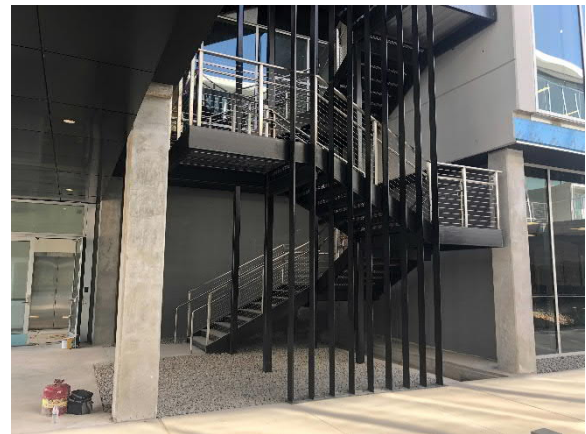

Angles Installed and Painted at Trade Bar B Exterior Stairs

Wylie Campus



July '20 Aerial



Outdoor Seating in Campus Quad
between Campus Commons and Student



Outdoor Seating in Front of Library



Level 2 of Campus Commons




Testing Center in Campus Commons



Seating in Level 1 of Student Center



Dining Area at Student Center

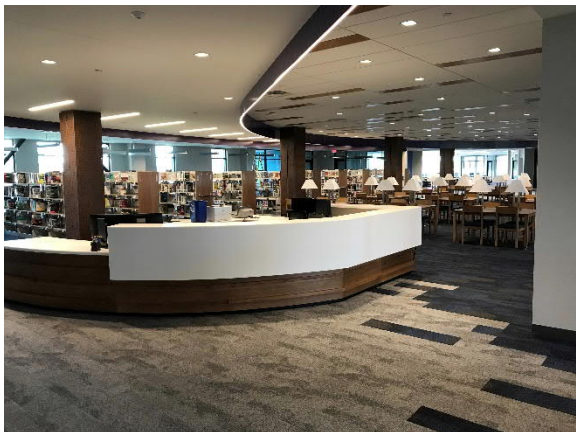

Circulation Desk and Table Install at Library




Bookcases at Library


Celina Campus



July '20 Aerial

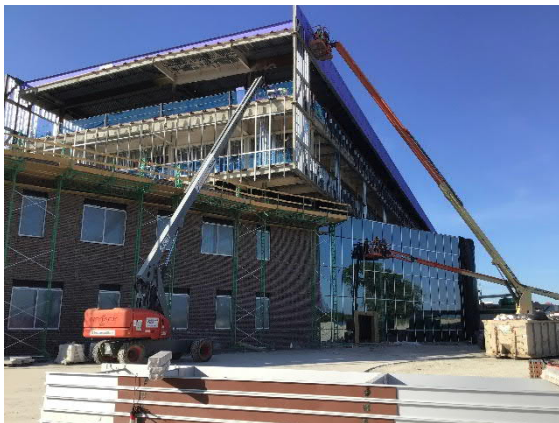

South View of North Building

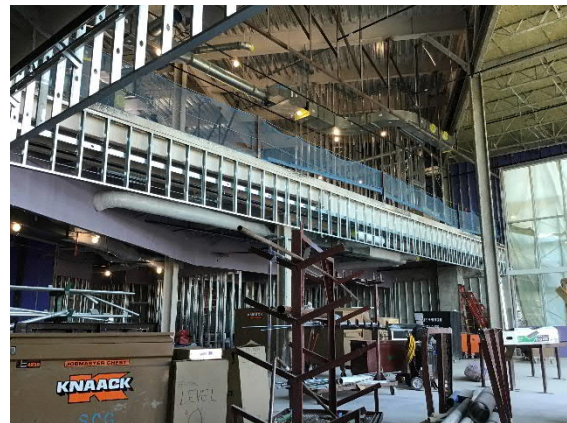

Rough-In of 1st Floor

Farmersville Campus



July '20 Aerial



Looking West at Campus



Curtain Wall at Library Area


IT Center at Frisco Campus



July '20 Aerial



South View of Atrium from Level 2 Bridge

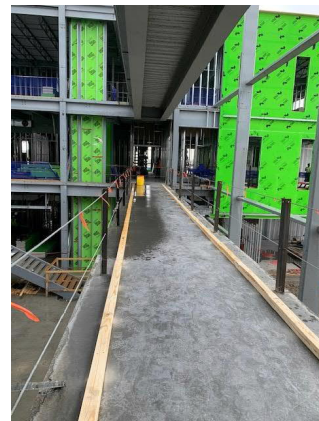

Level 2 Atrium Bridge
