




# Argyle Stadium

## August 2025 Update

# Site Photos

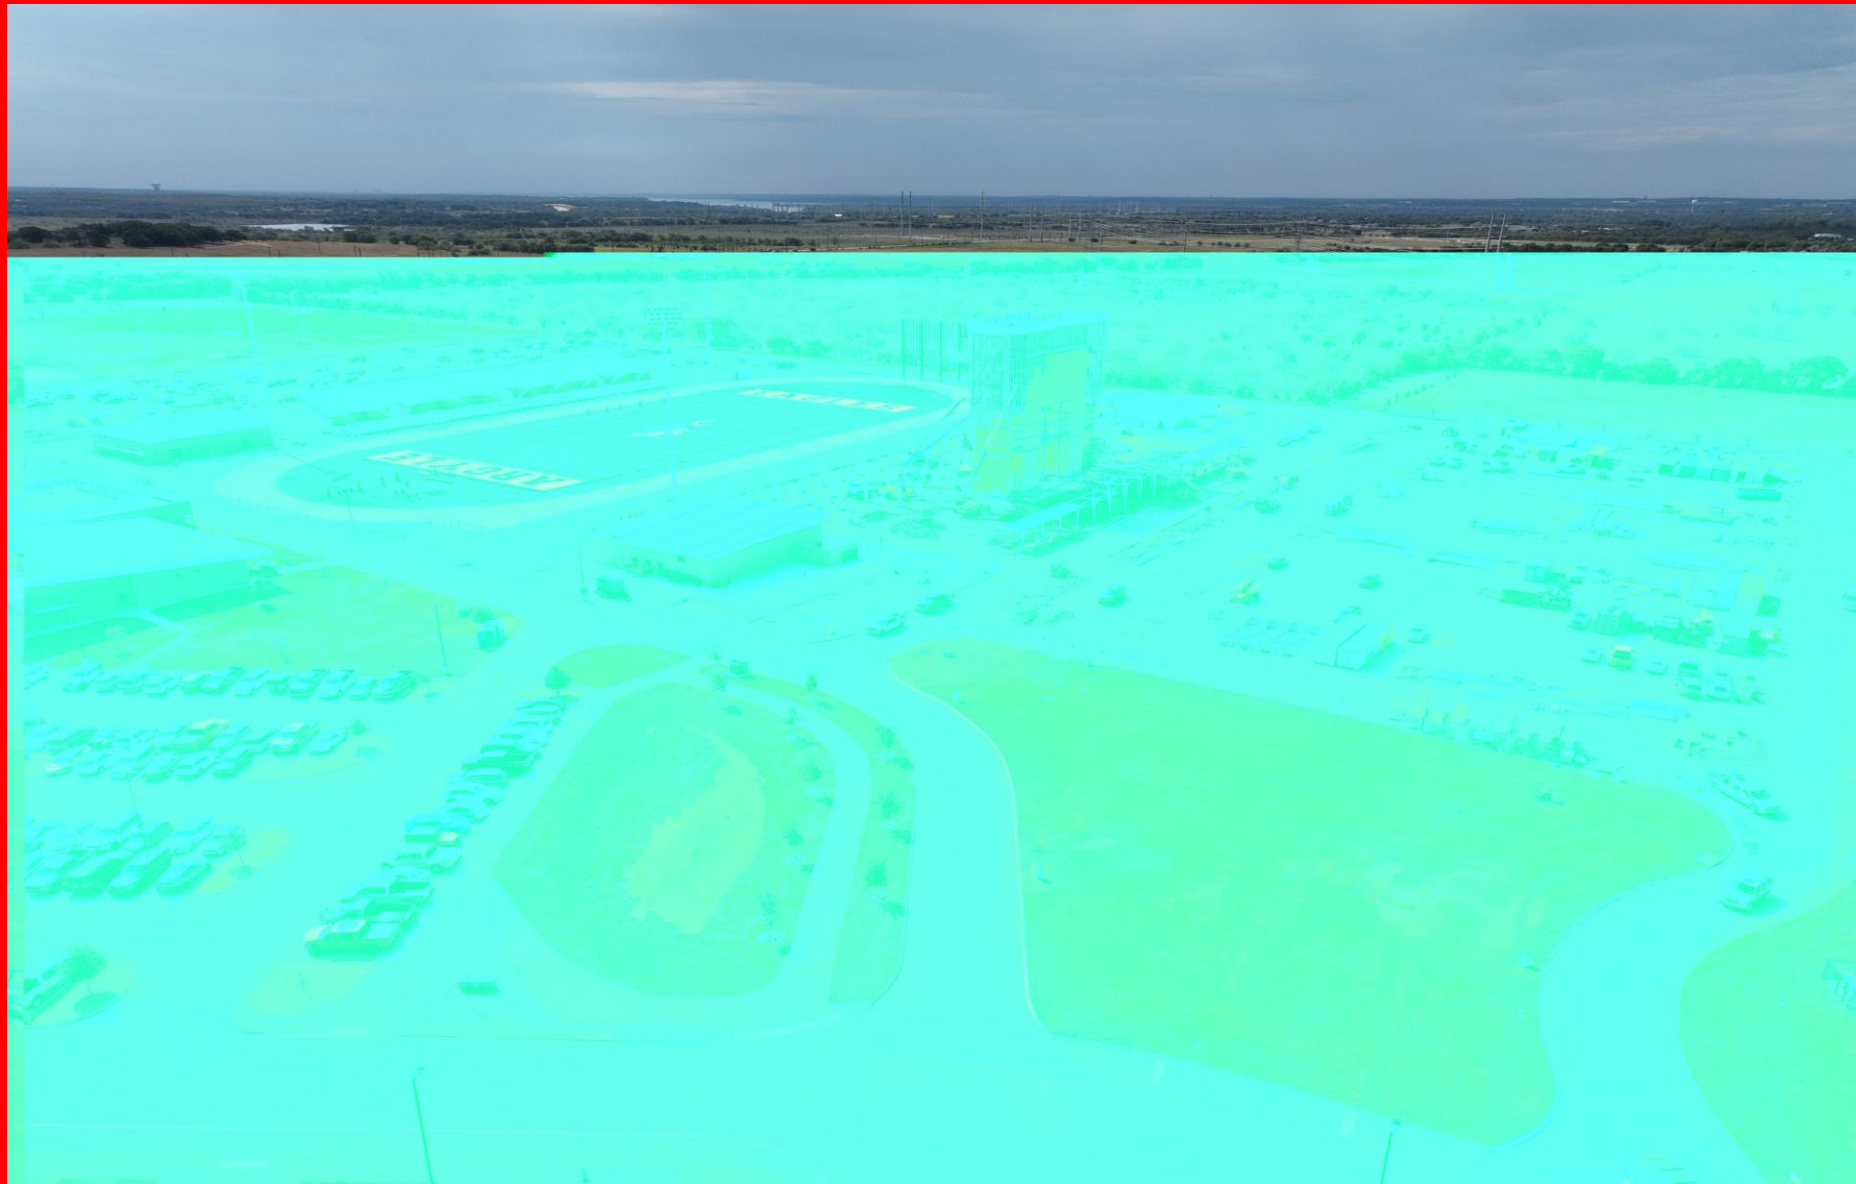



# Site Photos



**POGUE**  
CONSTRUCTION  
POWERED BY PEOPLE



# Site Photos



**POGUE**  
CONSTRUCTION  
POWERED BY PEOPLE



# Site Photos



**POGUE**  
CONSTRUCTION  
POWERED BY PEOPLE



# Site Photos





# Site Photos






# Site Photos





# Site Photos

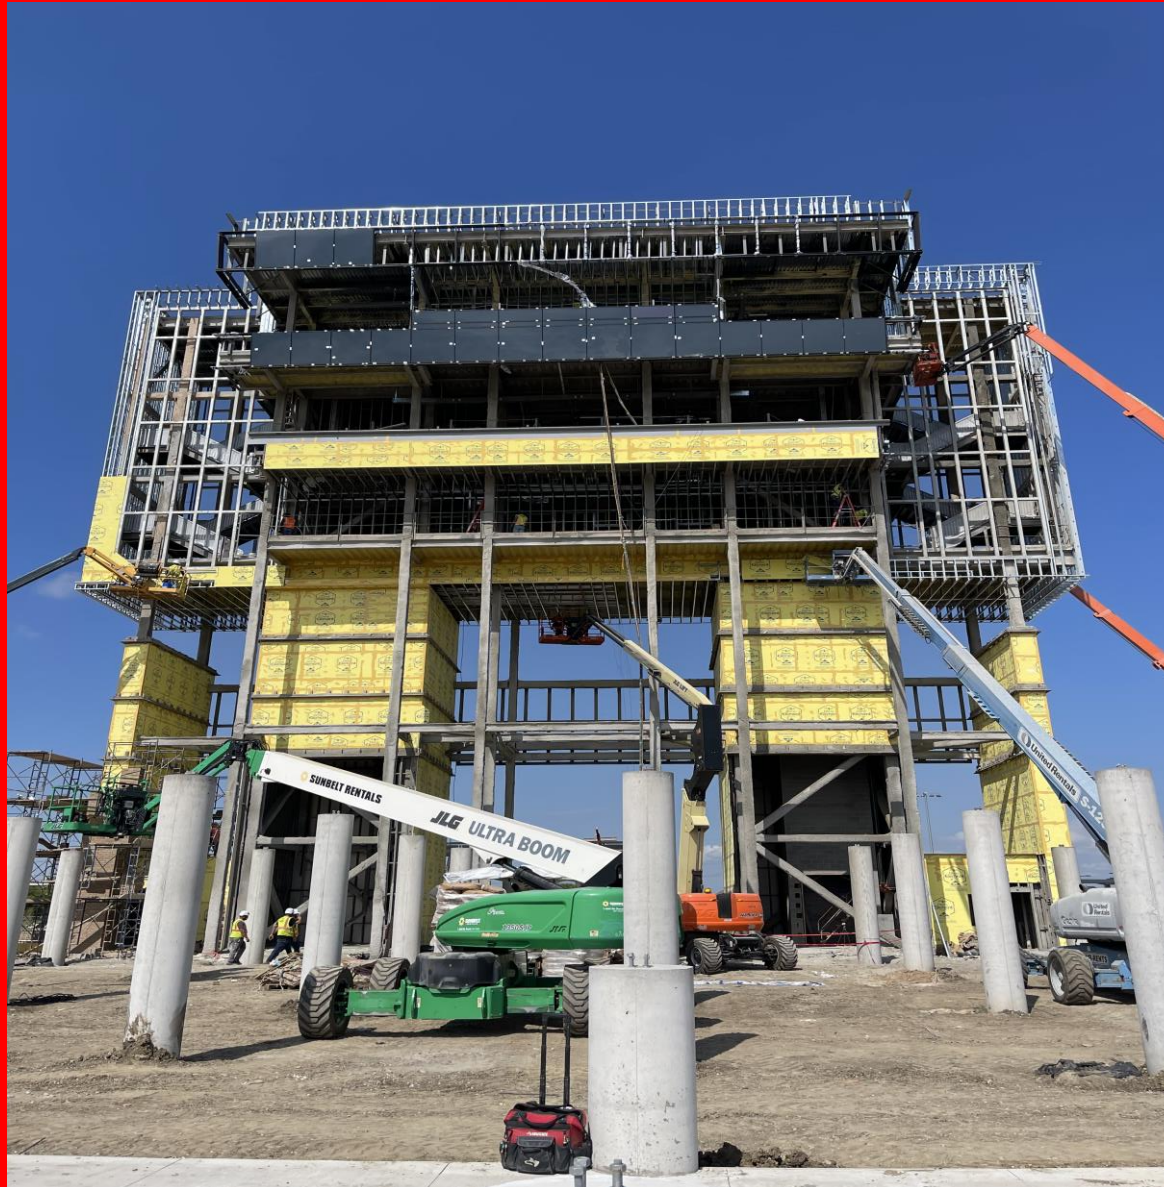



# Look Ahead

- Install LED's on Vision board  
Mid September
- Begin Home Grandstand  
Install
- Install Roof on Press Box
- Finish Home Entry Canopy





# Key Milestones

Key Milestone Tracking	
Town Permit Field Event Locations	September 5 <sup>th</sup> 2024 January 1 <sup>st</sup> 2025
Press Box Erection Begins IAC Erection Begins	March 2025 Spring 2025
Visitor Grandstand Install Home Grandstand Install	Spring 2025 Summer 2025
Substantial Completion	December 2025





# Middle School

# August 2025 Update




# Site Photos





# Site Photos

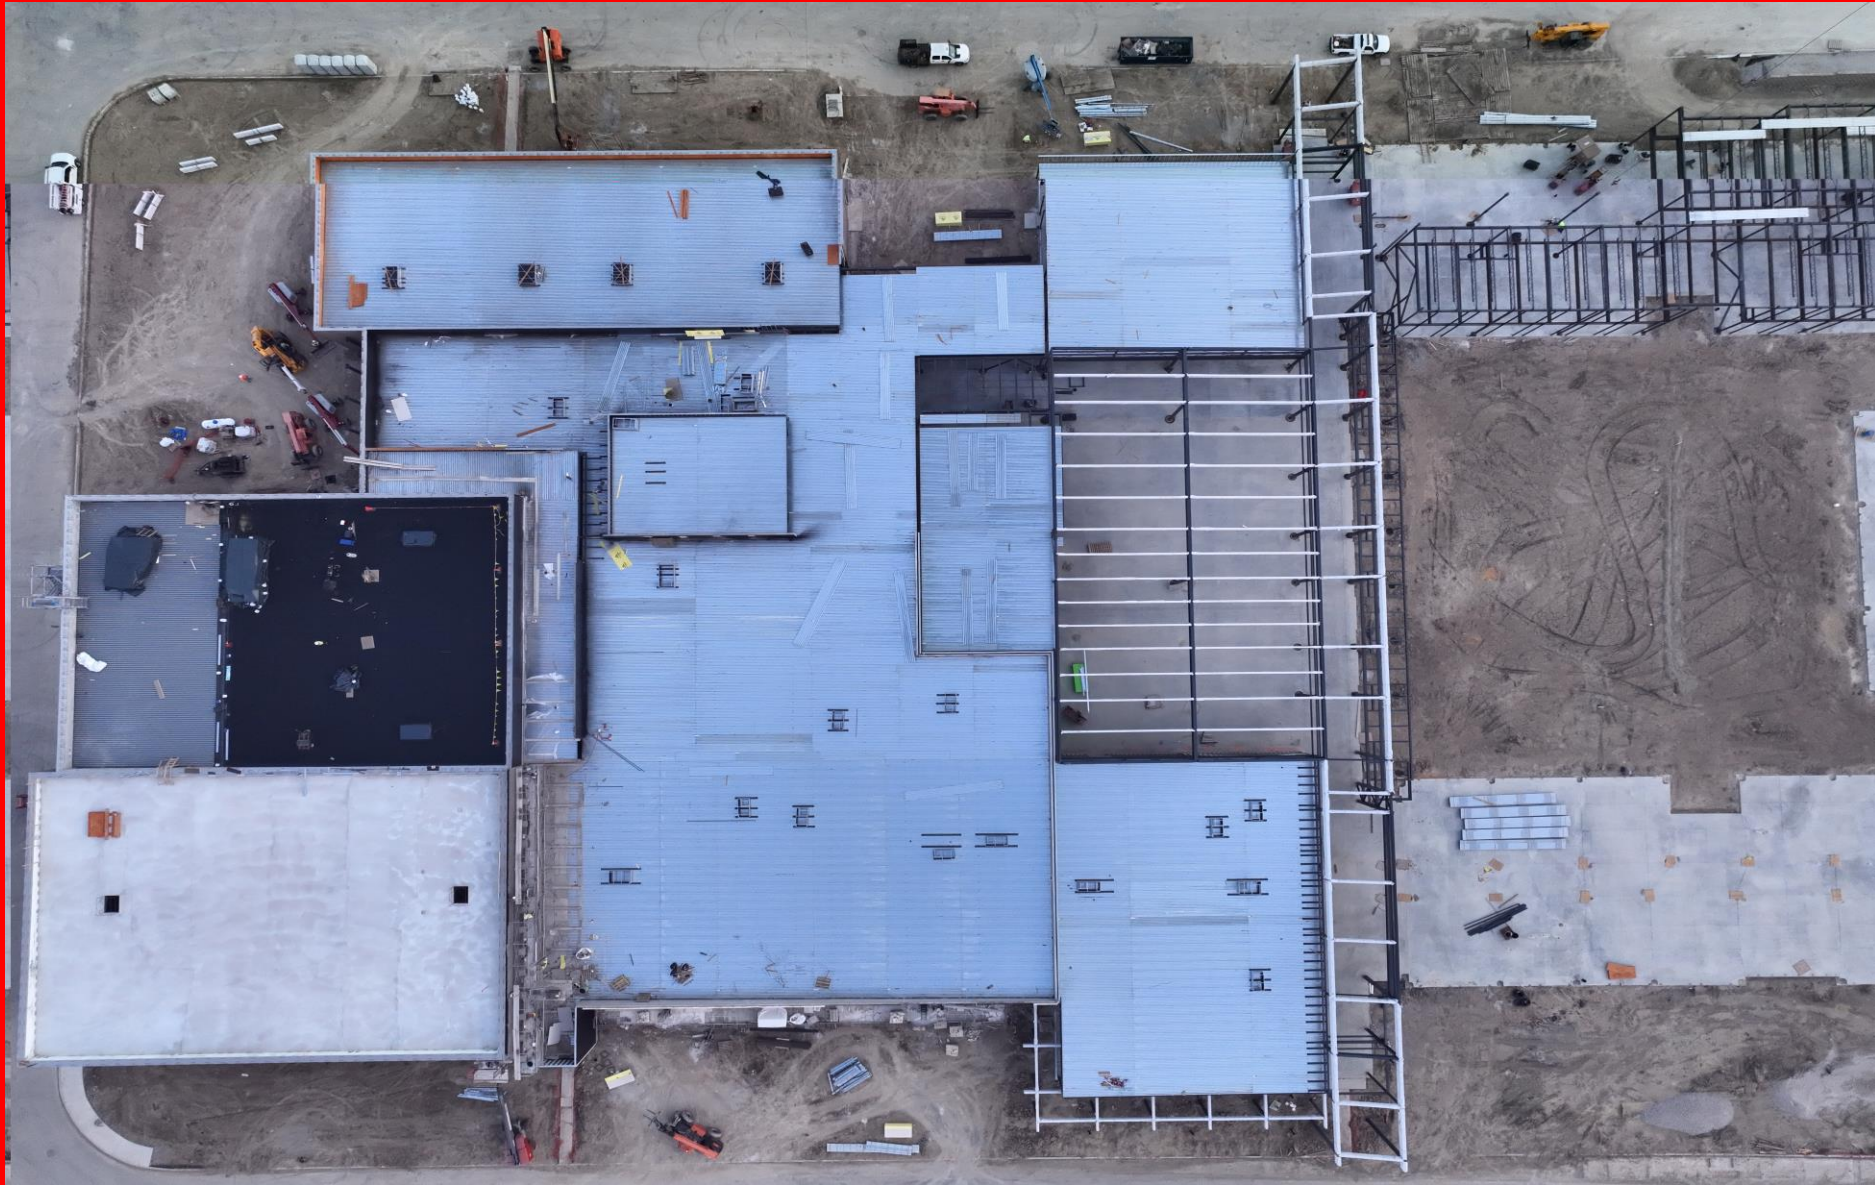



# Site Photos





# Site Photos





# Site Photos





# Site Photos





# Look Ahead

- Tennis Court Fence Install
- Storm Shelter Roof Complete
- 2<sup>nd</sup> Floor concrete pours
- FM 407 Landscape Completed
- Complete Retaining Wall





# Key Milestones

Key Milestone Tracking	
Town of Argyle Permit	December 20, 2024
Grading Completion	November 2024
Substantial Completion	July 2026
