



**DENTON INDEPENDENT SCHOOL DISTRICT**  
EMPOWERING LIFE-LONG LEARNERS

**Construction, Planning &  
Growth**

# Construction Report

**May  
2026**

**Prepared by:**

**Brandon Boyter Executive Director of Construction, Planning & Growth**

# Active Construction Timeline



Facility	Phase of Development	Move In Date
High School #5	In Progress	2028
Ginnings Elementary Rebuild	In Progress	2027
Borman Elementary School Replacement	In Progress	2026
Ryan High Renovation & Multipurpose	In Progress	2026
Houston Elementary School Renovation	In Progress	2026
McNair Elementary School Renovation	In Progress	2026
McMath Middle School Turf & Track Modification	In Progress	2026
Cross Oaks Elementary School Facility Upgrades	In Progress	2026
Crownover Middle School Facility Upgrades	In Progress	2026
Gallian Child Development Facility Upgrades	In Progress	2026
Providence Elementary School Facility Upgrades	In Progress	2026
Savannah Elementary School Facility Upgrades	In Progress	2026
Pecan Creek Elementary School Facility Upgrades	In Progress	2026
Paloma Creek Elementary School Marquee Upgrade	In Progress	2026
McMath Middle School Marquee Upgrade	In Progress	2026



DENTON INDEPENDENT SCHOOL DISTRICT  
EMPOWERING LIFE-LONG LEARNERS

Construction, Planning &  
Growth

Borman Elementary  
School

May  
2026

Prepared by:

Brandon Boyter Executive Director of Construction, Planning & Growth

# Borman Elementary School



**2023 Bond Authorization**  
**Architects – Corgan**  
**Contractor – Joeris**  
**Move In – August 2026**



# Borman Elementary School



**2023 Bond Authorization**  
**Architects – Corgan**  
**Contractor – Joeris**  
**Move In – August 2026**

## Tasks completed previous 90 days:

- Performing overhead punches in all areas
- All paving, retaining wall and site work is being completed.
- Courtyard work ongoing end of through end of May.
- Storm shelter will be completed.
- Finishes are ongoing throughout all areas.

## Upcoming tasks:

- All interior finishes are ongoing.
- Landscape, fencing, paving and all other site work is ongoing.
- Remaining exterior finishes is ongoing (metal panels).
- Substantial completion of phase I expected July 26<sup>th</sup>.
- Phase II demolition of existing building to start June 22 and will last about 3 weeks. Site work will begin end of July/first of August.

Prepared by:

Brandon Boyter Executive Director of Construction, Planning & Growth

# Borman Elementary School




**2023 Bond Authorization**  
**Architects – Corgan**  
**Contractor – Joeris**  
**Move In – August 2026**



# Borman Elementary School



**2023 Bond Authorization**  
**Architects – Corgan**  
**Contractor – Joeris**  
**Move In – August 2026**

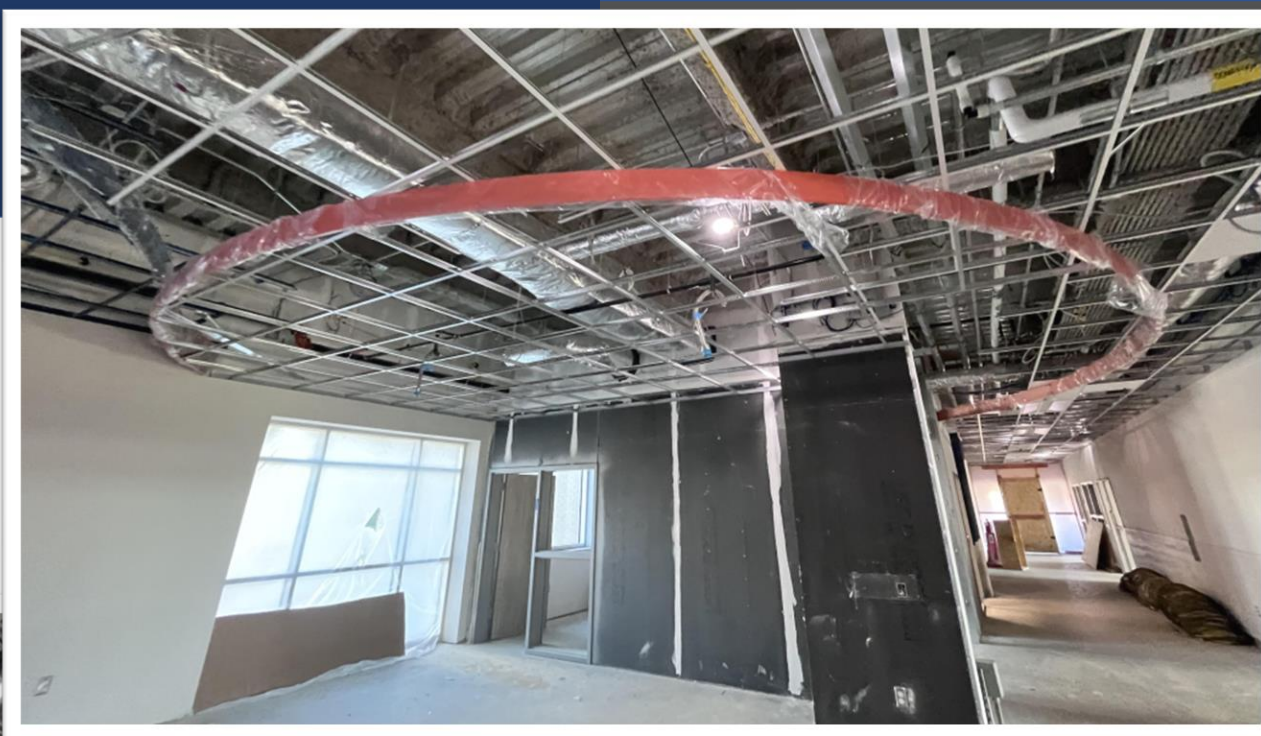

# Borman Elementary School



**2023 Bond Authorization**  
**Architects – Corgan**  
**Contractor – Joeris**  
**Move In – August 2026**





**DENTON INDEPENDENT SCHOOL DISTRICT**  
EMPOWERING LIFE-LONG LEARNERS

**Construction, Planning &  
Growth**

**Ginnings Elementary  
School**

**May  
2026**

**Prepared by:**

**Brandon Boyter Executive Director of Construction, Planning & Growth**

# Ginnings Elementary School



**2023 Bond Authorization**  
**Architects – Corgan**  
**Contractor – Balfour Beatty**  
**Move In – 2027**

# Ginnings Elementary School



## Tasks completed previous 90 days:

- Slab on grade to begin march with area A then going to areas D,C and finishing up with B.
- ICF walls will begin in April - Sept.
- Structural steel to begin end of May – Oct.

## Upcoming tasks:

- Structural steel erection ongoing
- ICF walls ongoing
- Slab on metal deck in all areas
- Exterior framing and sheathing July-August south and west side.

**2023 Bond Authorization**

**Architects – Corgan**

**Contractor – Balfour Beatty**

**Move In – 2027**

**Prepared by:**

**Brandon Boyter Executive Director of Construction, Planning & Growth**

# Ginnings Elementary School



**2023 Bond Authorization**

**Architects – Corgan**

**Contractor – Balfour Beatty**

**Move In – 2027**



# Ginnings Elementary School



**2023 Bond Authorization**  
**Architects – Corgan**  
**Contractor – Balfour Beatty**  
**Move In – 2027**

# Ginnings Elementary School



**2023 Bond Authorization**

**Architects – Corgan**

**Contractor – Balfour Beatty**

**Move In – 2027**





**DENTON INDEPENDENT SCHOOL DISTRICT**  
EMPOWERING LIFE-LONG LEARNERS

**Construction, Planning &  
Growth**

**Mia Price High School**

**May  
2026**

**Prepared by:**

**Brandon Boyter Executive Director of Construction, Planning & Growth**

# Mia Price High School



March 2026



May 2026

**2023 Bond Authorization**  
**Architects – VLK Architects**  
**Contractor – CORE**  
**Move In – TBD**

# Mia Price High School



**2023 Bond Authorization**  
**Architects – VLK Architects**  
**Contractor – CORE**  
**Move In – TBD**

## Tasks completed previous 90 days:

- Main Building Exterior - Brick and Metal Panels complete
- Sidewalks and Naylor Road Improvements to begin
- Main Building Interior – Walls, MEP rough in, Sheetrock, Tile in progress
- Sports Fields- Fencing and Turf installed throughout site
- Multi-Purpose Stadium: Brick, Metal Panels, walls, doors and windows

## Upcoming tasks:

- Main Building Exterior – Complete Walls, Roofing, Windows and Doors
- Main Building Interior – MEP rough, Sheetrock, Tile and Paint in progress
- Naylor Road Improvements – Utility relocation under construction
- Auxiliary Buildings – Complete Brick and Roof, MEP rough continues
- Sports Fields – install turf on fields, concrete walkways and fencing

Prepared by:

Brandon Boyter Executive Director of Construction, Planning & Growth

# Mia Price High School



**2023 Bond Authorization**

**Architects – VLK Architects**

**Contractor – CORE**

**Move In – TBD**



# Mia Price High School





**2023 Bond Authorization**

**Architects – VLK Architects**

**Contractor – CORE**

**Move In – TBD**

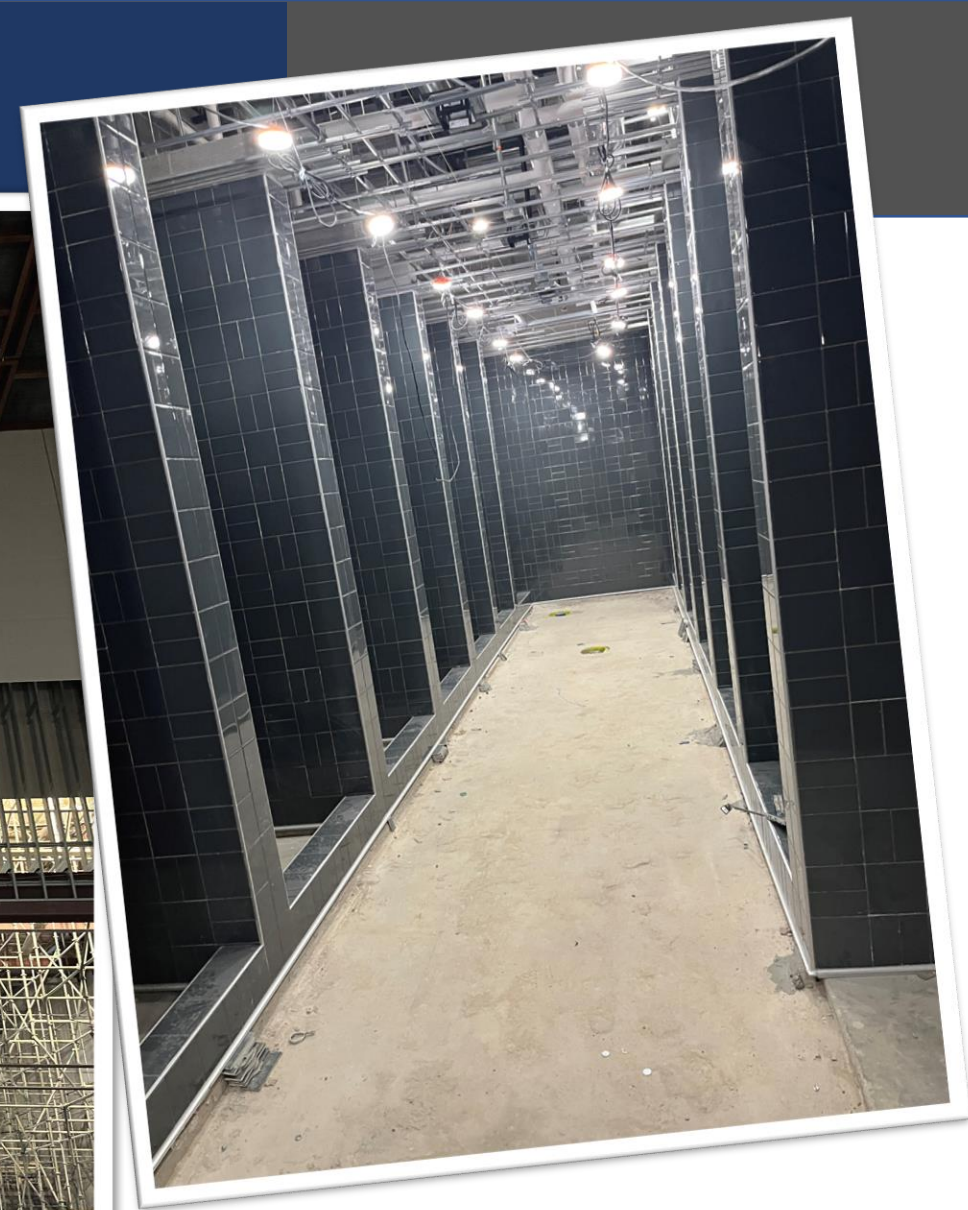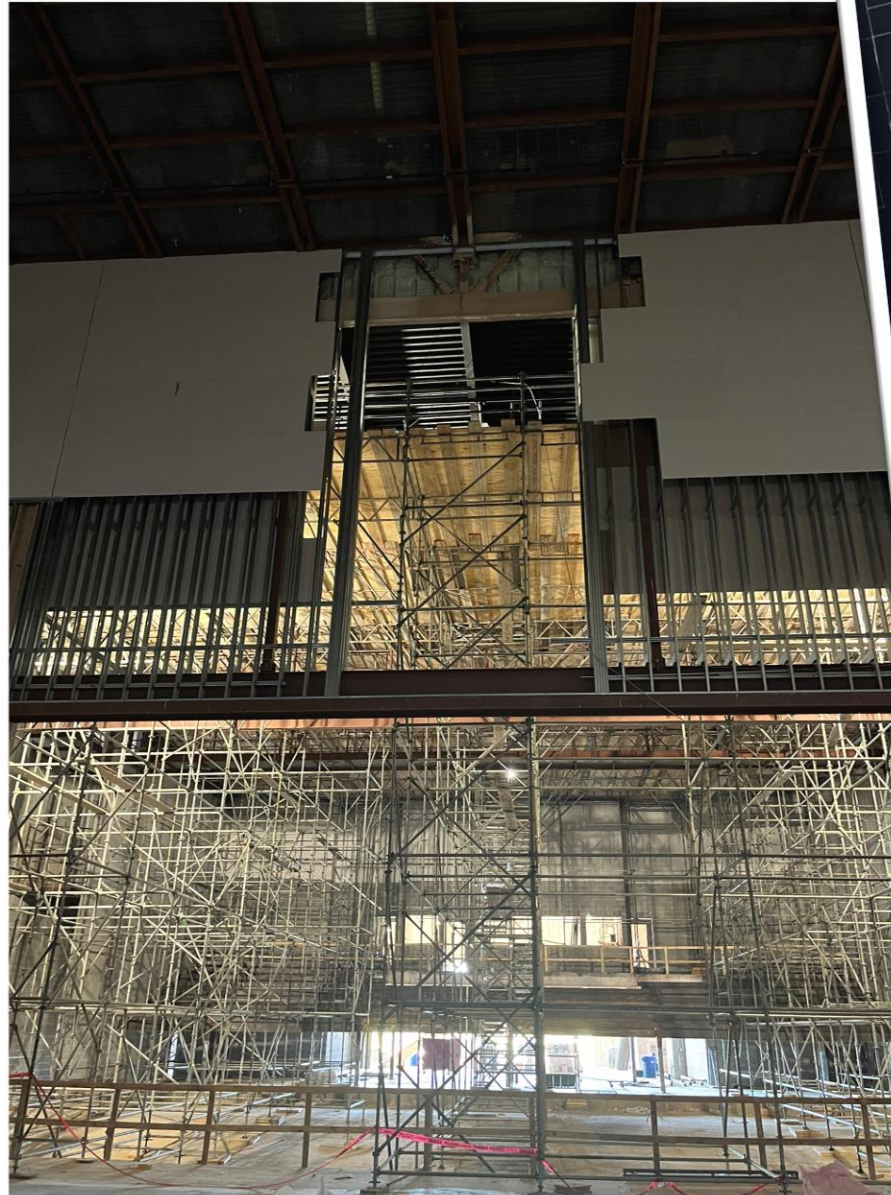

# Mia Price High School



**2023 Bond Authorization**

**Architects – VLK Architects**

**Contractor – CORE**

**Move In – TBD**

# Mia Price High School



**2023 Bond Authorization**  
**Architects – VLK Architects**  
**Contractor – CORE**  
**Move In – TBD**

