



Collin College

September 2025 Monthly Report

2023-2030 Master Plan Phase I
Collin County Community College District

Project Number: 60726232

October 07, 2025

Quality Information

Prepared by**Nuria Cortes**Nuria Cortes
Program Controls Manager**Reviewed by****Melissa Perette**Melissa Perette
Project Campus Manager**Approved By****Tim Smith**Tim Smith
Program Director

Revision History

Revision	Revision date	Details	Authorized	Name	Position
First Publication	October 7, 2025	September '25 Report	Yes	Tim Smith	Program Director

Distribution List

# Hard Copies	PDF Required	Association / Company Name
	1	Dr. Neil Matkin / Collin College
	1	Dr. Bill King / Collin College
	1	Chris Eyle / Collin College

Prepared for:

Collin County Community College District
3452 Spur 399
Suite 327
McKinney, TX 75069

Prepared by:

Nuria Cortes
Program Controls Manager
E: ncortes.aecom@collin.edu

AECOM
13355 Noel Road
4th Floor
Dallas TX, 75240
aecom.com

Copyright © 2025 by AECOM

All rights reserved. No part of this copyrighted work may be reproduced, distributed, or transmitted in any form or by any means without the prior written permission of AECOM.

Table of Contents

1.	Introduction	5
2.	Executive Summary	5
3.	Program Summary	6
3.1	Program Schedule	6
3.2	Program Budget	7
3.3	Current Personnel Estimate	7
4.	Project Summary	8
5	Completed Items	13
5.1	General Program	13
5.2	Procurement	13
5.3	Design	13
5.4	Pre-Construction	14
5.5	Construction	14
5.6	Acceptance and Close-Out	14
6	Pending Items	14
6.1	General Program	14
6.2	Procurement	15
6.3	Design	15
6.4	Pre-Construction	15
6.5	Construction	15
6.6	Acceptance and Close-Out	15
7	Progress Pictures	16
7.1	Plano Campus Renovations	16
7.2	Health Science Center	17
7.3	CHEC	18

1. Introduction

AECOM is currently managing 5 projects in this program. The total budget for the entire program is \$240,333,508.36, which includes 2 projects that AECOM is not managing.

On February 27, 2024, the Board of Trustees granted the District President authority to enter into and negotiate a contract with AECOM Technical Services, Inc. (AECOM) to provide Program Management Services for the Collin College 2023 Master Plan Program. On May 3, 2024, Collin College and AECOM executed the Collin contract for program management services. As part of these services, AECOM will deliver a monthly report to provide status and progress of key aspects of the Program.

2. Executive Summary

Completed and Pending Items

- Plano Campus – Roof work continues. Science labs, theater select restrooms and dining, and commercial music work continues.
- Courtyard Center – TCO for third and fourth floor was received. Furniture move was completed on 3rd and 4th floor. Punchlist items are ongoing.
- CHEC – On the first floor, new Foundation area mud, tape and paint has begun. At the old iCollin area, the walls have been framed and two-sided. On the second floor, the offices have been painted and carpet installed. Third floor new office areas have been mudded, taped and painted with overhead plumbing ongoing. The fourth-floor area for Phase 2 has been framed and two-siding has begun. TCO for third and fourth floor was received. Furniture move was completed on 3rd and 4th floor. Punchlist items are ongoing.
- Health Science Center – CM completed concrete pours for second level with one pour remaining. CM continues with prepping for third level pours to begin. CM nearing completion of onboarding all subcontractors for the project and refining scopes by trade.
- Wylie CTE – 100% Construction Documents are in progress and due on October 10th.

Items of close attention


- No items of close attention at this time

Budget Summary

- \$159,378,127.96 of the \$240,333,508.36 has been committed to-date in the form of contracts with various vendors.
- \$45,109,738.43 of the \$159,378,127.96 committed amount has been expended to-date.

3. Program Summary


3.1 Program Schedule

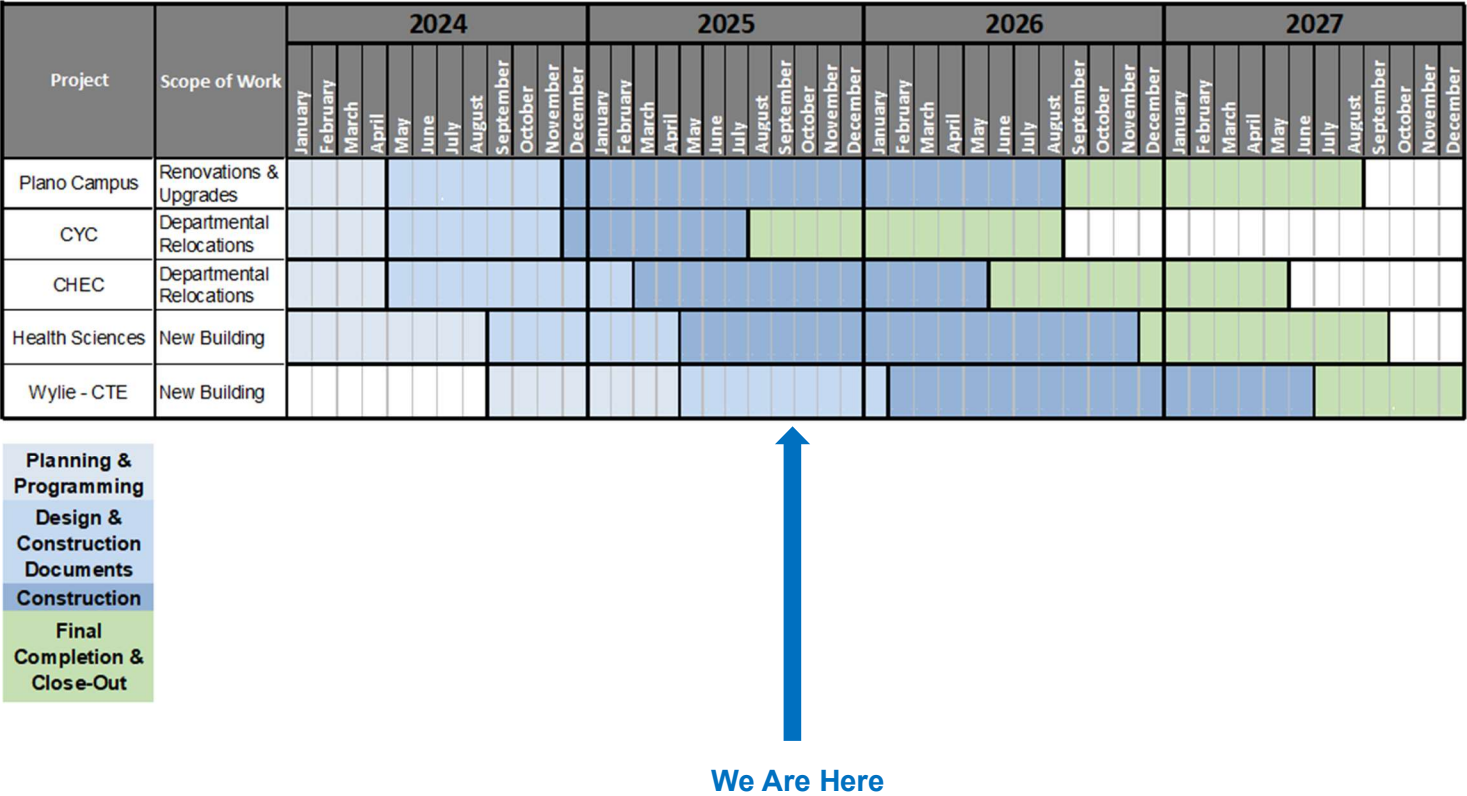

3.2 Program Budget

Cost Summary							
Budget Group	Original Budget	Current Budget	Commitments	Approved Changes	Total Commitments	Pending Commitments	Expended to Date
Construction, Equipment & Furnishings	\$157,491,962.00	\$197,052,751.00	\$94,659,258.31	\$45,618,277.82	\$140,277,536.13	\$379,526.66	\$32,844,019.33
Contingency	\$22,203,853.00	\$19,432,851.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
Investigation, Testing & Verification	\$2,847,939.00	\$3,309,483.00	\$1,206,287.00	\$5,115.00	\$1,211,402.00	\$0.00	\$330,961.53
Management, Design & Pre-Construction	\$17,145,727.36	\$20,078,376.36	\$16,984,594.01	\$822,870.00	\$17,807,464.01	\$0.00	\$11,934,757.57
Miscellaneous	\$393,015.00	\$460,047.00	\$81,725.82	\$0.00	\$81,725.82	\$2,895.42	\$0.00
Total	\$200,082,496.36	\$240,333,508.36	\$112,931,865.14	\$46,446,262.82	\$159,378,127.96	\$382,422.08	\$45,109,738.43

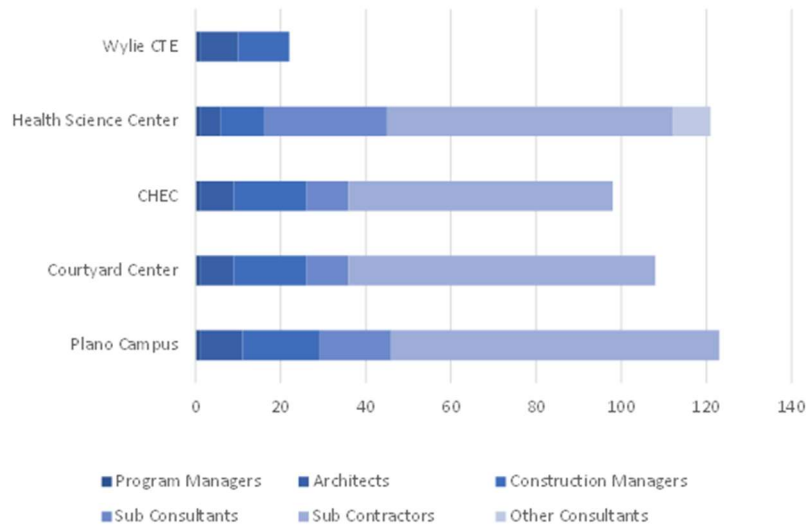

3.3 Current Personnel Estimate





It is estimated that the Program Managers, Architects, Construction Managers, Sub-Consultants, and Sub-Contractors, under contract with Collin College for the 2023 Master Plan Programs, have 472 employees contributing to the program's progress.

4. Project Summary



Courtyard Renovation

Project Name Courtyard Renovation			 		Schedule			
Project Name Courtyard Renovation			Project Number PJ1065		Activity			
Project Type Renovation			Project Phase Construction		Baseline Finish			
Project Manager Melissa Perette			Contractor/CM Skanska		Planned Finish			
Architect IN2 Architecture			Scope Description		Actual Finish			
Project Directory			* Renovations of the Courtyard Center * The Renovations include: - New Cosmetology Space - Relocate and expand Esthetician Space - New Medical Message space - Remodel of 4th floor for Information Technology and Police		BOT Approval of Construction Delivery Method 1/26/2024 1/26/2024 ↑ 1/26/2024 ✓ BOT Approval of Recommended A/E 1/26/2024 1/26/2024 ↑ 1/26/2024 ✓ BOT Approval of Program Manager 2/27/2024 2/27/2024 ↑ 2/27/2024 ✓ Architect Mobilized 5/17/2024 5/17/2024 ↑ 5/17/2024 ✓ BOT Approval of Recommended CMAR 5/26/2024 5/26/2024 ↑ 5/28/2024 ✓ 100% CDs Complete 11/1/2024 10/10/2024 ↑ 10/10/2024 ✓ GMP Submittal 12/1/2024 11/22/2024 ↑ 11/22/2024 ✓ BOT Approval of GMP 12/10/2024 12/10/2024 ↑ 12/10/2024 ✓ Obtain Building Permit 12/13/2024 12/13/2024 ↑ 1/16/2025 ✓ Contractor Mobilized 12/20/2024 12/20/2024 ↑ 1/20/2025 ✓ Substantial Completion 7/15/2025 8/18/2025 ↓ 8/18/2025 ✓ Final Completion 8/1/2025 9/10/2025 ↓ Student Occupancy 8/26/2025 8/26/2025 ↑ 9/2/2025 ✓			
Company AECOM Technical Services, Inc. Program Manager Collin College Owner Skanska Construction Manager-at-Risk IN2 Architecture A/E RWB Consulting Engineers			Project Role		Progress Summary			
					Status Date Notes 9/30/2025 TCO for third and fourth floor was received. Furniture move was completed on 3rd and 4th floor. Punchlist items are ongoing.			
Cost Summary								
Budget Group	Original Budget	Current Budget	Commitments	Approved Changes	Total Commitments	Pending Commitments	Expended to Date	
Construction, Equipment & Furnishings	\$4,991,556.00	\$5,222,037.00	\$4,999,577.35	\$251,369.00	\$5,250,946.35	\$0.00	\$3,056,600.88	
Contingency	\$294,481.00	\$50,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	
Investigation, Testing & Verification	\$82,073.00	\$82,073.00	\$72,151.00	\$0.00	\$72,151.00	\$0.00	\$26,607.00	
Management, Design & Pre-Construction	\$696,100.00	\$710,100.00	\$690,736.36	\$5,000.00	\$695,736.36	\$0.00	\$486,224.20	
Miscellaneous	\$4,551.00	\$4,551.00	\$1,847.00	\$0.00	\$1,847.00	\$1,750.50	\$0.00	
Total	\$6,068,761.00	\$6,068,761.00	\$5,764,311.71	\$256,369.00	\$6,020,680.71	\$1,750.50	\$3,569,432.08	

CHEC Renovation

Project Name CHEC Renovation			 		Schedule															
Project Name CHEC Renovation			Project Number PJ1066		Scope Description															
Project Type Renovation			Project Phase Construction		*Renovations Collin Higher Education Center - Renovations of selected spaces on 1st, 2nd, 3rd and 4th floor.															
Project Manager Melissa Perette		Contractor/CM Skanska		Architect IN2 Architecture		Project Directory														
Company		Project Role		<table border="1"> <thead> <tr> <th>Company</th> <th>Project Role</th> </tr> </thead> <tbody> <tr> <td>AECOM Technical Services, Inc.</td> <td>Program Manager</td> </tr> <tr> <td>Collin College</td> <td>Owner</td> </tr> <tr> <td>IN2 Architecture</td> <td>A/E</td> </tr> <tr> <td>Skanska</td> <td>A/E</td> </tr> <tr> <td>RWB Consulting Engineers</td> <td></td> </tr> </tbody> </table>					Company	Project Role	AECOM Technical Services, Inc.	Program Manager	Collin College	Owner	IN2 Architecture	A/E	Skanska	A/E	RWB Consulting Engineers	
Company	Project Role																			
AECOM Technical Services, Inc.	Program Manager																			
Collin College	Owner																			
IN2 Architecture	A/E																			
Skanska	A/E																			
RWB Consulting Engineers																				
Activity					Baseline Finish															
Planned Finish					Actual Finish															
BOT Approval of A/E Procurement Method					1/26/2024 1/26/2024 ↑ 1/26/2024 ✓															
BOT Approval of Construction Delivery Method					1/26/2024 1/26/2024 ↑ 1/26/2024 ✓															
BOT Approval of Recommended A/E					1/26/2024 1/26/2024 ↑ 1/26/2024 ✓															
BOT Approval of Program Manager					2/27/2024 2/27/2024 ↑ 2/27/2024 ✓															
Architect Mobilized					5/17/2024 5/17/2024 ↑ 5/17/2024 ✓															
BOT Approval of Recommended CMAR					5/26/2024 5/26/2024 ↑ 5/28/2024 ✓															
100% CDs Complete					11/1/2024 2/14/2025 ↓ 2/14/2025 ✓															
GMP Submittal					12/1/2024 2/20/2025 ↓ 2/20/2025 ✓															
BOT Approval of GMP					12/10/2024 3/25/2025 ↓ 3/25/2025 ✓															
Obtain Building Permit					12/20/2024 4/16/2025 ↓ 4/21/2025 ✓															
Contractor Mobilized					1/6/2025 4/17/2025 ↓ 4/21/2025 ✓															
Substantial Completion					4/1/2026 4/1/2026 ↑															
Final Completion					5/1/2026 5/1/2026 ↑															
Progress Summary																				
Status Date		Notes																		
9/30/2025		On the first floor, new Foundation area mud, tape and paint has began. At the old iCollin area, the walls have been framed and two-sided. On the second floor, the offices have been painted and carpet installed. Third floor new office areas have been mudded, taped and painted with overhead plumbing ongoing. The fourth floor area for Phase 2 has been framed and two-sided has began.																		
Cost Summary																				
Budget Group		Original Budget		Current Budget		Commitments		Approved Changes												
Total Commitments		Pending Commitments		Expended to Date																
Construction, Equipment & Furnishings		\$7,172,040.00		\$7,172,040.00		\$7,394,927.49		\$0.00												
Contingency		\$562,950.00		\$543,950.00		\$0.00		\$0.00												
Investigation, Testing & Verification		\$117,927.00		\$117,927.00		\$121,960.00		\$0.00												
Management, Design & Pre-Construction		\$860,348.36		\$879,348.36		\$844,348.36		\$5,000.00												
Miscellaneous		\$6,540.00		\$6,540.00		\$2,400.00		\$0.00												
Total		\$8,719,805.36		\$8,719,805.36		\$8,363,635.85		\$5,000.00												



Plano Renovation

Project Name Plano Renovation		 		Schedule					
Project Name Plano Renovation		Project Number PJ1064		Scope Description					
Project Type Renovation		Project Phase Construction		* Renovations to the Plano Campus * The Renovation includes: - Roof Replacement - Expanding Science Labs - Renovation and Expanding Health Sciences - Renovation in various other areas					
Project Manager Tim Smith		Contractor/CM Skanska						Architect IN2 Architecture	
Project Directory									
Company		Project Role		Activity					
AECOM Technical Services, Inc.		Program Manager		Baseline Finish					
Collin College		Owner		Planned Finish					
Skanska		Construction Manager-at-Risk		Actual Finish					
IN2 Architecture		A/E		BOT Approval of Construction Delivery Method					
BAI, LLC				BOT Approval of Recommended A/E					
Dunaway				BOT Approval of Program Manager					
Foodservice Design Professional				BOT Approval of Recommended CMAR					
MATSON DRISCOLL & DAMICO LLP				Architect Mobilized					
Price Consulting, Inc.				GMP 1 Construction Documents Submittal					
RWB Consulting Engineers				BOT Approval of GMP 1					
				GMP 2 Construction Documents Submittal					
				BOT Approval of GMP 2					
				Obtain Building Permit					
				Contractor Mobilized					
				Substantial Completion					
				Final Completion					
				Student Occupancy					
				Progress Summary					
				Status Date					
				Notes					
				9/30/2025 Plano Campus, Roof work continues. Science labs, Theater select Restrooms and Dining, Commercial Music has work continuing.					
Cost Summary									
Budget Group	Original Budget	Current Budget	Commitments	Approved Changes	Total Commitments	Pending Commitments	Expended to Date		
Construction, Equipment & Furnishings	\$62,835,304.00	\$74,193,298.00	\$68,916,953.21	\$1,626,402.82	\$70,543,356.03	\$308,765.66	\$26,672,958.17		
Contingency	\$2,372,401.00	\$1,008,102.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
Investigation, Testing & Verification	\$1,150,911.00	\$1,359,240.00	\$591,949.00	\$5,115.00	\$597,064.00	\$0.00	\$161,738.17		
Management, Design & Pre-Construction	\$6,895,542.00	\$8,078,310.00	\$6,987,542.26	(\$10,000.00)	\$6,977,542.26	\$0.00	\$5,177,365.60		
Miscellaneous	\$305,272.00	\$361,050.00	\$77,478.82	\$0.00	\$77,478.82	\$1,144.92	\$0.00		
Total	\$73,559,430.00	\$85,000,000.00	\$76,573,923.29	\$1,621,517.82	\$78,195,441.11	\$309,910.58	\$32,012,061.94		

Health Science Center

Project Name			Scope Description			Schedule				
Health Science Center						Activity	Baseline Finish	Planned Finish	Actual Finish	
Project Name						BOT Approval of Rec. A/E & CMAR Firms	3/26/2024	3/26/2024	3/26/2024	✓
Health Science Center						Architect Mobilized	4/30/2024	4/30/2024	4/30/2024	✓
Project Type						Programming	7/30/2024	8/15/2024	8/15/2024	✓
New			Project Phase			Schematic Design	9/30/2024	10/4/2024	10/4/2024	✓
Construction			The building will be:			Design Development Completion	12/20/2024	12/20/2024	12/18/2024	✓
Project Manager			3 stories totaling 116,902 square feet			GMP 1 Package Issuance	12/22/2024	12/18/2024	12/18/2024	✓
Contractor/CM			82,593 square feet to be finished out, 34,309 square feet to remain shell			GMP 1 Package Bidding	1/15/2025	1/24/2025	1/24/2025	✓
Architect			New Programs:			BOT Approval of GMP 1	2/25/2025	2/25/2025	2/25/2025	✓
Penny Busch			MLT			Contractor Mobilized	2/26/2025	5/1/2025	5/2/2025	✓
McCarthy Building Comp...			Radiography			GMP 2 - 100% CDs Bidding	3/28/2025	2/28/2025	2/28/2025	✓
PBK Architects, Inc.			Cath Lab			Foundations Complete	4/30/2025	9/11/2025	8/27/2025	✓
Project Directory			Nuclear Med			GMP 2 - 100% CDs Issuance	5/12/2025	6/9/2025	6/19/2025	✓
Company			CT Technology			BOT Approval of GMP 2	5/31/2025	5/27/2025	5/27/2025	✓
Project Role			MRI Technology			Structures Complete	2/28/2026	12/3/2025		
JQ Engineering (IMEG)			Programs Moving or Expanding:			Interior Finish-Out Complete	7/15/2026	9/16/2026		
AECOM Technical Services, Inc.			Nursing			Substantial Completion	7/31/2026	11/30/2026		
Collin College			Diagnostic Sonography (program move from McKinney)			Temporary CO	8/7/2026	10/31/2026		
RWB Consulting Engineers			Physical Therapy Assistant			Final CO	8/14/2026	11/30/2026		
CCA Landscape Architects, Inc.			Health Professions			Final Completion	8/31/2026	12/11/2026		
McCarthy Building Companies, Inc.			Interdisciplinary Spaces:			Owner Occupancy	8/31/2026	1/19/2027		
RLK Engineering			AR/VR Lab space			Student Occupancy	8/31/2026	1/19/2027		
PBK Architects, Inc.			Healthcare Simulation space							
PBK										
						Progress Summary				
						Status Date Notes				
						9/30/2025 CM completed concrete pours for second level with one pour remaining.				
						9/30/2025 CM continues with prepping for third level pours to begin.				
						9/30/2025 CM nearing completion of onboarding all subcontractors for the project and refining scopes by trade.				
Cost Summary										
Budget Group		Original Budget	Current Budget	Commitments	Approved Changes	Total Commitments	Pending Commitments	Expended to Date		
Construction, Equipment & Furnishings		\$47,793,062.00	\$63,833,786.00	\$13,347,800.26	\$43,740,506.00	\$57,088,306.26	\$0.00	\$7,062,474.65		
Contingency		\$1,987,031.00	\$1,066,438.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
Investigation, Testing & Verification		\$777,028.00	\$777,028.00	\$420,227.00	\$0.00	\$420,227.00	\$0.00	\$120,363.00		
Management, Design & Pre-Construction		\$5,212,227.00	\$6,092,097.00	\$5,244,227.03	\$822,870.00	\$6,067,097.03	\$0.00	\$4,326,055.00		
Miscellaneous		\$44,652.00	\$44,652.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
Total		\$55,814,000.00	\$71,814,001.00	\$19,012,254.29	\$44,563,376.00	\$63,575,630.29	\$0.00	\$11,508,892.65		

Wylie CTE

Project Name Wylie CTE		 		Schedule					
Project Name Wylie CTE		Project Number PJ1068		Scope Description					
Project Type New		Project Phase Design		Construction of a new Career Technical Education (CTE) building on the Wylie Campus. - Approximately 50,000 square feet - Building will provide space for the following: - Welding - HVAC - Electronic Engineering Technology (EET) - Certified Nurse Aid (CNA)					
Project Manager Kella Hilton		Contractor/CM Skanska						Architect Page Southerland Page...	
Project Directory									
Company AECOM Technical Services, Inc. Collin College Page Southerland Page, Inc. RWB Consulting Engineers Skanska				Progress Summary					
				Status Date Notes 9/30/2025 100% Construction Documents are in progress and due 10/10/25.					
Cost Summary									
Budget Group	Original Budget	Current Budget	Commitments	Approved Changes	Total Commitments	Pending Commitments	Expended to Date		
Construction, Equipment & Furnishings	\$34,700,000.00	\$46,631,590.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
Contingency	\$1,066,490.00	\$2,100,731.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
Investigation, Testing & Verification	\$720,000.00	\$973,215.00	\$0.00	\$0.00	\$0.00	\$278,755.00	\$0.00		
Management, Design & Pre-Construction	\$3,481,510.00	\$4,318,521.00	\$3,217,740.00	\$0.00	\$3,217,740.00	\$0.00	\$1,457,655.87		
Miscellaneous	\$32,000.00	\$43,254.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
Total	\$40,000,000.00	\$54,067,311.00	\$3,217,740.00	\$0.00	\$3,217,740.00	\$278,755.00	\$1,457,655.87		

5 Completed Items

5.1 General Program

- Facilities Meeting were held on September 8th, 15th, 22nd, and 29th

5.2 Procurement

- No Procurement items were completed at this time

5.3 Design

- Wylie CTE, City of Wylie Pre-Submittal meeting was held between City of Wylie, Collin College, Page Southerland and AECOM on September 2nd.
- Wylie CTE, Estimate review meeting was held between Collin College, Page Southerland, Skanska and AECOM on September 3rd.
- Wylie CTE, Design Development drawing review meeting was held between Collin College, Page Southerland and AECOM on September 3rd .
- Wylie CTE, Access Controls and Low Voltage, (IT) design coordination meeting was held between Collin College, Page Southerland and AECOM on September 4th.
- Wylie CTE, Parking Lot scope review meeting was held between Page Southerland, Skanska and AECOM on September 5th.
- Wylie CTE, Lincoln Predesign meeting was held between Collin College, Page Southerland, Lincoln and AECOM on September 10th.
- Wylie CTE, Matheson Gas (for welding) design review meeting was held between Collin College, Page Southerland, Matheson Gas and AECOM on September 10th.
- Wylie CTE, Welding Department design review meeting was held between Collin College, Page Southerland and AECOM on September 12th.
- Wylie CTE, Classroom equipment (projectors, podiums, etc.) design review meeting was held between Collin College, Page Southerland and AECOM on September 12th.
- Wylie CTE, Value Engineering review meeting was held between Page Southerland, Skanska and AECOM on September 17th.
- Wylie CTE, Interior Palette Design Review meeting was held between Collin College, Page Southerland and AECOM on September 18th.
- Wylie CTE, HVAC Department design review meeting was held between Collin College, Page Southerland and AECOM on September 18th.
- Wylie CTE, Welding Department design review meeting was held between Collin College, Page Southerland and AECOM on September 19th.
- Wylie CTE, Value Engineering review meeting was held between Page Southerland, Skanska and AECOM on September 23rd.
- Wylie CTE, Value Engineering review meeting was held between Collin College, Page Southerland and AECOM on September 25th.
- Wylie CTE, HVAC Department design review meeting was held between Collin College, Page Southerland and AECOM on September 25th.
- Wylie CTE, Welding Department design review meeting was held between Collin College, Page Southerland and AECOM on September 26th.

- Wylie CTE, Matheson Gas (for welding) design review meeting was held between Collin College, Page Southerland, Matheson Gas and AECOM on September 26th.

5.4 Pre-Construction

- No Pre-Construction items were completed at this time

5.5 Construction

- Plano Campus OAC meetings were held on September 4th, 11th, 18th, and 25th
- CHEC OAC meetings were held on September 4th, 11th, 18th, and 25th
- Courtyard OAC meetings was held on September 11th
- Courtyard Center, Walk for miscellaneous items with Collin College and AECOM was held on September 2nd.
- Plano Campus, AV Coordination meeting was held between Collin College, AECOM, IN2, Skanska, and RWB on September 4th
- Courtyard Center, Punch Walk for the third and fourth floor was held between Collin College, AECOM, IN2, RWB and Skanska on September 4th
- Plano Campus, Punch Walk for the weight room, storage room, and dance studio was held between Collin College, AECOM, IN2, and Skanska on September 4th
- Courtyard Center, 4th floor Walk with Collin College and AECOM was held on September 5th
- CHEC, Saturday Work meeting was held between Collin College, AECOM, and Skanska on September 9th
- CHEC, Temporary Moves for Third Floor Meeting was held between Collin College, AECOM, and Skanska on September 10th
- CHEC, President Suite's Data meeting was held between Collin College and AECOM on September 17th
- Courtyard Center, 4th Floor Keys meeting was held between Collin College and AECOM on September 22nd
- Courtyard Center, Access Control meeting was held between Collin College and AECOM on September 23rd
- Plano Campus, New room screen review was held between Collin College and AECOM on September 23rd
- CHEC, 4th Floor Conference Room OFE Installation meeting was held between Collin College, AECOM, Skanska and Taurus on September 25th
- Plano Campus, Moves for telephone, computers, Data closet concerns, TV monitors from old to new locations for Career Center, Student Engagement and Student Enrollment Services was done on September 25th
- Health Science Center, CM completed all foundations for the building along with the slab on grade concrete pours. Foundation for the building mockup is complete.

5.6 Acceptance and Close-Out

- No Acceptance and Close-Out items were completed at this time

6 Pending Items

6.1 General Program

- No General Program items are pending at this time

6.2 Procurement

- Health Science Center, design team obtaining proposal for physicist to complete a shielding report for the RF room.

6.3 Design

- Wylie CTE, 100% Construction Documents are due October 10th
- Health Science Center, Design team coordinating with Shimadzu to incorporate the (2) x-ray and (1) RF units.
- Health Science Center, design team working with City of Frisco on Dance Studio landscape design and then to issue for construction.
- Health Science Center, design team collaborating with Collin on possible procurement of a mock MRI.

6.4 Pre-Construction

- Health Science Center, GMP 2 subcontractor contracts are nearing completion for executing and onboard the subcontractors.

6.5 Construction

- Plano Campus, roof work continues. On-going work in science labs, theater, commercial music, fine arts courtyard, various restrooms and the dining area. Welcome Center work to start the end of October. Welcome Center will be relocated to the Conference Center.
- Health Science Center, CM continuing to set tables and pour second level slab out along with beginning the placement of tables for the third level slab.
- Health Science Center, CM has begun removing shoring and strip pans on first level that supports the second level pours that are now complete. Reshoring on first level to follow in support of the remainder of upper level pours.
- Courtyard Center, Punchlist items on levels 3 and 4. Final Certificate of Occupancy is expected to be received by the City of Plano.
- CHEC, Phase 2 painting, overhead plumbing, door frames, and installation of hard ceilings are to be completed.

6.6 Acceptance and Close-Out

- No Acceptance and Close-out Items are pending at this time

7 Progress Pictures


7.1 Plano Campus Renovations



Commercial Music Control Room




Science Lab HVAC Install

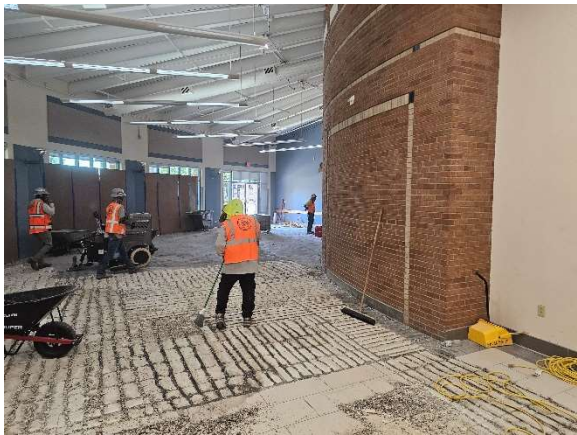

Dining Area Floor Demo



Dressing Room

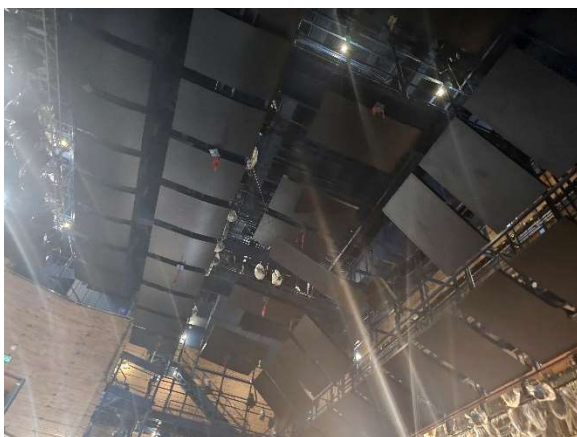

Theater Acoustical Panels



Theater Flooring Install

7.2 Health Science Center



View North



View Northwest



Overview of Site



View to Southwest

7.3 CHEC



1st Floor – New Foundation Offices



2nd Floor – Institutional Research Offices



3rd Floor – Business Offices



4th floor – Presidential Suite Offices
