

Observation Report

Type: ☐ Pre-Install ☒ Weekly ☐ Random ☐ Monthly ☐ Other ☐ Owner Request ☐ Warranty 11 or 23

Date: Sept 05/07, 2017 Time (arrived): 07:45 am (departed): 10:45 am (total hours): 3.0 Hrs.

Project: Collin College Public Safety Training Facility

Project No.: 15250

General Contractor: CORE

Substantial Completion Date: May 01, 2018

Weather Conditions: ☐ Sunny ☒ Cloudy ☐ Windy ☐ Rain ☐ Drizzle Temperature: 79°F


TRADES ON PROJECT	TRADES ON PROJECT
01 <input checked="" type="checkbox"/> Gen'l Supt. – Bahman Zamhariri	17 <input type="checkbox"/> Low Voltage –
02 <input type="checkbox"/> Site Work – WRIGHT	18 <input type="checkbox"/> Stand Pipe Sprinkler System –
03 <input checked="" type="checkbox"/> Forms/Building Slab – MILLER SIERRA	19 <input type="checkbox"/> Kitchen Equipment –
04 <input checked="" type="checkbox"/> Structural Steel – GLEN ARCH/BASDEN STEEL	20 <input checked="" type="checkbox"/> Hollow Metal Doors and Frame – Piper
05 <input checked="" type="checkbox"/> Masonry – DMG	21 <input type="checkbox"/> Canopy –
06 <input type="checkbox"/> Waterproofing –	22 <input type="checkbox"/> Other –
07 <input type="checkbox"/> Roofing –	23 <input type="checkbox"/> Other –
08 <input type="checkbox"/> Glazing –	24 <input type="checkbox"/> Canceled Activity –
09 <input checked="" type="checkbox"/> Drywall – JCR	25 <input type="checkbox"/> Concrete
10 <input type="checkbox"/> Plaster –	Type:
11 <input type="checkbox"/> Acoustical –	Yards:
12 <input type="checkbox"/> Carpentry –	Testing Lab: <input type="checkbox"/> Present <input type="checkbox"/> Not Present
13 <input type="checkbox"/> Painting –	Name of Testing Lab: GME
14 <input checked="" type="checkbox"/> Mechanical –	CONTACTS:
15 <input checked="" type="checkbox"/> Electrical Underground – GENTZLER	Project Engineer GEO – Mark Kawalek, GME
16 <input checked="" type="checkbox"/> Plumbing Underground – MECHANICAL PARTNERS	Project Engineer Structural – Mike Hubbard, AG&E
	Project Manager – Matt Letlow, CORE




Site panorama viewed from SE

Submitted By: **David Briggs, PBK**

Attachments: **Images**

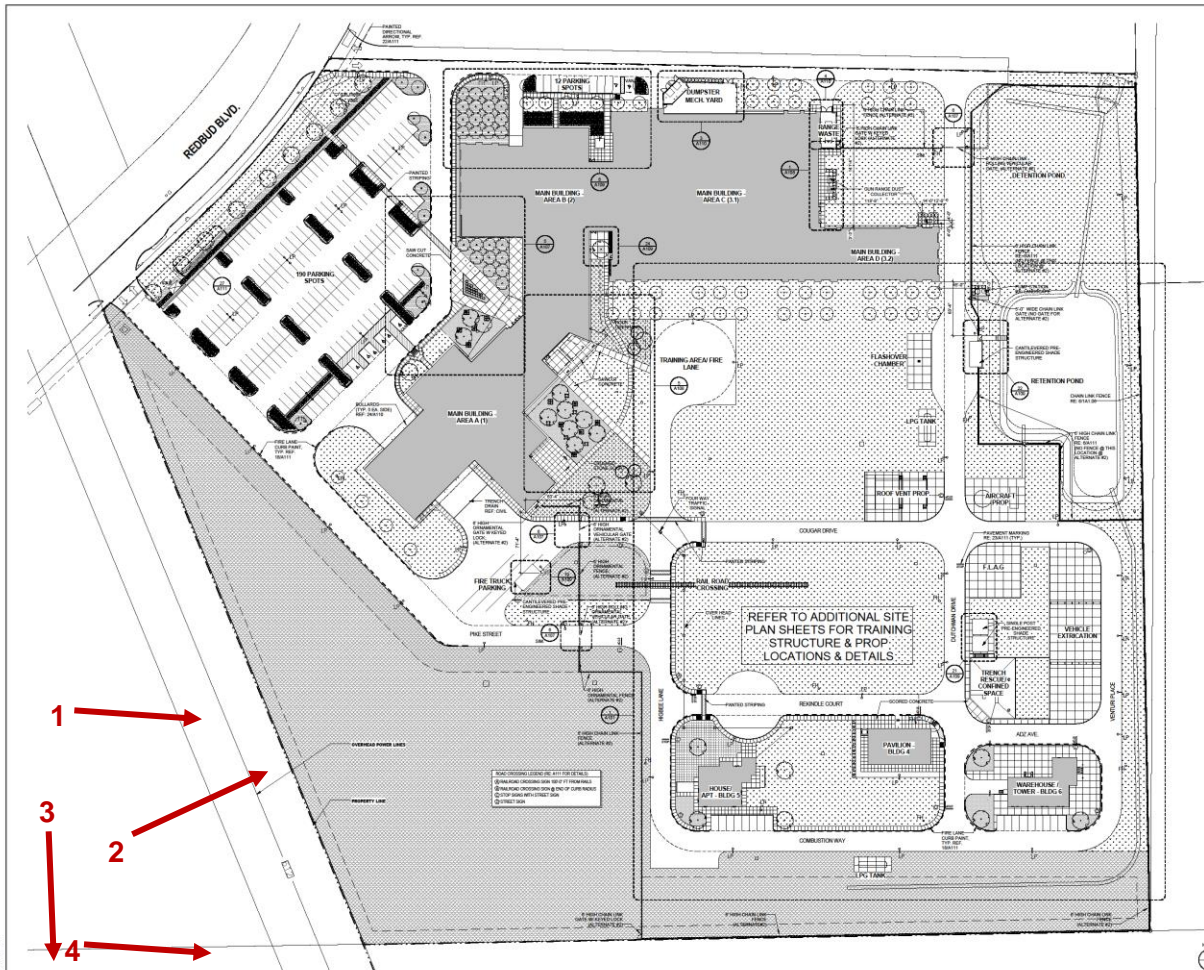

Key Plan

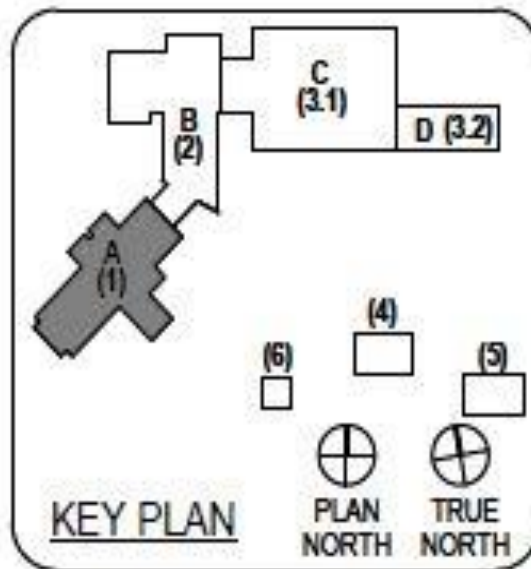



General Notes:



1. Rain days to date (36) Most recently claimed 08/17/2017.
2. All piers completed, total 462.
3. 56/78 wall panels poured to date. Scheduled to pour (16) this week and remaining (6) next week.
4. Remainder Bldg. "A" slab scheduled to be poured next week.
5. Trench rescue grade beams poured.
6. Apartment Bldg. grade beams poured.

Current Activity:




1. Bldg. "B" CMU in progress.
2. Bldg. "B" HVAC duct rough and roof drain plumbing in progress.
3. Bldg. "B" structural steel, joists, decking and moment welding in progress.
4. Bldg. "B" exterior wall studs in progress.
5. Framing and reveal panel layout Bldgs C & D in progress.
6. Tower Bldg. CMU in progress.


Date	Item #	Images	Description
09/05/2017	1		Bldg. A Slab completed last week.
09/05/2017	2		Bldg. A Remaining slab to pour next week.

09/05/2017	3		<p>Bldg. B</p> <p>CMU walls in progress.</p>
09/05/2017	4		<p>Bldg. B</p> <p>Structural steel in progress.</p>
09/05/2017	5		<p>Bldg. B</p> <p>Deck and HVAC rough in progress.</p>

09/05/2017	6			<p>Bldg. B</p> <p>Exterior wall studs in progress.</p>
09/05/2017	7			<p>Bldgs C & D</p> <p>Wall panels in progress/p rep'g to stand panels.</p>
09/05/2017	8			<p>Warehouse Bldg.</p> <p>Grade beams poured.</p>

09/05/2017	9		Apartment Bldg. Grade beams poured.
09/05/2017	10		Tower Bldg. CMU walls in progress.
09/05/2017	11		Trench Rescue Grade beam prep in progress.

09/07/2017	12		Bldg B Rough mechanical progress.
09/07/2017	13		Bldg B CMU progress.
09/07/2017	14		Bldg B Steel and exterior wall stud progress.

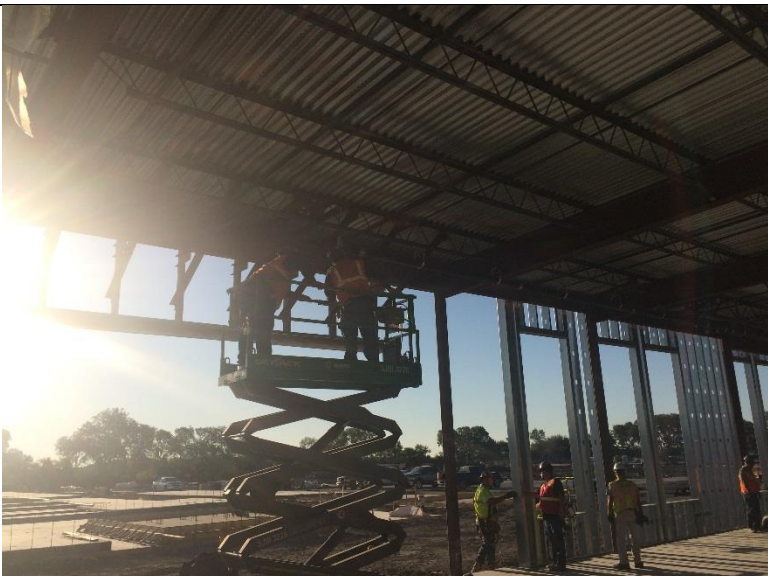09/07/2017	15		Bldg B Roof drains in progress.
------------	----	--	--

Copies To:

- Bill King, Collin College
- Jon Hardesty, Collin College
- Pat McAuliff, Collin College
- Todd Eubanks, Collin College
- P Grimes, City of McKinney
- D Kistner, City of McKinney
- G Conley, City of McKinney
- P Vargas, City of Allen
- B Hawley, City of Allen
- B Harvey, City of Allen
- Bahman Zamhariri, CORE
- Matt Letlow, CORE
- Mark Berg, PBK
- Mike Ghormley, PBK
- Grecia Jimenez, PBK
