

DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

Construction Report

November 2024

Prepared by:

Active Construction Timeline



Facility	Phase of Development	Move In Date	
Hill Elementary School	Under Construction	TBD	
Reeves Elementary School	Under Construction	Summer 2025	
Denton High School Multipurpose	Under Construction	Fall 2025	
Braswell High School Multipurpose & Additions	Under Construction	2025	
Guyer High School Multipurpose & Ag Facility	Under Construction	2025	
Ryan High Renovation & Multipurpose	Under Construction	2026	
High School #5	Awaiting Permit	2027	

Active Construction Timeline



Facility	Phase of Development	Move In Date
Crownover Middle School Track & Field	Under Construction	December 2024
Myers Middle School Track & Field	Under Construction	December 2024
Rodriguez Middle School Track & Field	Under Construction	December 2024
Harpool Middle School Track & Field	Awaiting Permit	2025
Navo Middle School Track & Field	Awaiting Permit	2025
Strickland Middle School Track & Field	Awaiting Permit	2025

Completed Projects



Facility	Phase of Development	
Evers Park Elementary School Renovation	Completed	
Alexander Elementary School Renovation	Completed	
Blanton Elementary School Renovation	Completed	
Nelson Elementary School Renovation	Completed	
Strickland Middle School Renovation	Completed	
Fred Moore Day Nursery School Roof Replacement	Completed	

Future Project Timeline



Facility	Phase of Development	Construction Commencing	Move In Date
W.S. Ryan Elementary School Renovation	Planning and Design	June 2025	August 2025
Hodge Elementary School Renovation	Planning and Design	June 2025	August 2025
C.H. Collins Facility Upgrades	Planning and Design	June 2025	August 2025
Crownover Middle School Facility Upgrades	Planning and Design	June 2025	August 2025
Harpool Middle School Facility Upgrades	Planning and Design	June 2025	August 2025
McMath Middle School Facility Upgrades	Planning and Design	June 2025	August 2025
Providence Elementary School Facility Upgrades	Planning and Design	June 2025	August 2025
Stephens Elementary School Facility Upgrades	Planning and Design	June 2025	August 2025
E.P. Rayzor Roofing	Planning and Design	June 2025	August 2025
Stephens Administration Roofing	Planning and Design	June 2025	August 2025



DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

Reeves Elementary School

November 2024



2023 Bond Authorization
Architects – Pfluger
Contractor – Balfour Beatty
Move In – Summer 2025







2023 Bond Authorization
Architects – Pfluger
Contractor – Balfour Beatty
Move In – Summer 2025

Tasks completed previous 90 days:

- Parking/Paving to be completed
- Foundations/slab to be completed
- Structural steel erection
- Storm shelter to be completed
- Roofing will begin
- Framing & Mechanical, Electrical,
 Plumbing rough in is ongoing

Upcoming Tasks:

- Steel detailing and decking
- Brick installation at Gym
- Slab on metal deck in multiple areas to be completed
- Punch Windows
- Exterior Framing and Sheathing ongoing
- Storefronts and curtain walls will begin



2023 Bond Authorization
Architects – Pfluger
Contractor – Balfour Beatty
Move In – Summer 2025





2023 Bond Authorization
Architects – Pfluger
Contractor – Balfour Beatty
Move In – Summer 2025



DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

Denton High School Multipurpose Facility

November 2024



2023 Bond Authorization
Architects – VLK Architects
Contractor – BWC
Move In – August 2025







2023 Bond Authorization
Architects – VLK Architects
Contractor – BWC
Move In – August 2025

Tasks completed previous 90 days:

- Concrete Sidewalks and Retaining Walls are complete
- Practice Field subgrade is complete
- Installing Electric, Data, and Fire Protection systems
- Insulated the Roof and Walls
- Installed all Utility Lines to the Building
- Completed Roof, Exterior
 Sheathing and Waterproofing

Upcoming tasks:

Exterior:

- Brick, Metal Panels and Windows
- Storefronts, Doors, Roll-Up Doors and Railing
- Practice Field installation complete

Interior:

- Impact Resistance Walls and Pads
- Paint Walls
- Install Viewing Platform
- Lighting and Trim out



2023 Bond Authorization
Architects – VLK Architects
Contractor – BWC
Move In – August 2025





2023 Bond Authorization
Architects – VLK Architects
Contractor – BWC
Move In – August 2025



DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

Braswell High School Multipurpose Facility

November 2024



2023 Bond Authorization
Architects – VLK
Contractor – Balfour Beatty
Move In – 2025





2023 Bond Authorization
Architects – VLK
Contractor – Balfour Beatty
Move In – 2025

Tasks completed previous 90 days:


- Baseball and Softball field turf construction
- Batting cages slab completed
- Batting cages CMU and steel
- Piers on indoor facility
- Footings and grade beams for indoor facility started
- All steel for building is onsite.

Upcoming tasks:

- Prep of fire lanes ongoing
- Grade beams and piers ongoing
- Slab on grade to begin
- Erecting steel for indoor facility will begin
- Batting cages for Baseball/Softball to be completed




2023 Bond Authorization
Architects – VLK
Contractor – Balfour Beatty
Move In – 2025

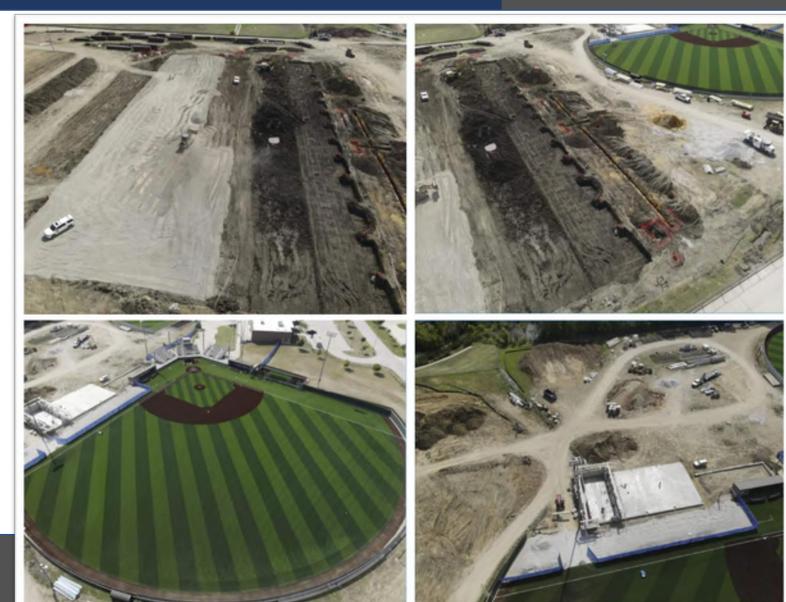



2023 Bond Authorization
Architects – VLK
Contractor – Balfour Beatty
Move In – 2025

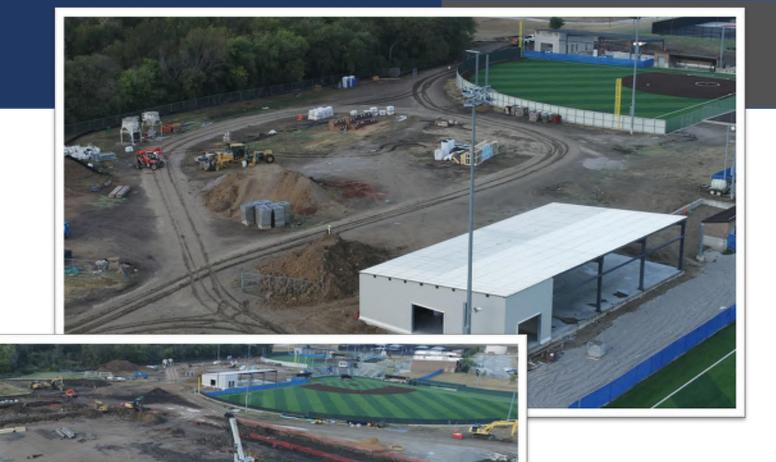

DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

Borman Elementary School

November 2024

Prepared by:























