



Collin College

2017 Capital Improvement Program
Monthly Report
April 2021

Collin County Community College District

Project Reference: 60541060
Project Number: 60541060

May 07, 2021


Quality information

Prepared by




Nuria Cortes
Program Controls Manager

Reviewed by



Nick Fiehler
Deputy Program Director

Reviewed By



Jeff Hagerich
Deputy Program Director

Approved By



Adrian Grimes
Program Director

Revision History

Revision	Revision date	Details	Authorized	Name	Position
First Publication	May 07, 2021	April '21 Report	Yes	Adrian Grimes	Program Director

Distribution List

# Hard Copies	PDF Required	Association / Company Name

Prepared for:

Collin County Community College District
3452 Spur 399
Suite 327
McKinney, TX 75069

Prepared by:

Nuria Cortes
Program Controls Manager
E: ncortes.aecom@collin.edu

AECOM
13355 Noel Road
4th Floor
Dallas TX, 75240
aecom.com

Copyright © 2020 by AECOM

All rights reserved. No part of this copyrighted work may be reproduced, distributed, or transmitted in any form or by any means without the prior written permission of AECOM.

Table of Contents

1.	Introduction	5
2.	Executive Summary	5
3.	Scope	7
3.1	Phase 1	7
3.2	Phase 2	7
3.3	Phase 3	8
4.	Community	8
4.1	Project Teams	8
4.1.1	Phase 1	8
4.1.2	Phase 2	9
4.1.3	Phase 3	10
4.2	Current Personnel Estimate	11
4.3	Community Outreach	11
5.	Schedule	12
5.1	Program	12
5.2	Phase 1	12
5.3	Phase 2	13
5.4	Phase 3	15
6.	Budget	16
6.1	Program Summary	16
6.2	Phase 1	16
6.3	Phase 2	17
6.4	Phase 3	18
6.5	Phase A	19
6.6	Additional Program Budgets	20
7.	Completed Items	20
7.1	General Program	20
7.2	Procurement	20
7.3	Design	20
7.4	Pre-Construction	20
7.5	Construction	20
7.6	Acceptance and Close-Out	21
8.	Pending Items	21
8.1	General Program	21
8.2	Procurement	21
8.3	Design	21
8.4	Pre-Construction	21
8.5	Construction	21
8.6	Acceptance and Close-Out	21
	Appendix A – Construction Progress Photos	22

1. Introduction

On May 6, 2017, voters approved Collin College's \$600 million bond proposal to facilitate a long-range plan to accommodate the projected population growth in Collin County over the next two decades. The program consists of 4 new campuses and 2 new facilities.

On May 16, 2017, in a special session, the Board of Trustees granted the District President authority to enter and negotiate into contract with AECOM Technical Services, Inc. (AECOM) to provide Program Management Services to the Collin College 2017 Capital Improvement Program. On May 25, 2017, Collin College issued a Notice to Proceed to AECOM. As part of these services, AECOM will deliver a monthly report to provide status and progress of key aspects of the Program.

2. Executive Summary

The Program is progressing as planned with no major issues to report at this time.

Completed and Pending Items

- **Technical Campus – Final items requested by the City of Allen officials were completed and approved by the City Fire. We are now awaiting receipt of full CO from the City.**
- **Wylie Campus – The replacement kitchen exhaust fans have been installed. Installation of scuppers at the Conference Center scheduled to be completed by mid-May.**
- **Celina Campus – Concrete work at the breezeway is complete, with irrigation and landscaping work about to begin. Interior finishes work is in final stages throughout the building. Lab casework and millwork is complete throughout the building. Architect/Owner punchlist walks are on-going. The city's Choate Parkway road project on the north side of the campus is complete.**
- **Farmersville Campus – Punch list items are on-going. Two additional flag poles are to be installed, waiting for those to be delivered. Construction of the City's Collin Parkway road project is ongoing.**
- **IT Center – Overhead MEP is near completion in Area A & B. Programming of the door hardware and lighting controls is in progress. Finishing of the bridges, monumental stairs, and terrazzo flooring is on-going. Restroom finishes and fixtures are on-going. Priming, painting, and floor installation is on-going. At the Quad area, light fixtures and pavers are being installed, irrigation and planting is on-going, and the water feature is nearing completion. Architect/Owner punchlist walks are on-going.**
- **Frisco Campus (Addition and Renovations) – The project team is completing the detailed schedule for the renovation and addition scopes of work at the campus. All plans were submitted for building permit on the week of April 26th. The GMP for the Addition and Renovations was approved by the Board of Trustees on April 29th. Fire lane construction work is underway. The north-south run of the fire lane has been poured; the east-west run will be completed after the relocation of the 4-pipe system.**
- **McKinney Campus (Welcome Center and Renovations) – Site Upgrades: Installation of underground storm and water lines is on-going. Lime stabilization is on-going. Welcome Center: Chemical injection of building pad is complete and passed inspection. Building permit has been issued. Renovations: Demo work has begun in the kitchen.**

Items of close attention

- **Completion of the new outer loop access road in Celina by Collin County/NTTA**
- **Monitoring the progress of the new road the City of Farmersville is installing along the west entrance of the Farmersville Campus**
- **Monitoring the progress of the Celina Campus and the IT Center to ensure they are completed in time for Fall 2021 classes.**

Budget Summary

- \$553,956,841 of the \$600,000,000 has been committed to-date in the form of contracts with various vendors. This represents 92.33% of the overall program budget committed.
- \$500,184,260 of the \$553,956,841 committed amount has been expended to-date. This represents 90.29% of the commitments to date and 83.36% of the program budget.

3. Scope

3.1 Phase 1

- Wylie Campus
 - Construction of a campus on a new approximately 97-acre site
 - The campus includes:
 - Campus Commons
 - Library
 - Student Center/Conference Center
 - Central Utility Plant
- Technical Campus
 - Construction of a Technical Campus on a new 32-acre site in Allen, Texas
 - The campus includes:
 - 450 space underground parking garage
 - Academic Building (includes space for dual credit students)
 - 3 Trade Bar Buildings to support CTE programs

3.2 Phase 2

- Celina Campus
 - Construction of a campus on a new approximately 75-acre site
 - The campus includes:
 - Student Union / Workforce / Instructional Building
- Farmersville Campus
 - Construction of a campus on a new approximately 76-acre site
 - The campus includes:
 - Student Union / Workforce / Instructional Building
- Frisco Campus
 - Construction of a new IT Center building on the existing campus

3.3 Phase 3

- Additions and Renovations at Frisco Campus
 - Alumni Hall Renovations and Additions
 - Lawler Hall Renovations
 - Heritage Hall Upgrades
 - Founders Hall Renovations
 - Wayfinding
- Additional Frisco Campus Projects
 - Construction of a new fire lane, parking lot, and loop road on the existing campus
 - Trane Upgrades
- Additions and Renovations at McKinney Campus
 - Construction of a new Welcome Center on the existing campus
 - New Entry Drive and Parking
 - Pistol Range Demo
 - Kitchen and Dining Renovations in Main Building
 - Dental Hygiene Renovations
 - Wayfinding
- Additional McKinney Campus Projects
 - Trane Upgrades
- Additional Plano Campus Projects
 - Trane Upgrades
 - Wayfinding
- Additional Courtyard Center Projects
 - Trane Upgrades
- Additional CHEC Projects
 - Trane Upgrades

4. Community

4.1 Project Teams

4.1.1 Phase 1

- Wylie Campus
 - Program Manager: AECOM Technical Services, Inc.
 - A/E: Page Southerland Page, Inc.
 - MEP: Reed, Wells, Benson & Co.
 - Civil Engineer: Pacheco Koch Consulting Engineers, Inc.

- Cost Consulting: Vermeulens
- Construction Manager-at-Risk: Skanska USA Building, Inc.
- Commissioning Agent: Bath Group, Inc.
- Technical Campus
 - Program Manager: AECOM Technical Services, Inc.
 - A/E: Perkins+Will, Inc.
 - Associate Architect: Hoefer Wysocki Architecture
 - MEP: Purdy McGuire
 - Civil Engineer: Pacheco Koch Consulting Engineers, Inc.
 - Structural Engineer: L.A. Fuess Partners, Inc.
 - Cost Consulting: Vermeulens
 - Construction Manager-at-Risk: McCarthy Building Companies, Inc.
 - Commissioning Agent: Farnsworth


4.1.2 Phase 2

- Celina Campus
 - Program Manager: AECOM
 - A/E: Beck Architecture, LLC
 - Structural Engineer: L.A. Fuess Partners, Inc.
 - MEP: Reed, Wells, Benson & Co.
 - Civil Engineer: RLK Engineering
 - Construction Manager-at-Risk: JT Vaughn Construction
- Farmersville Campus
 - Program Manager: AECOM
 - A/E: Beck Architecture, LLC
 - Structural Engineer: L.A. Fuess Partners, Inc.
 - MEP: Reed, Wells, Benson & Co.
 - Civil Engineer: RLK Engineering
 - Construction Manager-at-Risk: JT Vaughn Construction
- IT Center
 - Program Manager: AECOM
 - A/E: Beck Architecture, LLC
 - Structural Engineer: L.A. Fuess Partners, Inc.
 - MEP: ME Engineers
 - Civil Engineer: RLK Engineering
 - Construction Manager-at-Risk: JE Dunn Construction

4.1.3 Phase 3

- Welcome Center at the McKinney Campus
 - Program Manager: AECOM Technical Service, Inc.
 - A/E: PBK
 - Construction Manager-at-Risk: Skanska USA Building, Inc.
 - Commissioning Agent: Bath Group, Inc.
- Loop Road/Parking at Frisco Campus
 - Program Manager: AECOM Technical Service, Inc.
 - Civil Engineer: RLK Engineering
 - Construction Manager-at-Risk: JE Dunn Construction
- Fire Lane at Frisco Campus
 - Program Manager: AECOM Technical Service, Inc.
 - Civil Engineer: RLK Engineering
 - Construction Manager-at-Risk: Skanska USA Building, Inc.
- Additional Projects at Frisco Campus
 - Program Manager: AECOM Technical Service, Inc.
 - A/E: Page Southerland Page, Inc.
 - Construction Manager-at-Risk: Skanska USA Building, Inc.
- Additional Projects at McKinney Campus
 - Program Manager: AECOM Technical Service, Inc.
 - A/E: PBK
 - Construction Manager-at-Risk: Skanska USA Building, Inc.
- Trane Upgrades at 5 Existing Campuses
 - Program Manager: AECOM Technical Service, Inc
 - Design – Builder: Trane Companies, Inc.
- Additional Projects at Plano Campus (Wayfinding)
 - Program Manager: AECOM Technical Service, Inc
 - A/E: IN2 Architects
 - Construction Manager-at-Risk: TBD

4.2 Current Personnel Estimate

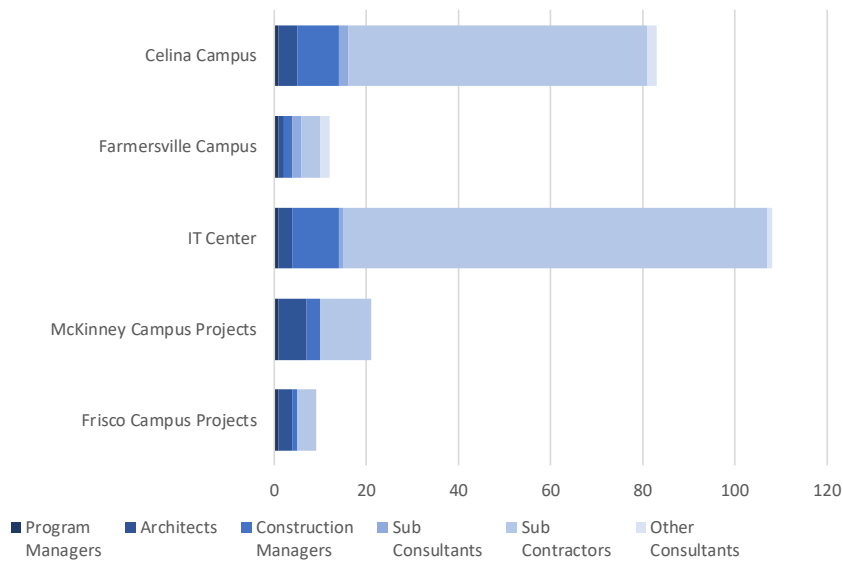


It is estimated that the Program Managers, Architects, Construction Managers, Sub-Consultants, and Sub-Contractors, under contract with Collin College for the 2017 Capital Improvement Program, have 233 employees contributing to the program's progress.

4.3 Community Outreach

- Collin College 2017 Capital Improvement Program Website
 - <https://CollinCollege2017CIP.com>
 - Includes the following features:
 - Program Overview
 - Project Scopes
 - Project Schedules
 - Project Budgets
 - Progress Photos/Renderings
 - Live On-Site Camera Feeds

5. Schedule

5.1 Program

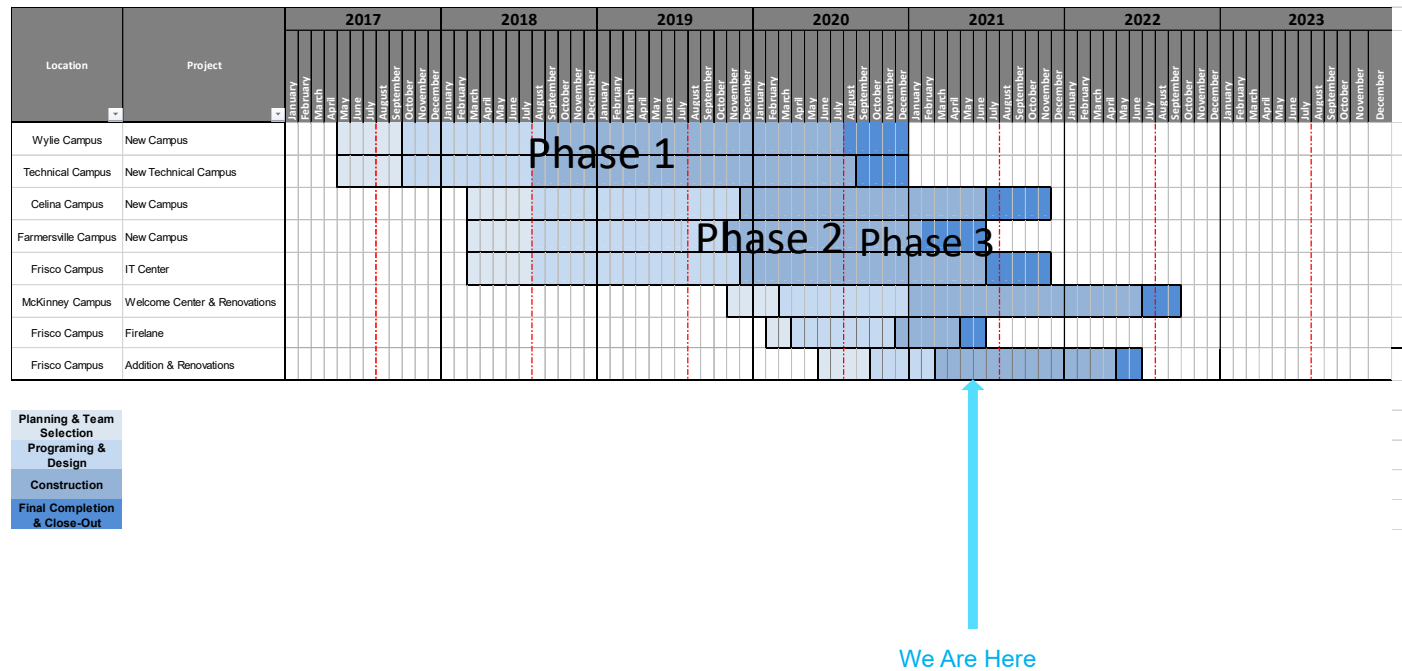

5.2 Phase 1

Wylie Campus

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	May 16, 2017	May 16, 2017	👍	May 16, 2017	👍
BOT Approval of A/E Procurement Method	May 23, 2017	May 23, 2017	👍	May 23, 2017	👍
BOT Approval of Construction Delivery Method	May 23, 2017	May 23, 2017	👍	May 23, 2017	👍
BOT Approval of Recommended Firms	August 22, 2017	August 22, 2017	👍	August 22, 2017	👍
Architect Mobilized	September 12, 2017	September 29, 2017	👎	September 28, 2017	👍
GMP Construction Documents Submittal	June 26, 2018	June 26, 2018	👍	June 26, 2018	👍
BOT Approval of GMP	August 28, 2018	August 28, 2018	👍	August 28, 2018	👍
Contractor Mobilized	September 10, 2018	September 12, 2018	👎	September 12, 2018	👍
Foundations Complete	May 18, 2019	April 30, 2019	👍	April 23, 2019	👍
Structures Complete	June 28, 2019	June 28, 2019	👍	May 23, 2019	👍
Dry-In of Buildings Complete	October 26, 2019	October 26, 2019	👍	October 29, 2019	👍
Permanent Power Complete	September 17, 2019	September 17, 2019	👍	September 21, 2019	👍
Interior Finish-Out Complete	May 1, 2020	June 10, 2020	👎	July 1, 2020	👍
Substantial Completion	June 25, 2020	June 25, 2020	👍	June 30, 2020	👍
Final Completion	August 23, 2020	May 2021	👎	-	
Student Occupancy	August 2020	August 2020	👍	August 1, 2020	👍

Technical Campus

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	May 16, 2017	May 16, 2017	↑	May 16, 2017	✓
BOT Approval of A/E Procurement Method	May 23, 2017	May 23, 2017	↑	May 23, 2017	✓
BOT Approval of Construction Delivery Method	May 23, 2017	May 23, 2017	↑	May 23, 2017	✓
BOT Approval of Recommended Firms	August 22, 2017	August 22, 2017	↑	August 22, 2017	✓
Architect Mobilized	September 12, 2017	September 29, 2017	↓	September 28, 2017	✓
GMP Construction Documents Submittal	April 16, 2018	April 16, 2018	↑	April 19, 2018	✓
BOT Approval of GMP	June 26, 2018	June 26, 2018	↑	June 26, 2018	✓
Contractor Mobilized	July 6, 2018	July 20, 2018	👉	July 26, 2018	✓
Foundations Complete	September 23, 2019	September 23, 2019	↑	July 29, 2019	✓
Structures Complete	November 18, 2019	November 18, 2019	↑	November 13, 2019	✓
Roofing of Buildings Complete	December 20, 2019	December 20, 2019	↑	December 20, 2019	✓
Permanent Power Complete	December 15, 2019	January 10, 2020	↓	January 15, 2020	✓
Building A Punchlist Generated	June 5, 2020	June 12, 2020	👉	June 12, 2020	✓
Building B Punchlist Generated	June 12, 2020	June 19, 2020	👉	June 19, 2020	✓
Building C Punchlist Generated	June 30, 2020	July 6, 2020	👉	July 9, 2020	✓
Building D Punchlist Generated	July 6, 2020	July 20, 2020	👉	July 15, 2020	✓
Substantial Completion	July 6, 2020	August 10, 2020	↓	August 10, 2020	✓
Final Completion	September 4, 2020	May 10, 2021	↓	-	
Student Occupancy	August 2020	August 2020	↑	August 8, 2020	✓

5.3 Phase 2

Celina Campus

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	September 25, 2018	February 14, 2018	↑	February 14, 2018	✓
BOT Approval of A/E Procurement Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Construction Delivery Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Recommended A/E Firm	June 26, 2018	June 26, 2018	↑	June 26, 2018	✓
BOT Approval of Recommended CM Firm	August 2018	August 2018	↑	August 28, 2018	✓
Architect Mobilized	July 24, 2018	July 24, 2018	↑	July 31, 2018	✓
Schematic Design Submittal	January 8, 2019	January 15, 2019	👉	January 16, 2019	✓
Design Development Submittal	April 30, 2019	April 30, 2019	↑	April 26, 2019	✓
Construction Document Submittal	September 20, 2019	September 20, 2019	↑	September 3, 2019	✓
Contractor Mobilized	December 2019	December 2019	↑	November 25, 2019	✓
Foundations Complete	April 9, 2020	April 14, 2020	👉	April 21, 2020	✓
Structures Complete	July 7, 2020	July 7, 2020	↑	June 9, 2020	✓
Roofing of Buildings Complete	December 2, 2020	December 2, 2020	↑	November 13, 2020	✓
Permanent Power Complete	October 7, 2020	October 7, 2020	↑	May 28, 2020	✓
Interior Finish-Out Complete	May 18, 2021	May 18, 2021	↑	-	
Substantial Completion	July 15, 2021	June 30, 2021	↑	-	
Final Completion	August 12, 2021	August 30, 2021	↓	-	
Student Occupancy	August 2021	August 2021	↑	-	

Farmersville Campus

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	September 25, 2018	February 14, 2018	↑	February 14, 2018	✓
BOT Approval of A/E Procurement Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Construction Delivery Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Recommended A/E Firm	June 26, 2018	June 26, 2018	↑	June 26, 2018	✓
BOT Approval of Recommended CM Firm	August 2018	August 2018	↑	August 28, 2018	✓
Architect Mobilized	July 24, 2018	July 24, 2018	↑	July 31, 2018	✓
Schematic Design Submittal	December 20, 2018	December 18, 2018	↑	December 18, 2018	✓
Design Development Submittal	April 2, 2019	April 19, 2019	↓	April 26, 2019	✓
Construction Document Submittal	July 25, 2019	August 9, 2019	↓	August 9, 2019	✓
Contractor Mobilized	November 2019	November 2019	↑	October 21, 2019	✓
Foundations Complete	March 5, 2020	March 13, 2020	👉	April 2, 2020	✓
Structures Complete	April 13, 2020	April 13, 2020	↑	April 30, 2020	✓
Roofing of Buildings Complete	June 29, 2020	June 29, 2020	↑	June 30, 2020	✓
Permanent Power Complete	June 30, 2020	July 7, 2020	👉	May 4, 2020	✓
Interior Finish-Out Complete	November 30, 2020	November 30, 2020	↑	December 11, 2020	✓
Substantial Completion	January 5, 2021	January 5, 2021	↑	December 21, 2020	✓
Final Completion	February 2, 2021	July 2021	↓	-	
Student Occupancy	August 2021	March 2021	↑	March 12, 2021	✓

IT Center

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	September 25, 2018	February 14, 2018	↑	February 14, 2018	✓
BOT Approval of A/E Procurement Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Construction Delivery Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Recommended A/E Firm	June 26, 2018	June 26, 2018	↑	June 26, 2018	✓
BOT Approval of Recommended CM Firm	August 2018	August 2018	↑	August 28, 2018	✓
Architect Mobilized	July 24, 2018	July 24, 2018	↑	July 31, 2018	✓
Schematic Design Submittal	May 24, 2019	May 24, 2019	↑	May 24, 2019	✓
Design Development Submittal	August 23, 2019	August 23, 2019	↑	August 23, 2019	✓
Construction Document Submittal	December 9, 2019	December 9, 2019	↑	December 9, 2019	✓
Contractor Mobilized	December 2019	January 6, 2020	↓	January 20, 2020	✓
Construction Start for Loop Road/Parking	June 1, 2020	July 13, 2020	↓	July 27, 2020	✓
Foundations Complete	June 22, 2020	June 22, 2020	↑	May 2, 2020	✓
Structures Complete	August 14, 2020	August 14, 2020	↑	July 14, 2020	✓
Phase 1 Construction Complete for Loop Road/Parking	August 15, 2020	August 15, 2020	↑	August 22, 2020	✓
Phase 2 Construction Complete for Loop Road/Parking	October 31, 2020	March 15, 2021	↓	March 15, 2021	✓
Roofing of Buildings Complete	November 3, 2020	November 23, 2020	↓	October 23, 2020	✓
Permanent Power Complete	January 4, 2021	January 4, 2021	↑	January 29, 2021	✓
Interior Finish-Out Complete	May 13, 2021	May 13, 2021	↑	-	
Substantial Completion	June 30, 2021	July 7, 2021	👉	-	
Final Completion	August 26, 2021	August 26, 2021	↑	-	
Student Occupancy	August 2021	August 2021	↑	-	

* Phase 3 (Loop Road and Parking Lot) at Frisco Campus is included in this schedule

5.4 Phase 3

McKinney Campus (Welcome Center and Renovations)

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	August 27, 2019	August 27, 2019	↑	August 27, 2019	✓
BOT Approval of A/E Procurement Method	October 22, 2019	October 22, 2019	↑	October 22, 2019	✓
BOT Approval of Construction Delivery Method	February 2020	February 2020	↑	October 22, 2019	✓
BOT Approval of Recommended A/E Firm	March 24, 2020	March 24, 2020	↑	April 28, 2020	✓
BOT Approval of Recommended CM Firm	March 24, 2020	March 24, 2020	↑	April 28, 2020	✓
Architect NTP	April 14, 2020	April 14, 2020	↑	April 8, 2020	✓
Schematic Design Submittal	August 1, 2020	August 1, 2020	↑	August 1, 2020	✓
Site Construction Document Submittal	October 2, 2020	October 2, 2020	↑	October 2, 2020	✓
Welcome Center Construction Document Submittal	November 20, 2020	November 20, 2020	↑	October 30, 2020	✓
GMP #1 * Board Approval	December 8, 2020	December 8, 2020	↑	December 8, 2021	✓
GMP #2 ** Board Approval	January 26, 2021	February 23, 2021	↓	January 26, 2021	✓
GMP #1 * Construction Start	January 18, 2021	January 18, 2021	↑	January 28, 2021	✓
GMP #2 ** Construction Start	March 1, 2021	March 1, 2021	↑	March 15, 2021	✓
Substantial Completion	May 2022	May 2022	↑	-	
Student Occupancy	July 2022	July 2022	↑	-	

* GMP #1 Site, Civil, and Demolition for Renovation Work

** GMP #2 Construction of New Welcome Center and Renovation

Frisco Campus (Addition and Renovations)

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	August 27, 2019	August 27, 2019	↑	August 27, 2019	✓
BOT Approval of Recommended AE Firm	June 23, 2020	June 23, 2020	↑	June 23, 2020	✓
BOT Approval of Recommended CM Firm	August 25, 2020	August 25, 2020	↑	August 25, 2020	✓
GMP #1 * Board Approval	October 27, 2020	October 27, 2020	↑	October 27, 2020	✓
GMP #1 * Construction Start	December 15, 2020	December 15, 2020	↑	December 2, 2020	✓
GMP #2 ** Board Approval	March 2021	April 2021	↓	April 25, 2021	✓
GMP #2 ** Construction Start	April 2021	May 2021	↓	-	
Substantial Completion	March 25, 2022	April 2022	👉	-	

* GMP #1 Fire Lane

** GMP #2 Alumni Hall Remaining Work, Renovations and Foundation Work

6. Budget

6.1 Program Summary

Program Wide Budget Summary

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$47,226,570	\$43,162,257	\$43,034,783	\$40,046,132	100%	93%
Investigation, Testing & Verification	\$8,185,410	\$7,004,680	\$5,565,510	\$4,277,208	79%	77%
Construction, Equipment & Furnishings	\$486,561,069	\$511,591,028	\$504,954,009	\$455,465,517	99%	90%
Misc.	\$394,411	\$391,933	\$136,039	\$135,203	35%	99%
Contingency	\$61,621,273	\$12,465,022	\$0	\$0	0%	0%
Total Program Budget	\$600,000,000	\$600,000,000	\$553,956,841	\$500,184,260		
% of Total Program Budget Committed	92.33%					
% of Total Commitments Expended	90.29%					
% of Total Program Budget Expended	83.36%					

6.2 Phase 1

Wylie Campus

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$15,051,440	\$13,460,383	\$13,442,958	\$13,434,860	100%	100%
Investigation, Testing & Verification	\$2,679,247	\$2,084,678	\$1,777,394	\$1,580,489	85%	89%
Construction, Equipment & Furnishings	\$133,174,284	\$150,289,548	\$150,279,054	\$148,988,539	100%	99%
Misc.	\$126,082	\$176,483	\$61,361	\$61,361	35%	100%
Contingency	\$6,571,649	\$19,153	\$0	\$0	0%	0%
Total Project Budget	\$157,602,702	\$166,030,244	\$165,560,767	\$164,065,249		
% of Total Project Budget Committed	99.72%					
% of Total Commitments Expended	99.10%					
% of Total Project Budget Expended	98.82%					

Technical Campus

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$14,713,206	\$13,833,223	\$13,830,223	\$13,693,418	100%	99%
Investigation, Testing & Verification	\$2,619,039	\$1,694,355	\$1,544,626	\$1,261,690	91%	82%
* Construction, Equipment & Furnishings	\$130,181,602	\$161,588,160	\$161,525,434	\$160,081,001	100%	99%
Misc.	\$123,249	\$38,857	\$38,163	\$38,163	98%	100%
Contingency	\$6,423,972	\$22,757	\$0	\$0	0%	0%
Total Project Budget	\$154,061,068	\$177,177,352	\$176,938,446	\$175,074,272		
Allen ISD Reimbursement	-	(\$12,000,000)	(\$12,000,000)	-		
Allen EDC Grant	-	(\$400,000)	(\$400,000)	-		
% of Total Project Budget Committed	99.87%					
% of Total Commitments Expended	98.95%					
% of Total Project Budget Expended	98.81%					

* Actual Budget from bond funds is \$149,188,160 (\$161,588,160 less \$12,000,000 Allen ISD Reimbursement and \$400,000 Allen EDC Grant)

6.3 Phase 2

Celina Campus

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$5,078,807	\$4,008,264	\$3,976,655	\$3,504,931	99%	88%
Investigation, Testing & Verification	\$936,908	\$936,908	\$585,520	\$442,153	62%	76%
Construction, Equipment & Furnishings	\$46,569,862	\$49,118,500	\$46,876,373	\$38,569,088	95%	82%
Misc.	\$44,090	\$64,108	\$21,976	\$21,140	34%	96%
Contingency	\$2,482,596	\$984,482	\$0	\$0	0%	0%
Total Project Budget	\$55,112,263	\$55,112,263	\$51,460,524	\$42,537,312		
% of Total Project Budget Committed	93.37%					
% of Total Commitments Expended	82.66%					
% of Total Project Budget Expended	77.18%					

Farmersville Campus

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$2,539,404	\$2,185,319	\$2,171,319	\$1,991,348	99%	92%
Investigation, Testing & Verification	\$468,453	\$540,867	\$444,545	\$327,775	82%	74%
Construction, Equipment & Furnishings	\$23,284,932	\$25,523,763	\$25,335,325	\$20,521,599	99%	81%
Misc.	\$22,045	\$26,912	\$6,107	\$6,107	23%	100%
Contingency	\$1,241,298	\$229,272	\$0	\$0	0%	0%
Total Project Budget	\$27,556,132	\$28,506,132	\$27,957,295	\$22,846,828		
% of Total Project Budget Committed	98.07%					
% of Total Commitments Expended	81.72%					
% of Total Project Budget Expended	80.15%					

IT Center

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$5,472,853	\$4,884,249	\$4,850,347	\$4,080,417	99%	84%
Investigation, Testing & Verification	\$1,009,600	\$1,193,900	\$867,038	\$628,712	73%	73%
Construction, Equipment & Furnishings	\$50,183,042	\$46,223,400	\$44,974,015	\$32,201,063	97%	72%
Misc.	\$47,510	\$53,157	\$5,647	\$5,647	11%	100%
Contingency	\$2,675,210	\$4,814,688	\$0	\$0	0%	0%
Total Project Budget	\$59,388,215	\$57,169,393	\$50,697,047	\$36,915,839		
% of Total Project Budget Committed	88.68%					
% of Total Commitments Expended	72.82%					
% of Total Project Budget Expended	64.57%					

* Project Budget contains funds for Phase 3 (Loop Road and Parking Lot) at Frisco Campus

6.4 Phase 3**McKinney Campus (Welcome Center and Renovations)**

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$4,370,860	\$4,420,820	\$4,393,281	\$2,989,659	99%	68%
Investigation, Testing & Verification	\$472,163	\$553,973	\$346,388	\$36,389	63%	11%
Construction, Equipment & Furnishings	\$30,179,816	\$38,342,104	\$35,458,255	\$2,430,853	92%	7%
Misc.	\$31,435	\$32,416	\$2,785	\$2,785	9%	100%
Contingency	\$2,833,454	\$3,180,282	\$0	\$0	0%	0%
Total Project Budget	\$37,887,728	\$46,529,595	\$40,200,708	\$5,459,686		
% of Total Project Budget Committed	86.40%					
% of Total Commitments Expended	13.58%					
% of Total Project Budget Expended	11.73%					

Frisco Campus (Addition and Renovations)

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$2,883,468	\$1,942,048	\$1,826,404	\$1,132,186	94%	62%
Investigation, Testing & Verification	\$347,015	\$347,015	\$79,219	\$26,233	23%	33%
Construction, Equipment & Furnishings	\$16,724,000	\$16,724,000	\$1,474,924	\$549,489	9%	37%
Misc.	\$70,820	\$77,569	\$8,553	\$8,553	11%	100%
Contingency	\$1,094,995	\$3,850,406	\$0	\$0	0%	0%
Total Project Budget	\$21,120,298	\$22,941,038	\$3,389,099	\$1,716,461		
% of Total Project Budget Committed	14.77%					
% of Total Commitments Expended	50.65%					
% of Total Project Budget Expended	7.48%					

Plano Campus (Additional Projects)

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Total Project Budget	\$0	\$2,177,541	\$13,625	\$6,125		
% of Total Project Budget Committed	0.63%					
% of Total Commitments Expended	44.95%					
% of Total Project Budget Expended	0.28%					

6.5 Phase A**Public Safety Training Center**

Budget Group	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Construction Costs	\$31,068,022	\$31,068,022	\$31,068,022	100%	100%
Total Project Budget	\$31,068,022	\$31,068,022	\$31,068,022		

Trane Energy PACT

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Frisco Campus	\$9,725,336	\$9,725,336	\$9,725,336	\$9,493,156	100%	98%
Plano Campus	\$6,797,834	\$6,797,834	\$6,797,834	\$6,797,834	100%	100%
McKinney Campus	\$4,044,983	\$4,044,983	\$4,044,983	\$4,044,983	100%	100%
Courtyard Center	\$548,720	\$548,720	\$548,720	\$548,720	100%	100%
Collin Higher Education Center	\$720,659	\$720,659	\$720,659	\$720,659	100%	100%
Total Program Budget	\$21,837,531	\$21,837,531	\$21,837,531	\$21,605,351		
% of Total Project Budget Committed	100.00%					
% of Total Commitments Expended	98.94%					
% of Total Project Budget Expended	98.94%					

6.6 Additional Program Budgets

Program Level

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Building Fund Reimbursement	\$51,150,000	\$0	\$0	\$0	0%	0%
Program Wide Traffic Study	\$0	\$370,000	\$370,000	\$351,500	100%	95%
Program Contingency	\$39,393,094	\$3,214,389	\$0	\$0	0%	0%
Trane PACT Program Management		\$99,500	\$99,500	\$99,500	100%	100%
Bond Fees		\$9,500	\$9,500	\$9,500	100%	100%
District Wide Air Cleaning		\$140,000	\$140,000	\$133,700	100%	96%
District Wide Commissioning		\$17,500	\$17,500	\$17,500	100%	100%
Total Project Budget	\$90,543,094	\$3,850,889	\$636,500	\$611,700		

7. Completed Items

7.1 General Program

- [AECOM issued the Monthly Program Report for March '21 to Collin College on April 8th](#)
- [AECOM conducted coordination meetings with the Executive Committee on April 5th and 12th](#)

7.2 Procurement

- [Frisco Campus GMP #2 was approved by the Campus Facilities and Construction Committee and Board of Trustees on April 27th](#)

7.3 Design

- [AECOM, Page Southerland Page, Inc., and Skanska USA Building, Inc. conducted a Design Review meeting on April 7th for the Frisco Campus](#)

7.4 Pre-Construction

- [No Pre-Construction Items have been completed at this time](#)

7.5 Construction

- [Collin College, AECOM, Beck Architecture, LLC, and JT Vaughn Construction conducted Weekly OAC meetings on April 7th, 14th, 21st, and 28th for the Celina Campus](#)
- [Collin College, AECOM, Beck Architecture, LLC, and JE Dunn Construction conducted an OAC meeting on April 6th, 13th, 20th, and 27th for the IT Center at the Frisco Campus](#)
- [AECOM, RLK Engineering, Page Southerland Page, Inc. and Skanska USA Building, Inc. conducted an OAC meeting on April 7th, 14th, 21st, and 28th for the Fire Lane at the Frisco Campus](#)
- [Collin College, AECOM, Page Southerland Page, Inc. and Skanska USA Building, Inc. conducted an OAC meeting on March 6th, 13th, 20th, and 27th for the McKinney Campus Addition and Renovations](#)
- [JT Vaughn Construction held a Level 1 Punch walk for Collin College, AECOM, and Beck Architecture, LLC on April 23rd for the Celina Campus](#)

- [JT Vaughn Construction held an Exterior Punch walk for Collin College, AECOM, and Beck Architecture, LLC on April 28th for the Celina Campus](#)
- [City of Celina held a Kinship Parkway Punch Walk on April 20th](#)

See Appendix A for Construction Progress Photos

7.6 Acceptance and Close-Out

- No Acceptance and Close-Out Phase Items have been completed at this time

8. Pending Items

8.1 General Program

- No General Program items are pending at this time

8.2 Procurement

- [Execution of Skanska USA Building, Inc. GMP for the Frisco Campus Additions and Renovations](#)

8.3 Design

- No Design items are pending at this time

8.4 Pre-Construction

- [Coordination with the City of Frisco on the permitting/zoning requirements for the work on the Frisco Campus](#)
- [Coordination with the City of McKinney on the permitting/zoning requirements for the Welcome Center at the McKinney Campus](#)

8.5 Construction

- [Punch list at the Farmersville Campus and IT Center at Frisco Campus](#)

See Appendix A for Construction Progress Photos

8.6 Acceptance and Close-Out

- [Wylie and Technical Campuses achieved Substantial Completion and were accepted by the College in preparation for the Fall 2020 semester. Final close-out activities are nearing completion on both projects.](#)

Appendix A – Construction Progress Photos

Celina Campus



April '21 Aerial



Roundabout at Choate Parkway/Kinship Parkway



April Aerial Looking Northwest



Collin Logo at Main Entrance



Main Entrance at North Building



Lockers Outside of Testing Center in South Building



Bursar's Office Space in North Building

IT Center at Frisco Campus



April '21 Aerial



Main Entrance at North Side of Building



Glass Handrail Installation at Stars in Atrium




South Façade of Building



Quad Area



Classroom on 1st Floor, Northeast End

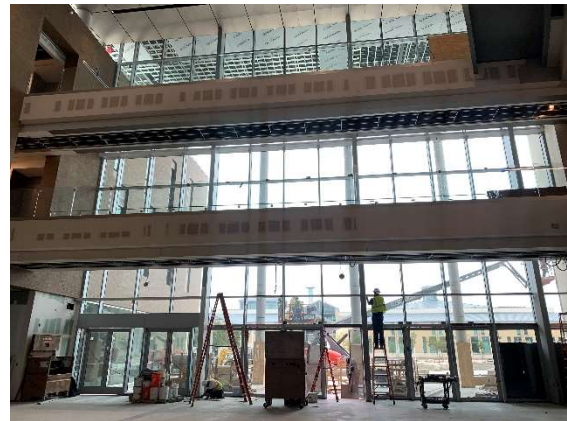

Glass Handrail Installation at Bridges

Firelane at Frisco Campus



Guardrails Installed



Fire Lane Poured, North to South View

Welcome Center and Parking Lot at McKinney Campus



April Aerial



April Aerial
