



Executive Program Summary June 2026

This report outlines, at an executive review level, the progress planned by the Construction Program Supervisor through June 2026 and key activities planned for July 2026.

PHASE 1 OVERVIEW

Safety Security & Police Building – Construction ongoing with foundation work, site work, and utilities working concurrently and is on track for a November 2026 substantial completion.

Early Learning Center 2.0 – Site work, utilities, and foundation ongoing and tracking for a spring 2027 substantial completion.

P1, P2, P3 - Middle Schools Fine Arts Additions – All 6 campus have ongoing construction for the fine arts additions, and HVAC replacements started in June. Substantial completion set for July 2027 for all campuses.

P15 - Ben Barber Innovation Academy and Frontier HS Addition & Renovations – Construction is ongoing for the addition and renovations in the existing building started in June. A February 2027 substantial completion is expected.

A1-A5 - High School Baseball & Softball Turf & Batting Cages – All campuses are working through padding corrections and final closeouts are near completion.

P14 - 6th Avenue & Main Transportation – No summer 2026 work will occur but reoccurring design meetings are in place.

S2 – Safety & Security Infrastructure District Wide

NextGen Security has begun procuring devices & servers. Device swap outs will begin on 5/22 during nights and weekends.

T1 – Fiber Ring

The storage replacement of this project is complete and city permits are expected to be approved sometime in May for the fiber ring.

PHASE 2 OVERVIEW

P4 - Capital Improvements – Anderson ES, Davis ES, Harmon ES, Holt ES, Morris ES, Tipps ES – Work has begun at Davis ES, Holt ES, & Morris ES.

P7 - Capital Improvements – Daulton ES, Miller ES, Smith ES, Spencer ES, Norwood ES – Work has begun at all campuses.

P8 - Capital Improvements – Brockett ES, Cabaniss ES, Gideon ES, Jones ES, Jandrucko ELA – Work has begun at all campuses.

P9 - Capital Improvements – Mansfield HS, Low IS, Orr IS – Demolition for summer work on all campuses has begun.

P11 - Capital Improvements – Timberview HS, Icenhower IS – Summer work on both campuses has begun.



PHASE 3 OVERVIEW

P4 - Capital Improvements – Anderson ES, Davis ES, Harmon ES, Holt ES, Morris ES, Tipps ES – This package will have Phase 3 scope in summer 2027. Phase 3 campuses with summer 2027 work will be Anderson ES, Harmon ES and Tipps ES.

P5 - Capital Improvements – Boren ES, Brown ES, Nash ES, Perry ES, Reid ES – This package will be bid fall of 2026 for Board approval with a Summer 2027 Construction completion.

P6 - Capital Improvements – Neal ES, Ponder ES, Rendon ES, Sheppard ES – This package will be bid fall of 2026 for Board approval with a Summer 2027 Construction completion.

P10 - Capital Improvements – Summit HS, Cross Timbers IS – This package will be bid fall of 2026 for Board approval with a Summer 2027 Construction completion.

P12 - Capital Improvements – Legacy HS, Shepard IS – This package will be bid fall of 2026 for Board approval with a Summer 2027 Construction completion.

P13 - Capital Improvements – Lake Ridge HS, Lillard IS, McKinzey IS – This package will be bid fall of 2026 for Board approval with a Summer 2027 Construction completion.

SCHEDULE:





The Report for each project is attached herewith.

BUDGET:

The Program Report Summary of expenditures is attached herewith.

The 2024 Bond Program website is complete with progress updates, information, and photos. The website will be consistently updated with project information.


7.4.1 Bond 2024 Program

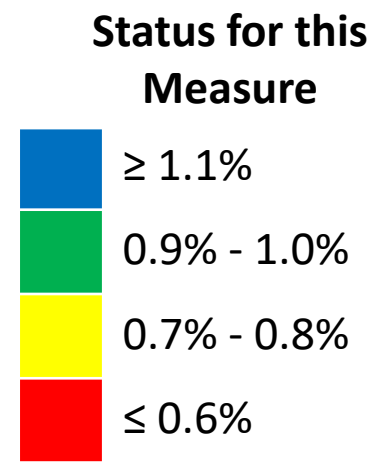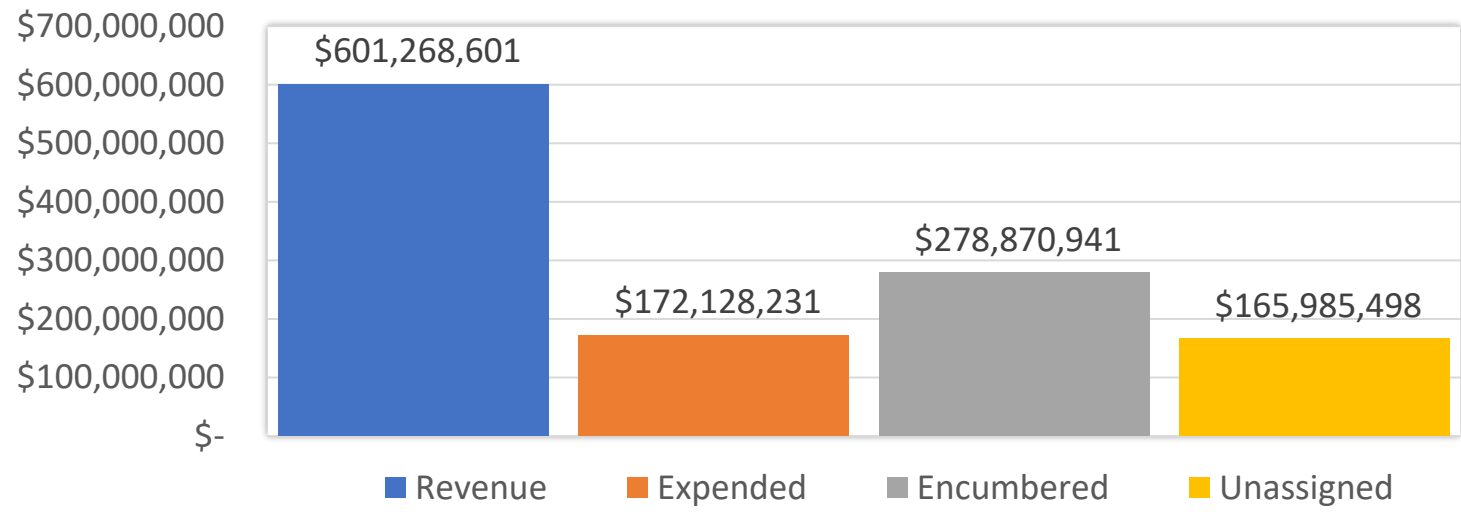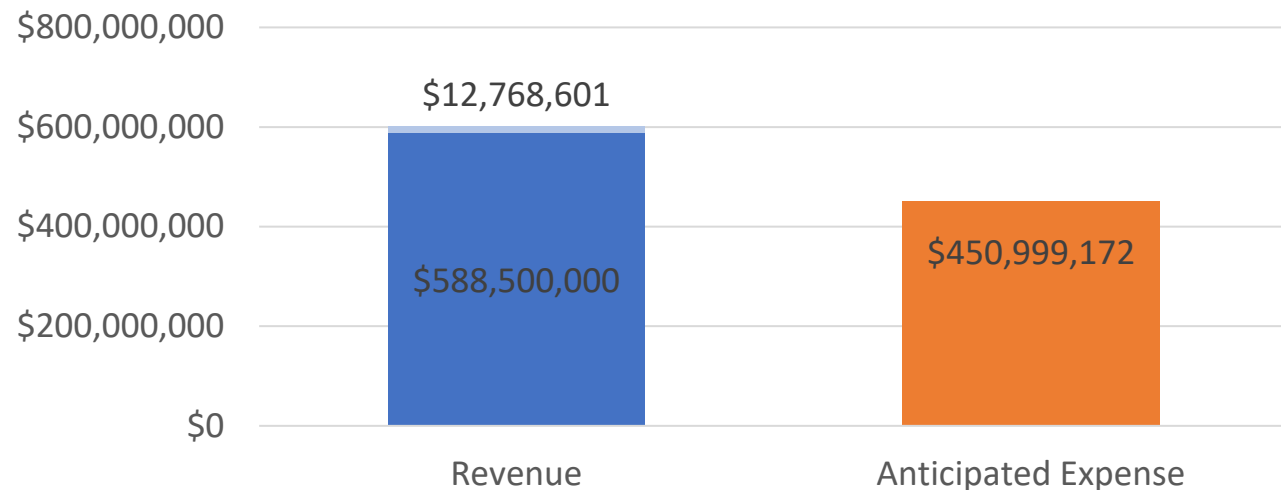

Goal: Under Budget ≤ 1.0% or \$5.88 million

MISD New Early Learners Academy

Schedule Summary

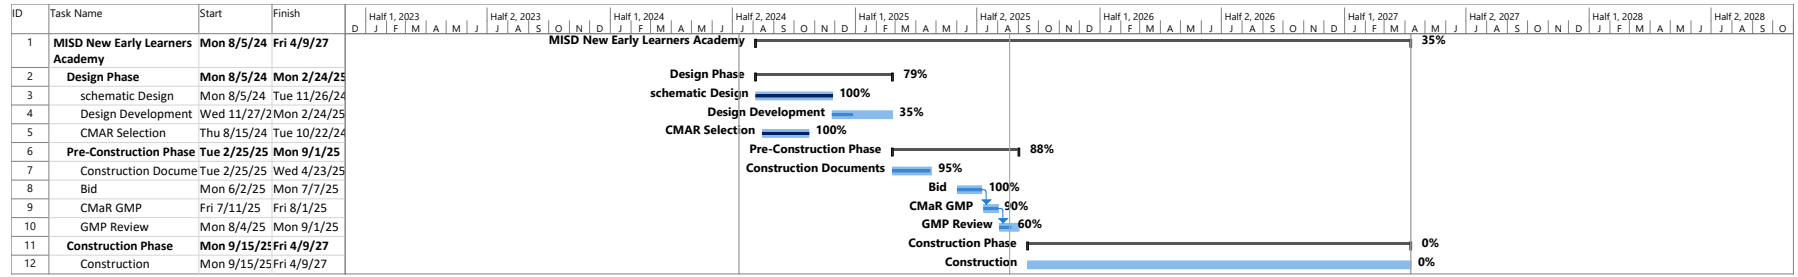

Budget

\$53,000,000.00

Cost Summary

Pre-Construction Fee: \$ 65,000.00

Contract Award Amount:

Change Order:

New Contract Amount

Scope of Work


1. Build a New Early Learners Academy

Status Summary

1. Preparation for Area A slab is scheduled to begin soon, weather permitting.
2. Lift station utilities are being set and underground plumbing was completed the first week of June.
3. Area B slab pour is finalized.
4. ICF pours for Area E & F are completed with subsequent areas being prepared.
5. The final graphics review Exhibit Concepts was completed.
6. Precast panels are completed and are in preparation for inspection.
7. Work on the topping slab is ongoing; structural steel install is scheduled to begin mid-June.
8. The project remains on track for a substantial completion of March 2027.

Package 1 Jobe & Worley MS Fine Arts Addition & CIP Package

Schedule Summary

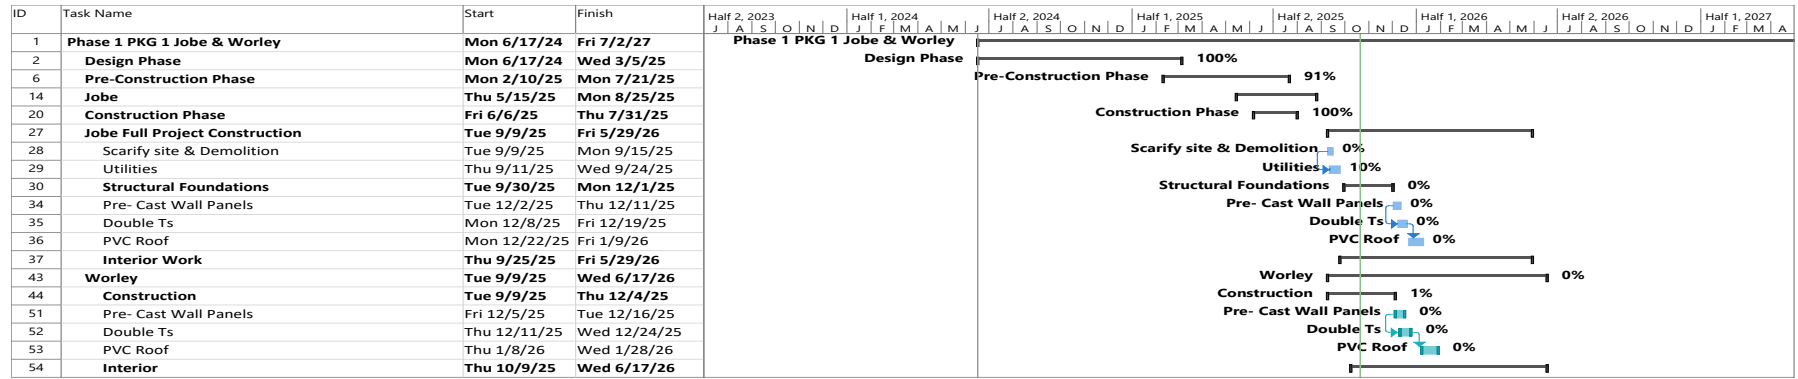

Cost Summary

Budget Amount: \$ 34,232,820.00 Change Order: Contract Award Amount: \$31,608,506.00
 Pre-Construction Fee: \$40,000.00
 New Contract Amount: Early Flooring Jobe: \$914,345.00
 New Contract Amount: Jobe GMP#2 \$15,767,159.00 New Contract Amount: Worley GMP#2 \$14,927,003.00


Scope of Work

1. New Fine Arts additions for Jobe & Worley Middle Schools.
2. Replace the running tracks at both schools.
3. Replacing all bathroom ceilings at Linda Jobe.
4. Life cycle replacements on air conditioning, flooring, fire alarm, & paving as required.
5. Linda Jobe will get new serving lines.

Status Summary

1. All exterior brick has been installed around the tornado shelter at Worley.
2. Waterproofing ongoing at the exterior of Jobe’s tornado shelter.
3. 100% of grade beam concrete has been poured at Jobe, and all underground utilities are complete.
4. Interior CIP renovations are ongoing at both campuses.

Middle School Fine Arts Additions PKG 2 T A Howard & James Coble Middle School with Life Cycle Replacement
Schedule Summary

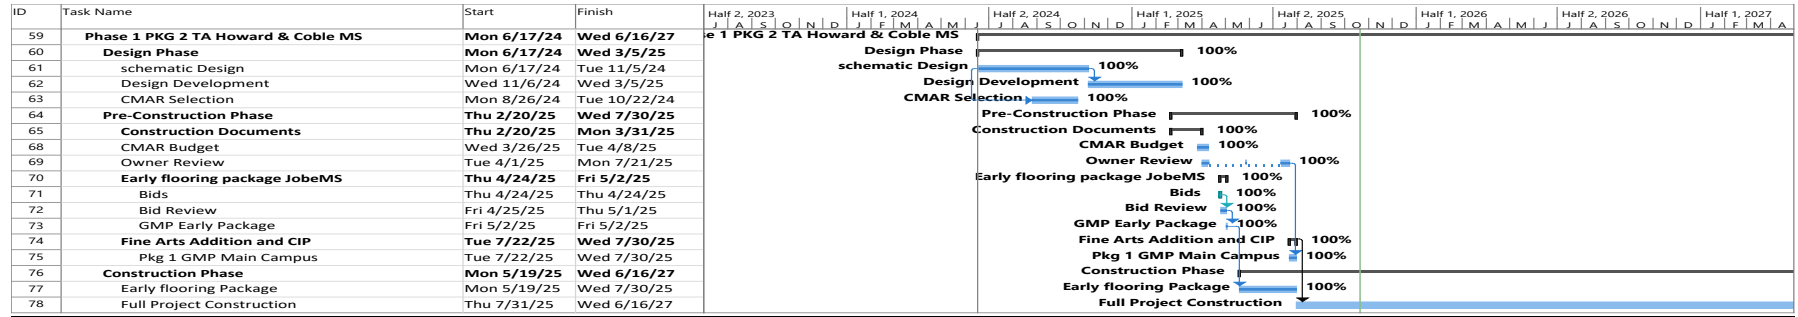

Cost Summary

Budget Amount: \$ 34,600,000.00

Change Order:

Contract Award Amount: \$ 29,785,236

Pre-Con Fee: \$80,000.00

New Contract Amount: Early Flooring Coble: \$967,084.00

New Contract Amount: Coble GMP#2 \$16,380,462.00

New Contract Amount: Howard GMP#2 \$12,432,560.00

Scope of Work

1. Construct Fine Arts additions.
2. Safety & Security Upgrades including weapons detection systems.
3. Technology infrastructure & life cycle replacements.
4. MEP life cycle replacements.
5. New serving lines in the cafeteria.
6. Civil work, track, bleacher, and scoreboard replacements.
7. Proposition B, interactive panels in classrooms and common spaces and digital signage.

Status Summary

1. Fire lane has been put in at Coble and is being inspected.
2. Soil retainer boards were placed along the grade beams at Coble & backfilled.
3. The electricians & plumbers made disconnections for the RTU swap at Coble, including the fire alarm. The curb adapters & RTUs were delivered on 6/8 & 6/9. Installation of RTUs begin 6/15.
4. The sidewalk at the front of Coble has been removed.
5. Excavation & soil stabilization for the new fire lane and head-in parking began at Howard.
6. Installation of the new fire lane system at Howard began and fiber connection to the concessions has been restored.
7. All grade beam excavation & decking is completed at Howard. First section of rebar is completed, and rebar in the second section is being installed.

Ben Barber Innovation Academy / Frontier STEM Academy CTE Addition & Life Cycle Replacement Phoenix Academy
Schedule Summary

ID	Task Name	Start	Finish	2021 2022 2023 2024 2025 2026 2027 2028 2029																											
				Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
1	Ben Barber / Frontier DTEM CTE Addition CIP & Phoenix CIP	Thu 7/11/24	Wed 11/25/26	Ben Barber / Frontier DTEM CTE Addition CIP & Phoenix CIP 45%																											
2	Design Phase	Thu 7/11/24	Fri 4/18/25	Design Phase 100%																											
9	Pre-Construction Phase	Wed 2/26/25	Wed 6/25/25	Pre-Construction Phase 100%																											
10	Construction Documents	Wed 2/26/25	Wed 5/14/25	Construction Documents 100%																											
11	Bid	Thu 5/15/25	Mon 6/9/25	Bid 100%																											
12	GMP	Tue 6/10/25	Wed 6/25/25	GMP 100%																											
13	Construction Phase	Thu 6/26/25	Wed 8/6/25	Construction Phase 15%																											
14	Contract Buy out	Thu 6/26/25	Wed 8/6/25	Contract Buy out 15%																											
15	Ben Barber / Frontier DTEM CTE	Fri 8/8/25	Tue 8/11/26	Ben Barber / Frontier DTEM CTE 6%																											
16	Mobilize	Fri 8/8/25	Wed 9/3/25	Mobilize 39%																											
17	Fence	Fri 8/8/25	Mon 8/11/25	Fence 100%																											
18	Job Trailer	Tue 8/26/25	Wed 8/27/25	Job Trailer 100%																											
19	Rock For laydown Yard	Thu 8/28/25	Wed 9/3/25	Rock For laydown Yard 80%																											
20	Shelter Construction	Thu 8/28/25	Tue 8/11/26	Shelter Construction 4%																											
31	Phoenix Academy	Mon 9/16/24	Wed 11/25/26	Phoenix Academy 39%																											
32	Design Phase	Mon 9/16/24	Wed 11/25/26	Design Phase 39%																											

Cost Summary

Proposed Budget: Ben Barber CTE \$18,319,424.00

Pre – Construction Fee: \$40,000.00

Contract Award Amount: \$21,728,789.00

Change Order:

New Contract Amount

Scope of Work

1. Ben Barber CTE Addition & CIP
 - a. New CTE Addition
 - b. Roof Top Unit R-22 replacement, life safety & security upgrades, Day Care play surface replacement.
 - c. Paving repairs
2. Phoenix Academy
 - a. Life safety & security upgrades, Interior Lighting replacement
 - b. Paving repairs

Status Summary

1. Storm structure topping slab is complete at Ben Barber.
2. Work on the roof flashing is underway at Ben Barber.
3. Cabinetry in both biomedical labs have been demoed at Ben Barber.
4. The existing construction lab ceiling at Ben Barber has been removed and everything has been made safe.
5. Concrete demo is underway at Phoenix and exterior sealants are scheduled for 6/15.

A-1 Mansfield High School Baseball & Softball Field Turf Upgrades, Batting Cages & Bull Pens

Schedule Summary

ID	Task Name	Start	Finish	2023	2024	2025	2026	2027	2028		
				Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
1	A-1 Mansfield High School Baseball, Softball Turf Projects, Batting Cages & Bullpens	Tue 9/3/24	Tue 12/30/25								
2	Design Phase	Tue 9/3/24	Mon 1/20/25								
5	Pre-Construction Phase	Tue 1/21/25	Tue 5/27/25								
11	Construction Phase	Tue 5/27/25	Tue 12/30/25								
12	NTP	Mon 6/2/25	Mon 6/2/25								
13	Contract Buy Out	Tue 5/27/25	Thu 6/19/25								
14	Construction	Mon 6/30/25	Tue 12/30/25								

Cost Summary

Pre – Construction Fee: \$10,000.00

Budget Amount: \$6,508,530

Contract Award Amount: \$5,976,120.00

Change Order:

New Contract Amount

Scope of Work

1. New Turf for Baseball & Softball fields at the 5 High Schools.
2. New batting cages for baseball & softball at each campus.

Status Summary

1. Core Construction & MISD are working on final closeouts to include updated as-built drawings for the district to keep.
2. Correction to the padding at the back stops is underway.
3. Additional field drag & magnets have been delivered to the campus.

A-2 Summit High School Baseball & Softball Field Turf Upgrades, Batting Cages & Bull Pens

Schedule Summary

ID	Task Name	Start	Finish	2024												2025				2026				2027		
				Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3		
18	A-2 Summit High School Baseball, Softball Turf Projects, Batting Cages & Bullpens	Sun 9/15/24	Tue 12/30/25	Batting Cages & Bullpens												66%										
19	Design Phase	Sun 9/15/24	Mon 1/20/25	Design Phase												100%										
22	Pre-Construction Phase	Tue 1/21/25	Tue 5/27/25	Pre-Construction Phase												99%										
28	Construction Phase	Tue 5/27/25	Tue 12/30/25	Construction Phase												23%										
29	NTP	Mon 6/2/25	Mon 6/2/25	NTP												100%										
30	Contract Buy Out	Tue 5/27/25	Thu 6/19/25	Contract Buy Out												80%										
31	Construction	Mon 6/30/25	Tue 12/30/25	Construction												15%										

Cost Summary

Pre – Construction Fee: \$15,750.00

Budget Amount: \$7,226,792

Contract Award Amount: \$6,626,421.00

Change Order:

New Contract Amount

Scope of Work

1. New Turf for Baseball & Softball fields at the 5 High Schools.
2. New batting cages for baseball & softball at each campus.

Status Summary

1. Lee Lewis & MISD are working on final closeouts to include updated as-built drawings for the district to keep.
2. Correction to the padding at the back stops is underway.
3. Additional field drag & magnets have been delivered to the campus.
4. Repairs have been made to baseball netting over the bleachers.

A-3 Legacy High School Baseball, Softball Turf Project, Batting Cages & Bullpens

Schedule Summary

ID	Task Name	Start	Finish	2024				2025				2026				2027		
				Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1
33	A-3 Legacy High School Baseball, Softball Turf Projects, Batting Cages & Bullpens	Sun 9/15/24	Tue 12/30/25	Batting Cages & Bullpens												72%		
34	Design Phase	Sun 9/15/24	Mon 1/20/25	Design Phase				100%										
37	Pre-Construction Phase	Tue 1/21/25	Tue 5/27/25	Pre-Construction Phase				99%										
43	Construction Phase	Tue 5/27/25	Tue 12/30/25	Construction Phase				37%										
44	NTP	Mon 6/2/25	Mon 6/2/25					NTP				100%						
45	Contract Buy Out	Tue 5/27/25	Thu 6/19/25					Contract Buy Out				90%						
46	Construction	Mon 6/30/25	Tue 12/30/25					Construction				30%						

Cost Summary

Pre -Construction Fee: \$ 10,000.00

Budget Amount: \$6,135,302.00

Contract Award Amount: \$5,563,466.00

Change Order:

New Contract Amount

Scope of Work

1. New Turf for Baseball & Softball fields at the 5 High Schools.
2. New batting cages for baseball & softball at each campus.

Status Summary

1. Crossland & MISD are working on final closeouts to include updated as-built drawings for the district to keep.
2. Additional field drag & magnets have been delivered to the campus.
3. Repairs to the concrete outside of the softball batting cages were determined to be necessary and are being planned.

A-4 Lake Ridge High School Baseball, Softball Turf Project, Batting Cages & Bullpens

Schedule Summary

ID	Task Name	Start	Finish	2021												2022				2023				2024				2025				2026		
				Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3							
88	A-4 Lake Ridge High School Baseball, Softball Turf Projects, Batting Cages & Bullpens	Tue 9/3/24	Wed 12/31/25	A-4 Lake Ridge High School Baseball, Softball Turf Projects, Batting Cages & Bullpens																								63%						
89	Design Phase	Tue 9/3/24	Mon 1/20/25	Design Phase																								100%						
92	Pre-Construction Phase	Tue 1/21/25	Tue 5/27/25	Pre-Construction Phase																								99%						
98	Construction Phase	Tue 5/27/25	Wed 12/31/25	Construction Phase																								41%						
99	NTP	Mon 6/2/25	Mon 6/2/25	NTP																								100%						
100	Contract Buy Out	Tue 5/27/25	Mon 6/30/25	Contract Buy Out																								15%						
101	Construction	Tue 5/27/25	Wed 12/31/25	Construction																								43%						

Cost Summary

Pre -Construction Fee: \$ 10,000.00

Budget Amount: \$5,937,467.00

Contract Award Amount: \$5,812,794.00

Change Order:

New Contract Amount

Scope of Work

1. New Turf for Baseball & Softball fields at the 5 High Schools.
2. New batting cages for baseball & softball at each campus.

Status Summary

1. Crossland & MISD are working on final closeouts to include updated as-built drawings for the district to keep.
2. Additional field drag & magnets have been delivered to the campus.

A-5 Timberview High School Baseball & Softball Field Turf Upgrades, Batting Cages & Bull Pens

Schedule Summary

ID	Task Name	Start	Finish	2021 2022 2023 2024 2025 2026 2027																												
				Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
63	A-5 Timberview High School Baseball, Softball Turf Projects, Batting Cages & Bullpens	Tue 9/3/24	Tue 12/30/25	A-5 Timberview High School Baseball, Softball Turf Projects, Batting Cages & Bullpens																												
64	Design Phase	Tue 9/3/24	Mon 1/20/25	Design Phase 100%																												
67	Pre-Construction Phase	Tue 1/21/25	Tue 5/27/25	Pre-Construction Phase 99%																												
73	Construction Phase	Tue 5/27/25	Tue 12/30/25	Construction Phase 20%																												
74	NTP	Mon 6/2/25	Mon 6/2/25	NTP 100%																												
75	Contract Buy Out	Tue 5/27/25	Thu 6/19/25	Contract Buy Out 50%																												
76	Construction	Mon 6/30/25	Tue 12/30/25	Construction 15%																												

Cost Summary

Pre -Construction Fee: \$ 10,000.00

Budget Amount: \$6,229,786.00

Contract Award Amount: \$5,652,763.00

Change Order:

New Contract Amount

Scope of Work


1. New Turf for Baseball & Softball fields at the 5 High Schools.
2. New batting cages for baseball & softball at each campus.

Status Summary

1. Authers Building Group & MISD are working on final closeouts to include updated as-built drawings for the district to keep.
2. Additional field drag & magnets have been delivered to the campus.

6th Ave Transportation Building Main Transportation, Danny Griffin OPS

Schedule Summary

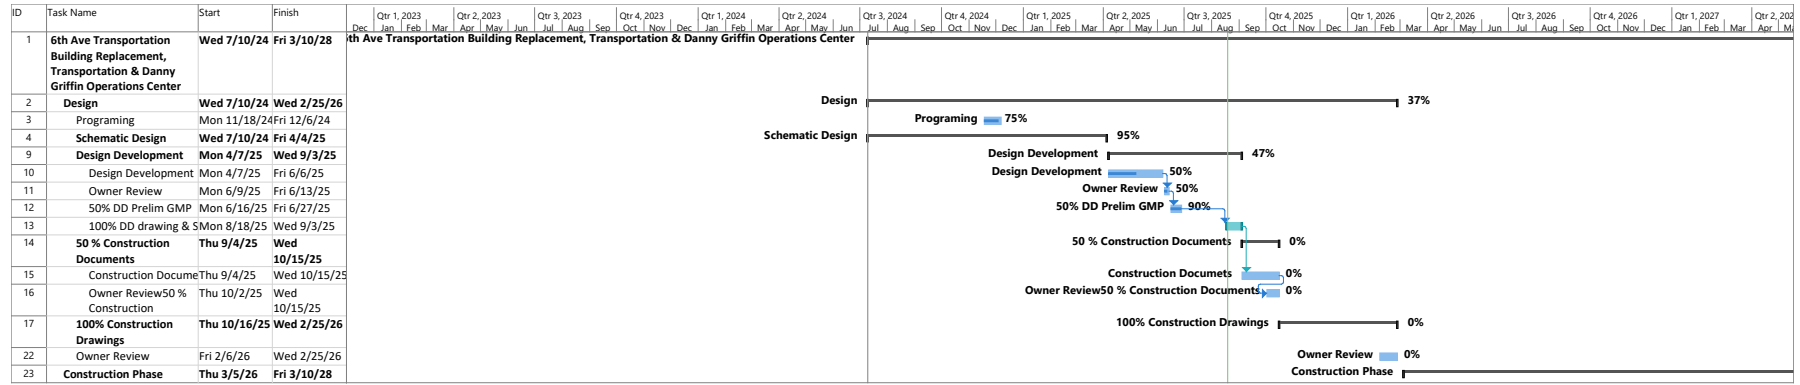

Cost Summary

Revised Budget Amount: \$25,330,120.00

Change Order:

New Contract Amount

Scope of Work:

1. New transportation offices with enough office space for staff, increased space for technology closet. Provide adequate space for training the 6th Avenue transportation department.
2. A new bus mechanic repair shop, so mechanics can safely work on buses out of the weather.
3. Additional bus parking for up to 150 buses, and the staff parking to accommodate the additional buses.
4. The design now will have a 10,000 gal unleaded and 20,000-gal diesel tanks with enough pumps to meet the future needs of the district.

Status Summary:

1. ABG will hold off on bidding until we resubmit back to the city and potentially until we receive an approved permit.
2. No summer 2026 work will occur.

Phase 2, Package 11: Timberview High School & Della Icenhower Intermediate School

Schedule Summary

Cost Summary

Contract Award Amount: \$ 858,619.73

Change Order:

New Contract Amount

Scope of Work


1. Construction projects at Timberview High School and Icenhower Intermediate School are focused on providing a safe and comfortable learning environment by replacing equipment and finishes that have exceeded their life cycle.
2. At Timberview High School, work includes resurfacing tennis courts, installing practice field fencing, replacing ice machines, gym and game field scoreboards, and completing key infrastructure and system upgrades.
3. At Icenhower Intermediate School, improvements include renovations to student nutrition serving lines, kitchen ceilings, coolers and freezers, gym floors, playground canopies and surfacing, and the fire alarm system.
4. Additional campus upgrades address building reliability and safety through HVAC replacements, electrical switchgear and irrigation pump replacements, masonry and concrete repairs, and redesigned greenspace.
5. These projects collectively enhance campus functionality, safety, and long-term sustainability for students and staff.

Status Summary

1. Flooring renovations, exterior concrete repairs, and water fountains replacements are underway at both campuses.
2. CMU repairs are completed at Timberview in Area A & B, now working in Area D with paint to follow.
3. HVAC curbs arriving at both campuses on 6/8 & 6/9. New HVAC units arriving at both campuses on 6/15 & 6/16 and setting will begin upon arrival.
4. The second-floor ceilings are demoed at Icenhower to run ductwork; the second-floor wall framing is underway to drop ductwork to the first floor.
5. Work on water heaters has begun at Icenhower, and fire alarm raceways are being installed.

Phase 2 Package 4 Anderson, Davis, Harmon, Holt, Morris, & Tipps Elementary CIP Package

Schedule Summary

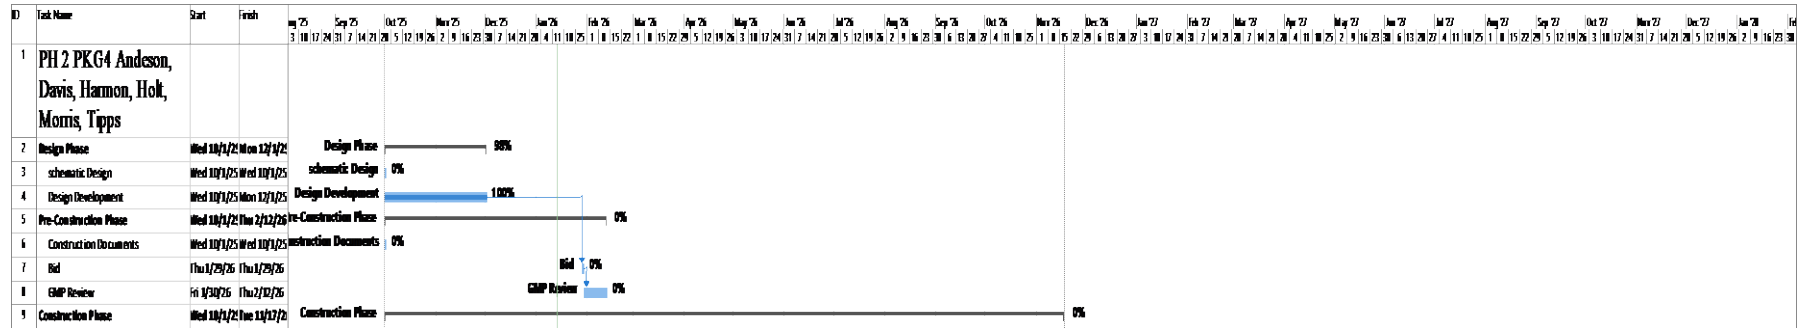

Cost Summary

Budgeted Amount: \$11,765,858.85

Change Order:

New Contract Amount:

Scope of Work:

1. Replace rubber playground surface with turf at all 6 campuses.
2. Lifecycle replacement of all exterior vertical control joint sealant.
3. Lifecycle replacement of water heaters, RTU’s, carpet, VCT, hand dryers, air conditioning, roof, fire alarm, gym flooring, cooler/freezer, hand sinks, & water fountains throughout campus.
4. Minor exterior paving & sidewalk repairs.

Status Summary

1. Flooring is demoed at Holt’s entire campus and kitchen ceiling is completed. New HVAC units will be installed on 6/11.
2. New HVAC units will be installed at Davis on 6/12.
3. The work on playgrounds at all three campuses will begin within the next two weeks.
4. Tipps, Harmon, & Anderson to be completed over the summer of 2027.

Phase 2 Package 7 Norwood, Smith, Miller, Spencer & Daulton Elementary CIP Package

Schedule Summary

Cost Summary

Budgeted Amount: \$12,704,766.91

Change Order:

New Contract Amount

Scope of Work

1. All schools included to have hand sinks, water fountains, and water heaters replaced
2. Smith, Spencer, and Daulton to have RTU R-22 replacements
3. Playground surfaces, cooler/freezer, exterior sealant replacements are to be captured in the CIP for each pertained school
4. Carpet/LVT, Gym flooring, paving, kitchen ceiling/ flooring, canopies, and fire alarm system replacements are to be captured in the CIP as well for each pertained school.

Status Summary

1. All RTUs at Daulton, Spencer, & Smith have been disconnected; Daulton & Spencer have swapped over their RTUs for new ones. RTU swap will begin on 6/15 at Smith.
2. Flooring demo is underway and new flooring will be installed afterwards.
3. Water heaters have been replaced at all campuses.
4. Playground demo for turf installation is underway.

Phase 2, Package 8: Janet Brockett, Imogene Gideon, Thelma Jones, Louise Cabaniss, & Dr. Jandrucko Early Learners Academy
Schedule Summary

Cost Summary

Budgeted Amount: \$19,196,633.15

Change Order:

New Contract Amount

Scope of Work

1. Resurface playgrounds for improved safety and durability as well as improvements and expansion of playground at Dr. Jandrucko Early Learners Academy.
2. Update digital signage in office reception areas and replace outdated classroom projectors with full interactive panels (Smart Boards).
3. Replace kitchen flooring and ceiling at Gideon Elementary School, update coolers and freezers in kitchens, replace and repair gym floors, and replace select carpet and VCT flooring at Brockett, Cabaniss, Jones, and Jandrucko.
4. Replace plumbing, HVAC, carpentry, and lighting features as needed to address safety and security.
5. Refurbish exhibit set pieces and parts at Jandrucko Early Learners Academy.
6. Replace playground canopy at Jones Elementary.

Status Summary

1. Work is underway at all campuses, including fire alarm cabling installation and interior demolition of current carpet & VCT in preparation for new flooring.
2. RTUs were removed from Cabaniss via helicopter on 6/1. Thelma Jones had the RTUs swapped via helicopter on the entire campus on 6/1.
3. Kitchen work is underway at Gideon.
4. Jandrucko pod classroom demolition is underway with a substantial completion of upgraded experiences set for the end of June.

Pakcage-9 CIP Renovations for Mansfield HS, Asa Low IS, Mary Orr IS

Schedule Summary

Cost Summary

Proposed Budget:

Pre – Construction Fee:

Contract Award Amount:

Change Order:

New Contract Amount

Scope of Work

1. Mansfield HS
 - a. RTU R-22, Split System Replacement
 - b. Roof replacement, exterior sealants,
 - c. LVT Flooring, rubber-weight room
 - d. Paving repairs, irrigation pump, fence practice fields

2. Asa Low IS
 - a. Gym floor, Carpet, LVT, hand sinks
 - b. Serving lines, cooler-freezer replacement
 - c. Exterior sealants, paving repairs, playground surface replacement

3. Mary Orr IS
 - a. Kitchen Flooring, hand sinks
 - b. Irrigation, pump, grease trap, exterior sealants
 - c. Exterior sealants, paving repairs, playground surface replacement

Status Summary

1. RTUs will be delivered at MHS 6/9-6/14. Existing RTUs will be removed on 6/24.
2. Flooring demo was done at Asa Low and the cooler/freezer replacement is underway. The furniture on the second floor was moved to the first floor.
3. The kitchen flooring demo and playground surface demo were done at Mary Orr. The grease trap replacement is underway.
