


PROJECT UPDATE

SEPTEMBER 2025

TOM BANSCHBACH MIDDLE SCHOOL



OVERALL SITE

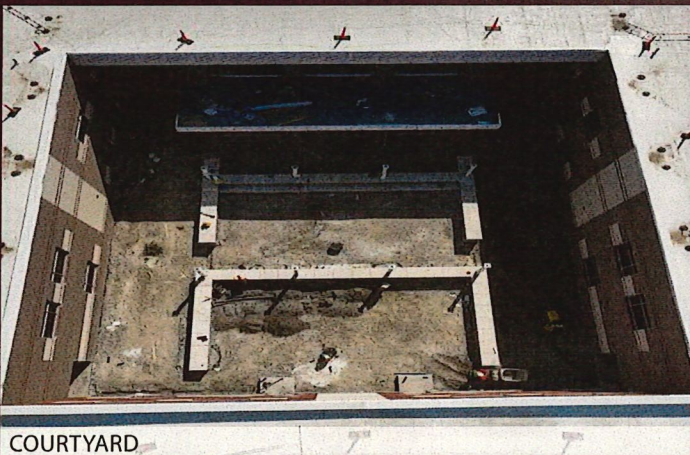

COURTYARD



MAIN STAIR #2

CONSTRUCTION STATUS

SITE WORK


- LONG JUMP PAD COMPLETE
- ONSITE WATER TESTING IN PROGRESS

BUILDING

- FIRST FLOOR CLASSROOM LOW VOLTAGE COMPLETE
- WALL TILE INSTALL CONTINUES
- OVERHEAD MEP COMPLETE AT KITCHEN, CAFETERIA, & MUSIC HALL

LOOKING FORWARD

- FENCING INSTALL AT ATHLETIC FIELDS & TENNIS COURTS
- SITE LIGHTING INSTALL
- BEGIN CEILING GRIDS

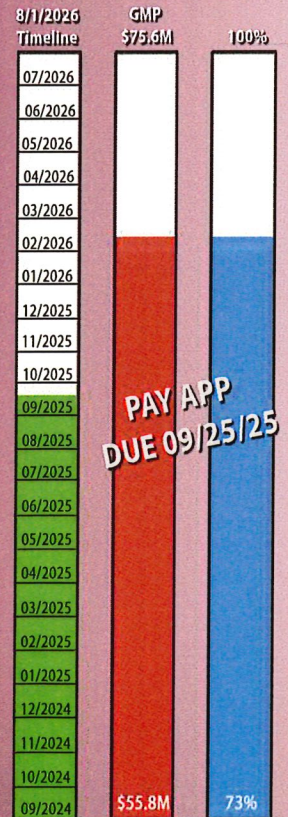

PROJECT UPDATE

SEPTEMBER 2025

CARRELL ELEMENTARY SCHOOL



OVERALL SITE



EXTERIOR PROGRESS



INTERIOR PROGRESS

CONSTRUCTION STATUS

BUILDING

- ROOFING INSTALL IN PROGRESS
- EXTERIOR WALL FINISH NEAR COMPLETION
- INTERIOR IN-WALL INSPECTIONS IN PROGRESS

LOOKING FORWARD

- ROOFTOP UNITS TO BE SET NEXT WEEK
- CLOSING WALLS WITH 2-SIDE GYP
- CEILING GRID, TILE, & FLOORING INSTALL TO BEGIN

