

Collin College February 2026 Monthly Report

2023-2030 Master Plan Phase I
Collin County Community College District

Project Number: 60726232

March 03, 2026

Quality Information

Prepared by	Reviewed by	Approved By
Nuria Cortes	Melissa Perette	Tim Smith
Nuria Cortes Program Controls Manager	Melissa Perette Deputy Program Director	Tim Smith Program Director

Revision History

Revision	Revision date	Details	Authorized	Name	Position
First Publication	March 03, 2026	February '26 Report	Yes	Tim Smith	Program Director

Distribution List

# Hard Copies	PDF Required	Association / Company Name
1		Dr. Neil Matkin / Collin College
1		Dr. Bill King / Collin College
1		Chris Eyle / Collin College

Prepared for:

Collin County Community College District
3452 Spur 399
Suite 327
McKinney, TX 75069

Prepared by:

Nuria Cortes
Program Controls Manager
E: ncortes.aecom@collin.edu

AECOM
13355 Noel Road
4th Floor
Dallas TX, 75240
aecom.com

Copyright © 2026 by AECOM

All rights reserved. No part of this copyrighted work may be reproduced, distributed, or transmitted in any form or by any means without the prior written permission of AECOM.

Table of Contents

1.	Introduction	5
2.	Executive Summary	5
3.	Program Summary	6
	3.1 Program Schedule	6
	3.2 Program Budget	7
	3.3 Current Personnel Estimate	7
4.	Project Summary	8
5	Completed Items	13
	5.1 General Program	13
	5.2 Procurement	13
	5.3 Design	13
	5.4 Pre-Construction	13
	5.5 Construction	13
	5.6 Acceptance and Close-Out	14
6	Pending Items	14
	6.1 General Program	14
	6.2 Procurement	14
	6.3 Design	14
	6.4 Pre-Construction	14
	6.5 Construction	14
	6.6 Acceptance and Close-Out	14
7	Progress Pictures	15
	7.1 Plano Campus Renovations	15
	7.2 Health Science Center	16
	7.3 CHEC	17

1. Introduction

AECOM is currently managing five projects in this program. The total budget for the entire program is \$240,333,508.36, which includes two projects that AECOM is not managing.

On February 27, 2024, the Board of Trustees granted the District President authority to enter into and negotiate a contract with AECOM Technical Services, Inc. (AECOM) to provide Program Management Services for the Collin College 2023 Master Plan Program. On May 3, 2024, Collin College and AECOM executed the Collin contract for program management services. As part of these services, AECOM will deliver a monthly report to provide status and progress of key aspects of the Program.

2. Executive Summary

Completed and Pending Items

- Plano Campus – Roof work Punchlist underway. Courtyard MEP work finishing up getting to install equipment. Theater installing temp solution for the balcony make ready for performance in March. Comm. Music, construction ready to punch programming system. Welcome Center, Kitchen/ Dining and E first floor work is continuing.
- Courtyard Center – Project closeout in progress.
- CHEC – Phase 3 carpet has been installed and painting has been completed. Millwork was installed in breakroom and workroom areas. Punchlist walk was completed and punchlist items are ongoing. City inspections for TCO on Phase 3 is ongoing.
- Health Science Center – Glazing frame installation in progress on north elevation. Mechanical, electrical, and plumbing rough-in complete on first level, city approval pending. Sheathing and waterproofing continues.
- Wylie CTE – Skanska Notice to Proceed issued. City of Wylie Preconstruction Meeting complete. Skanska to begin mobilization in March.

Items of close attention

- No items of close attention at this time

Budget Summary

- \$162,003,705.30 of the \$240,333,508.36 has been committed to date in the form of contracts with various vendors.
- \$94,030,343.03 of the \$162,003,705.30 committed amount has expended to-date.

3. Program Summary

3.1 Program Schedule

Project	Scope of Work	2024												2025												2026												2027											
		Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
Plano Campus	Renovations & Upgrades																																																
CYC	Departmental Relocations																																																
CHEC	Departmental Relocations																																																
Health Sciences	New Building																																																
Wylie - CTE	New Building																																																

- Planning & Programming
- Design & Construction Documents
- Construction
- Final Completion & Close-Out




We Are Here

3.2 Program Budget

Cost Summary							
Budget Group	Original Budget	Current Budget	Commitments	Approved Changes	Total Commitments	Pending Commitments	Expended to Date
Construction, Equipment & Furnishings	\$157,491,962.00	\$197,607,179.85	\$96,163,077.41	\$45,610,224.64	\$141,773,302.05	\$124,981.00	\$79,598,330.96
Contingency	\$22,203,853.00	\$18,895,647.65	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
Investigation, Testing & Verification	\$2,847,939.00	\$3,303,594.00	\$1,591,446.00	\$18,975.00	\$1,610,421.00	\$4,945.00	\$547,820.66
Management, Design & Pre-Construction	\$17,145,727.36	\$20,064,533.36	\$17,651,494.01	\$832,690.00	\$18,484,184.01	\$0.00	\$13,760,710.67
Miscellaneous	\$393,015.00	\$462,553.50	\$131,772.24	\$4,026.00	\$135,798.24	\$0.00	\$123,480.74
Total	\$200,082,496.36	\$240,333,508.36	\$115,537,789.66	\$46,465,915.64	\$162,003,705.30	\$129,926.00	\$94,030,343.03

3.3 Current Personnel Estimate

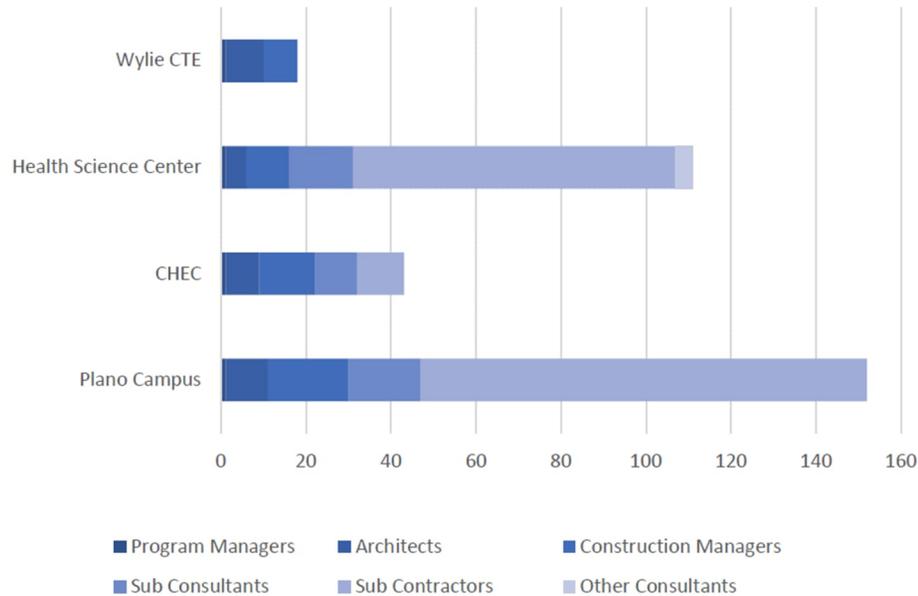

It is estimated that the Program Managers, Architects, Construction Managers, Sub-Consultants, and Sub-Contractors, under contract with Collin College for the 2023 Master Plan Programs, have an average of 324 employees contributing to the program's progress.

4. Project Summary

Courtyard Renovation

Project Name Courtyard Renovation		 	Schedule																																																																								
Project Name Courtyard Renovation	Project Number PJ1065		<table border="1"> <thead> <tr> <th>Activity</th> <th>Baseline Finish</th> <th>Planned Finish</th> <th>Actual Finish</th> <th></th> </tr> </thead> <tbody> <tr> <td>BOT Approval of Construction Delivery Method</td> <td>1/26/2024</td> <td>1/26/2024</td> <td>↑</td> <td>1/26/2024 ✓</td> </tr> <tr> <td>BOT Approval of Recommended A/E</td> <td>1/26/2024</td> <td>1/26/2024</td> <td>↑</td> <td>1/26/2024 ✓</td> </tr> <tr> <td>BOT Approval of Program Manager</td> <td>2/27/2024</td> <td>2/27/2024</td> <td>↑</td> <td>2/27/2024 ✓</td> </tr> <tr> <td>Architect Mobilized</td> <td>5/17/2024</td> <td>5/17/2024</td> <td>↑</td> <td>5/17/2024 ✓</td> </tr> <tr> <td>BOT Approval of Recommended CMAR</td> <td>5/26/2024</td> <td>5/26/2024</td> <td>↑</td> <td>5/28/2024 ✓</td> </tr> <tr> <td>100% CDs Complete</td> <td>11/1/2024</td> <td>10/10/2024</td> <td>↑</td> <td>10/10/2024 ✓</td> </tr> <tr> <td>GMP Submittal</td> <td>12/1/2024</td> <td>11/22/2024</td> <td>↑</td> <td>11/22/2024 ✓</td> </tr> <tr> <td>BOT Approval of GMP</td> <td>12/10/2024</td> <td>12/10/2024</td> <td>↑</td> <td>12/10/2024 ✓</td> </tr> <tr> <td>Obtain Building Permit</td> <td>12/13/2024</td> <td>12/13/2024</td> <td>↑</td> <td>1/16/2025 ✓</td> </tr> <tr> <td>Contractor Mobilized</td> <td>12/20/2024</td> <td>12/20/2024</td> <td>↑</td> <td>1/20/2025 ✓</td> </tr> <tr> <td>Substantial Completion</td> <td>7/15/2025</td> <td>8/18/2025</td> <td>↓</td> <td>8/18/2025 ✓</td> </tr> <tr> <td>Final Completion</td> <td>8/1/2025</td> <td>9/10/2025</td> <td>↓</td> <td>10/8/2025 ✓</td> </tr> <tr> <td>Student Occupancy</td> <td>8/26/2025</td> <td>8/26/2025</td> <td>↑</td> <td>9/2/2025 ✓</td> </tr> </tbody> </table>				Activity	Baseline Finish	Planned Finish	Actual Finish		BOT Approval of Construction Delivery Method	1/26/2024	1/26/2024	↑	1/26/2024 ✓	BOT Approval of Recommended A/E	1/26/2024	1/26/2024	↑	1/26/2024 ✓	BOT Approval of Program Manager	2/27/2024	2/27/2024	↑	2/27/2024 ✓	Architect Mobilized	5/17/2024	5/17/2024	↑	5/17/2024 ✓	BOT Approval of Recommended CMAR	5/26/2024	5/26/2024	↑	5/28/2024 ✓	100% CDs Complete	11/1/2024	10/10/2024	↑	10/10/2024 ✓	GMP Submittal	12/1/2024	11/22/2024	↑	11/22/2024 ✓	BOT Approval of GMP	12/10/2024	12/10/2024	↑	12/10/2024 ✓	Obtain Building Permit	12/13/2024	12/13/2024	↑	1/16/2025 ✓	Contractor Mobilized	12/20/2024	12/20/2024	↑	1/20/2025 ✓	Substantial Completion	7/15/2025	8/18/2025	↓	8/18/2025 ✓	Final Completion	8/1/2025	9/10/2025	↓	10/8/2025 ✓	Student Occupancy	8/26/2025	8/26/2025	↑
Activity	Baseline Finish	Planned Finish	Actual Finish																																																																								
BOT Approval of Construction Delivery Method	1/26/2024	1/26/2024	↑	1/26/2024 ✓																																																																							
BOT Approval of Recommended A/E	1/26/2024	1/26/2024	↑	1/26/2024 ✓																																																																							
BOT Approval of Program Manager	2/27/2024	2/27/2024	↑	2/27/2024 ✓																																																																							
Architect Mobilized	5/17/2024	5/17/2024	↑	5/17/2024 ✓																																																																							
BOT Approval of Recommended CMAR	5/26/2024	5/26/2024	↑	5/28/2024 ✓																																																																							
100% CDs Complete	11/1/2024	10/10/2024	↑	10/10/2024 ✓																																																																							
GMP Submittal	12/1/2024	11/22/2024	↑	11/22/2024 ✓																																																																							
BOT Approval of GMP	12/10/2024	12/10/2024	↑	12/10/2024 ✓																																																																							
Obtain Building Permit	12/13/2024	12/13/2024	↑	1/16/2025 ✓																																																																							
Contractor Mobilized	12/20/2024	12/20/2024	↑	1/20/2025 ✓																																																																							
Substantial Completion	7/15/2025	8/18/2025	↓	8/18/2025 ✓																																																																							
Final Completion	8/1/2025	9/10/2025	↓	10/8/2025 ✓																																																																							
Student Occupancy	8/26/2025	8/26/2025	↑	9/2/2025 ✓																																																																							
Project Type Renovation		Project Phase Construction		Scope Description <ul style="list-style-type: none"> * Renovations of the Courtyard Center <ul style="list-style-type: none"> * The Renovations include: <ul style="list-style-type: none"> - New Cosmetology Space - Relocate and expand Esthetician Space - New Medical Message space - Remodel of 4th floor for Information Technology and Police 																																																																							
Project Manager Melissa Perette	Contractor/CM Skanska	Architect IN2 Architecture																																																																									
Project Directory				Progress Summary																																																																							
<table border="1"> <thead> <tr> <th>Company</th> <th>Project Role</th> </tr> </thead> <tbody> <tr> <td>AECOM Technical Services, Inc.</td> <td>Program Manager</td> </tr> <tr> <td>Collin College</td> <td>Owner</td> </tr> <tr> <td>Skanska</td> <td>Construction Manager-at-Risk</td> </tr> <tr> <td>IN2 Architecture</td> <td>A/E</td> </tr> <tr> <td>RWB Consulting Engineers</td> <td></td> </tr> </tbody> </table>		Company	Project Role	AECOM Technical Services, Inc.	Program Manager	Collin College	Owner	Skanska	Construction Manager-at-Risk	IN2 Architecture	A/E	RWB Consulting Engineers		<table border="1"> <thead> <tr> <th>Status Date</th> <th>Notes</th> </tr> </thead> <tbody> <tr> <td>2/27/2026</td> <td>Project closeout in progress.</td> </tr> </tbody> </table>				Status Date	Notes	2/27/2026	Project closeout in progress.																																																						
Company	Project Role																																																																										
AECOM Technical Services, Inc.	Program Manager																																																																										
Collin College	Owner																																																																										
Skanska	Construction Manager-at-Risk																																																																										
IN2 Architecture	A/E																																																																										
RWB Consulting Engineers																																																																											
Status Date	Notes																																																																										
2/27/2026	Project closeout in progress.																																																																										
Cost Summary																																																																											
<table border="1"> <thead> <tr> <th>Budget Group</th> <th>Original Budget</th> <th>Current Budget</th> <th>Commitments</th> <th>Approved Changes</th> <th>Total Commitments</th> <th>Pending Commitments</th> <th>Expended to Date</th> </tr> </thead> <tbody> <tr> <td>Construction, Equipment & Furnishings</td> <td>\$4,991,556.00</td> <td>\$5,282,515.85</td> <td>\$5,013,360.34</td> <td>\$269,556.50</td> <td>\$5,282,916.84</td> <td>\$0.00</td> <td>\$4,949,700.06</td> </tr> <tr> <td>Contingency</td> <td>\$294,481.00</td> <td>\$18,409.65</td> <td>\$0.00</td> <td>\$0.00</td> <td>\$0.00</td> <td>\$0.00</td> <td>\$0.00</td> </tr> <tr> <td>Investigation, Testing & Verification</td> <td>\$82,073.00</td> <td>\$72,151.00</td> <td>\$72,151.00</td> <td>\$0.00</td> <td>\$72,151.00</td> <td>\$0.00</td> <td>\$56,055.90</td> </tr> <tr> <td>Management, Design & Pre-Construction</td> <td>\$696,100.00</td> <td>\$692,087.00</td> <td>\$690,736.36</td> <td>\$5,000.00</td> <td>\$695,736.36</td> <td>\$0.00</td> <td>\$559,766.75</td> </tr> <tr> <td>Miscellaneous</td> <td>\$4,551.00</td> <td>\$3,597.50</td> <td>\$3,597.50</td> <td>\$0.00</td> <td>\$3,597.50</td> <td>\$0.00</td> <td>\$1,847.00</td> </tr> <tr> <td>Total</td> <td>\$6,068,761.00</td> <td>\$6,068,761.00</td> <td>\$5,779,845.20</td> <td>\$274,556.50</td> <td>\$6,054,401.70</td> <td>\$0.00</td> <td>\$5,567,369.71</td> </tr> </tbody> </table>	Budget Group	Original Budget	Current Budget	Commitments	Approved Changes	Total Commitments	Pending Commitments	Expended to Date	Construction, Equipment & Furnishings	\$4,991,556.00	\$5,282,515.85	\$5,013,360.34	\$269,556.50	\$5,282,916.84	\$0.00	\$4,949,700.06	Contingency	\$294,481.00	\$18,409.65	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	Investigation, Testing & Verification	\$82,073.00	\$72,151.00	\$72,151.00	\$0.00	\$72,151.00	\$0.00	\$56,055.90	Management, Design & Pre-Construction	\$696,100.00	\$692,087.00	\$690,736.36	\$5,000.00	\$695,736.36	\$0.00	\$559,766.75	Miscellaneous	\$4,551.00	\$3,597.50	\$3,597.50	\$0.00	\$3,597.50	\$0.00	\$1,847.00	Total	\$6,068,761.00	\$6,068,761.00	\$5,779,845.20	\$274,556.50	\$6,054,401.70	\$0.00	\$5,567,369.71																			
Budget Group	Original Budget	Current Budget	Commitments	Approved Changes	Total Commitments	Pending Commitments	Expended to Date																																																																				
Construction, Equipment & Furnishings	\$4,991,556.00	\$5,282,515.85	\$5,013,360.34	\$269,556.50	\$5,282,916.84	\$0.00	\$4,949,700.06																																																																				
Contingency	\$294,481.00	\$18,409.65	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00																																																																				
Investigation, Testing & Verification	\$82,073.00	\$72,151.00	\$72,151.00	\$0.00	\$72,151.00	\$0.00	\$56,055.90																																																																				
Management, Design & Pre-Construction	\$696,100.00	\$692,087.00	\$690,736.36	\$5,000.00	\$695,736.36	\$0.00	\$559,766.75																																																																				
Miscellaneous	\$4,551.00	\$3,597.50	\$3,597.50	\$0.00	\$3,597.50	\$0.00	\$1,847.00																																																																				
Total	\$6,068,761.00	\$6,068,761.00	\$5,779,845.20	\$274,556.50	\$6,054,401.70	\$0.00	\$5,567,369.71																																																																				

CHEC Renovation

Project Name CHEC Renovation			 	Schedule																																																																									
Project Name CHEC Renovation		Project Number PJ1066		Scope Description																																																																									
Project Type Renovation		Project Phase Construction		*Renovations Collin Higher Education Center - Renovations of selected spaces on 1st, 2nd, 3rd and 4th floor.																																																																									
Project Manager Melissa Perette	Contractor/CM Skanska	Architect IN2 Architecture		<table border="1"> <thead> <tr> <th>Activity</th> <th>Baseline Finish</th> <th>Planned Finish</th> <th>Actual Finish</th> <th></th> </tr> </thead> <tbody> <tr> <td>BOT Approval of A/E Procurement Method</td> <td>1/26/2024</td> <td>1/26/2024</td> <td>↑</td> <td>1/26/2024 ✓</td> </tr> <tr> <td>BOT Approval of Construction Delivery Method</td> <td>1/26/2024</td> <td>1/26/2024</td> <td>↑</td> <td>1/26/2024 ✓</td> </tr> <tr> <td>BOT Approval of Recommended A/E</td> <td>1/26/2024</td> <td>1/26/2024</td> <td>↑</td> <td>1/26/2024 ✓</td> </tr> <tr> <td>BOT Approval of Program Manager</td> <td>2/27/2024</td> <td>2/27/2024</td> <td>↑</td> <td>2/27/2024 ✓</td> </tr> <tr> <td>Architect Mobilized</td> <td>5/17/2024</td> <td>5/17/2024</td> <td>↑</td> <td>5/17/2024 ✓</td> </tr> <tr> <td>BOT Approval of Recommended CMAR</td> <td>5/26/2024</td> <td>5/26/2024</td> <td>↑</td> <td>5/28/2024 ✓</td> </tr> <tr> <td>100% CDs Complete</td> <td>11/1/2024</td> <td>2/14/2025</td> <td>↓</td> <td>2/14/2025 ✓</td> </tr> <tr> <td>GMP Submittal</td> <td>12/1/2024</td> <td>2/20/2025</td> <td>↓</td> <td>2/20/2025 ✓</td> </tr> <tr> <td>BOT Approval of GMP</td> <td>12/10/2024</td> <td>3/25/2025</td> <td>↓</td> <td>3/25/2025 ✓</td> </tr> <tr> <td>Obtain Building Permit</td> <td>12/20/2024</td> <td>4/16/2025</td> <td>↓</td> <td>4/21/2025 ✓</td> </tr> <tr> <td>Contractor Mobilized</td> <td>1/6/2025</td> <td>4/17/2025</td> <td>↓</td> <td>4/21/2025 ✓</td> </tr> <tr> <td>Substantial Completion</td> <td>4/1/2026</td> <td>4/24/2026</td> <td>↓</td> <td></td> </tr> <tr> <td>Final Completion</td> <td>5/1/2026</td> <td>5/26/2026</td> <td>↓</td> <td></td> </tr> </tbody> </table>				Activity	Baseline Finish	Planned Finish	Actual Finish		BOT Approval of A/E Procurement Method	1/26/2024	1/26/2024	↑	1/26/2024 ✓	BOT Approval of Construction Delivery Method	1/26/2024	1/26/2024	↑	1/26/2024 ✓	BOT Approval of Recommended A/E	1/26/2024	1/26/2024	↑	1/26/2024 ✓	BOT Approval of Program Manager	2/27/2024	2/27/2024	↑	2/27/2024 ✓	Architect Mobilized	5/17/2024	5/17/2024	↑	5/17/2024 ✓	BOT Approval of Recommended CMAR	5/26/2024	5/26/2024	↑	5/28/2024 ✓	100% CDs Complete	11/1/2024	2/14/2025	↓	2/14/2025 ✓	GMP Submittal	12/1/2024	2/20/2025	↓	2/20/2025 ✓	BOT Approval of GMP	12/10/2024	3/25/2025	↓	3/25/2025 ✓	Obtain Building Permit	12/20/2024	4/16/2025	↓	4/21/2025 ✓	Contractor Mobilized	1/6/2025	4/17/2025	↓	4/21/2025 ✓	Substantial Completion	4/1/2026	4/24/2026	↓		Final Completion	5/1/2026	5/26/2026	↓	
Activity	Baseline Finish	Planned Finish	Actual Finish																																																																										
BOT Approval of A/E Procurement Method	1/26/2024	1/26/2024	↑	1/26/2024 ✓																																																																									
BOT Approval of Construction Delivery Method	1/26/2024	1/26/2024	↑	1/26/2024 ✓																																																																									
BOT Approval of Recommended A/E	1/26/2024	1/26/2024	↑	1/26/2024 ✓																																																																									
BOT Approval of Program Manager	2/27/2024	2/27/2024	↑	2/27/2024 ✓																																																																									
Architect Mobilized	5/17/2024	5/17/2024	↑	5/17/2024 ✓																																																																									
BOT Approval of Recommended CMAR	5/26/2024	5/26/2024	↑	5/28/2024 ✓																																																																									
100% CDs Complete	11/1/2024	2/14/2025	↓	2/14/2025 ✓																																																																									
GMP Submittal	12/1/2024	2/20/2025	↓	2/20/2025 ✓																																																																									
BOT Approval of GMP	12/10/2024	3/25/2025	↓	3/25/2025 ✓																																																																									
Obtain Building Permit	12/20/2024	4/16/2025	↓	4/21/2025 ✓																																																																									
Contractor Mobilized	1/6/2025	4/17/2025	↓	4/21/2025 ✓																																																																									
Substantial Completion	4/1/2026	4/24/2026	↓																																																																										
Final Completion	5/1/2026	5/26/2026	↓																																																																										
Project Directory			Progress Summary																																																																										
<table border="1"> <thead> <tr> <th>Company</th> <th>Project Role</th> </tr> </thead> <tbody> <tr> <td>AECOM Technical Services, Inc.</td> <td>Program Manager</td> </tr> <tr> <td>Collin College</td> <td>Owner</td> </tr> <tr> <td>IN2 Architecture</td> <td>A/E</td> </tr> <tr> <td>Skanska</td> <td>A/E</td> </tr> <tr> <td>RWB Consulting Engineers</td> <td></td> </tr> </tbody> </table>		Company	Project Role	AECOM Technical Services, Inc.	Program Manager	Collin College	Owner	IN2 Architecture	A/E	Skanska	A/E	RWB Consulting Engineers		Status Date		Notes																																																													
Company	Project Role																																																																												
AECOM Technical Services, Inc.	Program Manager																																																																												
Collin College	Owner																																																																												
IN2 Architecture	A/E																																																																												
Skanska	A/E																																																																												
RWB Consulting Engineers																																																																													
		2/28/2026		Phase 3 carpet has been installed and painting has been completed. Millwork was installed in breakroom and workroom areas. Punchlist walk was completed and punchlist items are ongoing. City inspections for TCO on phase 3 is ongoing.																																																																									
Cost Summary																																																																													
<table border="1"> <thead> <tr> <th>Budget Group</th> <th>Original Budget</th> <th>Current Budget</th> <th>Commitments</th> <th>Approved Changes</th> <th>Total Commitments</th> <th>Pending Commitments</th> <th>Expended to Date</th> </tr> </thead> <tbody> <tr> <td>Construction, Equipment & Furnishings</td> <td>\$7,172,040.00</td> <td>\$7,665,990.00</td> <td>\$7,512,583.49</td> <td>\$3,439.00</td> <td>\$7,516,022.49</td> <td>\$0.00</td> <td>\$5,084,085.82</td> </tr> <tr> <td>Contingency</td> <td>\$562,950.00</td> <td>\$42,507.00</td> <td>\$0.00</td> <td>\$0.00</td> <td>\$0.00</td> <td>\$0.00</td> <td>\$0.00</td> </tr> <tr> <td>Investigation, Testing & Verification</td> <td>\$117,927.00</td> <td>\$121,960.00</td> <td>\$121,960.00</td> <td>\$0.00</td> <td>\$121,960.00</td> <td>\$0.00</td> <td>\$67,214.02</td> </tr> <tr> <td>Management, Design & Pre-Construction</td> <td>\$860,348.36</td> <td>\$879,348.36</td> <td>\$844,348.36</td> <td>\$5,000.00</td> <td>\$849,348.36</td> <td>\$0.00</td> <td>\$660,253.75</td> </tr> <tr> <td>Miscellaneous</td> <td>\$6,540.00</td> <td>\$10,000.00</td> <td>\$17,420.00</td> <td>\$120.00</td> <td>\$17,540.00</td> <td>\$0.00</td> <td>\$14,480.00</td> </tr> <tr> <td>Total</td> <td>\$8,719,805.36</td> <td>\$8,719,805.36</td> <td>\$8,496,311.85</td> <td>\$8,559.00</td> <td>\$8,504,870.85</td> <td>\$0.00</td> <td>\$5,826,033.59</td> </tr> </tbody> </table>	Budget Group	Original Budget	Current Budget	Commitments	Approved Changes	Total Commitments	Pending Commitments	Expended to Date	Construction, Equipment & Furnishings	\$7,172,040.00	\$7,665,990.00	\$7,512,583.49	\$3,439.00	\$7,516,022.49	\$0.00	\$5,084,085.82	Contingency	\$562,950.00	\$42,507.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	Investigation, Testing & Verification	\$117,927.00	\$121,960.00	\$121,960.00	\$0.00	\$121,960.00	\$0.00	\$67,214.02	Management, Design & Pre-Construction	\$860,348.36	\$879,348.36	\$844,348.36	\$5,000.00	\$849,348.36	\$0.00	\$660,253.75	Miscellaneous	\$6,540.00	\$10,000.00	\$17,420.00	\$120.00	\$17,540.00	\$0.00	\$14,480.00	Total	\$8,719,805.36	\$8,719,805.36	\$8,496,311.85	\$8,559.00	\$8,504,870.85	\$0.00	\$5,826,033.59																					
Budget Group	Original Budget	Current Budget	Commitments	Approved Changes	Total Commitments	Pending Commitments	Expended to Date																																																																						
Construction, Equipment & Furnishings	\$7,172,040.00	\$7,665,990.00	\$7,512,583.49	\$3,439.00	\$7,516,022.49	\$0.00	\$5,084,085.82																																																																						
Contingency	\$562,950.00	\$42,507.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00																																																																						
Investigation, Testing & Verification	\$117,927.00	\$121,960.00	\$121,960.00	\$0.00	\$121,960.00	\$0.00	\$67,214.02																																																																						
Management, Design & Pre-Construction	\$860,348.36	\$879,348.36	\$844,348.36	\$5,000.00	\$849,348.36	\$0.00	\$660,253.75																																																																						
Miscellaneous	\$6,540.00	\$10,000.00	\$17,420.00	\$120.00	\$17,540.00	\$0.00	\$14,480.00																																																																						
Total	\$8,719,805.36	\$8,719,805.36	\$8,496,311.85	\$8,559.00	\$8,504,870.85	\$0.00	\$5,826,033.59																																																																						

Plano Renovation

Project Name Plano Renovation		 	Schedule																																																																															
Project Name Plano Renovation			Project Number PJ1064		<table border="1"> <thead> <tr> <th>Activity</th> <th>Baseline Finish</th> <th>Planned Finish</th> <th>Actual Finish</th> <th></th> </tr> </thead> <tbody> <tr> <td>BOT Approval of Construction Delivery Method</td> <td>1/26/2024</td> <td>1/26/2024</td> <td>1/26/2024</td> <td>↑ ✓</td> </tr> <tr> <td>BOT Approval of Recommended A/E</td> <td>1/26/2024</td> <td>1/26/2024</td> <td>1/26/2024</td> <td>↑ ✓</td> </tr> <tr> <td>BOT Approval of Program Manager</td> <td>2/27/2024</td> <td>2/27/2024</td> <td>2/27/2024</td> <td>↑ ✓</td> </tr> <tr> <td>BOT Approval of Recommended CMAR</td> <td>3/26/2024</td> <td>3/26/2024</td> <td>3/26/2024</td> <td>↑ ✓</td> </tr> <tr> <td>Architect Mobilized</td> <td>4/19/2024</td> <td>4/19/2024</td> <td>4/19/2024</td> <td>↑ ✓</td> </tr> <tr> <td>GMP 1 Construction Documents Submittal</td> <td>7/26/2024</td> <td>8/2/2024</td> <td>8/2/2024</td> <td>↓ ✓</td> </tr> <tr> <td>BOT Approval of GMP 1</td> <td>9/24/2024</td> <td>9/24/2024</td> <td>9/24/2024</td> <td>↑ ✓</td> </tr> <tr> <td>GMP 2 Construction Documents Submittal</td> <td>10/21/2024</td> <td>9/19/2024</td> <td>9/20/2024</td> <td>↑ ✓</td> </tr> <tr> <td>BOT Approval of GMP 2</td> <td>12/10/2024</td> <td>12/10/2024</td> <td>12/10/2024</td> <td>↑ ✓</td> </tr> <tr> <td>Obtain Building Permit</td> <td>12/13/2024</td> <td>1/13/2025</td> <td>1/30/2025</td> <td>↓ ✓</td> </tr> <tr> <td>Contractor Mobilized</td> <td>12/20/2024</td> <td>12/20/2024</td> <td>12/20/2024</td> <td>↑ ✓</td> </tr> <tr> <td>Substantial Completion</td> <td>6/1/2026</td> <td>7/30/2026</td> <td></td> <td>↓</td> </tr> <tr> <td>Final Completion</td> <td>7/21/2026</td> <td>8/6/2026</td> <td></td> <td>↓</td> </tr> <tr> <td>Student Occupancy</td> <td>8/17/2026</td> <td>8/17/2026</td> <td></td> <td>↑</td> </tr> </tbody> </table>				Activity	Baseline Finish	Planned Finish	Actual Finish		BOT Approval of Construction Delivery Method	1/26/2024	1/26/2024	1/26/2024	↑ ✓	BOT Approval of Recommended A/E	1/26/2024	1/26/2024	1/26/2024	↑ ✓	BOT Approval of Program Manager	2/27/2024	2/27/2024	2/27/2024	↑ ✓	BOT Approval of Recommended CMAR	3/26/2024	3/26/2024	3/26/2024	↑ ✓	Architect Mobilized	4/19/2024	4/19/2024	4/19/2024	↑ ✓	GMP 1 Construction Documents Submittal	7/26/2024	8/2/2024	8/2/2024	↓ ✓	BOT Approval of GMP 1	9/24/2024	9/24/2024	9/24/2024	↑ ✓	GMP 2 Construction Documents Submittal	10/21/2024	9/19/2024	9/20/2024	↑ ✓	BOT Approval of GMP 2	12/10/2024	12/10/2024	12/10/2024	↑ ✓	Obtain Building Permit	12/13/2024	1/13/2025	1/30/2025	↓ ✓	Contractor Mobilized	12/20/2024	12/20/2024	12/20/2024	↑ ✓	Substantial Completion	6/1/2026	7/30/2026		↓	Final Completion	7/21/2026	8/6/2026		↓	Student Occupancy	8/17/2026	8/17/2026	
Activity	Baseline Finish	Planned Finish	Actual Finish																																																																															
BOT Approval of Construction Delivery Method	1/26/2024	1/26/2024	1/26/2024	↑ ✓																																																																														
BOT Approval of Recommended A/E	1/26/2024	1/26/2024	1/26/2024	↑ ✓																																																																														
BOT Approval of Program Manager	2/27/2024	2/27/2024	2/27/2024	↑ ✓																																																																														
BOT Approval of Recommended CMAR	3/26/2024	3/26/2024	3/26/2024	↑ ✓																																																																														
Architect Mobilized	4/19/2024	4/19/2024	4/19/2024	↑ ✓																																																																														
GMP 1 Construction Documents Submittal	7/26/2024	8/2/2024	8/2/2024	↓ ✓																																																																														
BOT Approval of GMP 1	9/24/2024	9/24/2024	9/24/2024	↑ ✓																																																																														
GMP 2 Construction Documents Submittal	10/21/2024	9/19/2024	9/20/2024	↑ ✓																																																																														
BOT Approval of GMP 2	12/10/2024	12/10/2024	12/10/2024	↑ ✓																																																																														
Obtain Building Permit	12/13/2024	1/13/2025	1/30/2025	↓ ✓																																																																														
Contractor Mobilized	12/20/2024	12/20/2024	12/20/2024	↑ ✓																																																																														
Substantial Completion	6/1/2026	7/30/2026		↓																																																																														
Final Completion	7/21/2026	8/6/2026		↓																																																																														
Student Occupancy	8/17/2026	8/17/2026		↑																																																																														
Project Type Renovation		Project Phase Construction		Scope Description * Renovations to the Plano Campus * The Renovation includes: - Roof Replacement - Expanding Science Labs - Renovation and Expanding Health Sciences - Renovation in various other areas																																																																														
Project Manager Tim Smith		Contractor/CM Skanska						Architect IN2 Architecture																																																																										
Project Directory						Progress Summary																																																																												
<table border="1"> <thead> <tr> <th>Company</th> <th>Project Role</th> </tr> </thead> <tbody> <tr> <td>AECOM Technical Services, Inc.</td> <td>Program Manager</td> </tr> <tr> <td>Collin College</td> <td>Owner</td> </tr> <tr> <td>Skanska</td> <td>Construction Manager-at-Risk</td> </tr> <tr> <td>IN2 Architecture</td> <td>A/E</td> </tr> <tr> <td>BAi, LLC</td> <td></td> </tr> <tr> <td>Dunaway</td> <td></td> </tr> <tr> <td>Foodservice Design Professional</td> <td></td> </tr> <tr> <td>MATSON DRISCOLL & DAMICO LLP</td> <td></td> </tr> <tr> <td>Price Consulting, Inc.</td> <td></td> </tr> <tr> <td>RWB Consulting Engineers</td> <td></td> </tr> </tbody> </table>		Company	Project Role	AECOM Technical Services, Inc.	Program Manager	Collin College	Owner	Skanska	Construction Manager-at-Risk	IN2 Architecture	A/E	BAi, LLC		Dunaway		Foodservice Design Professional		MATSON DRISCOLL & DAMICO LLP		Price Consulting, Inc.		RWB Consulting Engineers		Status Date		Notes 2/27/2026 Plano Campus, Roof work Punchlist underway. Courtyard MEP work finishing up getting to install equipment. Theater installing temp solution for the balcony make ready for performance in March. Comm. Music, construction ready to punch programming system. Welcome Center, Kitchen/ Dining and E first floor work is continuing.																																																								
Company	Project Role																																																																																	
AECOM Technical Services, Inc.	Program Manager																																																																																	
Collin College	Owner																																																																																	
Skanska	Construction Manager-at-Risk																																																																																	
IN2 Architecture	A/E																																																																																	
BAi, LLC																																																																																		
Dunaway																																																																																		
Foodservice Design Professional																																																																																		
MATSON DRISCOLL & DAMICO LLP																																																																																		
Price Consulting, Inc.																																																																																		
RWB Consulting Engineers																																																																																		
Cost Summary																																																																																		
<table border="1"> <thead> <tr> <th>Budget Group</th> <th>Original Budget</th> <th>Current Budget</th> <th>Commitments</th> <th>Approved Changes</th> <th>Total Commitments</th> <th>Pending Commitments</th> <th>Expended to Date</th> </tr> </thead> <tbody> <tr> <td>Construction, Equipment & Furnishings</td> <td>\$62,835,304.00</td> <td>\$74,193,298.00</td> <td>\$69,759,212.48</td> <td>\$1,596,723.14</td> <td>\$71,355,935.62</td> <td>\$59,267.40</td> <td>\$45,978,250.38</td> </tr> <tr> <td>Contingency</td> <td>\$2,372,401.00</td> <td>\$1,008,102.00</td> <td>\$0.00</td> <td>\$0.00</td> <td>\$0.00</td> <td>\$0.00</td> <td>\$0.00</td> </tr> <tr> <td>Investigation, Testing & Verification</td> <td>\$1,150,911.00</td> <td>\$1,359,240.00</td> <td>\$599,068.00</td> <td>\$18,975.00</td> <td>\$618,043.00</td> <td>\$6,120.00</td> <td>\$279,071.94</td> </tr> <tr> <td>Management, Design & Pre-Construction</td> <td>\$6,895,542.00</td> <td>\$8,078,310.00</td> <td>\$6,987,542.26</td> <td>(\$10,000.00)</td> <td>\$6,977,542.26</td> <td>\$0.00</td> <td>\$5,824,097.90</td> </tr> <tr> <td>Miscellaneous</td> <td>\$305,272.00</td> <td>\$361,050.00</td> <td>\$110,754.74</td> <td>\$3,906.00</td> <td>\$114,660.74</td> <td>\$0.00</td> <td>\$107,153.74</td> </tr> <tr> <td>Total</td> <td>\$73,559,430.00</td> <td>\$85,000,000.00</td> <td>\$77,456,577.48</td> <td>\$1,609,604.14</td> <td>\$79,066,181.62</td> <td>\$65,387.40</td> <td>\$52,188,573.96</td> </tr> </tbody> </table>		Budget Group	Original Budget	Current Budget	Commitments	Approved Changes	Total Commitments	Pending Commitments	Expended to Date	Construction, Equipment & Furnishings	\$62,835,304.00	\$74,193,298.00	\$69,759,212.48	\$1,596,723.14	\$71,355,935.62	\$59,267.40	\$45,978,250.38	Contingency	\$2,372,401.00	\$1,008,102.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	Investigation, Testing & Verification	\$1,150,911.00	\$1,359,240.00	\$599,068.00	\$18,975.00	\$618,043.00	\$6,120.00	\$279,071.94	Management, Design & Pre-Construction	\$6,895,542.00	\$8,078,310.00	\$6,987,542.26	(\$10,000.00)	\$6,977,542.26	\$0.00	\$5,824,097.90	Miscellaneous	\$305,272.00	\$361,050.00	\$110,754.74	\$3,906.00	\$114,660.74	\$0.00	\$107,153.74	Total	\$73,559,430.00	\$85,000,000.00	\$77,456,577.48	\$1,609,604.14	\$79,066,181.62	\$65,387.40	\$52,188,573.96																									
Budget Group	Original Budget	Current Budget	Commitments	Approved Changes	Total Commitments	Pending Commitments	Expended to Date																																																																											
Construction, Equipment & Furnishings	\$62,835,304.00	\$74,193,298.00	\$69,759,212.48	\$1,596,723.14	\$71,355,935.62	\$59,267.40	\$45,978,250.38																																																																											
Contingency	\$2,372,401.00	\$1,008,102.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00																																																																											
Investigation, Testing & Verification	\$1,150,911.00	\$1,359,240.00	\$599,068.00	\$18,975.00	\$618,043.00	\$6,120.00	\$279,071.94																																																																											
Management, Design & Pre-Construction	\$6,895,542.00	\$8,078,310.00	\$6,987,542.26	(\$10,000.00)	\$6,977,542.26	\$0.00	\$5,824,097.90																																																																											
Miscellaneous	\$305,272.00	\$361,050.00	\$110,754.74	\$3,906.00	\$114,660.74	\$0.00	\$107,153.74																																																																											
Total	\$73,559,430.00	\$85,000,000.00	\$77,456,577.48	\$1,609,604.14	\$79,066,181.62	\$65,387.40	\$52,188,573.96																																																																											

Health Science Center

Project Name Health Science Center		 		Schedule																																																																																																																																							
Project Name Health Science Center		Project Number PJ1067		<table border="1"> <thead> <tr> <th>Activity</th> <th>Baseline Finish</th> <th>Planned Finish</th> <th>Actual Finish</th> <th></th> <th></th> </tr> </thead> <tbody> <tr> <td>BOT Approval of REC, A/E & CMAA Firms</td> <td>3/26/2024</td> <td>3/26/2024</td> <td>3/26/2024</td> <td>↑</td> <td>✓</td> </tr> <tr> <td>Architect Mobilized</td> <td>4/30/2024</td> <td>4/30/2024</td> <td>4/30/2024</td> <td>↑</td> <td>✓</td> </tr> <tr> <td>Programming</td> <td>7/30/2024</td> <td>8/15/2024</td> <td>8/15/2024</td> <td>↓</td> <td>✓</td> </tr> <tr> <td>Schematic Design</td> <td>9/30/2024</td> <td>10/4/2024</td> <td>10/4/2024</td> <td>↓</td> <td>✓</td> </tr> <tr> <td>Design Development Completion</td> <td>12/20/2024</td> <td>12/20/2024</td> <td>12/18/2024</td> <td>↑</td> <td>✓</td> </tr> <tr> <td>GMP 1 Package Issuance</td> <td>12/22/2024</td> <td>12/18/2024</td> <td>12/18/2024</td> <td>↑</td> <td>✓</td> </tr> <tr> <td>GMP 1 Package Bidding</td> <td>1/15/2025</td> <td>1/24/2025</td> <td>1/24/2025</td> <td>↓</td> <td>✓</td> </tr> <tr> <td>BOT Approval of GMP 1</td> <td>2/25/2025</td> <td>2/25/2025</td> <td>2/25/2025</td> <td>↑</td> <td>✓</td> </tr> <tr> <td>Contractor Mobilized</td> <td>2/26/2025</td> <td>5/1/2025</td> <td>5/2/2025</td> <td>↓</td> <td>✓</td> </tr> <tr> <td>GMP 2 - 100% CDs Bidding</td> <td>3/28/2025</td> <td>2/28/2025</td> <td>2/28/2025</td> <td>↑</td> <td>✓</td> </tr> <tr> <td>Foundations Complete</td> <td>4/30/2025</td> <td>9/11/2025</td> <td>8/27/2025</td> <td>↓</td> <td>✓</td> </tr> <tr> <td>GMP 2 - 100% CDs Issuance</td> <td>5/12/2025</td> <td>6/9/2025</td> <td>6/19/2025</td> <td>↓</td> <td>✓</td> </tr> <tr> <td>BOT Approval of GMP 2</td> <td>5/31/2025</td> <td>5/27/2025</td> <td>5/27/2025</td> <td>↑</td> <td>✓</td> </tr> <tr> <td>Structures Complete</td> <td>2/28/2026</td> <td>12/3/2025</td> <td>12/3/2025</td> <td>↑</td> <td>✓</td> </tr> <tr> <td>Interior Finish-Out Complete</td> <td>7/15/2026</td> <td>9/16/2026</td> <td></td> <td>↓</td> <td></td> </tr> <tr> <td>Substantial Completion</td> <td>7/31/2026</td> <td>12/15/2026</td> <td></td> <td>↓</td> <td></td> </tr> <tr> <td>Temporary CO</td> <td>8/7/2026</td> <td>11/6/2026</td> <td></td> <td>↓</td> <td></td> </tr> <tr> <td>Final CO</td> <td>8/14/2026</td> <td>12/15/2026</td> <td></td> <td>↓</td> <td></td> </tr> <tr> <td>Final Completion</td> <td>8/31/2026</td> <td>12/15/2026</td> <td></td> <td>↓</td> <td></td> </tr> <tr> <td>Owner Occupancy</td> <td>8/31/2026</td> <td>1/19/2027</td> <td></td> <td>↓</td> <td></td> </tr> <tr> <td>Student Occupancy</td> <td>8/31/2026</td> <td>1/19/2027</td> <td></td> <td>↓</td> <td></td> </tr> </tbody> </table>				Activity	Baseline Finish	Planned Finish	Actual Finish			BOT Approval of REC, A/E & CMAA Firms	3/26/2024	3/26/2024	3/26/2024	↑	✓	Architect Mobilized	4/30/2024	4/30/2024	4/30/2024	↑	✓	Programming	7/30/2024	8/15/2024	8/15/2024	↓	✓	Schematic Design	9/30/2024	10/4/2024	10/4/2024	↓	✓	Design Development Completion	12/20/2024	12/20/2024	12/18/2024	↑	✓	GMP 1 Package Issuance	12/22/2024	12/18/2024	12/18/2024	↑	✓	GMP 1 Package Bidding	1/15/2025	1/24/2025	1/24/2025	↓	✓	BOT Approval of GMP 1	2/25/2025	2/25/2025	2/25/2025	↑	✓	Contractor Mobilized	2/26/2025	5/1/2025	5/2/2025	↓	✓	GMP 2 - 100% CDs Bidding	3/28/2025	2/28/2025	2/28/2025	↑	✓	Foundations Complete	4/30/2025	9/11/2025	8/27/2025	↓	✓	GMP 2 - 100% CDs Issuance	5/12/2025	6/9/2025	6/19/2025	↓	✓	BOT Approval of GMP 2	5/31/2025	5/27/2025	5/27/2025	↑	✓	Structures Complete	2/28/2026	12/3/2025	12/3/2025	↑	✓	Interior Finish-Out Complete	7/15/2026	9/16/2026		↓		Substantial Completion	7/31/2026	12/15/2026		↓		Temporary CO	8/7/2026	11/6/2026		↓		Final CO	8/14/2026	12/15/2026		↓		Final Completion	8/31/2026	12/15/2026		↓		Owner Occupancy	8/31/2026	1/19/2027		↓		Student Occupancy	8/31/2026	1/19/2027		↓	
Activity	Baseline Finish	Planned Finish	Actual Finish																																																																																																																																								
BOT Approval of REC, A/E & CMAA Firms	3/26/2024	3/26/2024	3/26/2024	↑	✓																																																																																																																																						
Architect Mobilized	4/30/2024	4/30/2024	4/30/2024	↑	✓																																																																																																																																						
Programming	7/30/2024	8/15/2024	8/15/2024	↓	✓																																																																																																																																						
Schematic Design	9/30/2024	10/4/2024	10/4/2024	↓	✓																																																																																																																																						
Design Development Completion	12/20/2024	12/20/2024	12/18/2024	↑	✓																																																																																																																																						
GMP 1 Package Issuance	12/22/2024	12/18/2024	12/18/2024	↑	✓																																																																																																																																						
GMP 1 Package Bidding	1/15/2025	1/24/2025	1/24/2025	↓	✓																																																																																																																																						
BOT Approval of GMP 1	2/25/2025	2/25/2025	2/25/2025	↑	✓																																																																																																																																						
Contractor Mobilized	2/26/2025	5/1/2025	5/2/2025	↓	✓																																																																																																																																						
GMP 2 - 100% CDs Bidding	3/28/2025	2/28/2025	2/28/2025	↑	✓																																																																																																																																						
Foundations Complete	4/30/2025	9/11/2025	8/27/2025	↓	✓																																																																																																																																						
GMP 2 - 100% CDs Issuance	5/12/2025	6/9/2025	6/19/2025	↓	✓																																																																																																																																						
BOT Approval of GMP 2	5/31/2025	5/27/2025	5/27/2025	↑	✓																																																																																																																																						
Structures Complete	2/28/2026	12/3/2025	12/3/2025	↑	✓																																																																																																																																						
Interior Finish-Out Complete	7/15/2026	9/16/2026		↓																																																																																																																																							
Substantial Completion	7/31/2026	12/15/2026		↓																																																																																																																																							
Temporary CO	8/7/2026	11/6/2026		↓																																																																																																																																							
Final CO	8/14/2026	12/15/2026		↓																																																																																																																																							
Final Completion	8/31/2026	12/15/2026		↓																																																																																																																																							
Owner Occupancy	8/31/2026	1/19/2027		↓																																																																																																																																							
Student Occupancy	8/31/2026	1/19/2027		↓																																																																																																																																							
Project Type New		Project Phase Construction		Scope Description																																																																																																																																							
Project Manager Penny Busch		Contractor/CM McCarthy Building Comp...		Construction of new Health Science Center, Frisco, Texas The building will be: 3 stories totaling 116,902 square feet 82,593 square feet to be finished out, 34,309 square feet to remain shell New Programs: MLT Radiography Cath Lab Nuclear Med CT Technology MRI Technology Programs Moving or Expanding: Nursing Diagnostic Sonography (program move from McKinney) Physical Therapy Assistant Health Professions Interdisciplinary Spaces: AR/VR Lab space Healthcare Simulation space																																																																																																																																							
Architect PBK Architects, Inc.		Project Directory																																																																																																																																									
<table border="1"> <thead> <tr> <th>Company</th> <th>Project Role</th> </tr> </thead> <tbody> <tr> <td>JQ Engineering (IMEG)</td> <td>Structural Engineer</td> </tr> <tr> <td>AECOM Technical Services, Inc.</td> <td>Program Manager</td> </tr> <tr> <td>Collin College</td> <td>Owner</td> </tr> <tr> <td>RWB Consulting Engineers</td> <td>MEP</td> </tr> <tr> <td>CCA Landscape Architects, Inc.</td> <td>Landscape Architect</td> </tr> <tr> <td>McCarthy Building Companies, Inc.</td> <td>Construction Manager-at-Risk</td> </tr> <tr> <td>RLK Engineering</td> <td>Civil Engineer</td> </tr> <tr> <td>PBK Architects, Inc.</td> <td>A/E</td> </tr> <tr> <td>PBK</td> <td></td> </tr> </tbody> </table>		Company	Project Role	JQ Engineering (IMEG)	Structural Engineer	AECOM Technical Services, Inc.	Program Manager	Collin College	Owner	RWB Consulting Engineers	MEP	CCA Landscape Architects, Inc.	Landscape Architect	McCarthy Building Companies, Inc.	Construction Manager-at-Risk	RLK Engineering	Civil Engineer	PBK Architects, Inc.	A/E	PBK		Progress Summary																																																																																																																					
Company	Project Role																																																																																																																																										
JQ Engineering (IMEG)	Structural Engineer																																																																																																																																										
AECOM Technical Services, Inc.	Program Manager																																																																																																																																										
Collin College	Owner																																																																																																																																										
RWB Consulting Engineers	MEP																																																																																																																																										
CCA Landscape Architects, Inc.	Landscape Architect																																																																																																																																										
McCarthy Building Companies, Inc.	Construction Manager-at-Risk																																																																																																																																										
RLK Engineering	Civil Engineer																																																																																																																																										
PBK Architects, Inc.	A/E																																																																																																																																										
PBK																																																																																																																																											
		<table border="1"> <thead> <tr> <th>Status Date</th> <th>Notes</th> </tr> </thead> <tbody> <tr> <td>2/27/2026</td> <td>Glazing frame installation in progress on north elevation</td> </tr> <tr> <td>2/27/2026</td> <td>Mechanical, electrical, and plumbing rough-in complete on first level, city approval pending</td> </tr> <tr> <td>2/27/2026</td> <td>Sheathing and waterproofing continues</td> </tr> </tbody> </table>				Status Date	Notes	2/27/2026	Glazing frame installation in progress on north elevation	2/27/2026	Mechanical, electrical, and plumbing rough-in complete on first level, city approval pending	2/27/2026	Sheathing and waterproofing continues																																																																																																																														
Status Date	Notes																																																																																																																																										
2/27/2026	Glazing frame installation in progress on north elevation																																																																																																																																										
2/27/2026	Mechanical, electrical, and plumbing rough-in complete on first level, city approval pending																																																																																																																																										
2/27/2026	Sheathing and waterproofing continues																																																																																																																																										
Cost Summary																																																																																																																																											
Budget Group	Original Budget	Current Budget	Commitments	Approved Changes	Total Commitments	Pending Commitments	Expended to Date																																																																																																																																				
Construction, Equipment & Furnishings	\$47,793,062.00	\$63,833,786.00	\$13,877,921.10	\$43,740,506.00	\$57,618,427.10	\$108,882.50	\$23,585,194.70																																																																																																																																				
Contingency	\$1,987,031.00	\$1,062,268.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00																																																																																																																																				
Investigation, Testing & Verification	\$777,028.00	\$777,028.00	\$420,227.00	\$0.00	\$420,227.00	\$0.00	\$145,478.80																																																																																																																																				
Management, Design & Pre-Construction	\$5,212,227.00	\$6,096,267.00	\$5,244,227.03	\$827,040.00	\$6,071,267.03	\$0.00	\$4,715,399.59																																																																																																																																				
Miscellaneous	\$44,652.00	\$44,652.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00																																																																																																																																				
Total	\$55,814,000.00	\$71,814,001.00	\$19,542,375.13	\$44,567,546.00	\$64,109,921.13	\$108,882.50	\$28,446,073.09																																																																																																																																				

Wylie CTE

Project Name Wylie CTE			 		Schedule						
Project Name Wylie CTE		Project Number PJ1068	Scope Description Construction of a new Career Technical Education (CTE) building on the Wylie Campus. - Approximately 66,000 square feet - Building will provide space for the following: - Welding - HVAC - Electronic Engineering Technology (EET) - Certified Nurse Aid (CNA)			Activity	Baseline Finish	Planned Finish	Actual Finish		
Project Type New		Project Phase Construction				BOT Approval of Construction Delivery Method	1/26/2024	1/26/2024	↑	1/26/2024	✓
Project Manager Kella Hilton	Contractor/CM Skanska	Architect Stantec Architecture (f...				BOT Approval of Program Manager	9/24/2024	9/24/2024	↑	9/24/2024	✓
Project Directory						BOT Approval of Recommended A/E and CMAR Firms	9/24/2024	9/24/2024	↑	9/24/2024	✓
Company	Project Role					Architect Mobilized	10/21/2024	10/21/2024	↑	11/11/2024	✓
AECOM Technical Services, Inc.						Programming	12/17/2024	4/30/2025	↓	4/30/2025	✓
Collin College						Schematic Design	2/18/2025	5/30/2025	↓	5/30/2025	✓
RWB Consulting Engineers						Design Development Drawings	4/22/2025	8/8/2025	↓	8/8/2025	✓
Skanska						100% Construction Documents	8/29/2025	10/10/2025	↓	10/12/2025	✓
Stantec Architecture (fka Page)						GMP - Submitted to AECOM/Page for Review	10/27/2025	12/12/2025	↓	12/17/2025	✓
						BOT Approval of GMP	12/9/2025	1/27/2026	↓	1/30/2026	✓
						Structures Complete	11/13/2026	11/13/2026	↑		
						Interior Finish-Out Complete	4/28/2027	5/18/2027	↓		
						Substantial Completion	5/3/2027	6/30/2027	↓		
						Final CO	5/14/2027	6/30/2027	↓		
						Final Completion	6/4/2027	7/30/2027	↓		
						Student Occupancy	8/25/2027	8/25/2027	↑		
						Progress Summary					
						Status Date	Notes				
						2/27/2026	Skanska Notice to Proceed issued. City of Wylie Preconstruction Meeting complete. Skanska to begin mobilization in March.				
Cost Summary											
Budget Group	Original Budget	Current Budget	Commitments	Approved Changes	Total Commitments	Pending Commitments	Expended to Date				
Construction, Equipment & Furnishings	\$34,700,000.00	\$46,631,590.00	\$0.00	\$0.00	\$0.00	\$0.00	\$1,100.00				
Contingency	\$1,066,490.00	\$2,100,731.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00				
Investigation, Testing & Verification	\$720,000.00	\$973,215.00	\$378,040.00	\$0.00	\$378,040.00	\$0.00	\$0.00				
Management, Design & Pre-Construction	\$3,481,510.00	\$4,318,521.00	\$3,884,640.00	\$5,650.00	\$3,890,290.00	\$0.00	\$2,001,192.68				
Miscellaneous	\$32,000.00	\$43,254.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00				
Total	\$40,000,000.00	\$54,067,311.00	\$4,262,680.00	\$5,650.00	\$4,268,330.00	\$0.00	\$2,002,292.68				

5 Completed Items

5.1 General Program

- Facilities Meeting held on February 3rd, 9th, and 27th

5.2 Procurement

- Wylie CTE, Skanska GMP Notice to Proceed has been issued.
- Wylie CTE, Braun Material Testing PO has been issued.

5.3 Design

- No Design items completed at this time.

5.4 Pre-Construction

- Wylie CTE, City of Wylie Preconstruction meeting with Collin College, AECOM, Skanska, and Stantec was completed February 27th

5.5 Construction

- Plano Campus provost meetings held between Collin College, AECOM, and Skanska on February 3rd, 4th, 6th, 10th, 11th, 13th, 17th, 18th, 20th, 24th, 25th, and 27th
- Plano Campus OAC meetings held on February 5th, 12th, 19th, and 26th
- CHEC OAC meetings held on February 5th, 12th, 19th, and 26th
- CHEC 4th Floor Graphics Wall Meeting was held on February 9th between Collin College, AECOM and Skanska
- Plano Campus Commercial Music Equipment Programing was held on February 9th between Collin College, AECOM, Skanska, and Lantek
- Plano Campus Kitchen Meeting was held on February 10th between Collin College, AECOM, and Skanska
- Plano Campus Owner Training Session for Fume Hoods and Safety Stations was held on February 13th between Collin College, AECOM, and Skanska
- CHEC Phase 3 Move Meeting was held between Collin College and AECOM on February 24th
- CHEC Phase 3 Punchlist was held between Collin College, IN2, AECOM and Skanska on February 26th
- Plano Campus, Review change events between Collin College and AECOM on February 2nd
- Plano Campus, Allowance and Contingency review meeting was held between AECOM and Skanska on February 4th, 11th, 18th, and 25th
- Plano Campus, Furniture Walk for 1st Floor E South was held between Collin College, AECOM and Skanska on February 4th
- Plano Campus, Dining Area Ceiling/Fire Sprinkler and E 1st Floor Review Structural Brace meeting was held between AECOM, IN2, Skanska and RWB on February 5th
- Plano Campus, Plumbing discussion was held between AECOM, Skanska and Mechanical Partners on February 23rd
- Plano Campus, Coordination meeting was held between Collin College and AECOM on February 24th
- Health Science Center, Review of Submittal/RFI log was held on February 2nd, 9th, 16th, and 23rd
- Health Science Center, OAC meetings held on February 4th, 11th, 18th, and 25th

- Health Science Center, Schedule Review Meeting was held between AECOM, PBK, and McCarthy on February 16th
- Health Science Center, AV/Network/Security/Data Drops coordination meeting was held between Collin College and AECOM on February 6th
- Wylie CTE, OAC meetings held on February 12th, 19th, and 26th
- Wylie CTE, Onsite coordination meeting with Stg. Shafer, Ken Mayfield, AECOM, Skanska, and Stantec to review existing security camera locations completed February 27th

5.6 Acceptance and Close-Out

- No Acceptance and Close-Out items were completed at this time.

6 Pending Items

6.1 General Program

- No General Program items are pending at this time.

6.2 Procurement

- Wylie CTE, Skanska GMP contract has been routed for review.

6.3 Design

- No Design items pending at this time.

6.4 Pre-Construction

- No Pre-Construction pending at this time

6.5 Construction

- Plano Campus, Roof work Punchlist underway. Courtyard MEP work finishing up getting to install equipment. Theater installing temp solution for the balcony make ready for performance in March. Comm. Music, construction ready to punch programming system. Welcome Center, Kitchen/ Dinning and E first floor work is continuing..
- Health Science Center, Sheathing and waterproofing install continues and expected to complete in March. Glazing frame install has started. Glass on site and glazing install to begin in March. Mechanical/Electrical/Plumbing finals to be obtained by first of March for first level. Mechanical/Electrical/Plumbing rough-in install continuing in second level.
- Courtyard Center, financial close out in progress. With pending paperwork remaining and auditor requirements.
- CHEC, Phase 3 Punchlist items to be addressed and TCO to be issued at the beginning of March.
- Wylie CTE, Skanska mobilization to begin in March

6.6 Acceptance and Close-Out

- Courtyard Center auditor comments in progress.

7 Progress Pictures

7.1 Plano Campus Renovations




Classrooms 1st Floor E




Fine Arts Courtyard Welding Booths



Fine Arts Courtyard

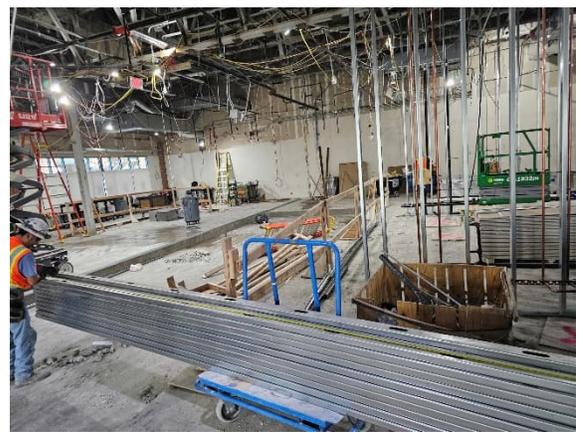

Kitchen Slab Depression for Cooler

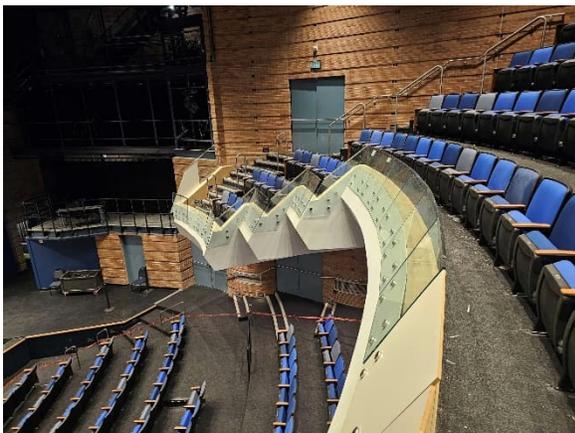

Theater Balcony



Welcome Center Millwork

7.2 Health Science Center




North Elevation – Sheathing, Waterproofing and Glazing Frame Installations




South Elevation – Sheathing and Waterproofing Installations



Mechanical Room

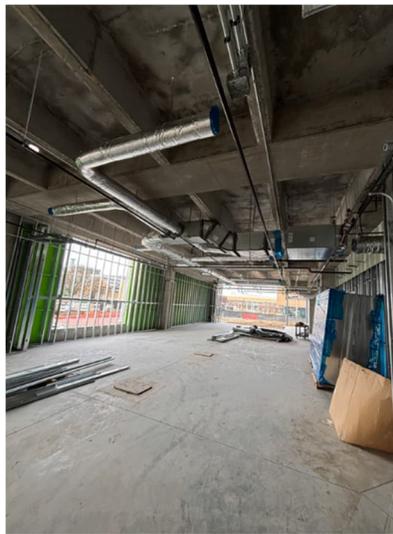

First Level – Cardio Sonography Skills

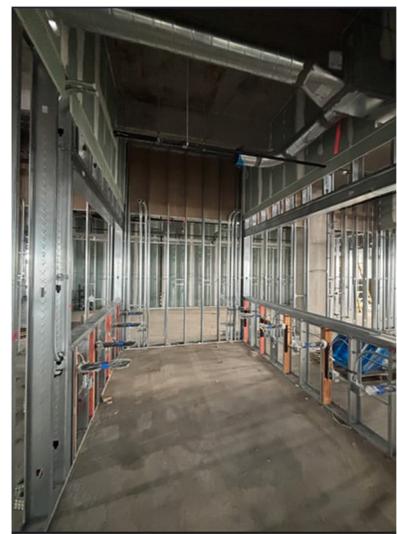

First Level - Control Room

7.3 CHEC




3rd Floor – Reception Area



3rd Floor – Phase 3 New Offices



4th Floor – Phase 3 New Offices

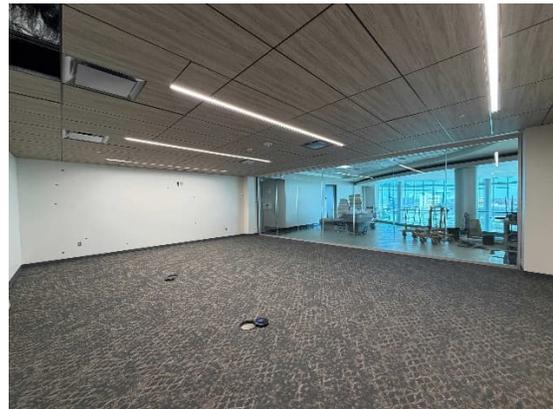

4th floor – Communications Conference Room
