



Boyceville Community School District

November 2025 Construction Update

Project Updates

PROJECT DATE

- Fall 2026

BUDGET

- \$18,000,000

INVOICED TO DATE

- \$8,682,038

CLIENT

- Boyceville Community School District


LOCATION

- 1003 Tiffany Street, Boyceville, WI 54725

PROJECT CONTACT

- Alex Larson

- Installation of exterior and vestibule doors continues at HS and TCE
- Interior hollow metal and wood door installation continues
- New wash sinks are installed at TCE
- New AC units arrived and were set on the roof at the MS/HS

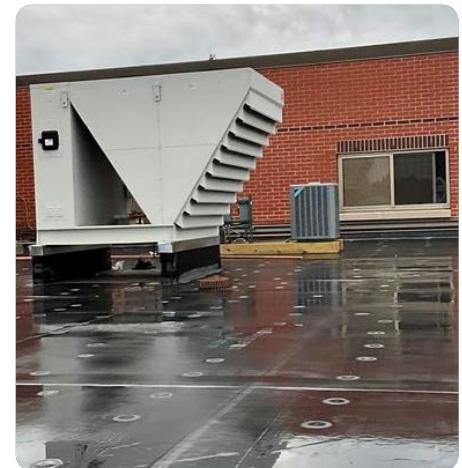

A construction update will be provided monthly by CESA 10 to communicate the project budget, recent work, and upcoming deliverables.
