



Ashland High School site wall concrete at the new raised lawn area in the quad!



## ASHLAND SCHOOL DISTRICT CAPITAL BOND PROGRAM

END OF MONTH REPORT – MAY 2025



## GENERAL PROGRAM UPDATE

Through the month of May, the Ashland High School Modernization project continued to progress through the closeout process. The primary points of focus through this part of the project include commissioning, demonstration and trainings and final punch work to resolve any outstanding issues or conclude open scopes of work.

The Science Building Seismic Retrofit project has been very active with areas of impact extending to every accessible space in order to be positioned for a successful summer completion. The shear wall footings and carpentry at the building perimeter are the most apparent points of progress. These surfaces are scheduled to receive siding starting in early June. The concrete formwork in the quad renovation is starting to hint at what the final layout will be with introduction of site wall elevations which add geometry to the new raised lawn areas.

With Summer break starting at the beginning of June, construction crews are eagerly prepared for full shift workdays and the next few months of unrestricted access. The next phase of this project will move quickly and provide gratifying daily progress. The project is on schedule for summer completion in big part due to the flexibility of AHS staff and students and their willingness to navigate construction enclosures for the early construction access. This will truly be the fundamental piece of the project schedule that ensures summer completion.

## PROJECT ADMINISTRATION

Project administration and accounting support are two key areas critical to Program success. This is a combined effort of HMK Company and ASD Accounting Department. In the month of May, we requested 1 additional purchase order and processed 9 invoices.

Contract Type	Number of Contracts	Value
Professional Service Agreements / Design Contracts	--	\$ 22,755,464
Construction Contracts	1	\$ 107,603,085



## LOCAL VENDORS AND CONTRACTORS

The following list of local vendors are currently working on the projects.

### ASHLAND AREA VENDORS and CONTRACTORS

Arkitek:design&architecture	Adroit Construction Co.
Ciota Engineering	DOBRIN
Covey Pardee Landscape Architecture	Infinity Electric
Douglas Engineering Pacific	Van Row Mechanical
HMK Company	Cascade Communications
KenCairn Landscape Architecture	Quality Fence
Bean Electric	Pacific 3D Reality Capture
Renfro	Welburn Electric
Pariani Land Surveying	Britannia
Powell Engineering	Patriot Landscaping
ZCS Engineering & Architecture	Sandeem Masonry
Beflor	Alco
Top Notch	Quality Fence
Sandeem Masonry	S&S Sheetmetal
Metal Masters	Urban Racks
Moore Construction	Curtis Huntley
Devry	Cut N' Break
Precision Electric	Advanced Air
Hall of Fame Movers	New Horizons Woodworks
Milestone Landscape Group	Viking Concrete Cutting
Figueroa's Landscaping & Construction	Artoff Construction
North Core Excavation	LLAD
Southern Oregon Painting Company	True South Solar
Pressure Point Roofing	

### Ashland Area, defined as Rogue Valley



## ASHLAND MIDDLE SCHOOL & TRAILS

### PROJECT ADDITION & RENOVATIONS TO EXISTING BUILDING

#### PROJECT DESCRIPTION

- New and renovated classroom space to replace 3 existing classroom wings, approx. 65,000 sq. ft.
- Campus security
- Air Quality improvements and Climate resilience for existing buildings, including new construction
- Required tech infrastructure

SCHEDULE & KEY MILESTONES	START	COMPLETION	% CPL	COMMENT
Pre-Design & Schematics	08/12/19	11/15/19	100%	
Design Development	12/09/19	02/28/20	100%	
Construction Documents	03/23/20	08/07/20	100%	
Bid and Award Site Package	10/27/20	11/02/20	100%	
Bid and Award Building Package	10/27/20	11/02/20	100%	
Construction	11/03/20	10/21/22	100%	
Substantial Completion	10/21/22	03/01/23	100%	
Owner Occupancy	08/24/22	10/31/22	100%	
Post Occupancy Evaluation	03/01/23	12/21/23	100%	
Warranty Period	03/01/23	03/01/24	100%	
Other			0%	

#### CURRENT ACTIVITIES

Ashland Middle School and TRAILS Outdoor School are complete, and staff and students are fully occupying the new spaces.

Throughout each campus, upgrades in HVAC systems, plumbing, and electrical are prevalent, introducing energy efficiency air quality improvements and climate resilience resulting in more accommodating environments for maximum learning opportunities. Each school has received upgraded windows, new roof systems, new restrooms and redesigned administrative/office spaces. The project also resulted in improvements to overall campus security, technology infrastructure, seismic upgrades and accessibility. Both schools have been retrofitted with fire alarm and fire suppression systems as well. Each school campus has its own vehicle entry and exit with clear-cut pick up and drop off areas to assist with reduced congestion during high traffic periods.



Ashland Middle School comprises about 40,000 sq. ft. of the project including a new library and addition of a newly constructed two-story 6<sup>th</sup> grade building with an elevator. The campus includes a leadership room with full kitchen designed to host campus events. The SPED area includes multiple classrooms and offices with an additional calming space, private restrooms, and secure outdoor learning area. The covered courtyard is central to the campus with a multifunctional design including reclaimed wood beam stadium style benches for outdoor educational purposes and skateboard accommodating features allowing students a safe and fresh outdoor space for various activities. The kitchen and cafeteria have also been upgraded with new appliances and renewed finishes.

TRAILS Outdoor School has an entirely separate, newly renovated building stretching across 26,000 sq. ft. of useable space. The campus now includes 5 classrooms, a library, art lab, testing room, SPED room, music facility and multi-purpose room. There is also a grand outdoor structure attached to the building, allowing activities in adverse weather, including an integrated rock-climbing wall. The multi-purpose room, also known as the community room, is the highlight of the building. This area not only provides a place for staff and students to congregate for events but is equipped with large windows and roll up doors that can be opened to connect to the outdoors. Designing this aspect of the multi-purpose room was fully intentional and a defining characteristic of the school culture. The adjacent ready room has a full kitchen, which accommodates preparation for outdoor activities as well as daily meal requirements.

## ACTIVITIES SCHEDULED FOR NEXT PERIOD

- Warranty Work

## ADDITIONAL INFORMATION

For questions, comments or additional information, please contact:

Josh Whitaker, Project Manager

[josh.whitaker@hmkco.org](mailto:josh.whitaker@hmkco.org)

541.601.3638





## PROJECT PHOTO GALLERY

### Combined Ashland Middle School and TRAILS Outdoor School Campus







## TRAILS Outdoor School







## Ashland Middle School







## HELMAN ELEMENTARY SCHOOL

### PROJECT ADDITION & RENOVATIONS TO EXISTING BUILDING

#### PROJECT DESCRIPTION

- New secure classroom wing to replace 2 classroom pods, approx. 23,000 sq. ft.
- Campus security
- Includes District Wide HVAC improvements which includes Climate resilience for all buildings, rather than just new construction
- Required tech infrastructure upgrades

SCHEDULE & KEY MILESTONES	START	COMPLETION	% CPL	COMMENT
Pre-Design & Schematics	06/17/19	01/23/20	100%	
Design Development	02/01/20	04/30/20	100%	
Construction Documents	05/14/20	09/24/20	100%	
Bid and Award Site Package	09/04/20	10/16/20	100%	
Bid and Award Building Package	10/15/20	12/15/20	100%	
Construction	10/30/20	08/31/22	100%	
Building Commissioning	06/01/22	03/31/23	100%	
Substantial Completion	08/31/22	03/01/23	100%	
Owner Occupancy	08/23/22	08/24/22	100%	
Post Occupancy Evaluation	03/02/23	08/01/23	100%	
Warranty Period	03/01/23	03/01/24	100%	
Other			0%	

#### CURRENT ACTIVITIES

With the completion of this project, Helman Elementary School staff, students and community members are now able to fully utilize the renovated campus. The renovations included a brand new approximately 23,000 square foot classroom building to replace two of the existing quad buildings.



The construction of this building has a net reduction in the school's energy use that truly models the Ashland School District's adoption of the City of Ashland's Climate and Energy Action Plan (CEAP). The new classroom building also includes a SPED instructional space with exterior play area, sensory room with state-of-the-art furnishings, a large multipurpose room with an operable exterior wall and multiple breakout spaces scattered throughout the building.

The front administration area underwent a full renovation that included an access-controlled entry. New reception area, conference room and staff work room concluded the new spaces included in the administration area.

Campus wide, a new 4-Pipe hydronic HVAC system that includes new high efficiency boilers, new air handlers and a new chiller was installed. A new building controls system, allowing the district to operate the new systems as efficiently as possible and minimize any maintenance or troubleshooting delays, was also included. The campus also received a new fire alarm system bringing everything up to current building codes.

On the exterior of the site, a new entry drive was installed that will aid with traffic congestion during high traffic periods. Additional parking was installed at the south end of the campus. There is a brand new 1/8<sup>th</sup> mile walking track and new playground that is accessible to all. New landscaping wraps up the remainder of the campus.

## ACTIVITIES SCHEDULED FOR NEXT PERIOD

- N/A

## ADDITIONAL INFORMATION

For questions, comments, or additional information, please contact:

Mike Freeman, Project Manager  
[Mike.freeman@hmkco.org](mailto:Mike.freeman@hmkco.org)  
541.499.7996



## PROJECT PHOTO GALLERY

### Completed Project







## ASHLAND HIGH SCHOOL

### PROJECT ASHLAND HIGH SCHOOL RENOVATION

#### PROJECT DESCRIPTION

- Improved accessibility and flexibility for the Humanities and Science Buildings.
- Repurpose or reconfigure existing spaces for science program requirements.
- Upgrades for air quality, security, restrooms, and technology infrastructure.
- Seismic rehabilitation at both Humanities and Science buildings

SCHEDULE & KEY MILESTONES	START	COMPLETION	% CPL	COMMENT
Pre-Design & Schematics	01/27/20	10/02/20	100%	
Design Development	10/02/20	01/29/21	100%	
Construction Documents	01/29/21	1/31/24	100%	
Permits, Bid and Award	05/31/23	3/29/24	100%	
Construction	06/16/23	12/31/24	98%	
Substantial Completion	12/31/24	12/31/24	92%	
Post Occupancy Evaluation	TBD	TBD	0%	
Warranty Period	01/01/25	01/01/26	0%	TBD
Other				

#### CURRENT ACTIVITIES

The Modernization project is on track to be completed in August. The delayed completion was anticipated due to limitations in timely procurement of electrical gear for the gym chiller system. KNO and their subcontractors have utilized the additional time to work through final punch related items and commissioning of systems that are complete. Contractor provided demonstration and trainings will be the final piece of closeout for this project.

May was the final month that construction activities are limited to off hours work for the Science Building Seismic Retrofit and quad renovation. The challenges of effectively navigating construction through these restricted conditions has proven to be worthwhile allowing Outlier Construction the opportunity to meet the demanding schedule for these scopes of work. The accommodations of AHS staff and students has proven to be the only opportunity to complete the seismic retrofit and quad renovations by the end of summer. While progress is very evident in with the exterior footings, shear walls, interior library work and quad upgrades, the summer push will increase drastically as work ramps up for full time shifts through August.



## ACTIVITIES SCHEDULED FOR NEXT PERIOD

- Excavation and prep for quad paver installation
- Completion of commissioning at the Humanities and Science Buildings
- Shear wall siding and finish at the Science Building exterior
- Final concrete wall form work pour in the quad

## ADDITIONAL INFORMATION

For questions, comments, or additional information, please contact:

Josh Whitaker, Project Manager

[josh.whitaker@hmkco.org](mailto:josh.whitaker@hmkco.org)

541.601.3638



## PROJECT PHOTO GALLERY

### New Shear Wall Framing at the Lower Level of the Science Building









## Concrete Formwork in The Quad





## Shearwall Framing in the Science Building Breezeway

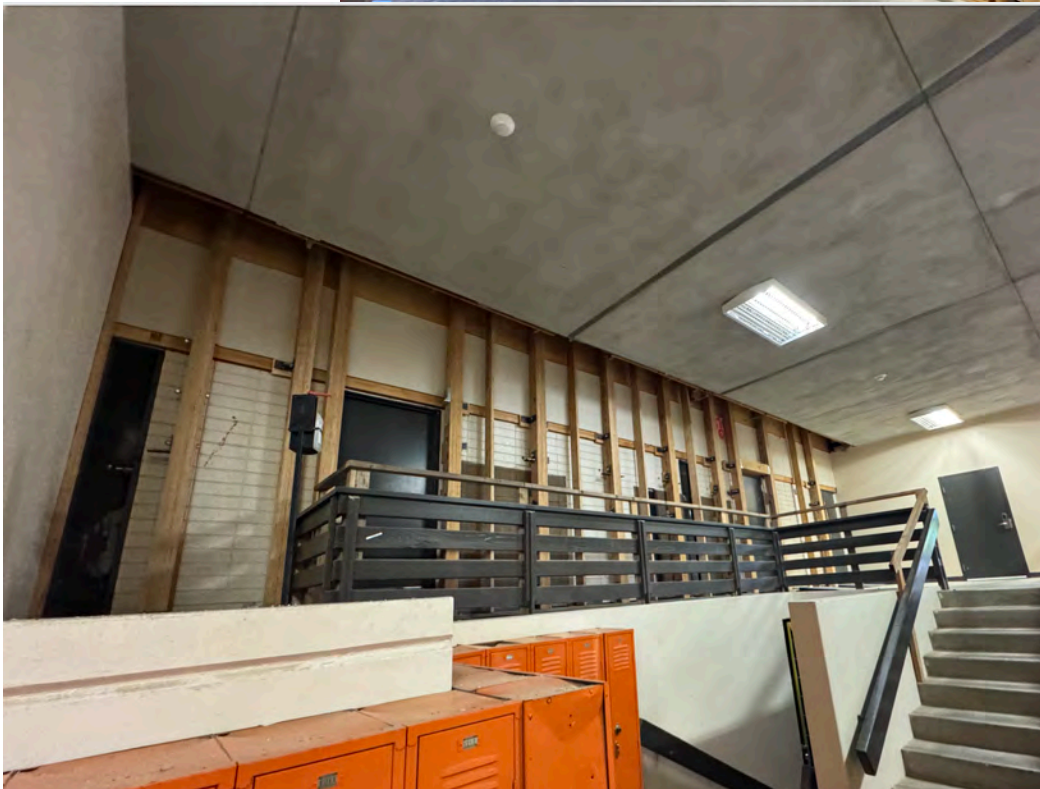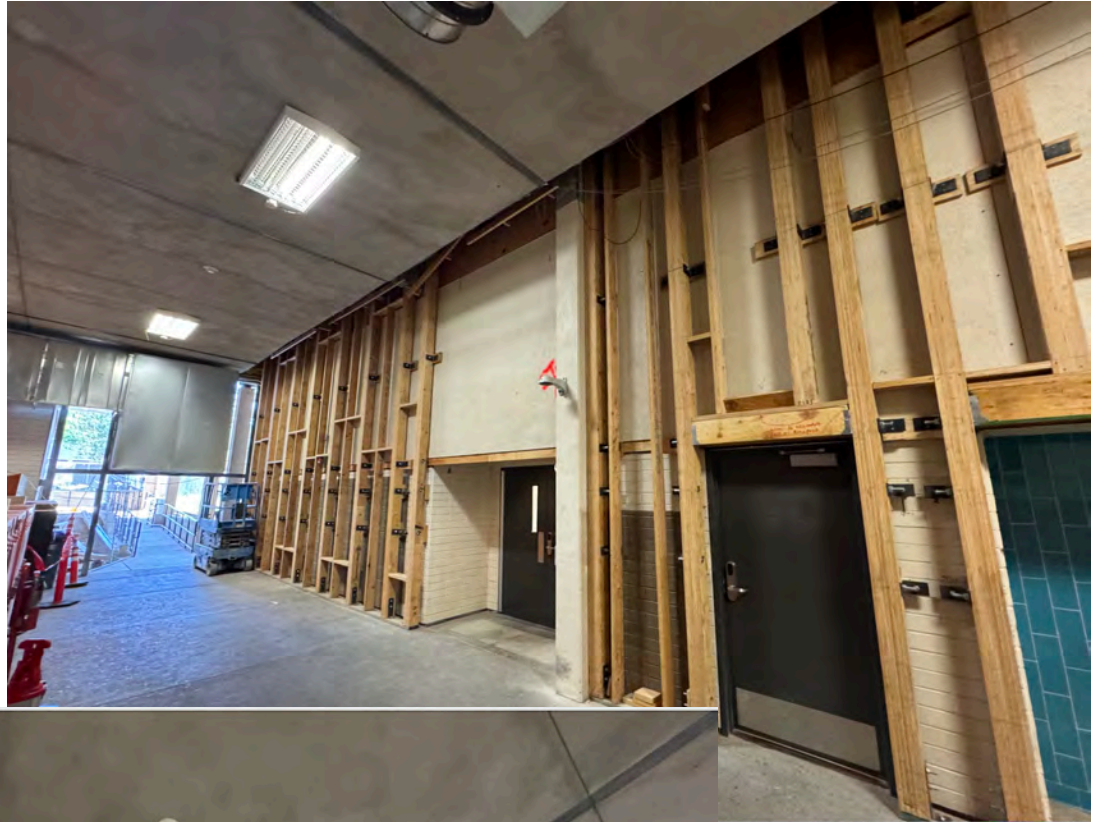





## WALKER ELEMENTARY SCHOOL

### PROJECT ADDITION & RENOVATIONS PROJECT

#### PROJECT DESCRIPTION

- Comprehensive renovation and seismic improvement of historic Walker Elementary School main building and gymnasium
- Includes replacement of classroom wing, with new classrooms, redesigned entry, new finishes, doors, windows and roof
- Also, includes the district wide HVAC improvements

SCHEDULE & KEY MILESTONES	START	COMPLETION	% CPL	COMMENT
Pre-Design & Schematics	01/07/20	09/22/20	100%	Complete
Design Development	09/22/20	12/10/20	100%	Complete
Construction Documents	12/10/20	08/13/21	100%	Complete
Bid and Award	03/22/21	05/14/21	100%	Complete
Construction Documents Phase 2	10/18/20	11/16/21	100%	Complete
Bid and Award Phase 2	03/22/21	12/14/21	100%	Complete
Construction	07/17/21	04/17/23	100%	Complete
Building Commissioning	01/16/23	04/17/23	100%	Complete
Owner Occupancy	04/17/23	04/18/23	100%	Complete
Post Occupancy Evaluation	04/18/23	07/17/23	100%	Complete
Warranty Period	04/18/23	04/18/24	100%	Complete
Other			0%	

#### CURRENT ACTIVITIES

The Walker Elementary School renovation is now complete. This project brought much needed improvements to the existing Walker School that will provide the community with a state-of-the-art educational facility for many years to come. The older classroom annex was demolished in order to construct a new classroom wing that also allowed the front entrance to be relocated creating a much more intuitive office space. The historical wing of the building received structural upgrades by way of a state funded seismic grant. The entire classroom building received new finishes, upgraded energy efficient exterior envelope that included new windows and new furniture.

The renovation and addition has a net reduction in the school's energy use that truly models the Ashland School District's adoption of the City of Ashland's Climate and Energy Action Plan (CEAP). The





new addition also includes a SPED instructional space with exterior play area, sensory room with state-of-the-art furnishings, dedicated resource rooms and multiple breakout spaces scattered throughout the building.

Campus wide, a new 4-Pipe hydronic HVAC system that includes new high efficiency boilers, new air handlers and a new chiller was installed. A new building controls system, allowing the district to operate the new systems as efficiently as possible and minimize any maintenance or troubleshooting delays, was also included. The campus also received a new fire alarm system bringing everything up to current building codes.

The gym underwent a seismic upgrade making this building now rated to withstand a seismic event. In addition, it received a new roof and exterior paint as well as HVAC upgrades.

The exterior of the site underwent extensive renovations in order to improve campus security and student and automobile circulation. The parking area was extended, and the traffic flow was reconfigured to create a more cohesive format for pick up and drop off that eases congestion in the neighborhood and adjoining streets. The exterior was fenced creating a secure campus and the newly configured front entrance added access control in order to create a single point of entrance. A new fully accessible playground was installed as well. New landscaping wraps up the exterior improvements.

## ACTIVITIES SCHEDULED FOR NEXT PERIOD

- N/A

## HIGHLIGHTS, CHALLENGES, SOLUTIONS

### HIGHLIGHTS:

- Project completion.

### CHALLENGES:

- No current challenges to note.

## ADDITIONAL INFORMATION

For questions, comments, or additional information, please contact:

Josh Whitaker, Project Manager

[josh.whitaker@hmkco.org](mailto:josh.whitaker@hmkco.org)

541.601.3638



## PROJECT PHOTO GALLERY

### Aerial Photos of New Renovation and Addition









Placard Depicting the Seismic Upgrade through the Oregon Seismic Rehabilitation Grant





**ASHLAND SCHOOL DISTRICT  
CAPITAL CONSTRUCTION  
DISTRICT WIDE ROLLUP BUDGET  
MAY 31, 2025**

<b>Project Expense</b>	<b>Original Budget</b>	<b>Paid to Date</b>	<b>Remaining Balance</b>	<b>Revised Budget</b>
<b>Hard Cost</b>				
Technology	\$ 3,420,000	\$ 3,912,749	\$ (513,525)	\$ 3,399,224
Restrooms	\$ 3,087,500	\$ -	\$ -	\$ -
Security	\$ 2,850,000	\$ 299,527	\$ 7,415	\$ 306,942
HVAC & MEP	\$ 13,569,000	\$ -	\$ -	\$ -
Transportation	\$ -	\$ 559,844	\$ 1	\$ 559,845
Bellview	\$ -	\$ 1,590,709	\$ 106,573	\$ 1,697,282
Maintenance	\$ -	\$ 676,982	\$ -	\$ 676,982
District Office	\$ -	\$ -	\$ -	\$ -
Asbestos Abatement	\$ 316,447	\$ -	\$ -	\$ -
Construction Contingency	\$ 1,348,640	\$ -	\$ 300,769	\$ 300,769
<b>Construction Sub Total</b>	<b>\$ 24,591,587</b>	<b>\$ 7,039,811</b>	<b>\$ (98,767)</b>	<b>\$ 6,941,044</b>
<b>Soft Cost</b>				
<b>Administrative Cost</b>				
Legal Fees	\$ 35,000	\$ -	\$ -	\$ -
Bond Counsel	\$ -	\$ -	\$ -	\$ -
Bond Issuance Cost	* \$ -	\$ -	\$ -	\$ -
Builders Risk Insurance	\$ -	\$ -	\$ -	\$ -
Project Management	** \$ 733,063	\$ -	\$ -	\$ -
Reimbursable Expenses	** \$ 48,870	\$ -	\$ -	\$ -
Communications	\$ -	\$ -	\$ -	\$ -
Sustainability	\$ -	\$ -	\$ -	\$ -
<b>Site Cost</b>				
Site Survey	\$ 30,000	\$ 2,270	\$ 30,000	\$ 32,270
Geo-Tech Report	\$ -	\$ -	\$ -	\$ -
<b>Planning Cost</b>				
Design Fees	\$ 2,026,632	\$ 117,637	\$ 164,421	\$ 282,058
A & E Reimbursable Expenses	\$ 41,670	\$ -	\$ 10,000	\$ 10,000
Commissioning	\$ 145,267	\$ 183,995	\$ (15,995)	\$ 168,000
Printing & Plan Distribution	\$ 9,416	\$ -	\$ -	\$ -
Hazardous Materials Consultant	\$ 138,808	\$ 20,890	\$ 460	\$ 21,350
Construction Testing	\$ -	\$ -	\$ -	\$ -
Constructability Review	\$ 72,634	\$ -	\$ -	\$ -
Plan Review & Building Permits	\$ 250,971	\$ 60,724	\$ 46,754	\$ 107,478
Special Inspection and Testing	\$ 50,053	\$ -	\$ 21,000	\$ 21,000
Miscellaneous Fees	\$ -	\$ 43,513	\$ (11,213)	\$ 32,300
Ed Specs	\$ -	\$ -	\$ -	\$ -
Kitchen	\$ -	\$ -	\$ -	\$ -
<b>Miscellaneous</b>				
Legal Advertisements	\$ 4,823	\$ 1,217	\$ 3,690	\$ 4,907
Furniture, Fixtures, and Equipment (FF&E)	\$ -	\$ 7,631	\$ 17,369	\$ 25,000
Technology	\$ -	\$ 40,623	\$ 377	\$ 41,000
Technology (Design)	\$ 210,634	\$ 1,847	\$ 26,830	\$ 28,677
Acoustics	\$ 36,317	\$ -	\$ -	\$ -
Criminal Background Checks	\$ 3,162	\$ -	\$ -	\$ -
System Development Charges	\$ -	\$ -	\$ -	\$ -
Value Engineering	\$ 72,634	\$ -	\$ -	\$ -
Utility Connection Fee	\$ 116,214	\$ -	\$ -	\$ -
Unallocated Owner Contingency	\$ 2,964,431	\$ -	\$ 37,587	\$ 37,587
Inflation	\$ 1,885,566	\$ -	\$ 74,433	\$ 74,433
<b>Sub Total Soft Cost</b>	<b>\$ 8,876,165</b>	<b>\$ 480,347</b>	<b>\$ 405,713</b>	<b>\$ 886,060</b>
<b>Total Project Cost</b>	<b>\$ 33,467,752</b>	<b>\$ 7,520,159</b>	<b>\$ 306,946</b>	<b>\$ 7,827,104</b>

\* Budget has been moved to the Project Level

\*\*Budget has been moved to the Program Level



**ASHLAND SCHOOL DISTRICT  
CAPITAL CONSTRUCTION  
PROGRAM LEVEL BUDGET  
MAY 31, 2025**

<b>Program Revenue <sup>1</sup></b>	<b>Original Budget</b>	<b>Received to Date</b>	<b>Allocated to Date</b>	<b>Unallocated Balance</b>	<b>Revised Budget</b>
<b>Bond and Other Proceeds</b>					
Bond Proceeds	\$ 107,380,000	\$ 107,380,000	\$ 107,380,000	\$ -	\$ 107,380,000
Bond Premium	\$ 22,436,690	\$ 22,436,690	\$ 20,743,997	\$ 1,692,692	\$ 22,436,690
OSCM Grant (Ashland Middle School)	\$ 1,032,927	\$ 4,000,000	\$ 4,000,000	\$ -	\$ 4,000,000
Seismic (Walker)	\$ 2,500,000	\$ 2,497,447	\$ 2,497,447	\$ -	\$ 2,497,447
Seismic (Walker-Gymnasium)	\$ -	\$ 1,816,151	\$ 1,816,151	\$ -	\$ 1,816,151
Seismic (Ashland High School)	\$ -	\$ 2,011,704	\$ 2,011,704	\$ -	\$ 2,011,704
Seismic (Ashland High School Science)	\$ -	\$ -	\$ 2,500,000	\$ -	\$ 2,500,000
Investment Interest	\$ 5,000,000	\$ 5,919,485	\$ 4,628,566	\$ 1,290,919	\$ 5,919,485
Miscellaneous	\$ -	\$ 428,941	\$ -	\$ 428,941	\$ 428,941
<b>Total Revenue</b>	<b>\$ 138,349,617</b>	<b>\$ 146,490,418</b>	<b>\$ 145,577,865</b>	<b>\$ 3,412,552</b>	<b>\$ 148,990,418</b>

1. Program Revenue is an estimate. Accuracy should be verified by district personnel

The financial statement presentation has been prepared as a courtesy by HMK. They are based on information derived from ledgers provided by the agency, which have not been independently verified. The financial information included in this presentation is unaudited and should be used for informational purposes only and should not be relied upon for any other use.





**ASHLAND SCHOOL DISTRICT  
CAPITAL CONSTRUCTION  
PROGRAM BUDGET  
MAY 31, 2025**

	Original Budget	Paid to Date	Remaining Balance	Revised Budget
<b>Program Expense</b>				
District Wide Programs	\$ 24,591,587	\$ 7,039,811	\$ (98,767)	\$ 6,941,044
District Wide Solar Projects	\$ -	\$ 931,886	\$ 718,912	\$ 1,650,798
Helman Elementary	\$ 11,294,084	\$ 15,367,756	\$ (232,685)	\$ 15,135,071
Walker Elementary	\$ 11,252,185	\$ 30,130,377	\$ 87,160	\$ 30,217,537
Ashland Middle School	\$ 21,960,270	\$ 35,813,522	\$ (366,146)	\$ 35,447,376
Ashland High School	\$ 9,124,089	\$ 24,629,279	\$ 2,987,810	\$ 27,617,089
Willow Wind Learning Center	\$ -	\$ 1,732,696	\$ 1,732	\$ 1,734,428
<b>Construction Sub Total</b>	<b>\$ 78,222,215</b>	<b>\$ 115,645,327</b>	<b>\$ 3,098,016</b>	<b>\$ 118,743,343</b>
<b>Soft Cost</b>				
<b>Administrative Cost</b>				
Legal Fees	\$ 100,000	\$ 29,844	\$ (6,430)	\$ 23,414
Bond Counsel	\$ -	\$ -	\$ -	\$ -
Bond Issuance Cost	\$ 625,293	\$ 625,293	\$ -	\$ 625,293
Builders Risk Insurance	\$ -	\$ 80,126	\$ (7,926)	\$ 72,200
Project Management	\$ 2,274,483	\$ 4,637,321	\$ (628,457)	\$ 4,008,864
Reimbursable Expenses	\$ 151,631	\$ 328,755	\$ (1,788)	\$ 326,967
Communications	\$ -	\$ 199,367	\$ (6,095)	\$ 193,272
Sustainability	\$ -	\$ -	\$ -	\$ -
Miscellaneous Fees (Bank, consulting)	\$ -	\$ 415,083	\$ (109,434)	\$ 305,649
Ashland SD Staff	\$ -	\$ 1,322,706	\$ (465,070)	\$ 857,636
Lincoln Elementary	\$ -	\$ 42,354	\$ 446	\$ 42,800
District Wide Roofing Project	\$ -	\$ 46,200	\$ -	\$ 46,200
<b>Site Cost</b>				
Site Survey	\$ 213,903	\$ 149,234	\$ 8,489	\$ 157,723
Geo-Tech Report	\$ 123,179	\$ 111,151	\$ 13,583	\$ 124,734
<b>Planning Cost</b>				
Design Fees	\$ 7,414,694	\$ 8,595,418	\$ (415,617)	\$ 8,179,800
A & E Reimbursable Expenses	\$ 144,431	\$ 35,420	\$ 81,103	\$ 116,523
Commissioning	\$ 334,589	\$ 393,279	\$ (32,970)	\$ 360,309
Printing & Plan Distribution	\$ 31,288	\$ 1,724	\$ 55	\$ 1,779
Hazardous Materials Consultant	\$ 418,761	\$ 560,005	\$ (84,149)	\$ 475,856
Construction Testing	\$ -	\$ -	\$ -	\$ -
Constructability Review	\$ 285,616	\$ 573,003	\$ 470	\$ 573,473
Plan Review & Building Permits	\$ 764,778	\$ 3,355,949	\$ 161,265	\$ 3,517,213
Special Inspection and Testing	\$ 391,469	\$ 899,276	\$ (358,571)	\$ 540,705
Miscellaneous Fees	\$ 205,522	\$ 1,060,432	\$ (218,228)	\$ 842,204
Ed Specs	\$ 73,532	\$ -	\$ -	\$ -
Kitchen	\$ 32,940	\$ -	\$ -	\$ -
<b>Miscellaneous</b>				
Legal Advertisements	\$ 12,823	\$ 1,457	\$ 5,450	\$ 6,907
Furniture, Fixtures, and Equipment (FF&E)	\$ 2,569,031	\$ 2,666,350	\$ 72,489	\$ 2,738,839
Technology	\$ 404,005	\$ 466,937	\$ 20,763	\$ 487,700
Technology (Design)	\$ 467,536	\$ 7,252	\$ 63,223	\$ 70,475
Acoustics	\$ 113,387	\$ -	\$ -	\$ -
Criminal Background Checks	\$ 9,862	\$ 12,213	\$ (130)	\$ 12,083
System Development Charges	\$ 332,544	\$ 19,692	\$ (600)	\$ 19,092
Value Engineering	\$ 194,985	\$ -	\$ -	\$ -
Utility Connection Fee	\$ 116,214	\$ -	\$ -	\$ -
Unallocated Owner Contingency	\$ 9,104,657	\$ -	\$ 38,849	\$ 38,849
Inflation	\$ 6,111,120	\$ -	\$ 74,433	\$ 74,433
<b>Sub Total Soft Cost</b>	<b>\$ 33,022,273</b>	<b>\$ 26,635,840</b>	<b>\$ (1,794,848)</b>	<b>\$ 24,840,992</b>
<b>Total Project Cost</b>	<b>\$ 111,244,488</b>	<b>\$ 142,281,167</b>	<b>\$ 1,303,168</b>	<b>\$ 143,584,335</b>



**ASHLAND SCHOOL DISTRICT  
CAPITAL CONSTRUCTION  
PROGRAM LEVEL BUDGET  
MAY 31, 2025**

		Original Budget	Paid to Date	Remaining Balance	Revised Budget
<b>Program Expense</b>					
<b>Soft Cost</b>					
Legal Fees		\$ -	\$ 26,896	\$ (3,482)	\$ 23,414
Bond Counsel		\$ -	\$ -	\$ -	\$ -
Bond Issuance Cost		\$ 625,293	\$ 625,293	\$ -	\$ 625,293
Builders Risk Insurance		\$ -	\$ -	\$ -	\$ -
Project Management	12	\$ -	\$ 4,275,868	\$ (307,004)	\$ 3,968,864
Reimbursable Expenses	11	\$ -	\$ 311,211	\$ 356	\$ 311,567
Communications	11	\$ -	\$ 199,367	\$ (6,095)	\$ 193,272
Sustainability		\$ -	\$ -	\$ -	\$ -
Criminal Background Checks	10,11	\$ -	\$ 12,213	\$ (130)	\$ 12,083
Printing & Plan Distribution	10	\$ -	\$ 779	\$ -	\$ 779
Miscellaneous Fees (Bank, consulting)	11	\$ -	\$ 415,083	\$ (109,434)	\$ 305,649
Ashland SD Staff	11,12	\$ -	\$ 1,322,706	\$ (465,070)	\$ 857,636
Lincoln Elementary		\$ -	\$ 42,354	\$ 446	\$ 42,800
District Wide Roofing Project		\$ -	\$ 46,200	\$ -	\$ 46,200
<b>Sub Total Soft Cost</b>		<b>\$ 625,293</b>	<b>\$ 7,277,969</b>	<b>\$ (890,412)</b>	<b>\$ 6,387,557</b>

1. Reallocated within budget
2. Reallocated within budget (06.30.21)
3. Reallocated within budget (03.31.22)
4. Reallocated Bond Issuance Costs back to Program Level (06.30.22)
5. Reallocated within budget (06.30.22)
6. Reallocated from investment for add'l staff time (08.31.22)
7. Reallocated from investment income and budget (09.30.22)
8. Reallocated within budget (10.31.22)
9. Reallocated within budget (12.31.22)
10. Reallocated within budget (01.31.23)
11. Reallocated \$360k from Security (04.30.23)
12. Reallocated within budget (05.31.23)

Intentionally left blank. Do not delete!





**ASHLAND SCHOOL DISTRICT  
CAPITAL CONSTRUCTION  
DW RESTROOMS BUDGET  
MAY 31, 2025**

		Original Budget	Paid to Date	Remaining Balance	Revised Budget
<b>Project Expense</b>					
<b>Hard Cost</b>					
Maximum Allowable Construction Cost (MACC)	2	\$ 3,087,500	\$ -	\$ -	\$ -
Asbestos		\$ 58,705	\$ -	\$ -	\$ -
Seismic Retro Upgrade		\$ -	\$ -	\$ -	\$ -
1.5% Solar (Total Project Major Building)		\$ -	\$ -	\$ -	\$ -
Construction Contingency	2	\$ 162,500	\$ -	\$ -	\$ -
<b>Construction Sub Total</b>		<b>\$ 3,308,705</b>	<b>\$ -</b>	<b>\$ -</b>	<b>\$ -</b>
<b>Soft Cost</b>					
<b>Administrative Cost</b>					
Legal Fees		\$ 5,000	\$ -	\$ -	\$ -
Bond Counsel		\$ -	\$ -	\$ -	\$ -
Bond Issuance Cost		\$ -	\$ -	\$ -	\$ -
Builders Risk Insurance	3	\$ -	\$ -	\$ -	\$ -
Project Management		\$ 99,261	\$ -	\$ -	\$ -
Reimbursable Expenses		\$ 6,617	\$ -	\$ -	\$ -
Communications		\$ -	\$ -	\$ -	\$ -
Sustainability		\$ -	\$ -	\$ -	\$ -
<b>Site Cost</b>					
Site Survey		\$ -	\$ -	\$ -	\$ -
Geo-Tech Report		\$ -	\$ -	\$ -	\$ -
<b>Planning Cost</b>					
Design Fees	2	\$ 363,958	\$ -	\$ -	\$ -
A & E Reimbursable Expenses	2	\$ 6,617	\$ -	\$ -	\$ -
Commissioning		\$ -	\$ -	\$ -	\$ -
Printing & Plan Distribution		\$ 2,316	\$ -	\$ -	\$ -
Hazardous Materials Consultant	2	\$ 66,174	\$ -	\$ -	\$ -
Construction Testing		\$ -	\$ -	\$ -	\$ -
Constructability Review		\$ -	\$ -	\$ -	\$ -
Plan Review & Building Permits	2	\$ 39,704	\$ -	\$ -	\$ -
Special Inspection and Testing		\$ -	\$ -	\$ -	\$ -
Miscellaneous Fees		\$ -	\$ -	\$ -	\$ -
Ed Specs		\$ -	\$ -	\$ -	\$ -
Kitchen		\$ -	\$ -	\$ -	\$ -
<b>Miscellaneous</b>					
Legal Advertisements	2	\$ 1,323	\$ -	\$ -	\$ -
Furniture, Fixtures, and Equipment (FF&E)		\$ -	\$ -	\$ -	\$ -
Technology		\$ -	\$ -	\$ -	\$ -
Technology (Design)		\$ -	\$ -	\$ -	\$ -
Acoustics		\$ -	\$ -	\$ -	\$ -
Criminal Background Checks		\$ 662	\$ -	\$ -	\$ -
System Development Charges		\$ -	\$ -	\$ -	\$ -
Value Engineering		\$ -	\$ -	\$ -	\$ -
Utility Connection Fee		\$ -	\$ -	\$ -	\$ -
Unallocated Owner Contingency	2	\$ 413,588	\$ -	\$ -	\$ -
Inflation		\$ 258,837	\$ -	\$ -	\$ -
<b>Sub Total Soft Cost</b>		<b>\$ 1,264,057</b>	<b>\$ -</b>	<b>\$ -</b>	<b>\$ -</b>
<b>Total Project Cost</b>		<b>\$ 4,572,762</b>	<b>\$ -</b>	<b>\$ -</b>	<b>\$ -</b>

1. Reallocated \$750,000 to AHS (07.31.21)
1. Reallocated \$641,400 to AHS (07.31.21)
1. Reallocated \$1,100,040 to AMS (07.31.21)
2. Reallocated \$ 684,164 to AHS (09.30.21)
3. Reallocated Bond Issuance Costs back to Program Level (06.30.22)



**ASHLAND SCHOOL DISTRICT  
CAPITAL CONSTRUCTION  
DW SECURITY BUDGET  
MAY 31, 2025**

Project Expense		Original Budget	Paid to Date	Remaining Balance	Revised Budget
Hard Cost					
Maximum Allowable Construction Cost (MACC)	10	\$ 2,850,000	\$ 299,527	\$ 7,415	\$ 306,942
Asbestos		\$ -	\$ -	\$ -	\$ -
Seismic Retro Upgrade		\$ -	\$ -	\$ -	\$ -
1.5% Solar (Total Project Major Building)		\$ -	\$ -	\$ -	\$ -
Construction Contingency		\$ 150,000	\$ -	\$ 137,207	\$ 137,207
<b>Construction Sub Total</b>		<b>\$ 3,000,000</b>	<b>\$ 299,527</b>	<b>\$ 144,622</b>	<b>\$ 444,149</b>
Soft Cost					
Administrative Cost					
Legal Fees		\$ 5,000	\$ -	\$ -	\$ -
Bond Counsel		\$ -	\$ -	\$ -	\$ -
Bond Issuance Cost		\$ -	\$ -	\$ -	\$ -
Builders Risk Insurance		\$ -	\$ -	\$ -	\$ -
Project Management		\$ 90,000	\$ -	\$ -	\$ -
Reimbursable Expenses		\$ 6,000	\$ -	\$ -	\$ -
Communications		\$ -	\$ -	\$ -	\$ -
Sustainability		\$ -	\$ -	\$ -	\$ -
Site Cost					
Site Survey		\$ 30,000	\$ -	\$ 30,000	\$ 30,000
Geo-Tech Report		\$ -	\$ -	\$ -	\$ -
Planning Cost					
Design Fees		\$ 210,000	\$ -	\$ 171,500	\$ 171,500
A & E Reimbursable Expenses		\$ 6,000	\$ -	\$ -	\$ -
Commissioning		\$ -	\$ -	\$ -	\$ -
Printing & Plan Distribution		\$ 2,100	\$ -	\$ -	\$ -
Hazardous Materials Consultant		\$ -	\$ -	\$ -	\$ -
Construction Testing		\$ -	\$ -	\$ -	\$ -
Constructability Review		\$ -	\$ -	\$ -	\$ -
Plan Review & Building Permits		\$ 30,000	\$ -	\$ 18,000	\$ 18,000
Special Inspection and Testing		\$ 21,000	\$ -	\$ 21,000	\$ 21,000
Miscellaneous Fees		\$ -	\$ -	\$ -	\$ -
Ed Specs		\$ -	\$ -	\$ -	\$ -
Kitchen		\$ -	\$ -	\$ -	\$ -
Miscellaneous					
Legal Advertisements		\$ 1,000	\$ -	\$ -	\$ -
Furniture, Fixtures, and Equipment (FF&E)		\$ -	\$ -	\$ -	\$ -
Technology		\$ -	\$ -	\$ -	\$ -
Technology (Design)		\$ 30,000	\$ -	\$ 27,000	\$ 27,000
Acoustics		\$ -	\$ -	\$ -	\$ -
Criminal Background Checks		\$ 500	\$ -	\$ -	\$ -
System Development Charges		\$ -	\$ -	\$ -	\$ -
Value Engineering		\$ -	\$ -	\$ -	\$ -
Utility Connection Fee		\$ -	\$ -	\$ -	\$ -
Unallocated Owner Contingency	6	\$ 375,000	\$ -	\$ 10,852	\$ 10,852
Inflation	7,8,9,10	\$ 228,396	\$ -	\$ 74,433	\$ 74,433
<b>Sub Total Soft Cost</b>		<b>\$ 1,034,996</b>	<b>\$ -</b>	<b>\$ 352,785</b>	<b>\$ 352,785</b>
<b>Total Project Cost</b>		<b>\$ 4,034,996</b>	<b>\$ 299,527</b>	<b>\$ 497,407</b>	<b>\$ 796,934</b>

1. Reallocated \$350,000 to new projects (transportation, bellview, maintenance, and district office)
2. Reallocated \$2,000,000 to AHS ( 09.30.21)
3. Reallocated Bond Issuance Costs back to Program Level (06.30.22)
4. Reallocated \$50k from Security to Transportation and \$40k to AMS (06.30.22)
5. Reallocated \$24k from Security to Maintenance (08.31.22)
6. Reallocated \$89k from Security to BES for Sentinel (03.31.23)
7. Reallocated \$26k from Security to AMS for Ednetics (03.31.23)
8. Reallocated \$24k from Security to Maintenance for Ednetics (03.31.23)
9. Reallocated \$17k from Security to Transportation for Ednetics(03.31.23)
10. Reallocated \$360k from Security to Program Level (04.30.23)



**ASHLAND SCHOOL DISTRICT  
CAPITAL CONSTRUCTION  
DW HVAC & MEP BUDGET  
MAY 31, 2025**

Project Expense		Original Budget	Paid to Date	Remaining Balance	Revised Budget
<b>Hard Cost</b>					
Maximum Allowable Construction Cost (MACC)	3	\$ 13,569,000	\$ -	\$ -	\$ -
Asbestos		\$ 257,742	\$ -	\$ -	\$ -
Seismic Retro Upgrade			\$ -	\$ -	\$ -
1.5% Solar (Total Project Major Building)			\$ -	\$ -	\$ -
Construction Contingency	3	\$ 856,140	\$ -	\$ -	\$ -
<b>Construction Sub Total</b>		<b>\$ 14,682,882</b>	<b>\$ -</b>	<b>\$ -</b>	<b>\$ -</b>
<b>Soft Cost</b>					
<b>Administrative Cost</b>					
Legal Fees		\$ 20,000	\$ -	\$ -	\$ -
Bond Counsel		\$ -	\$ -	\$ -	\$ -
Bond Issuance Cost		\$ -	\$ -	\$ -	\$ -
Builders Risk Insurance	5	\$ -	\$ -	\$ -	\$ -
Project Management		\$ 435,802	\$ -	\$ -	\$ -
Reimbursable Expenses		\$ 29,053	\$ -	\$ -	\$ -
Communications		\$ -	\$ -	\$ -	\$ -
Sustainability		\$ -	\$ -	\$ -	\$ -
<b>Site Cost</b>					
Site Survey		\$ -	\$ -	\$ -	\$ -
Geo-Tech Report		\$ -	\$ -	\$ -	\$ -
<b>Planning Cost</b>					
Design Fees	3	\$ 1,452,674	\$ -	\$ -	\$ -
A & E Reimbursable Expenses	3	\$ 29,053	\$ -	\$ -	\$ -
Commissioning	3	\$ 145,267	\$ -	\$ -	\$ -
Printing & Plan Distribution		\$ 5,000	\$ -	\$ -	\$ -
Hazardous Materials Consultant	3	\$ 72,634	\$ -	\$ -	\$ -
Construction Testing		\$ -	\$ -	\$ -	\$ -
Constructability Review	3	\$ 72,634	\$ -	\$ -	\$ -
Plan Review & Building Permits	3	\$ 145,267	\$ -	\$ -	\$ -
Special Inspection and Testing	3	\$ 29,053	\$ -	\$ -	\$ -
Miscellaneous Fees		\$ -	\$ -	\$ -	\$ -
Ed Specs		\$ -	\$ -	\$ -	\$ -
Kitchen		\$ -	\$ -	\$ -	\$ -
<b>Miscellaneous</b>					
Legal Advertisements		\$ 1,500	\$ -	\$ -	\$ -
Furniture, Fixtures, and Equipment (FF&E)		\$ -	\$ -	\$ -	\$ -
Technology		\$ -	\$ -	\$ -	\$ -
Technology (Design)		\$ 72,634	\$ -	\$ -	\$ -
Acoustics	3	\$ 36,317	\$ -	\$ -	\$ -
Criminal Background Checks		\$ 1,000	\$ -	\$ -	\$ -
System Development Charges		\$ -	\$ -	\$ -	\$ -
Value Engineering	3	\$ 72,634	\$ -	\$ -	\$ -
Utility Connection Fee	3	\$ 116,214	\$ -	\$ -	\$ -
Unallocated Owner Contingency	4	\$ 1,815,843	\$ -	\$ -	\$ -
Inflation	4	\$ 1,144,761	\$ -	\$ -	\$ -
<b>Sub Total Soft Cost</b>		<b>\$ 5,697,340</b>	<b>\$ -</b>	<b>\$ -</b>	<b>\$ -</b>
<b>Total Project Cost</b>		<b>\$ 20,380,222</b>	<b>\$ -</b>	<b>\$ -</b>	<b>\$ -</b>

2. Reallocated \$165,000 to AMS for HVAC upgrade (06.01.21)
3. Reallocated \$1,310,000 to AHS (07.01.21)
3. Reallocated \$7,100,000 to AHS -Phase II (07.01.21)
3. Reallocated \$475,000 to AHS -Phase II (07.01.21)
3. Reallocated \$972,316 to AHS -Phase II (07.01.21)
4. Reallocated \$486,606 to WES (02.28.22)
5. Reallocated Bond Issuance Costs back to Program Level (06.30.22)





**ASHLAND SCHOOL DISTRICT  
CAPITAL CONSTRUCTION  
DW TECHNOLOGY BUDGET  
MAY 31, 2025**

		Original Budget	Paid to Date	Remaining Balance	Revised Budget
<b>Project Expense</b>					
<b>Hard Cost</b>					
Maximum Allowable Construction Cost (MACC)	8/9	\$ 3,420,000	\$ 3,912,749	\$ (513,525)	\$ 3,399,224
Asbestos		\$ -	\$ -	\$ -	\$ -
Seismic Retro Upgrade		\$ -	\$ -	\$ -	\$ -
1.5% Solar (Total Project Major Building)		\$ -	\$ -	\$ -	\$ -
Construction Contingency		\$ 180,000	\$ -	\$ -	\$ -
<b>Construction Sub Total</b>		<b>\$ 3,600,000</b>	<b>\$ 3,912,749</b>	<b>\$ (513,525)</b>	<b>\$ 3,399,224</b>
<b>Soft Cost</b>					
<b>Administrative Cost</b>					
Legal Fees		\$ 5,000	\$ -	\$ -	\$ -
Bond Counsel		\$ -	\$ -	\$ -	\$ -
Bond Issuance Cost		\$ -	\$ -	\$ -	\$ -
Builders Risk Insurance		\$ -	\$ -	\$ -	\$ -
Project Management		\$ 108,000	\$ -	\$ -	\$ -
Reimbursable Expenses		\$ 7,200	\$ -	\$ -	\$ -
Communications		\$ -	\$ -	\$ -	\$ -
Sustainability		\$ -	\$ -	\$ -	\$ -
<b>Site Cost</b>					
Site Survey		\$ -	\$ -	\$ -	\$ -
Geo-Tech Report		\$ -	\$ -	\$ -	\$ -
<b>Planning Cost</b>					
Design Fees		\$ -	\$ -	\$ -	\$ -
A & E Reimbursable Expenses		\$ -	\$ -	\$ -	\$ -
Commissioning		\$ -	\$ -	\$ -	\$ -
Printing & Plan Distribution		\$ -	\$ -	\$ -	\$ -
Hazardous Materials Consultant		\$ -	\$ -	\$ -	\$ -
Construction Testing		\$ -	\$ -	\$ -	\$ -
Constructability Review		\$ -	\$ -	\$ -	\$ -
Plan Review & Building Permits	9	\$ 36,000	\$ -	\$ -	\$ -
Special Inspection and Testing		\$ -	\$ -	\$ -	\$ -
Miscellaneous Fees		\$ -	\$ -	\$ -	\$ -
Ed Specs		\$ -	\$ -	\$ -	\$ -
Kitchen		\$ -	\$ -	\$ -	\$ -
<b>Miscellaneous</b>					
Legal Advertisements	9	\$ 1,000	\$ -	\$ -	\$ -
Furniture, Fixtures, and Equipment (FF&E)		\$ -	\$ -	\$ -	\$ -
Technology		\$ -	\$ -	\$ -	\$ -
Technology (Design)	9	\$ 108,000	\$ 1,847	\$ (170)	\$ 1,677
Acoustics		\$ -	\$ -	\$ -	\$ -
Criminal Background Checks		\$ 1,000	\$ -	\$ -	\$ -
System Development Charges		\$ -	\$ -	\$ -	\$ -
Value Engineering		\$ -	\$ -	\$ -	\$ -
Utility Connection Fee		\$ -	\$ -	\$ -	\$ -
Unallocated Owner Contingency	6	\$ 360,000	\$ -	\$ -	\$ -
Inflation		\$ 253,572	\$ -	\$ -	\$ -
<b>Sub Total Soft Cost</b>		<b>\$ 879,772</b>	<b>\$ 1,847</b>	<b>\$ (170)</b>	<b>\$ 1,677</b>
<b>Total Project Cost</b>		<b>\$ 4,479,772</b>	<b>\$ 3,914,597</b>	<b>\$ (513,696)</b>	<b>\$ 3,400,901</b>

\* Budget has been moved to the Project Level

\*\*Budget has been moved to the Program Level

\*\*\* Re-allocated \$723,216 to Helman (05.31.20)

+Budget has been moved to the Program Level (10.31.20)

^ Re-allocated \$223,636 to Program Level (11.30.20)

1. Reallocated \$362,000 to AHS (09.30.21)

2. Reallocated from Contingency (12.31.21)

3. Reallocated from Contingency (03.31.22)

4. Reallocated from Contingency (05.31.22)

5. Reallocated Bond Issuance Costs back to Program Level (06.30.22)

6. Reallocated costs to MACC (06.30.22)

7. Reallocated from Invest Inc (08.31.22)

8. Reallocated 300k from Invest Inc (09.30.22)

9. Reallocated within Budget (09.30.22)



**ASHLAND SCHOOL DISTRICT  
CAPITAL CONSTRUCTION  
TRANSPORTATION BUDGET  
MAY 31, 2025**

		Original Budget	Paid to Date	Remaining Balance	Revised Budget
<b>Project Expense</b>					
<b>Hard Cost</b>					
Maximum Allowable Construction Cost (MACC)	8,10	\$ -	\$ 559,844	\$ 1	\$ 559,845
Asbestos		\$ -	\$ -	\$ -	\$ -
Seismic Retro Upgrade		\$ -	\$ -	\$ -	\$ -
1.5% Solar (Total Project Major Building)		\$ -	\$ -	\$ -	\$ -
Construction Contingency	8,10	\$ -	\$ -	\$ 1,652	\$ 1,652
<b>Construction Sub Total</b>		<b>\$ -</b>	<b>\$ 559,844</b>	<b>\$ 1,653</b>	<b>\$ 561,497</b>
<b>Soft Cost</b>					
<b>Administrative Cost</b>					
Legal Fees		\$ -	\$ -	\$ -	\$ -
Bond Counsel		\$ -	\$ -	\$ -	\$ -
Bond Issuance Cost		\$ -	\$ -	\$ -	\$ -
Builders Risk Insurance		\$ -	\$ -	\$ -	\$ -
Project Management		\$ -	\$ -	\$ -	\$ -
Reimbursable Expenses		\$ -	\$ -	\$ -	\$ -
Communications		\$ -	\$ -	\$ -	\$ -
Sustainability		\$ -	\$ -	\$ -	\$ -
<b>Site Cost</b>					
Site Survey		\$ -	\$ -	\$ -	\$ -
Geo-Tech Report		\$ -	\$ -	\$ -	\$ -
<b>Planning Cost</b>					
Design Fees		\$ -	\$ 32,860	\$ -	\$ 32,860
A & E Reimbursable Expenses		\$ -	\$ -	\$ -	\$ -
Commissioning		\$ -	\$ 19,501	\$ 499	\$ 20,000
Printing & Plan Distribution		\$ -	\$ -	\$ -	\$ -
Hazardous Materials Consultant	10	\$ -	\$ 8,850	\$ 0	\$ 8,850
Construction Testing		\$ -	\$ -	\$ -	\$ -
Constructability Review		\$ -	\$ -	\$ -	\$ -
Plan Review & Building Permits		\$ -	\$ 17,903	\$ 7,152	\$ 25,055
Special Inspection and Testing		\$ -	\$ -	\$ -	\$ -
Miscellaneous Fees	8	\$ -	\$ 4,388	\$ 613	\$ 5,000
Ed Specs		\$ -	\$ -	\$ -	\$ -
Kitchen		\$ -	\$ -	\$ -	\$ -
<b>Miscellaneous</b>					
Legal Advertisements		\$ -	\$ 407	\$ 0	\$ 407
Furniture, Fixtures, and Equipment (FF&E)		\$ -	\$ 7,631	\$ 17,369	\$ 25,000
Technology	9	\$ -	\$ 16,822	\$ 178	\$ 17,000
Technology (Design)		\$ -	\$ -	\$ -	\$ -
Acoustics		\$ -	\$ -	\$ -	\$ -
Criminal Background Checks		\$ -	\$ -	\$ -	\$ -
System Development Charges		\$ -	\$ -	\$ -	\$ -
Value Engineering		\$ -	\$ -	\$ -	\$ -
Utility Connection Fee		\$ -	\$ -	\$ -	\$ -
Unallocated Owner Contingency	8	\$ -	\$ -	\$ -	\$ -
Inflation		\$ -	\$ -	\$ -	\$ -
<b>Sub Total Soft Cost</b>		<b>\$ -</b>	<b>\$ 108,361</b>	<b>\$ 25,812</b>	<b>\$ 134,172</b>
<b>Total Project Cost</b>		<b>\$ -</b>	<b>\$ 668,205</b>	<b>\$ 27,465</b>	<b>\$ 695,669</b>

1. Reallocated from DW Security and HVAC (04.18.21)
2. Reallocated within Budget(12.31.21)
3. Reallocated to Maintenance Bldg (02.28.22)
4. Reallocated to Maintenance Bldg (03.31.22)
5. Reallocated within Budget (05.31.22)
6. Reallocated \$50k from Security to Transportation (06.30.22)
7. Reallocated within Budget (08.31.22)
8. Reallocated within Budget (09.30.22)
9. Reallocated from Security (03.31.23)



**ASHLAND SCHOOL DISTRICT  
CAPITAL CONSTRUCTION  
BELLVIEW BUDGET  
MAY 31, 2025**

		Original Budget	Paid to Date	Remaining Balance	Revised Budget
<b>Project Expense</b>					
<b>Hard Cost</b>					
Maximum Allowable Construction Cost (MACC)	6	\$ -	\$ 352,879	\$ 54,763	\$ 407,642
Asbestos		\$ -	\$ -	\$ -	\$ -
Seismic Retro Upgrade		\$ -	\$ -	\$ -	\$ -
1.5% Solar (Total Project Major Building)		\$ -	\$ -	\$ -	\$ -
Phase 2	5,6	\$ -	\$ 1,237,830	\$ 51,810	\$ 1,289,640
Construction Contingency	6	\$ -	\$ -	\$ 144,186	\$ 144,186
<b>Construction Sub Total</b>		<b>\$ -</b>	<b>\$ 1,590,709</b>	<b>\$ 250,759</b>	<b>\$ 1,841,468</b>
<b>Soft Cost</b>					
<b>Administrative Cost</b>					
Legal Fees		\$ -	\$ -	\$ -	\$ -
Bond Counsel		\$ -	\$ -	\$ -	\$ -
Bond Issuance Cost		\$ -	\$ -	\$ -	\$ -
Builders Risk Insurance		\$ -	\$ -	\$ -	\$ -
Project Management		\$ -	\$ -	\$ -	\$ -
Reimbursable Expenses		\$ -	\$ -	\$ -	\$ -
Communications		\$ -	\$ -	\$ -	\$ -
Sustainability		\$ -	\$ -	\$ -	\$ -
<b>Site Cost</b>					
Site Survey	4	\$ -	\$ 2,270	\$ -	\$ 2,270
Geo-Tech Report		\$ -	\$ -	\$ -	\$ -
<b>Planning Cost</b>					
Design Fees	4,7	\$ -	\$ 55,927	\$ (7,234)	\$ 48,693
A & E Reimbursable Expenses		\$ -	\$ -	\$ 5,000	\$ 5,000
Commissioning	4,7	\$ -	\$ 141,992	\$ (18,992)	\$ 123,000
Printing & Plan Distribution	7	\$ -	\$ -	\$ -	\$ -
Hazardous Materials Consultant		\$ -	\$ 4,540	\$ 460	\$ 5,000
Construction Testing		\$ -	\$ -	\$ -	\$ -
Constructability Review		\$ -	\$ -	\$ -	\$ -
Plan Review & Building Permits		\$ -	\$ 8,508	\$ 21,405	\$ 29,913
Special Inspection and Testing		\$ -	\$ -	\$ -	\$ -
Miscellaneous Fees		\$ -	\$ 32,270	\$ (13,270)	\$ 19,000
Ed Specs		\$ -	\$ -	\$ -	\$ -
Kitchen		\$ -	\$ -	\$ -	\$ -
<b>Miscellaneous</b>					
Legal Advertisements		\$ -	\$ 404	\$ 2,096	\$ 2,500
Furniture, Fixtures, and Equipment (FF&E)		\$ -	\$ -	\$ -	\$ -
Technology		\$ -	\$ -	\$ -	\$ -
Technology (Design)		\$ -	\$ -	\$ -	\$ -
Acoustics		\$ -	\$ -	\$ -	\$ -
Criminal Background Checks		\$ -	\$ -	\$ -	\$ -
System Development Charges		\$ -	\$ -	\$ -	\$ -
Value Engineering		\$ -	\$ -	\$ -	\$ -
Utility Connection Fee		\$ -	\$ -	\$ -	\$ -
Unallocated Owner Contingency	4,7	\$ -	\$ -	\$ -	\$ -
Inflation		\$ -	\$ -	\$ -	\$ -
<b>Sub Total Soft Cost</b>		<b>\$ -</b>	<b>\$ 245,912</b>	<b>\$ (10,536)</b>	<b>\$ 235,376</b>
<b>Total Project Cost</b>		<b>\$ -</b>	<b>\$ 1,836,621</b>	<b>\$ 240,223</b>	<b>\$ 2,076,844</b>

1. Reallocated from DW Security and HVAC (04.18.21)
2. Reallocate within budget (12.31.21)
3. Reallocate within budget (06.30.22)
4. Reallocate within budget (09.30.22)
5. Reallocate from Premium and DW Security (03.31.23)





**ASHLAND SCHOOL DISTRICT  
CAPITAL CONSTRUCTION  
MAINTENANCE BLDG BUDGET  
MAY 31, 2025**

		Original Budget	Paid to Date	Remaining Balance	Revised Budget
<b>Project Expense</b>					
<b>Hard Cost</b>					
Maximum Allowable Construction Cost (MACC)		\$ -	\$ 653,092	\$ -	\$ 653,092
Security Fencing	7,10	\$ -	\$ 23,890	\$ -	\$ 23,890
Seismic Retro Upgrade		\$ -	\$ -	\$ -	\$ -
1.5% Solar (Total Project Major Building)		\$ -	\$ -	\$ -	\$ -
Construction Contingency	10	\$ -	\$ -	\$ 17,724	\$ 17,724
<b>Construction Sub Total</b>		<b>\$ -</b>	<b>\$ 676,982</b>	<b>\$ 17,724</b>	<b>\$ 694,706</b>
<b>Soft Cost</b>					
<b>Administrative Cost</b>					
Legal Fees		\$ -	\$ -	\$ -	\$ -
Bond Counsel		\$ -	\$ -	\$ -	\$ -
Bond Issuance Cost		\$ -	\$ -	\$ -	\$ -
Builders Risk Insurance		\$ -	\$ -	\$ -	\$ -
Project Management		\$ -	\$ -	\$ -	\$ -
Reimbursable Expenses		\$ -	\$ -	\$ -	\$ -
Communications		\$ -	\$ -	\$ -	\$ -
Sustainability		\$ -	\$ -	\$ -	\$ -
<b>Site Cost</b>					
Site Survey		\$ -	\$ -	\$ -	\$ -
Geo-Tech Report		\$ -	\$ -	\$ -	\$ -
<b>Planning Cost</b>					
Design Fees	6	\$ -	\$ 28,850	\$ 155	\$ 29,005
A & E Reimbursable Expenses		\$ -	\$ -	\$ 5,000	\$ 5,000
Commissioning		\$ -	\$ 22,501	\$ 2,499	\$ 25,000
Printing & Plan Distribution		\$ -	\$ -	\$ -	\$ -
Hazardous Materials Consultant		\$ -	\$ 7,500	\$ -	\$ 7,500
Construction Testing		\$ -	\$ -	\$ -	\$ -
Constructability Review		\$ -	\$ -	\$ -	\$ -
Plan Review & Building Permits	8	\$ -	\$ 34,313	\$ 197	\$ 34,510
Special Inspection and Testing		\$ -	\$ -	\$ -	\$ -
Miscellaneous Fees	6	\$ -	\$ 6,855	\$ 1,445	\$ 8,300
Ed Specs		\$ -	\$ -	\$ -	\$ -
Kitchen		\$ -	\$ -	\$ -	\$ -
<b>Miscellaneous</b>					
Legal Advertisements		\$ -	\$ 407	\$ 1,593	\$ 2,000
Furniture, Fixtures, and Equipment (FF&E)		\$ -	\$ -	\$ -	\$ -
Technology	8,9	\$ -	\$ 23,801	\$ 199	\$ 24,000
Technology (Design)		\$ -	\$ -	\$ -	\$ -
Acoustics		\$ -	\$ -	\$ -	\$ -
Criminal Background Checks		\$ -	\$ -	\$ -	\$ -
System Development Charges		\$ -	\$ -	\$ -	\$ -
Value Engineering		\$ -	\$ -	\$ -	\$ -
Utility Connection Fee		\$ -	\$ -	\$ -	\$ -
Unallocated Owner Contingency	6	\$ -	\$ -	\$ 26,735	\$ 26,735
Inflation		\$ -	\$ -	\$ -	\$ -
<b>Sub Total Soft Cost</b>		<b>\$ -</b>	<b>\$ 124,227</b>	<b>\$ 37,823</b>	<b>\$ 162,050</b>
<b>Total Project Cost</b>		<b>\$ -</b>	<b>\$ 801,209</b>	<b>\$ 55,547</b>	<b>\$ 856,756</b>

1. Reallocated from DW Security and HVAC (04.18.21)
2. Reallocated from Transportation (02.28.22)
3. Reallocated within Budget (02.28.22)
4. Reallocated within Budget (03.31.22)
5. Reallocated within Budget (05.31.22)
6. Reallocated within Budget (06.30.22)
7. Reallocated from Safety and Security (08.31.22)
8. Reallocate from investment income ( 09.30.22)
9. Reallocate 24k from Security ( 01.31.23)

Intentionally left blank. Do not delete!



**ASHLAND SCHOOL DISTRICT  
CAPITAL CONSTRUCTION  
HELMAN ELEMENTARY SCHOOL BUDGET  
MAY 31, 2025**

		Original Budget	Paid to Date	Remaining Balance	Revised Budget
<b>Project Expense</b>					
<b>Hard Cost</b>					
Maximum Allowable Construction Cost (MACC)	13	\$ 10,576,000	\$ 15,367,756	\$ (232,685)	\$ 15,135,071
Asbestos		\$ 189,259		\$ -	\$ -
Seismic Retro Upgrade				\$ -	
1.5% Solar (Total Project Major Building)				\$ -	\$ -
Construction Contingency	13	\$ 528,825	\$ -	\$ -	\$ -
<b>Construction Sub Total</b>		<b>\$ 11,294,084</b>	<b>\$ 15,367,756</b>	<b>\$ (232,685)</b>	<b>\$ 15,135,071</b>
<b>Soft Cost</b>					
<b>Administrative Cost</b>					
Legal Fees		\$ 15,000	\$ -	\$ -	\$ -
Bond Counsel		\$ -	\$ -	\$ -	\$ -
Bond Issuance Cost		\$ -	\$ -	\$ -	\$ -
Builders Risk Insurance		\$ -	\$ 10,869	\$ 131	\$ 11,000
Project Management		\$ 338,823	\$ -	\$ -	\$ -
Reimbursable Expenses		\$ 22,588	\$ -	\$ -	\$ -
Communications		\$ -	\$ -	\$ -	\$ -
Sustainability		\$ -	\$ -	\$ -	\$ -
<b>Site Cost</b>					
Site Survey		\$ 22,588	\$ 16,151	\$ -	\$ 16,151
Geo-Tech Report		\$ 33,882	\$ 22,170	\$ 30	\$ 22,200
<b>Planning Cost</b>					
Design Fees	13	\$ 1,129,408	\$ 1,213,367	\$ 0	\$ 1,213,367
A & E Reimbursable Expenses		\$ 22,588	\$ 271	\$ 0	\$ 271
Commissioning		\$ 56,470	\$ 42,420	\$ 1,000	\$ 43,420
Printing & Plan Distribution		\$ 2,500	\$ -	\$ -	\$ -
Hazardous Materials Consultant	13	\$ 56,470	\$ 79,820	\$ 13,200	\$ 93,020
Constructability Review		\$ 56,470	\$ 75,000	\$ 470	\$ 75,470
Plan Review & Building Permits		\$ 112,941	\$ 640,326	\$ 8,448	\$ 648,774
Special Inspection and Testing		\$ 79,059	\$ 144,118	\$ 38,102	\$ 182,220
Miscellaneous Fees	13,14	\$ 45,176	\$ 99,456	\$ 1,978	\$ 101,434
Ed Specs		\$ 22,588	\$ -	\$ -	\$ -
Kitchen		\$ -	\$ -	\$ -	\$ -
<b>Miscellaneous</b>					
Legal Advertisements		\$ 2,000	\$ -	\$ -	\$ -
Furniture, Fixtures, and Equipment (FF&E)		\$ 564,704	\$ 586,301	\$ (3,362)	\$ 582,939
Technology		\$ 112,941	\$ -	\$ -	\$ -
Technology (Design)		\$ 56,470	\$ 5,404	\$ 96	\$ 5,500
Acoustics		\$ 16,941	\$ -	\$ -	\$ -
Criminal Background Checks		\$ 2,000	\$ -	\$ -	\$ -
System Development Charges	13,14	\$ 112,941	\$ -	\$ -	\$ -
Value Engineering		\$ 56,470	\$ -	\$ -	\$ -
Utility Connection Fee		\$ -	\$ -	\$ -	\$ -
Unallocated Owner Contingency		\$ 1,129,408	\$ -	\$ -	\$ -
Inflation		\$ 921,871	\$ -	\$ -	\$ -
<b>Sub Total Soft Cost</b>		<b>\$ 4,992,297</b>	<b>\$ 2,935,673</b>	<b>\$ 60,093</b>	<b>\$ 2,995,766</b>
<b>Total Project Cost</b>		<b>\$ 16,286,381</b>	<b>\$ 18,303,429</b>	<b>\$ (172,592)</b>	<b>\$ 18,130,837</b>

12. ReAllocated within Budget (09.30.22)  
13. ReAllocated within Budget (01.31.23)  
14. Costs were recategorized (04.30.23)





**ASHLAND SCHOOL DISTRICT  
CAPITAL CONSTRUCTION  
WALKER ELEMENTARY SCHOOL BUDGET  
MAY 31, 2025**

		Original Budget	Paid to Date	Remaining Balance	Revised Budget
<b>Project Expense</b>					
<b>Hard Cost</b>					
Maximum Allowable Construction Cost (MACC)	15	\$ 8,533,000	\$ 26,829,423	\$ 197,268	\$ 27,026,691
Asbestos		\$ 42,535	\$ -	\$ -	
Seismic Retro Upgrade		\$ 2,250,000	\$ 1,535,626	\$ 77,795	\$ 1,613,421
Science Works		\$ -	\$ 88,667	\$ 333	\$ 89,000
Modular Rental			\$ 1,676,661	\$ (188,236)	\$ 1,488,425
Construction Contingency	15	\$ 426,650	\$ -	\$ (0)	\$ (0)
<b>Construction Sub Total</b>		<b>\$ 11,252,185</b>	<b>\$ 30,130,377</b>	<b>\$ 87,160</b>	<b>\$ 30,217,537</b>
<b>Soft Cost</b>					
<b>Administrative Cost</b>					
Legal Fees		\$ 15,000	\$ -	\$ -	\$ -
Bond Counsel		\$ -	\$ -	\$ -	\$ -
Bond Issuance Cost		\$ -	\$ -	\$ -	\$ -
Builders Risk Insurance	14	\$ -	\$ 69,257	\$ (8,057)	\$ 61,200
Project Management		\$ 270,066	\$ -	\$ -	\$ -
Reimbursable Expenses		\$ 18,004	\$ -	\$ -	\$ -
Communications		\$ -	\$ -	\$ -	\$ -
Sustainability		\$ -	\$ -	\$ -	\$ -
<b>Site Cost</b>					
Site Survey		\$ 90,022	\$ 28,177	\$ 1,637	\$ 29,814
Geo-Tech Report		\$ 18,004	\$ 26,462	\$ (0)	\$ 26,462
<b>Planning Cost</b>					
Design Fees	14	\$ 1,150,218	\$ 1,986,657	\$ (19,165)	\$ 1,967,492
A & E Reimbursable Expenses		\$ 18,004	\$ 415	\$ 17,589	\$ 18,004
Commissioning		\$ 45,011	\$ 92,144	\$ (18,259)	\$ 73,885
Printing & Plan Distribution		\$ 2,000	\$ 945	\$ 55	\$ 1,000
Hazardous Materials Consultant		\$ 90,022	\$ 147,085	\$ 4,537	\$ 151,622
Construction Testing		\$ -	\$ -	\$ -	\$ -
Constructability Review		\$ 45,011	\$ 75,000	\$ -	\$ 75,000
Plan Review & Building Permits		\$ 90,022	\$ 892,242	\$ 4,718	\$ 896,960
Special Inspection and Testing	14	\$ 63,015	\$ 139,809	\$ (26,719)	\$ 113,090
Miscellaneous Fees	16,17	\$ 36,009	\$ 418,679	\$ (132,529)	\$ 286,150
Ed Specs		\$ 18,004	\$ -	\$ -	\$ -
Kitchen		\$ -	\$ -	\$ -	\$ -
<b>Miscellaneous</b>					
Legal Advertisements		\$ 2,000	\$ -	\$ -	\$ -
Furniture, Fixtures, and Equipment (FF&E)	14	\$ 450,109	\$ 868,562	\$ 3,338	\$ 871,900
Technology	14	\$ 90,022	\$ 238,419	\$ 4,202	\$ 242,621
Technology (Design)		\$ 45,011	\$ -	\$ -	\$ -
Acoustics		\$ 13,503	\$ -	\$ -	\$ -
Criminal Background Checks		\$ 1,200	\$ -	\$ -	\$ -
System Development Charges	16	\$ -	\$ -	\$ -	\$ -
Value Engineering		\$ -	\$ -	\$ -	\$ -
Utility Connection Fee		\$ -	\$ -	\$ -	\$ -
Unallocated Owner Contingency		\$ 1,125,273	\$ -	\$ -	\$ -
Inflation		\$ 746,863	\$ -	\$ -	\$ -
<b>Sub Total Soft Cost</b>		<b>\$ 4,442,393</b>	<b>\$ 4,983,854</b>	<b>\$ (168,653)</b>	<b>\$ 4,815,200</b>
<b>Total Project Cost</b>		<b>\$ 15,694,578</b>	<b>\$ 35,114,231</b>	<b>\$ (81,494)</b>	<b>\$ 35,032,737</b>

10. Reallocated Bond Issuance Costs back to Program Level (06.30.22)
11. Reallocated within Budget (06.30.22)
12. Reallocated within Budget (08.31.22)
13. Increase budget with Investment Income (08.31.22)
14. Increase budget with Investment Income (03.31.23)
15. Reallocated within Budget (03.31.23)
16. Costs were recategorized (04.30.23)
17. Reallocated within Budget (04.30.23)



**ASHLAND SCHOOL DISTRICT  
CAPITAL CONSTRUCTION  
ASHLAND MIDDLE SCHOOL BUDGET  
MAY 31, 2025**

		Original Budget	Paid to Date	Remaining Balance	Revised Budget
<b>Project Expense</b>					
<b>Hard Cost</b>					
Maximum Allowable Construction Cost (MACC)	18	\$ 20,500,000	\$ 35,813,522	\$ (366,146)	\$ 35,447,376
Asbestos		\$ 384,870	\$ -	\$ -	\$ -
Seismic Retro Upgrade		\$ -	\$ -	\$ -	\$ -
1.5% Solar (Total Project Major Building)		\$ -	\$ -	\$ -	\$ -
Construction Contingency		\$ 1,075,400	\$ -	\$ 0	\$ 0
<b>Construction Sub Total</b>		<b>\$ 21,960,270</b>	<b>\$ 35,813,522</b>	<b>\$ (366,146)</b>	<b>\$ 35,447,376</b>
<b>Soft Cost</b>					
<b>Administrative Cost</b>					
Legal Fees		\$ 20,000	\$ -	\$ -	\$ -
Bond Counsel		\$ -	\$ -	\$ -	\$ -
Bond Issuance Cost		\$ -	\$ -	\$ -	\$ -
Builders Risk Insurance		\$ -	\$ -	\$ -	\$ -
Project Management		\$ 658,808	\$ -	\$ -	\$ -
Reimbursable Expenses		\$ 43,921	\$ -	\$ -	\$ -
Communications		\$ -	\$ -	\$ -	\$ -
Sustainability		\$ -	\$ -	\$ -	\$ -
<b>Site Cost</b>					
Site Survey	17	\$ 43,921	\$ 24,226	\$ 690	\$ 24,916
Geo-Tech Report		\$ 43,921	\$ 37,264	\$ 2,736	\$ 40,000
<b>Planning Cost</b>					
Design Fees		\$ 2,196,027	\$ 2,359,606	\$ 83,084	\$ 2,442,690
A & E Reimbursable Expenses		\$ 43,921	\$ 34,400	\$ 35,600	\$ 70,000
Commissioning		\$ 87,841	\$ 53,220	\$ -	\$ 53,220
Printing & Plan Distribution		\$ 15,372	\$ -	\$ -	\$ -
Hazardous Materials Consultant		\$ 87,841	\$ 149,293	\$ 2,057	\$ 151,350
Construction Testing		\$ -	\$ -	\$ -	\$ -
Constructability Review		\$ 65,881	\$ 88,403	\$ -	\$ 88,403
Plan Review & Building Permits		\$ 219,603	\$ 1,127,525	\$ 186	\$ 1,127,711
Special Inspection and Testing		\$ 153,722	\$ 115,193	\$ 3,749	\$ 118,942
Miscellaneous Fees	17	\$ 87,841	\$ 300,136	\$ (20,886)	\$ 279,250
Ed Specs		\$ 32,940	\$ -	\$ -	\$ -
Kitchen		\$ 32,940	\$ -	\$ -	\$ -
<b>Miscellaneous</b>					
Legal Advertisements		\$ 2,000	\$ -	\$ -	\$ -
Furniture, Fixtures, and Equipment (FF&E)		\$ 1,098,014	\$ 1,154,444	\$ (4,444)	\$ 1,150,000
Technology	16	\$ 109,801	\$ 56,821	\$ 15,964	\$ 72,785
Technology (Design)		\$ 109,801	\$ -	\$ -	\$ -
Acoustics		\$ 32,940	\$ -	\$ -	\$ -
Criminal Background Checks		\$ 2,000	\$ -	\$ -	\$ -
System Development Charges		\$ 219,603	\$ 4,350	\$ (600)	\$ 3,750
Value Engineering		\$ 65,881	\$ -	\$ -	\$ -
Utility Connection Fee		\$ -	\$ -	\$ -	\$ -
Unallocated Owner Contingency		\$ 2,745,034	\$ -	\$ -	\$ -
Inflation		\$ 1,810,791	\$ -	\$ -	\$ -
<b>Sub Total Soft Cost</b>		<b>\$ 10,030,365</b>	<b>\$ 5,504,880</b>	<b>\$ 118,137</b>	<b>\$ 5,623,017</b>
<b>Total Project Cost</b>		<b>\$ 31,990,635</b>	<b>\$ 41,318,402</b>	<b>\$ (248,009)</b>	<b>\$ 41,070,393</b>

15. Reallocated within Budget (01.31.23)

16. Reallocated \$26k from Security (03.31.23)

17. Reallocated within Budget (05.31.23)

18. Reallocated from Investment Inc (06.30.23)



**ASHLAND SCHOOL DISTRICT  
CAPITAL CONSTRUCTION  
ASHLAND HIGH SCHOOL BUDGET  
MAY 31, 2025**

		Original Budget	Paid to Date	Remaining Balance	Revised Budget
<b>Project Expense</b>					
Hard Cost					
Phase II: HVAC					
		\$ -	\$ 19,876,055	\$ (9,352,391)	\$ 10,523,664
Maximum Allowable Construction Cost (MACC)		\$ 8,544,000	\$ 4,753,224	\$ 9,088,776	\$ 13,842,000
Asbestos		\$ 152,889	\$ -	\$ 152,889	\$ 152,889
Seismic Retro Upgrade	13	\$ -	\$ -	\$ 2,500,000	\$ 2,500,000
1.5% Solar (Total Project Major Building)		\$ -	\$ -	\$ -	\$ -
Construction Contingency	13	\$ 427,200	\$ -	\$ 598,536	\$ 598,536
<b>Construction Sub Total</b>		<b>\$ 9,124,089</b>	<b>\$ 24,629,279</b>	<b>\$ 2,987,810</b>	<b>\$ 27,617,089</b>
<b>Soft Cost</b>					
<b>Administrative Cost</b>					
Legal Fees		\$ 15,000	\$ 2,948	\$ (2,948)	\$ -
Bond Counsel		\$ -	\$ -	\$ -	\$ -
Bond Issuance Cost		\$ -	\$ -	\$ -	\$ -
Builders Risk Insurance		\$ -	\$ -	\$ -	\$ -
Project Management	18	\$ 273,723	\$ 361,454	\$ (321,454)	\$ 40,000
Reimbursable Expenses	17	\$ 18,248	\$ 17,545	\$ (2,145)	\$ 15,400
Communications		\$ -	\$ -	\$ -	\$ -
Sustainability		\$ -	\$ -	\$ -	\$ -
<b>Site Cost</b>					
Site Survey		\$ 27,372	\$ 52,272	\$ (1,700)	\$ 50,572
Geo-Tech Report		\$ 27,372	\$ 38,293	\$ (2,221)	\$ 36,072
<b>Planning Cost</b>					
Design Fees	19	\$ 912,409	\$ 2,709,640	\$ (633,108)	\$ 2,076,532
A & E Reimbursable Expenses		\$ 18,248	\$ 334	\$ 17,914	\$ 18,248
Commissioning		\$ -	\$ -	\$ -	\$ -
Printing & Plan Distribution		\$ 2,000	\$ -	\$ -	\$ -
Hazardous Materials Consultant		\$ 45,620	\$ 152,023	\$ (104,403)	\$ 47,620
Construction Testing		\$ -	\$ -	\$ -	\$ -
Constructability Review		\$ 45,620	\$ 334,600	\$ 0	\$ 334,600
Plan Review & Building Permits		\$ 91,241	\$ 554,141	\$ 88,829	\$ 642,970
Special Inspection and Testing		\$ 45,620	\$ 496,324	\$ (394,704)	\$ 101,620
Miscellaneous Fees	19	\$ 36,496	\$ 142,386	\$ (57,582)	\$ 84,804
Ed Specs		\$ -	\$ -	\$ -	\$ -
Kitchen		\$ -	\$ -	\$ -	\$ -
<b>Miscellaneous</b>					
Legal Advertisements		\$ 2,000	\$ 240	\$ 1,760	\$ 2,000
Furniture, Fixtures, and Equipment (FF&E)		\$ 456,204	\$ 40,877	\$ 59,123	\$ 100,000
Technology		\$ 91,241	\$ 131,075	\$ 219	\$ 131,294
Technology (Design)		\$ 45,620	\$ -	\$ 36,298	\$ 36,298
Acoustics		\$ 13,686	\$ -	\$ -	\$ -
Criminal Background Checks		\$ 1,500	\$ -	\$ -	\$ -
System Development Charges		\$ -	\$ -	\$ -	\$ -
Value Engineering		\$ -	\$ -	\$ -	\$ -
Utility Connection Fee		\$ -	\$ -	\$ -	\$ -
Unallocated Owner Contingency	17,18	\$ 1,140,511	\$ -	\$ 1,262	\$ 1,262
Inflation	19	\$ 746,029	\$ -	\$ -	\$ -
<b>Sub Total Soft Cost</b>		<b>\$ 4,055,760</b>	<b>\$ 5,034,149</b>	<b>\$ (1,314,857)</b>	<b>\$ 3,719,292</b>
<b>Total Project Cost</b>		<b>\$ 13,179,849</b>	<b>\$ 29,663,428</b>	<b>\$ 1,672,953</b>	<b>\$ 31,336,381</b>

14. Reallocated within Budget (10.31.22)  
 15. Reallocated within Budget (01.31.23)  
 16. Reallocated within Budget (02.28.23)  
 17. Reallocated within Budget (03.31.23)  
 18. Reallocated within Budget (06.30.23)

**\$ 27,733,921**  
 \$ 1,929,507.17





**ASHLAND SCHOOL DISTRICT  
CAPITAL CONSTRUCTION  
WILLOW WIND LEARNING CENTER  
MAY 31, 2025**

<b>Project Expense</b>		<b>Original Budget</b>	<b>Paid to Date</b>	<b>Remaining Balance</b>	<b>Revised Budget</b>
<b>Hard Cost</b>					
Maximum Allowable Construction Cost (MACC)	4,8	\$ -	\$ 1,732,696	\$ 1,732	\$ 1,734,428
Other Contractor Costs		\$ -	\$ -	\$ -	\$ -
		\$ -	\$ -	\$ -	\$ -
		\$ -	\$ -	\$ -	\$ -
Construction Contingency		\$ -	\$ -	\$ -	\$ -
<b>Construction Sub Total</b>		<b>\$ -</b>	<b>\$ 1,732,696</b>	<b>\$ 1,732</b>	<b>\$ 1,734,428</b>
<b>Soft Cost</b>					
<b>Administrative Cost</b>					
Legal Fees		\$ -	\$ -	\$ -	\$ -
Bond Counsel		\$ -	\$ -	\$ -	\$ -
Bond Issuance Cost		\$ -	\$ -	\$ -	\$ -
Builders Risk Insurance		\$ -	\$ -	\$ -	\$ -
Project Management		\$ -	\$ -	\$ -	\$ -
Reimbursable Expenses		\$ -	\$ -	\$ -	\$ -
Communications		\$ -	\$ -	\$ -	\$ -
Sustainability		\$ -	\$ -	\$ -	\$ -
<b>Site Cost</b>					
Site Survey		\$ -	\$ -	\$ -	\$ -
Geo-Tech Report		\$ -	\$ -	\$ -	\$ -
<b>Planning Cost</b>					
Design Fees	5	\$ -	\$ 128,412	\$ (351)	\$ 128,061
A & E Reimbursable Expenses		\$ -	\$ -	\$ -	\$ -
Commissioning		\$ -	\$ 21,500	\$ 284	\$ 21,784
Printing & Plan Distribution		\$ -	\$ -	\$ -	\$ -
Hazardous Materials Consultant		\$ -	\$ 10,894	\$ -	\$ 10,894
Construction Testing		\$ -	\$ -	\$ -	\$ -
Constructability Review		\$ -	\$ -	\$ -	\$ -
Plan Review & Building Permits		\$ -	\$ 37,164	\$ (1,844)	\$ 35,320
Special Inspection and Testing		\$ -	\$ 3,833	\$ 0	\$ 3,833
Miscellaneous Fees	6,7	\$ -	\$ 54,272	\$ 3,994	\$ 58,266
Ed Specs		\$ -	\$ -	\$ -	\$ -
Kitchen		\$ -	\$ -	\$ -	\$ -
<b>Miscellaneous</b>					
Legal Advertisements		\$ -	\$ -	\$ -	\$ -
Furniture, Fixtures, and Equipment (FF&E)		\$ -	\$ 8,535	\$ 465	\$ 9,000
Technology		\$ -	\$ -	\$ -	\$ -
Technology (Design)		\$ -	\$ -	\$ -	\$ -
Acoustics		\$ -	\$ -	\$ -	\$ -
Criminal Background Checks		\$ -	\$ -	\$ -	\$ -
System Development Charges		\$ -	\$ 15,342	\$ -	\$ 15,342
Value Engineering		\$ -	\$ -	\$ -	\$ -
Utility Connection Fee		\$ -	\$ -	\$ -	\$ -
Unallocated Owner Contingency	5	\$ -	\$ -	\$ -	\$ -
Inflation		\$ -	\$ -	\$ -	\$ -
<b>Sub Total Soft Cost</b>		<b>\$ -</b>	<b>\$ 279,952</b>	<b>\$ 2,548</b>	<b>\$ 282,500</b>
<b>Total Project Cost</b>		<b>\$ -</b>	<b>\$ 2,012,648</b>	<b>\$ 4,280</b>	<b>\$ 2,016,928</b>

2. ReAllocated costs within budget (08.01.21)
2. ReAllocated costs within budget (08.01.21)
3. \$79,500 moved to WES (12.31.21)
4. ReAllocated costs within budget (03.31.22)
5. ReAllocated costs within budget (08.31.22)
6. ReAllocated costs from Investment Inc (09.30.22)
7. ReAllocated costs from Investment Inc (05.31.23)



**ASHLAND SCHOOL DISTRICT  
CAPITAL CONSTRUCTION  
DISTRICT WIDE SOLAR PROJECT  
MAY 31, 2025**

		Original Budget	Paid to Date	Remaining Balance	Revised Budget
<b>Project Expense</b>					
<b>Hard Cost</b>					
1.5% Solar (Walker Elementary)		\$ -	\$ 280,779	\$ 1,619	\$ 282,398
1.5% Solar (Helman Elementary)		\$ -	\$ 250,000	\$ -	\$ 250,000
1.5% Solar (Ashland Middle School)	2,3,4	\$ -	\$ 401,106	\$ 17,294	\$ 418,400
1.5% Solar (Ashland High School)		\$ -	\$ -	\$ 200,000	\$ 200,000
1.5% Solar (Willow Wind Learning Center)		\$ -	\$ -	\$ -	\$ -
Construction Contingency	1,5	\$ -	\$ -	\$ 500,000	\$ 500,000
<b>Construction Sub Total</b>		<b>\$ -</b>	<b>\$ 931,886</b>	<b>\$ 718,912</b>	<b>\$ 1,650,798</b>
<b>Soft Cost</b>					
<b>Administrative Cost</b>					
Legal Fees		\$ -	\$ -	\$ -	\$ -
Bond Counsel		\$ -	\$ -	\$ -	\$ -
Bond Issuance Cost		\$ -	\$ -	\$ -	\$ -
Builders Risk Insurance		\$ -	\$ -	\$ -	\$ -
Project Management		\$ -	\$ -	\$ -	\$ -
Reimbursable Expenses		\$ -	\$ -	\$ -	\$ -
Communications		\$ -	\$ -	\$ -	\$ -
Sustainability		\$ -	\$ -	\$ -	\$ -
<b>Site Cost</b>					
Site Survey	3	\$ -	\$ 13,100	\$ (9,100)	\$ 4,000
Geo-Tech Report		\$ -	\$ -	\$ -	\$ -
<b>Planning Cost</b>					
Design Fees	2,3,4	\$ -	\$ 80,100	\$ (10,500)	\$ 69,600
A & E Reimbursable Expenses		\$ -	\$ -	\$ -	\$ -
Commissioning		\$ -	\$ -	\$ -	\$ -
Printing & Plan Distribution		\$ -	\$ -	\$ -	\$ -
Hazardous Materials Consultant		\$ -	\$ -	\$ -	\$ -
Construction Testing		\$ -	\$ -	\$ -	\$ -
Constructability Review		\$ -	\$ -	\$ -	\$ -
Plan Review & Building Permits	3,4,5	\$ -	\$ 43,827	\$ 14,173	\$ 58,000
Special Inspection and Testing		\$ -	\$ -	\$ -	\$ -
Miscellaneous Fees		\$ -	\$ 1,989	\$ (1,989)	\$ -
Ed Specs		\$ -	\$ -	\$ -	\$ -
Kitchen		\$ -	\$ -	\$ -	\$ -
<b>Miscellaneous</b>					
Legal Advertisements		\$ -	\$ -	\$ -	\$ -
Furniture, Fixtures, and Equipment (FF&E)		\$ -	\$ -	\$ -	\$ -
Technology		\$ -	\$ -	\$ -	\$ -
Technology (Design)		\$ -	\$ -	\$ -	\$ -
Acoustics		\$ -	\$ -	\$ -	\$ -
Criminal Background Checks		\$ -	\$ -	\$ -	\$ -
System Development Charges		\$ -	\$ -	\$ -	\$ -
Value Engineering		\$ -	\$ -	\$ -	\$ -
Utility Connection Fee		\$ -	\$ -	\$ -	\$ -
Unallocated Owner Contingency		\$ -	\$ -	\$ -	\$ -
Inflation		\$ -	\$ -	\$ -	\$ -
<b>Sub Total Soft Cost</b>		<b>\$ -</b>	<b>\$ 139,016</b>	<b>\$ (7,416)</b>	<b>\$ 131,600</b>
<b>Total Project Cost</b>		<b>\$ -</b>	<b>\$ 1,070,902</b>	<b>\$ 711,496</b>	<b>\$ 1,782,398</b>

- |                                               |                 |
|-----------------------------------------------|-----------------|
| 1. ReAllocated from Investment Inc (09.30.22) | \$1,897,106     |
| 2. ReAllocated within Budget (09.30.22)       | \$ (114,708.00) |
| 3. ReAllocated within Budget (04.30.23)       |                 |
| 4. ReAllocated within Budget (06.30.23)       |                 |
