

Collin College May 2026 Monthly Report

2023-2030 Master Plan Phase I
Collin County Community College District

Project Number: 60726232

June 8, 2026

Quality Information

Prepared by	Reviewed by	Approved By
Nuria Cortes	Melissa Perette	Tim Smith
Nuria Cortes Program Controls Manager	Melissa Perette Deputy Program Director	Tim Smith Program Director

Revision History

Revision	Revision date	Details	Authorized	Name	Position
First Publication	June 8, 2026	May '26 Report	Yes	Tim Smith	Program Director

Distribution List

# Hard Copies	PDF Required	Association / Company Name
	1	Dr. Neil Matkin / Collin College
	1	Dr. Bill King / Collin College
	1	Chris Eyle / Collin College

Prepared for:

Collin County Community College District
3452 Spur 399
Suite 327
McKinney, TX 75069

Prepared by:

Nuria Cortes
Program Controls Manager
E: ncortes.aecom@collin.edu

AECOM
13355 Noel Road
4th Floor
Dallas TX, 75240
aecom.com

Copyright © 2026 by AECOM

All rights reserved. No part of this copyrighted work may be reproduced, distributed, or transmitted in any form or by any means without the prior written permission of AECOM.

Table of Contents

1.	Introduction	5
2.	Executive Summary	5
3.	Program Summary	6
3.1	Program Schedule	6
3.2	Program Budget	7
3.3	Current Personnel Estimate	7
4.	Project Summary	8
5	Completed Items	13
5.1	General Program	13
5.2	Procurement	13
5.3	Design	13
5.4	Pre-Construction	13
5.5	Construction	13
5.6	Acceptance and Close-Out	14
6	Pending Items	14
6.1	General Program	14
6.2	Procurement	14
6.3	Design	14
6.4	Pre-Construction	14
6.5	Construction	14
6.6	Acceptance and Close-Out	14
7	Progress Pictures	15
7.1	Plano Campus Renovations	15
7.2	Health Science Center	16
7.3	Wylie CTE	17

1. Introduction

AECOM is currently managing five projects in this program. The total budget for the entire program is \$240,333,508.36, which includes two projects that AECOM is not managing.

On February 27, 2024, the Board of Trustees granted the District President authority to enter into and negotiate a contract with AECOM Technical Services, Inc. (AECOM) to provide Program Management Services for the Collin College 2023 Master Plan Program. On May 3, 2024, Collin College and AECOM executed the Collin contract for program management services. As part of these services, AECOM will deliver a monthly report to provide status and progress of key aspects of the Program.

2. Executive Summary

Completed and Pending Items

- Plano Campus – Roof work continues. Contractor will install Theater balcony glass the weekend June 6th. Comm. Music system programming is almost complete working to schedule commissioning and training Mid-June. Kitchen/ Dining and E first floor work is continuing. Main Hallway ceiling demo and build back has begun.
- Courtyard Center – Project closeout in progress.
- CHEC – Final CO was obtained from the City of McKinney on May 12th. Project closeout is in progress. Pending is punchlist for fire-rated frames.
- Health Science Center – Glazing work nearing completion for the building while roofing continues for on north vestibule roof. Interior Level 1 - ceiling grid beginning in few areas, tape and float progressing, and restroom tile delivered to site. Interior Level 2 - walls are being two sided, flex duct install ongoing and prime/paint in progress.
- Wylie CTE – Building piers are complete and grade beams are in progress. Underground utility work continues. Preparation for the tilt wall panel pours has started.

Items of close attention

- No items of close attention at this time

Budget Summary


- \$205,129,401.70 of the \$240,333,508.36 has been committed to date in the form of contracts with various vendors.
- \$115,399,222.83 of the \$205,129,401.70 committed amount has expended to-date.

3. Program Summary

3.1 Program Schedule

Project	Scope of Work	2024												2025												2026												2027											
		Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
Plano Campus	Renovations & Upgrades																																																
CYC	Departmental Relocations																																																
CHEC	Departmental Relocations																																																
Health Sciences	New Building																																																
Wylie - CTE	New Building																																																


- Planning & Programming
- Design & Construction Documents
- Construction
- Final Completion & Close-Out


 We Are Here

3.2 Program Budget

Cost Summary							
Budget Group	Original Budget	Current Budget	Commitments	Approved Changes	Total Commitments	Pending Commitments	Expended to Date
Construction, Equipment & Furnishings	\$157,491,962.00	\$197,955,628.43	\$138,056,088.84	\$45,610,484.86	\$183,666,573.70	\$145,507.33	\$99,997,989.10
Contingency	\$22,203,853.00	\$18,532,993.07	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
Investigation, Testing & Verification	\$2,847,939.00	\$3,303,594.00	\$1,608,535.00	\$48,536.75	\$1,657,071.75	\$0.00	\$702,840.52
Management, Design & Pre-Construction	\$17,145,727.36	\$20,069,019.36	\$17,702,494.01	\$1,954,294.00	\$19,656,788.01	\$0.00	\$14,573,793.43
Miscellaneous	\$393,015.00	\$472,273.50	\$144,942.24	\$4,026.00	\$148,968.24	\$0.00	\$124,599.78
Total	\$200,082,496.36	\$240,333,508.36	\$157,512,060.09	\$47,617,341.61	\$205,129,401.70	\$145,507.33	\$115,399,222.83

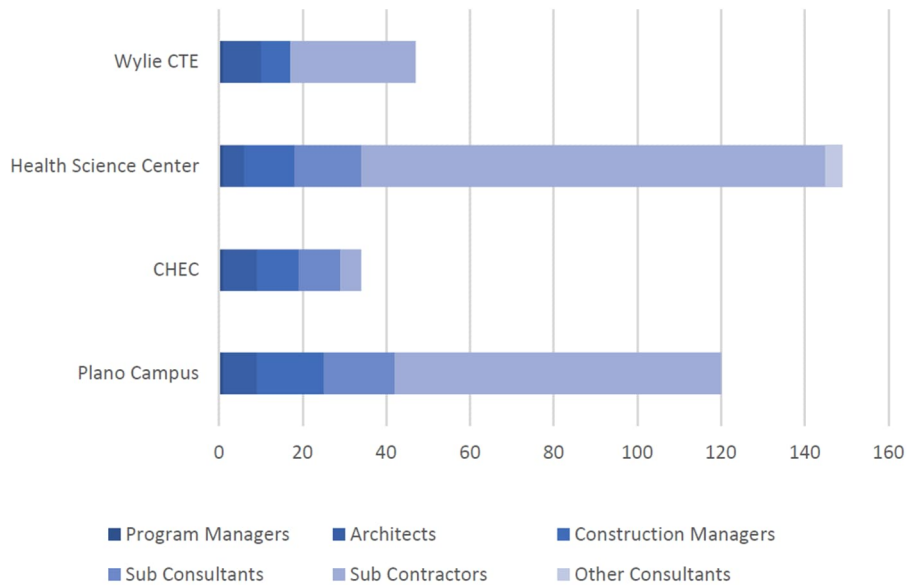

3.3 Current Personnel Estimate



It is estimated that the Program Managers, Architects, Construction Managers, Sub-Consultants, and Sub-Contractors, under contract with Collin College for the 2023 Master Plan Programs, have an average of 350 employees contributing to the program's progress.



4. Project Summary

Courtyard Renovation



Project Name Courtyard Renovation		 	Schedule																																																																										
Project Name Courtyard Renovation			Project Number PJ1065		<table border="1"> <thead> <tr> <th>Activity</th> <th>Baseline Finish</th> <th>Planned Finish</th> <th>Actual Finish</th> <th></th> </tr> </thead> <tbody> <tr> <td>BOT Approval of Construction Delivery Method</td> <td>1/26/2024</td> <td>1/26/2024</td> <td>↑</td> <td>1/26/2024 ✓</td> </tr> <tr> <td>BOT Approval of Recommended A/E</td> <td>1/26/2024</td> <td>1/26/2024</td> <td>↑</td> <td>1/26/2024 ✓</td> </tr> <tr> <td>BOT Approval of Program Manager</td> <td>2/27/2024</td> <td>2/27/2024</td> <td>↑</td> <td>2/27/2024 ✓</td> </tr> <tr> <td>Architect Mobilized</td> <td>5/17/2024</td> <td>5/17/2024</td> <td>↑</td> <td>5/17/2024 ✓</td> </tr> <tr> <td>BOT Approval of Recommended CMAR</td> <td>5/26/2024</td> <td>5/26/2024</td> <td>↑</td> <td>5/28/2024 ✓</td> </tr> <tr> <td>100% CDs Complete</td> <td>11/1/2024</td> <td>10/10/2024</td> <td>↑</td> <td>10/10/2024 ✓</td> </tr> <tr> <td>GMP Submittal</td> <td>12/1/2024</td> <td>11/22/2024</td> <td>↑</td> <td>11/22/2024 ✓</td> </tr> <tr> <td>BOT Approval of GMP</td> <td>12/10/2024</td> <td>12/10/2024</td> <td>↑</td> <td>12/10/2024 ✓</td> </tr> <tr> <td>Obtain Building Permit</td> <td>12/13/2024</td> <td>12/13/2024</td> <td>↑</td> <td>1/16/2025 ✓</td> </tr> <tr> <td>Contractor Mobilized</td> <td>12/20/2024</td> <td>12/20/2024</td> <td>↓</td> <td>1/20/2025 ✓</td> </tr> <tr> <td>Substantial Completion</td> <td>7/15/2025</td> <td>8/18/2025</td> <td>↓</td> <td>8/18/2025 ✓</td> </tr> <tr> <td>Final Completion</td> <td>8/1/2025</td> <td>9/10/2025</td> <td>↓</td> <td>10/8/2025 ✓</td> </tr> <tr> <td>Student Occupancy</td> <td>8/26/2025</td> <td>8/26/2025</td> <td>↑</td> <td>9/2/2025 ✓</td> </tr> </tbody> </table>				Activity	Baseline Finish	Planned Finish	Actual Finish		BOT Approval of Construction Delivery Method	1/26/2024	1/26/2024	↑	1/26/2024 ✓	BOT Approval of Recommended A/E	1/26/2024	1/26/2024	↑	1/26/2024 ✓	BOT Approval of Program Manager	2/27/2024	2/27/2024	↑	2/27/2024 ✓	Architect Mobilized	5/17/2024	5/17/2024	↑	5/17/2024 ✓	BOT Approval of Recommended CMAR	5/26/2024	5/26/2024	↑	5/28/2024 ✓	100% CDs Complete	11/1/2024	10/10/2024	↑	10/10/2024 ✓	GMP Submittal	12/1/2024	11/22/2024	↑	11/22/2024 ✓	BOT Approval of GMP	12/10/2024	12/10/2024	↑	12/10/2024 ✓	Obtain Building Permit	12/13/2024	12/13/2024	↑	1/16/2025 ✓	Contractor Mobilized	12/20/2024	12/20/2024	↓	1/20/2025 ✓	Substantial Completion	7/15/2025	8/18/2025	↓	8/18/2025 ✓	Final Completion	8/1/2025	9/10/2025	↓	10/8/2025 ✓	Student Occupancy	8/26/2025	8/26/2025	↑
Activity	Baseline Finish	Planned Finish	Actual Finish																																																																										
BOT Approval of Construction Delivery Method	1/26/2024	1/26/2024	↑	1/26/2024 ✓																																																																									
BOT Approval of Recommended A/E	1/26/2024	1/26/2024	↑	1/26/2024 ✓																																																																									
BOT Approval of Program Manager	2/27/2024	2/27/2024	↑	2/27/2024 ✓																																																																									
Architect Mobilized	5/17/2024	5/17/2024	↑	5/17/2024 ✓																																																																									
BOT Approval of Recommended CMAR	5/26/2024	5/26/2024	↑	5/28/2024 ✓																																																																									
100% CDs Complete	11/1/2024	10/10/2024	↑	10/10/2024 ✓																																																																									
GMP Submittal	12/1/2024	11/22/2024	↑	11/22/2024 ✓																																																																									
BOT Approval of GMP	12/10/2024	12/10/2024	↑	12/10/2024 ✓																																																																									
Obtain Building Permit	12/13/2024	12/13/2024	↑	1/16/2025 ✓																																																																									
Contractor Mobilized	12/20/2024	12/20/2024	↓	1/20/2025 ✓																																																																									
Substantial Completion	7/15/2025	8/18/2025	↓	8/18/2025 ✓																																																																									
Final Completion	8/1/2025	9/10/2025	↓	10/8/2025 ✓																																																																									
Student Occupancy	8/26/2025	8/26/2025	↑	9/2/2025 ✓																																																																									
Project Type Renovation		Project Phase Construction		Scope Description * Renovations of the Courtyard Center * The Renovations include: - New Cosmetology Space - Relocate and expand Esthetician Space - New Medical Message space - Remodel of 4th floor for Information Technology and Police																																																																									
Project Manager Melissa Perette		Contractor/CM Skanska						Architect IN2 Architecture																																																																					
Project Directory																																																																													
Company		Project Role																																																																											
AECOM Technical Services, Inc.		Program Manager																																																																											
Collin College		Owner																																																																											
Skanska		Construction Manager-at-Risk																																																																											
IN2 Architecture		A/E																																																																											
RWB Consulting Engineers																																																																													
				Progress Summary																																																																									
Status Date				Notes																																																																									
5/31/2026				Project closeout in progress.																																																																									

Cost Summary							
Budget Group	Original Budget	Current Budget	Commitments	Approved Changes	Total Commitments	Pending Commitments	Expended to Date
Construction, Equipment & Furnishings	\$4,991,556.00	\$5,282,993.84	\$5,013,360.34	\$269,556.50	\$5,282,916.84	\$0.00	\$4,961,065.05
Contingency	\$294,481.00	\$17,931.66	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
Investigation, Testing & Verification	\$82,073.00	\$72,151.00	\$72,151.00	\$0.00	\$72,151.00	\$0.00	\$58,549.80
Management, Design & Pre-Construction	\$696,100.00	\$692,087.00	\$690,736.36	\$1,350.00	\$692,086.36	\$0.00	\$597,398.75
Miscellaneous	\$4,551.00	\$3,597.50	\$3,597.50	\$0.00	\$3,597.50	\$0.00	\$1,847.00
Total	\$6,068,761.00	\$6,068,761.00	\$5,779,845.20	\$270,906.50	\$6,050,751.70	\$0.00	\$5,618,860.60



CHEC Renovation

Project Name CHEC Renovation		 	Schedule																																																																											
Project Name CHEC Renovation			Project Number PJ1066		<table border="1"> <thead> <tr> <th>Activity</th> <th>Baseline Finish</th> <th>Planned Finish</th> <th>Actual Finish</th> <th></th> </tr> </thead> <tbody> <tr> <td>BOT Approval of A/E Procurement Method</td> <td>1/26/2024</td> <td>1/26/2024</td> <td>1/26/2024</td> <td>↑ ✓</td> </tr> <tr> <td>BOT Approval of Construction Delivery Method</td> <td>1/26/2024</td> <td>1/26/2024</td> <td>1/26/2024</td> <td>↑ ✓</td> </tr> <tr> <td>BOT Approval of Recommended A/E</td> <td>1/26/2024</td> <td>1/26/2024</td> <td>1/26/2024</td> <td>↑ ✓</td> </tr> <tr> <td>BOT Approval of Program Manager</td> <td>2/27/2024</td> <td>2/27/2024</td> <td>2/27/2024</td> <td>↑ ✓</td> </tr> <tr> <td>Architect Mobilized</td> <td>5/17/2024</td> <td>5/17/2024</td> <td>5/17/2024</td> <td>↑ ✓</td> </tr> <tr> <td>BOT Approval of Recommended CMAR</td> <td>5/26/2024</td> <td>5/26/2024</td> <td>5/28/2024</td> <td>↑ ✓</td> </tr> <tr> <td>100% CDs Complete</td> <td>11/1/2024</td> <td>2/14/2025</td> <td>2/14/2025</td> <td>↓ ✓</td> </tr> <tr> <td>GMP Submittal</td> <td>12/1/2024</td> <td>2/20/2025</td> <td>2/20/2025</td> <td>↓ ✓</td> </tr> <tr> <td>BOT Approval of GMP</td> <td>12/10/2024</td> <td>3/25/2025</td> <td>3/25/2025</td> <td>↓ ✓</td> </tr> <tr> <td>Obtain Building Permit</td> <td>12/20/2024</td> <td>4/16/2025</td> <td>4/21/2025</td> <td>↓ ✓</td> </tr> <tr> <td>Contractor Mobilized</td> <td>1/6/2025</td> <td>4/17/2025</td> <td>4/21/2025</td> <td>↓ ✓</td> </tr> <tr> <td>Substantial Completion</td> <td>4/1/2026</td> <td>4/24/2026</td> <td>3/23/2026</td> <td>↓ ✓</td> </tr> <tr> <td>Final Completion</td> <td>5/1/2026</td> <td>5/26/2026</td> <td></td> <td>↓</td> </tr> </tbody> </table>					Activity	Baseline Finish	Planned Finish	Actual Finish		BOT Approval of A/E Procurement Method	1/26/2024	1/26/2024	1/26/2024	↑ ✓	BOT Approval of Construction Delivery Method	1/26/2024	1/26/2024	1/26/2024	↑ ✓	BOT Approval of Recommended A/E	1/26/2024	1/26/2024	1/26/2024	↑ ✓	BOT Approval of Program Manager	2/27/2024	2/27/2024	2/27/2024	↑ ✓	Architect Mobilized	5/17/2024	5/17/2024	5/17/2024	↑ ✓	BOT Approval of Recommended CMAR	5/26/2024	5/26/2024	5/28/2024	↑ ✓	100% CDs Complete	11/1/2024	2/14/2025	2/14/2025	↓ ✓	GMP Submittal	12/1/2024	2/20/2025	2/20/2025	↓ ✓	BOT Approval of GMP	12/10/2024	3/25/2025	3/25/2025	↓ ✓	Obtain Building Permit	12/20/2024	4/16/2025	4/21/2025	↓ ✓	Contractor Mobilized	1/6/2025	4/17/2025	4/21/2025	↓ ✓	Substantial Completion	4/1/2026	4/24/2026	3/23/2026	↓ ✓	Final Completion	5/1/2026	5/26/2026	
Activity	Baseline Finish	Planned Finish	Actual Finish																																																																											
BOT Approval of A/E Procurement Method	1/26/2024	1/26/2024	1/26/2024	↑ ✓																																																																										
BOT Approval of Construction Delivery Method	1/26/2024	1/26/2024	1/26/2024	↑ ✓																																																																										
BOT Approval of Recommended A/E	1/26/2024	1/26/2024	1/26/2024	↑ ✓																																																																										
BOT Approval of Program Manager	2/27/2024	2/27/2024	2/27/2024	↑ ✓																																																																										
Architect Mobilized	5/17/2024	5/17/2024	5/17/2024	↑ ✓																																																																										
BOT Approval of Recommended CMAR	5/26/2024	5/26/2024	5/28/2024	↑ ✓																																																																										
100% CDs Complete	11/1/2024	2/14/2025	2/14/2025	↓ ✓																																																																										
GMP Submittal	12/1/2024	2/20/2025	2/20/2025	↓ ✓																																																																										
BOT Approval of GMP	12/10/2024	3/25/2025	3/25/2025	↓ ✓																																																																										
Obtain Building Permit	12/20/2024	4/16/2025	4/21/2025	↓ ✓																																																																										
Contractor Mobilized	1/6/2025	4/17/2025	4/21/2025	↓ ✓																																																																										
Substantial Completion	4/1/2026	4/24/2026	3/23/2026	↓ ✓																																																																										
Final Completion	5/1/2026	5/26/2026		↓																																																																										
Project Type Renovation		Project Phase Construction		Scope Description *Renovations Collin Higher Education Center - Renovations of selected spaces on 1st, 2nd, 3rd and 4th floor.																																																																										
Project Manager Melissa Perette		Contractor/CM Skanska							Architect IN2 Architecture																																																																					
Project Directory					Progress Summary																																																																									
Company		Project Role			Status Date Notes																																																																									
AECOM Technical Services, Inc.		Program Manager			5/31/2026 Final CO was obtained from the City of McKinney on May 12th. Project closeout is in progress. Pending is punchlist for fire-rated frames.																																																																									
Collin College		Owner																																																																												
IN2 Architecture		A/E																																																																												
Skanska		A/E																																																																												
RWB Consulting Engineers																																																																														
Cost Summary																																																																														
Budget Group	Original Budget	Current Budget	Commitments	Approved Changes	Total Commitments	Pending Commitments	Expended to Date																																																																							
Construction, Equipment & Furnishings	\$7,172,040.00	\$7,665,990.00	\$7,512,880.90	\$3,439.00	\$7,516,319.90	\$0.00	\$6,819,069.12																																																																							
Contingency	\$562,950.00	\$28,301.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00																																																																							
Investigation, Testing & Verification	\$117,927.00	\$121,960.00	\$121,960.00	\$0.00	\$121,960.00	\$0.00	\$93,692.15																																																																							
Management, Design & Pre-Construction	\$860,348.36	\$883,834.36	\$844,348.36	\$39,486.00	\$883,834.36	\$0.00	\$701,695.75																																																																							
Miscellaneous	\$6,540.00	\$19,720.00	\$17,420.00	\$120.00	\$17,540.00	\$0.00	\$14,480.00																																																																							
Total	\$8,719,805.36	\$8,719,805.36	\$8,496,609.26	\$43,045.00	\$8,539,654.26	\$0.00	\$7,628,937.02																																																																							



Plano Renovation

Project Name Plano Renovation		 		Schedule																																																																																													
Project Name Plano Renovation		Project Number PJ1064		<table border="1"> <thead> <tr> <th>Activity</th> <th>Baseline Finish</th> <th>Planned Finish</th> <th>Actual Finish</th> <th></th> <th></th> </tr> </thead> <tbody> <tr> <td>BOT Approval of Construction Delivery Method</td> <td>1/26/2024</td> <td>1/26/2024</td> <td>1/26/2024</td> <td>↑</td> <td>✓</td> </tr> <tr> <td>BOT Approval of Recommended A/E</td> <td>1/26/2024</td> <td>1/26/2024</td> <td>1/26/2024</td> <td>↑</td> <td>✓</td> </tr> <tr> <td>BOT Approval of Program Manager</td> <td>2/27/2024</td> <td>2/27/2024</td> <td>2/27/2024</td> <td>↑</td> <td>✓</td> </tr> <tr> <td>BOT Approval of Recommended CMAR</td> <td>3/26/2024</td> <td>3/26/2024</td> <td>3/26/2024</td> <td>↑</td> <td>✓</td> </tr> <tr> <td>Architect Mobilized</td> <td>4/19/2024</td> <td>4/19/2024</td> <td>4/19/2024</td> <td>↑</td> <td>✓</td> </tr> <tr> <td>GMP 1 Construction Documents Submittal</td> <td>7/26/2024</td> <td>8/2/2024</td> <td>8/2/2024</td> <td>↓</td> <td>✓</td> </tr> <tr> <td>BOT Approval of GMP 1</td> <td>9/24/2024</td> <td>9/24/2024</td> <td>9/24/2024</td> <td>↑</td> <td>✓</td> </tr> <tr> <td>GMP 2 Construction Documents Submittal</td> <td>10/21/2024</td> <td>9/19/2024</td> <td>9/20/2024</td> <td>↑</td> <td>✓</td> </tr> <tr> <td>BOT Approval of GMP 2</td> <td>12/10/2024</td> <td>12/10/2024</td> <td>12/10/2024</td> <td>↑</td> <td>✓</td> </tr> <tr> <td>Obtain Building Permit</td> <td>12/13/2024</td> <td>1/13/2025</td> <td>1/30/2025</td> <td>↓</td> <td>✓</td> </tr> <tr> <td>Contractor Mobilized</td> <td>12/20/2024</td> <td>12/20/2024</td> <td>12/20/2024</td> <td>↑</td> <td>✓</td> </tr> <tr> <td>Substantial Completion</td> <td>6/1/2026</td> <td>7/30/2026</td> <td></td> <td>↓</td> <td></td> </tr> <tr> <td>Final Completion</td> <td>7/21/2026</td> <td>8/6/2026</td> <td></td> <td>↓</td> <td></td> </tr> <tr> <td>Student Occupancy</td> <td>8/17/2026</td> <td>8/17/2026</td> <td></td> <td>↑</td> <td></td> </tr> </tbody> </table>				Activity	Baseline Finish	Planned Finish	Actual Finish			BOT Approval of Construction Delivery Method	1/26/2024	1/26/2024	1/26/2024	↑	✓	BOT Approval of Recommended A/E	1/26/2024	1/26/2024	1/26/2024	↑	✓	BOT Approval of Program Manager	2/27/2024	2/27/2024	2/27/2024	↑	✓	BOT Approval of Recommended CMAR	3/26/2024	3/26/2024	3/26/2024	↑	✓	Architect Mobilized	4/19/2024	4/19/2024	4/19/2024	↑	✓	GMP 1 Construction Documents Submittal	7/26/2024	8/2/2024	8/2/2024	↓	✓	BOT Approval of GMP 1	9/24/2024	9/24/2024	9/24/2024	↑	✓	GMP 2 Construction Documents Submittal	10/21/2024	9/19/2024	9/20/2024	↑	✓	BOT Approval of GMP 2	12/10/2024	12/10/2024	12/10/2024	↑	✓	Obtain Building Permit	12/13/2024	1/13/2025	1/30/2025	↓	✓	Contractor Mobilized	12/20/2024	12/20/2024	12/20/2024	↑	✓	Substantial Completion	6/1/2026	7/30/2026		↓		Final Completion	7/21/2026	8/6/2026		↓		Student Occupancy	8/17/2026	8/17/2026		↑	
Activity	Baseline Finish	Planned Finish	Actual Finish																																																																																														
BOT Approval of Construction Delivery Method	1/26/2024	1/26/2024	1/26/2024	↑	✓																																																																																												
BOT Approval of Recommended A/E	1/26/2024	1/26/2024	1/26/2024	↑	✓																																																																																												
BOT Approval of Program Manager	2/27/2024	2/27/2024	2/27/2024	↑	✓																																																																																												
BOT Approval of Recommended CMAR	3/26/2024	3/26/2024	3/26/2024	↑	✓																																																																																												
Architect Mobilized	4/19/2024	4/19/2024	4/19/2024	↑	✓																																																																																												
GMP 1 Construction Documents Submittal	7/26/2024	8/2/2024	8/2/2024	↓	✓																																																																																												
BOT Approval of GMP 1	9/24/2024	9/24/2024	9/24/2024	↑	✓																																																																																												
GMP 2 Construction Documents Submittal	10/21/2024	9/19/2024	9/20/2024	↑	✓																																																																																												
BOT Approval of GMP 2	12/10/2024	12/10/2024	12/10/2024	↑	✓																																																																																												
Obtain Building Permit	12/13/2024	1/13/2025	1/30/2025	↓	✓																																																																																												
Contractor Mobilized	12/20/2024	12/20/2024	12/20/2024	↑	✓																																																																																												
Substantial Completion	6/1/2026	7/30/2026		↓																																																																																													
Final Completion	7/21/2026	8/6/2026		↓																																																																																													
Student Occupancy	8/17/2026	8/17/2026		↑																																																																																													
Project Type Renovation		Project Phase Construction		Scope Description																																																																																													
Project Manager Tim Smith		Contractor/CM Skanska		<ul style="list-style-type: none"> * Renovations to the Plano Campus * The Renovation includes: <ul style="list-style-type: none"> - Roof Replacement - Expanding Science Labs - Renovation and Expanding Health Sciences - Renovation in various other areas 																																																																																													
Project Directory		Architect IN2 Architecture		Progress Summary																																																																																													
<table border="1"> <thead> <tr> <th>Company</th> <th>Project Role</th> </tr> </thead> <tbody> <tr><td>AECOM Technical Services, Inc.</td><td>Program Manager</td></tr> <tr><td>Collin College</td><td>Owner</td></tr> <tr><td>Skanska</td><td>Construction Manager-at-Risk</td></tr> <tr><td>IN2 Architecture</td><td>A/E</td></tr> <tr><td>BAi, LLC</td><td></td></tr> <tr><td>Dunaway</td><td></td></tr> <tr><td>Foodservice Design Professional</td><td></td></tr> <tr><td>MATSON DRISCOLL & DAMICO LLP</td><td></td></tr> <tr><td>Price Consulting, Inc.</td><td></td></tr> <tr><td>RWB Consulting Engineers</td><td></td></tr> </tbody> </table>		Company	Project Role	AECOM Technical Services, Inc.	Program Manager	Collin College	Owner	Skanska	Construction Manager-at-Risk	IN2 Architecture	A/E	BAi, LLC		Dunaway		Foodservice Design Professional		MATSON DRISCOLL & DAMICO LLP		Price Consulting, Inc.		RWB Consulting Engineers				<table border="1"> <thead> <tr> <th>Status Date</th> <th>Notes</th> </tr> </thead> <tbody> <tr> <td>6/1/2026</td> <td>Plano Campus – Roof work continues. Contractor will install Theater balcony glass the weekend June 6th. Comm. Music system programming is almost complete working to schedule commissioning and training Mid-June. Kitchen/ Dining and E first floor work is continuing. Main Hallway ceiling demo and build back has begun.</td> </tr> </tbody> </table>				Status Date	Notes	6/1/2026	Plano Campus – Roof work continues. Contractor will install Theater balcony glass the weekend June 6th. Comm. Music system programming is almost complete working to schedule commissioning and training Mid-June. Kitchen/ Dining and E first floor work is continuing. Main Hallway ceiling demo and build back has begun.																																																																
Company	Project Role																																																																																																
AECOM Technical Services, Inc.	Program Manager																																																																																																
Collin College	Owner																																																																																																
Skanska	Construction Manager-at-Risk																																																																																																
IN2 Architecture	A/E																																																																																																
BAi, LLC																																																																																																	
Dunaway																																																																																																	
Foodservice Design Professional																																																																																																	
MATSON DRISCOLL & DAMICO LLP																																																																																																	
Price Consulting, Inc.																																																																																																	
RWB Consulting Engineers																																																																																																	
Status Date	Notes																																																																																																
6/1/2026	Plano Campus – Roof work continues. Contractor will install Theater balcony glass the weekend June 6th. Comm. Music system programming is almost complete working to schedule commissioning and training Mid-June. Kitchen/ Dining and E first floor work is continuing. Main Hallway ceiling demo and build back has begun.																																																																																																
Cost Summary																																																																																																	
Budget Group	Original Budget	Current Budget	Commitments	Approved Changes	Total Commitments	Pending Commitments	Expended to Date																																																																																										
Construction, Equipment & Furnishings	\$62,835,304.00	\$74,193,298.00	\$70,247,556.59	\$1,596,983.36	\$71,844,539.95	\$6,243.74	\$51,647,561.00																																																																																										
Contingency	\$2,372,401.00	\$1,008,102.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00																																																																																										
Investigation, Testing & Verification	\$1,150,911.00	\$1,359,240.00	\$616,157.00	\$41,936.75	\$658,093.75	\$0.00	\$332,193.19																																																																																										
Management, Design & Pre-Construction	\$6,895,542.00	\$8,078,310.00	\$6,987,542.26	\$1,080,768.00	\$8,068,310.26	\$0.00	\$6,156,169.90																																																																																										
Miscellaneous	\$305,272.00	\$361,050.00	\$123,924.74	\$3,906.00	\$127,830.74	\$0.00	\$108,272.78																																																																																										
Total	\$73,559,430.00	\$85,000,000.00	\$77,975,180.59	\$2,723,594.11	\$80,698,774.70	\$6,243.74	\$58,244,196.87																																																																																										

Health Science Center

Project Name Health Science Center		 		Schedule			
Project Name Health Science Center		Project Number PJ1067		Activity			
Project Type New		Project Phase Construction		Baseline Finish			
Project Manager Penny Busch		Contractor/CM McCarthy Building Comp...		Planned Finish			
		Architect PBK Architects, Inc.		Actual Finish			
Scope Description							
Construction of new Health Science Center, Frisco, Texas The building will be: 3 stories totaling 116,902 square feet 82,593 square feet to be finished out, 34,309 square feet to remain shell New Programs: MLT Radiography Cath Lab Nuclear Med CT Technology MRI Technology Programs Moving or Expanding: Nursing Diagnostic Sonography (program move from McKinney) Physical Therapy Assistant Health Professions Interdisciplinary Spaces: AR/VR Lab space Healthcare Simulation space							
Project Directory							
Company				Project Role			
JQ Engineering (IMEG)				Structural Engineer			
AECOM Technical Services, Inc.				Program Manager			
Collin College				Owner			
RWB Consulting Engineers				MEP			
CCA Landscape Architects, Inc.				Landscape Architect			
McCarthy Building Companies, Inc.				Construction Manager-at-Risk			
RLK Engineering				Civil Engineer			
PBK Architects, Inc.				A/E			
PBK							
Progress Summary							
Status Date Notes							
5/31/2026 Glazing work nearing completion for the building while roofing continues for on north vestibule roof.							
5/31/2026 Interior Level 1 - ceiling grid beginning in few areas, tape and float progressing, and restroom tile delivered to site							
5/31/2026 Interior Level 2 - walls are being two sided, flex duct install ongoing and prime/paint in progress.							
Cost Summary							
Budget Group	Original Budget	Current Budget	Commitments	Approved Changes	Total Commitments	Pending Commitments	Expended to Date
Construction, Equipment & Furnishings	\$47,793,062.00	\$64,093,786.00	\$15,107,588.60	\$43,740,506.00	\$58,848,094.60	\$0.00	\$33,383,132.32
Contingency	\$1,987,031.00	\$802,268.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
Investigation, Testing & Verification	\$777,028.00	\$777,028.00	\$420,227.00	\$0.00	\$420,227.00	\$0.00	\$175,242.49
Management, Design & Pre-Construction	\$5,212,227.00	\$6,096,267.00	\$5,244,227.03	\$827,040.00	\$6,071,267.03	\$0.00	\$5,022,913.09
Miscellaneous	\$44,652.00	\$44,652.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
Total	\$55,814,000.00	\$71,814,001.00	\$20,772,042.63	\$44,567,546.00	\$65,339,588.63	\$0.00	\$38,581,287.90

Wylie CTE

Project Name Wylie CTE		 		Schedule																																																																																																									
Project Name Wylie CTE		Project Number PJ1068		<table border="1"> <thead> <tr> <th>Activity</th> <th>Baseline Finish</th> <th>Planned Finish</th> <th>Actual Finish</th> <th></th> <th></th> </tr> </thead> <tbody> <tr> <td>BOT Approval of Construction Delivery Method</td> <td>1/26/2024</td> <td>1/26/2024</td> <td>1/26/2024</td> <td>↑</td> <td>✓</td> </tr> <tr> <td>BOT Approval of Program Manager</td> <td>9/24/2024</td> <td>9/24/2024</td> <td>9/24/2024</td> <td>↑</td> <td>✓</td> </tr> <tr> <td>BOT Approval of Recommended A/E and CMAR Firms</td> <td>9/24/2024</td> <td>9/24/2024</td> <td>9/24/2024</td> <td>↑</td> <td>✓</td> </tr> <tr> <td>Architect Mobilized</td> <td>10/21/2024</td> <td>10/21/2024</td> <td>11/11/2024</td> <td>↑</td> <td>✓</td> </tr> <tr> <td>Programming</td> <td>12/17/2024</td> <td>4/30/2025</td> <td>4/30/2025</td> <td>↓</td> <td>✓</td> </tr> <tr> <td>Schematic Design</td> <td>2/18/2025</td> <td>5/30/2025</td> <td>5/30/2025</td> <td>↓</td> <td>✓</td> </tr> <tr> <td>Design Development Drawings</td> <td>4/22/2025</td> <td>8/8/2025</td> <td>8/8/2025</td> <td>↓</td> <td>✓</td> </tr> <tr> <td>100% Construction Documents</td> <td>8/29/2025</td> <td>10/10/2025</td> <td>10/12/2025</td> <td>↓</td> <td>✓</td> </tr> <tr> <td>GMP - Submitted to AECOM/Page for Review</td> <td>10/27/2025</td> <td>12/12/2025</td> <td>12/17/2025</td> <td>↓</td> <td>✓</td> </tr> <tr> <td>BOT Approval of GMP</td> <td>12/9/2025</td> <td>1/27/2026</td> <td>1/30/2026</td> <td>↓</td> <td>✓</td> </tr> <tr> <td>Structures Complete</td> <td>11/13/2026</td> <td>11/13/2026</td> <td></td> <td>↑</td> <td></td> </tr> <tr> <td>Interior Finish-Out Complete</td> <td>4/28/2027</td> <td>5/18/2027</td> <td></td> <td>↓</td> <td></td> </tr> <tr> <td>Substantial Completion</td> <td>5/3/2027</td> <td>6/30/2027</td> <td></td> <td>↓</td> <td></td> </tr> <tr> <td>Final CO</td> <td>5/14/2027</td> <td>6/30/2027</td> <td></td> <td>↓</td> <td></td> </tr> <tr> <td>Final Completion</td> <td>6/4/2027</td> <td>7/30/2027</td> <td></td> <td>↓</td> <td></td> </tr> <tr> <td>Student Occupancy</td> <td>8/25/2027</td> <td>8/25/2027</td> <td></td> <td>↑</td> <td></td> </tr> </tbody> </table>				Activity	Baseline Finish	Planned Finish	Actual Finish			BOT Approval of Construction Delivery Method	1/26/2024	1/26/2024	1/26/2024	↑	✓	BOT Approval of Program Manager	9/24/2024	9/24/2024	9/24/2024	↑	✓	BOT Approval of Recommended A/E and CMAR Firms	9/24/2024	9/24/2024	9/24/2024	↑	✓	Architect Mobilized	10/21/2024	10/21/2024	11/11/2024	↑	✓	Programming	12/17/2024	4/30/2025	4/30/2025	↓	✓	Schematic Design	2/18/2025	5/30/2025	5/30/2025	↓	✓	Design Development Drawings	4/22/2025	8/8/2025	8/8/2025	↓	✓	100% Construction Documents	8/29/2025	10/10/2025	10/12/2025	↓	✓	GMP - Submitted to AECOM/Page for Review	10/27/2025	12/12/2025	12/17/2025	↓	✓	BOT Approval of GMP	12/9/2025	1/27/2026	1/30/2026	↓	✓	Structures Complete	11/13/2026	11/13/2026		↑		Interior Finish-Out Complete	4/28/2027	5/18/2027		↓		Substantial Completion	5/3/2027	6/30/2027		↓		Final CO	5/14/2027	6/30/2027		↓		Final Completion	6/4/2027	7/30/2027		↓		Student Occupancy	8/25/2027	8/25/2027		↑	
Activity	Baseline Finish	Planned Finish	Actual Finish																																																																																																										
BOT Approval of Construction Delivery Method	1/26/2024	1/26/2024	1/26/2024	↑	✓																																																																																																								
BOT Approval of Program Manager	9/24/2024	9/24/2024	9/24/2024	↑	✓																																																																																																								
BOT Approval of Recommended A/E and CMAR Firms	9/24/2024	9/24/2024	9/24/2024	↑	✓																																																																																																								
Architect Mobilized	10/21/2024	10/21/2024	11/11/2024	↑	✓																																																																																																								
Programming	12/17/2024	4/30/2025	4/30/2025	↓	✓																																																																																																								
Schematic Design	2/18/2025	5/30/2025	5/30/2025	↓	✓																																																																																																								
Design Development Drawings	4/22/2025	8/8/2025	8/8/2025	↓	✓																																																																																																								
100% Construction Documents	8/29/2025	10/10/2025	10/12/2025	↓	✓																																																																																																								
GMP - Submitted to AECOM/Page for Review	10/27/2025	12/12/2025	12/17/2025	↓	✓																																																																																																								
BOT Approval of GMP	12/9/2025	1/27/2026	1/30/2026	↓	✓																																																																																																								
Structures Complete	11/13/2026	11/13/2026		↑																																																																																																									
Interior Finish-Out Complete	4/28/2027	5/18/2027		↓																																																																																																									
Substantial Completion	5/3/2027	6/30/2027		↓																																																																																																									
Final CO	5/14/2027	6/30/2027		↓																																																																																																									
Final Completion	6/4/2027	7/30/2027		↓																																																																																																									
Student Occupancy	8/25/2027	8/25/2027		↑																																																																																																									
Project Type New		Project Phase Construction		Scope Description																																																																																																									
Project Manager Kella Hilton		Contractor/CM Skanska		Construction of a new Career Technical Education (CTE) building on the Wylie Campus. - Approximately 66,000 square feet - Building will provide space for the following: - Welding - HVAC - Electronic Engineering Technology (EET) - Certified Nurse Aid (CNA)																																																																																																									
Architect Stantec Architecture (f...		Project Directory		Progress Summary																																																																																																									
<table border="1"> <thead> <tr> <th>Company</th> <th>Project Role</th> </tr> </thead> <tbody> <tr> <td>AECOM Technical Services, Inc.</td> <td></td> </tr> <tr> <td>Collin College</td> <td></td> </tr> <tr> <td>RWB Consulting Engineers</td> <td></td> </tr> <tr> <td>Skanska</td> <td></td> </tr> <tr> <td>Stantec Architecture (fka Page)</td> <td></td> </tr> </tbody> </table>		Company	Project Role	AECOM Technical Services, Inc.		Collin College		RWB Consulting Engineers		Skanska		Stantec Architecture (fka Page)				<table border="1"> <thead> <tr> <th>Status Date</th> <th>Notes</th> </tr> </thead> <tbody> <tr> <td>5/31/2026</td> <td>Building piers are complete and grade beams are in progress. Underground utility work continues. Preparation for the tilt wall panel pours has started.</td> </tr> </tbody> </table>				Status Date	Notes	5/31/2026	Building piers are complete and grade beams are in progress. Underground utility work continues. Preparation for the tilt wall panel pours has started.																																																																																						
Company	Project Role																																																																																																												
AECOM Technical Services, Inc.																																																																																																													
Collin College																																																																																																													
RWB Consulting Engineers																																																																																																													
Skanska																																																																																																													
Stantec Architecture (fka Page)																																																																																																													
Status Date	Notes																																																																																																												
5/31/2026	Building piers are complete and grade beams are in progress. Underground utility work continues. Preparation for the tilt wall panel pours has started.																																																																																																												
Cost Summary																																																																																																													
Budget Group	Original Budget	Current Budget	Commitments	Approved Changes	Total Commitments	Pending Commitments	Expended to Date																																																																																																						
Construction, Equipment & Furnishings	\$34,700,000.00	\$46,719,560.59	\$40,313,966.00	\$0.00	\$40,313,966.00	\$152,153.56	\$3,283,661.50																																																																																																						
Contingency	\$1,066,490.00	\$2,012,760.41	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00																																																																																																						
Investigation, Testing & Verification	\$720,000.00	\$973,215.00	\$378,040.00	\$6,600.00	\$384,640.00	\$0.00	\$43,162.89																																																																																																						
Management, Design & Pre-Construction	\$3,481,510.00	\$4,318,521.00	\$3,935,640.00	\$5,650.00	\$3,941,290.00	\$0.00	\$2,236,250.81																																																																																																						
Miscellaneous	\$32,000.00	\$43,254.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00																																																																																																						
Total	\$40,000,000.00	\$54,067,311.00	\$44,627,646.00	\$12,250.00	\$44,639,896.00	\$152,153.56	\$5,563,075.20																																																																																																						

5 Completed Items

5.1 General Program

- Facilities Meeting held on May 4th and 11th

5.2 Procurement

- No Procurement items completed at this time.

5.3 Design

- No Design items completed at this time.

5.4 Pre-Construction

- No Pre-Construction items completed at this time.

5.5 Construction

- CHEC, Final CO was obtained on May 12th.
- Plano Campus, provost meetings held between Collin College, AECOM, and Skanska on May 1st, 5th, 6th, 8th, 12th, 13th, 15th, 19th, 20th, 22nd, 26th, 27th, and 29th
- Plano Campus, OAC meetings held on May 7th, 14th, 21st, 28th,
- Plano Campus, Allowance and Contingency review meeting was held between AECOM and Skanska on May 6th, 13th, 20th, 27th,
- Plano Campus, Coordination meeting was held between Collin College and AECOM on May 5th, 12th, 19th, 26th,
- Plano Campus, Project Closeout meeting was held between Collin College, AECOM, IN2, Skanska, Mechanical Partners, Alterman, Merit Roofing, and Lascoadi on May 1st
- Plano Campus, Kitchen coordination meeting was held between Collin College, AECOM, and Skanska on May 7th
- Plano Campus, Signage meeting was held between Collin College, AECOM, IN2, and Skanska on May 14th
- Plano Campus, Costume shop electrical meeting was held between Collin College, AECOM, and Skanska on May 15th
- Plano Campus, Existing panels/backfeeds/issues meeting was held between Collin College, AECOM, Skanska, and Alterman on May 18th
- Plano Campus, Pre-meeting for the Plano project was held between Collin College and AECOM on May 20th
- Plano Campus, Outage schedule meeting was held between Collin College, AECOM, and Skanska on May 21st
- Plano Campus, met to discuss electrical panels and plans moving forward with Collin College, AECOM, and Skanska on May 27th
- Plano Campus, Kitchen ceiling coordination meeting was held between Collin College, AECOM, Skanska, The Brass Effect, and Bearcom on May 28th
- Health Science Center, OAC meetings held on May 6th, 13th, 20th, and 27th
- Wylie CTE, OAC meetings held on May 7th, 14th, 21st and 28th
- Wylie CTE, Coordination meetings were held between Collin, Stantec, Skanska and AECOM with Lincoln, Airgas and HVAC on May 7th, 12th and 21st

- Wylie CTE, Construction cost review meetings were held between Stantec, Skanska and AECOM on May 5th, 12th, 19th and 26th

5.6 Acceptance and Close-Out

- Courtyard Center, Financial Meeting was held between AECOM and Skanska to reconcile and work on a final change order to the GMP on May 28th

6 Pending Items

6.1 General Program

- No General Program items are pending at this time.

6.2 Procurement

- No Procurement items pending at this time

6.3 Design

- No Design items pending at this time

6.4 Pre-Construction

- No Pre-Construction pending at this time

6.5 Construction

- Plano Campus, Roof work continues. Contractor will install Theater balcony glass the weekend June 6th. Comm. Music system programming is almost complete working to schedule commissioning and training Mid-June. Kitchen/ Dining and E first floor work is continuing. Main Hallway ceiling demo and build back has begun.
- Health Science Center, Exterior work continues with greengirt for metal panels being installed, brick onsite and masonry moving forward, final glazing modifications being completed, north roof install in progress and west roof to follow. Interior work is progressing with ceiling grid install on first level along with tape and float ongoing. Level 2 work includes the ongoing work of two siding walls, prime and paint in progress and flex duct install.
- Wylie CTE, activities for May include building pier cages and concrete pours to finish the piers. Grade beams are starting to be formed. Site grading and underground utilities will continue. The new underground water lines are being flushed and tested. Saw cutting for the new drive entrances and framing for the fire lane is in progress.

6.6 Acceptance and Close-Out

- Courtyard Center, financial close out in progress, with closeout documents under review.
- CHEC, All closeout documents have been submitted and are currently under review. Financial close out in progress.

7 Progress Pictures


7.1 Plano Campus Renovations




E Wing 1st Floor Computer Lab




E Wing 1st Floor Hallway

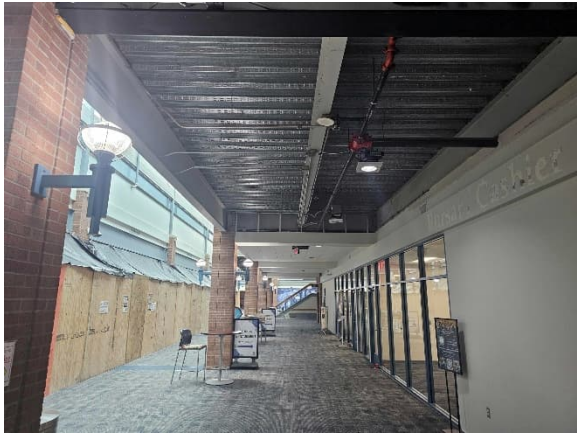

Hallway Demo and Buildback

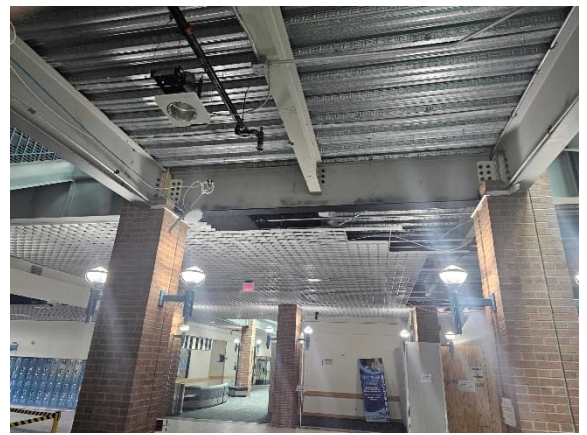

Hallway Demo

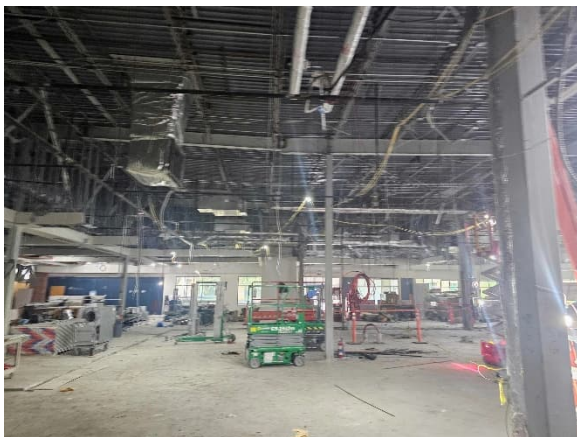

Kitchen Dining Area



Kitchen Walk In Coolers

7.2 Health Science Center



East Elevation




West Elevation




Northwest Elevations



Southwest Elevations

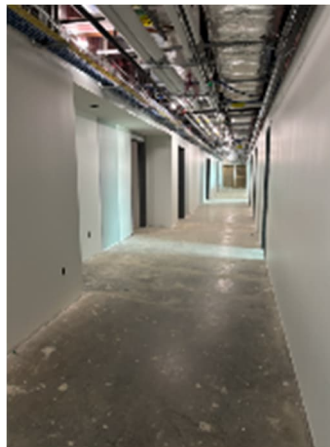

Level 1 NE Corridor

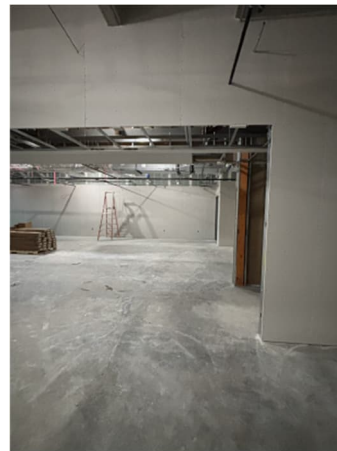

Level 2 Classroom 221

7.3 Wylie CTE



Jobsite Aerial



Forming Grade Beams



Building Piers



Forming Fire Lane
