


Argyle ISD Stadium

February 2026 Update

Overall Site




Grandstands

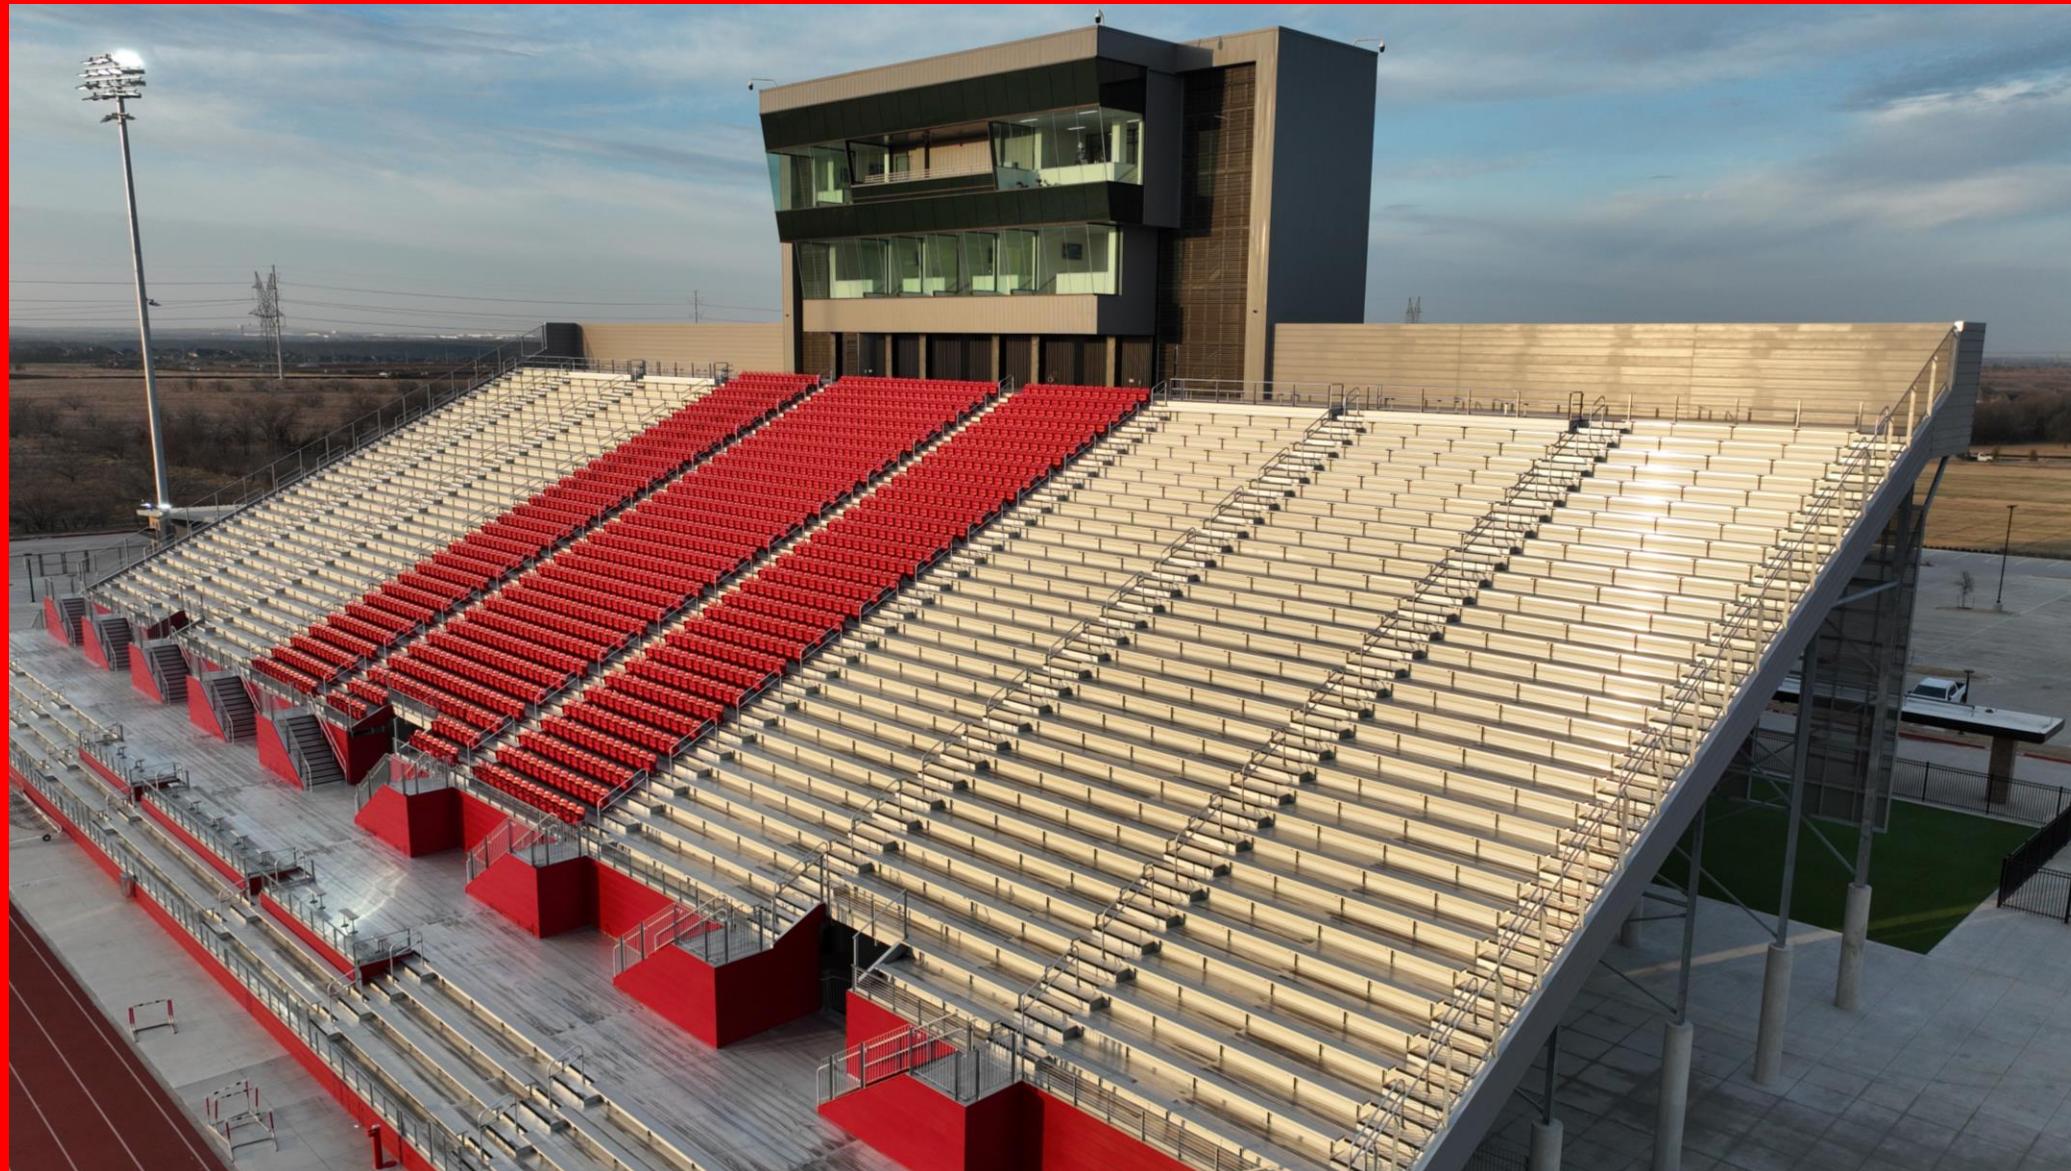

Turf at Entrance



Production Suite

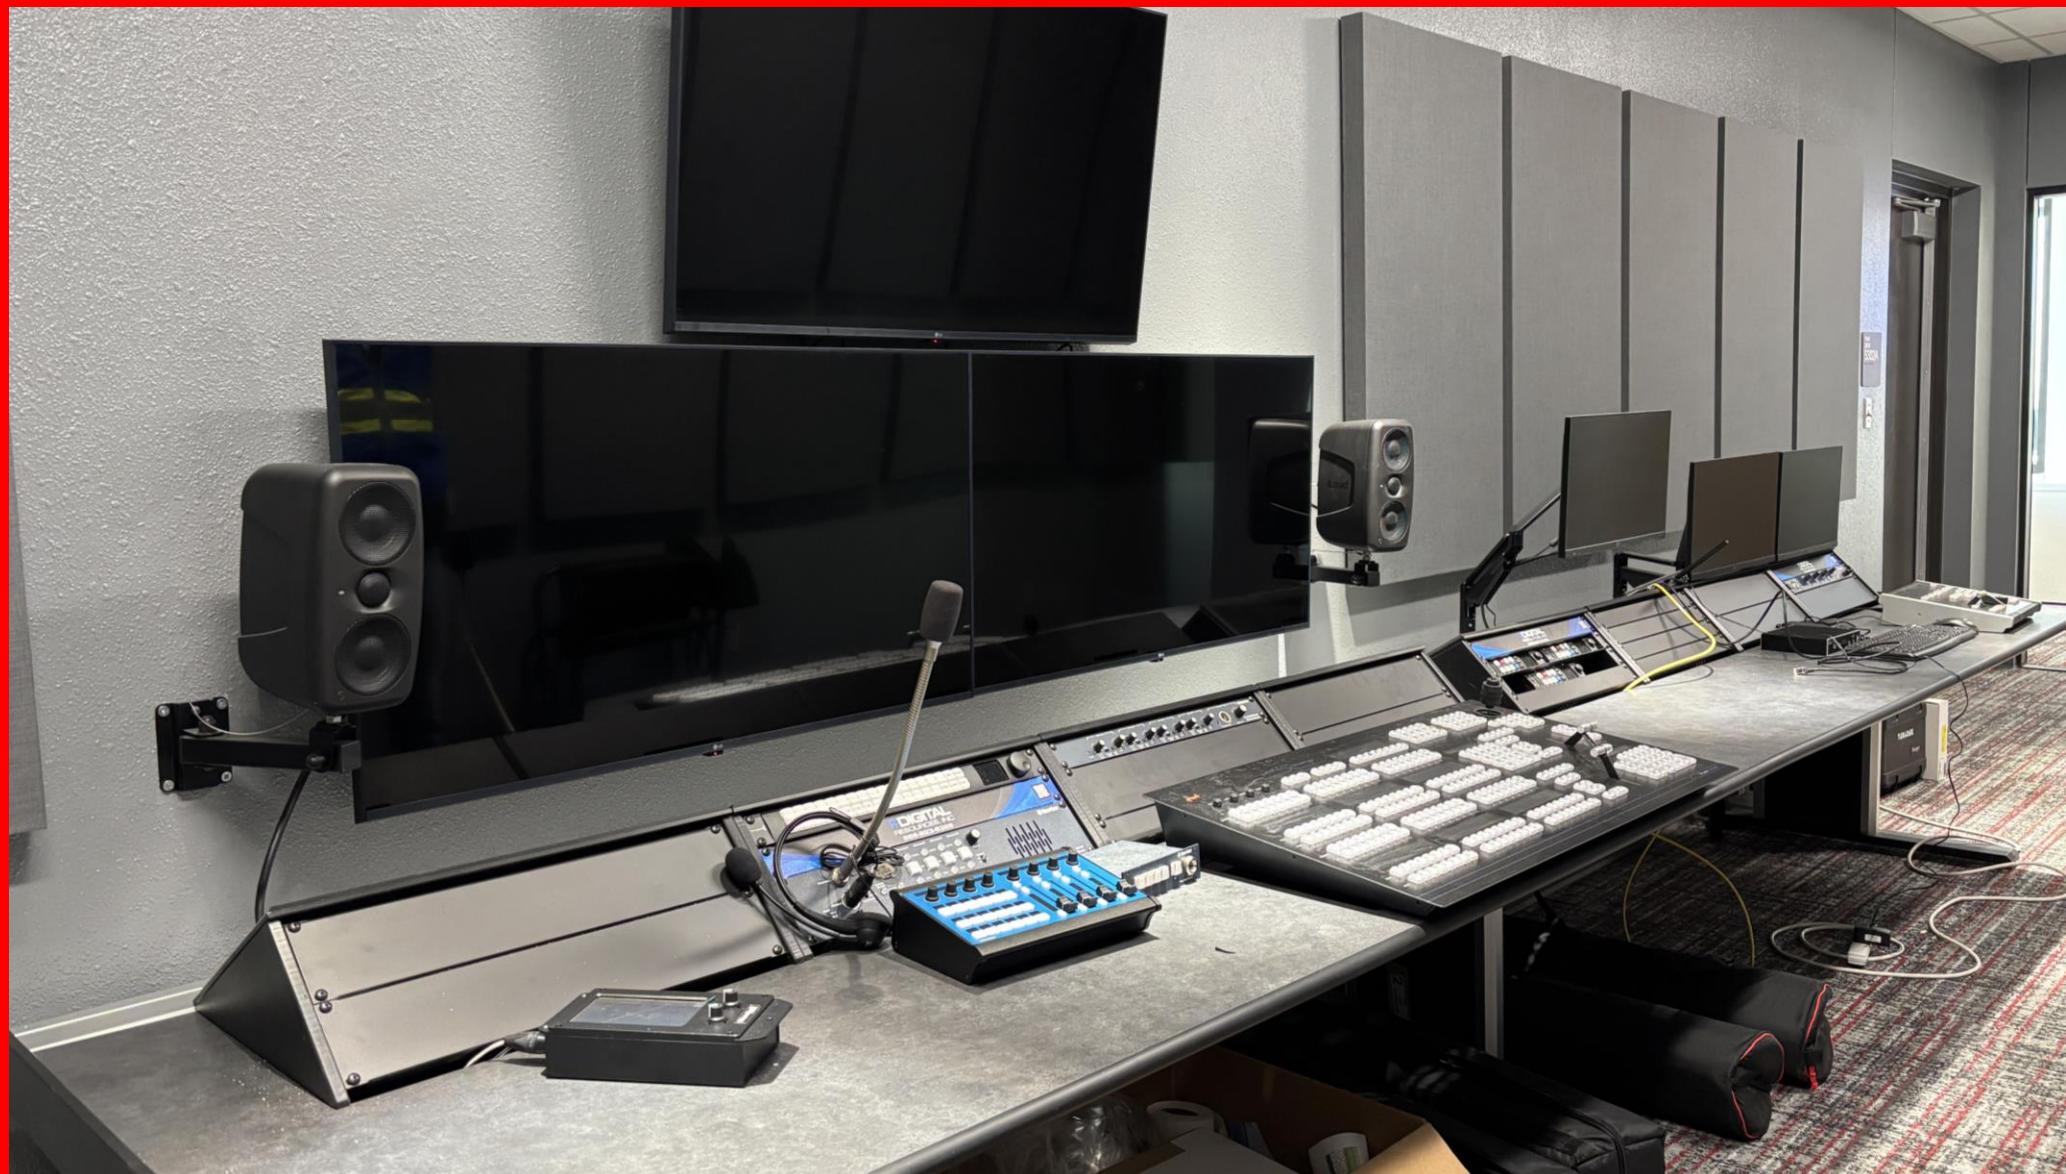

Production Equipment




IAC Exterior



IAC Exterior



IAC Interior

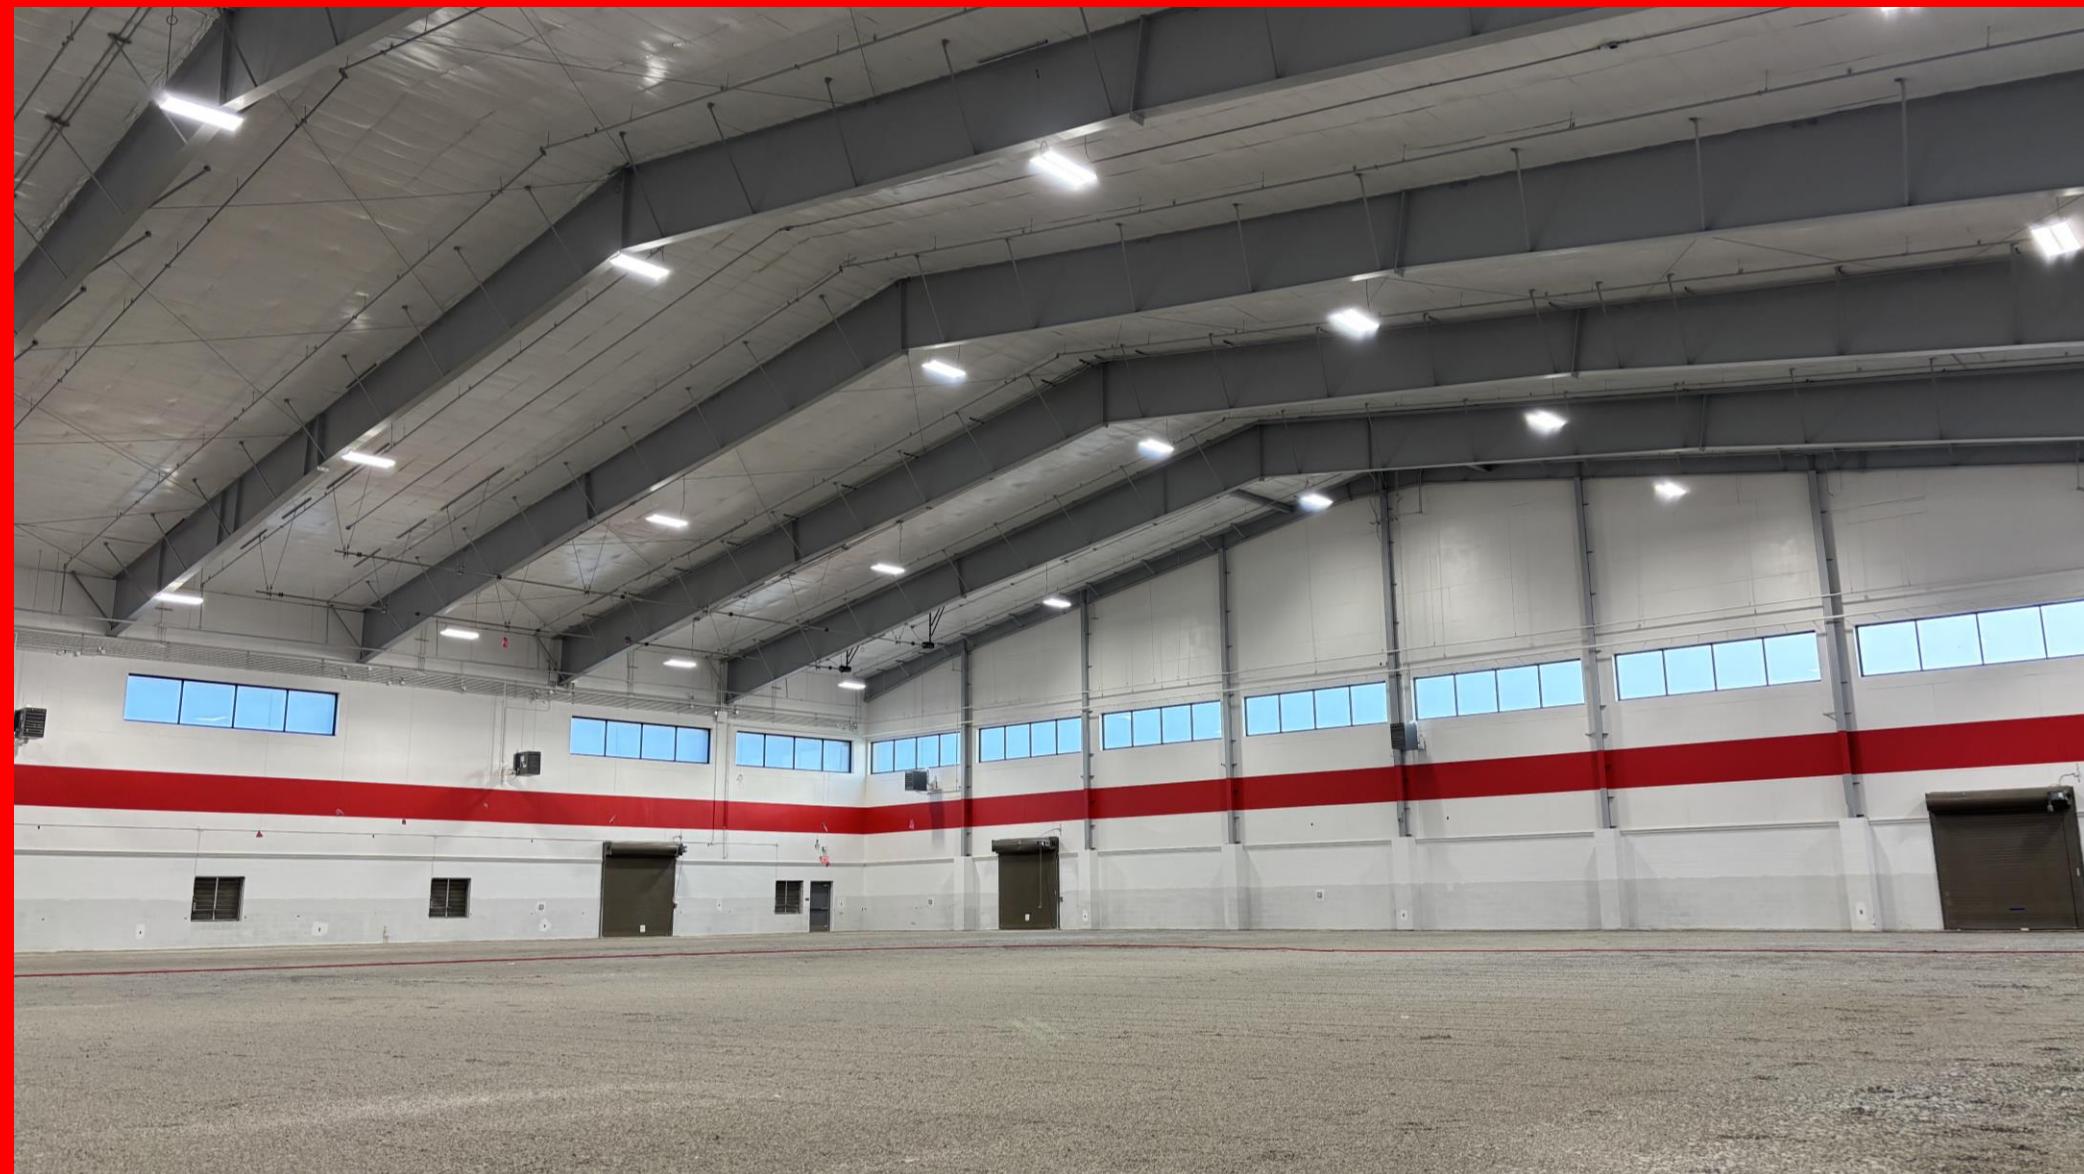

IAC Locker Room Showers



Look Ahead

- Testing & Training on Production System
- Interior Finishes at IAC
- Substantial Completion



Key Milestones

Key Milestone Tracking

Town Permit	September 5, 2024
Steel Erection Begins	Spring 2025
Grandstand & LED Board Install	Fall 2025
Interior Finishes	Fall 2025
Substantial Completion	January 2026



Scott Gibson Middle School

February 2026 Update

Overall Site



Courtyard




Exterior Classroom Wing



Drama Hall



Main Corridor

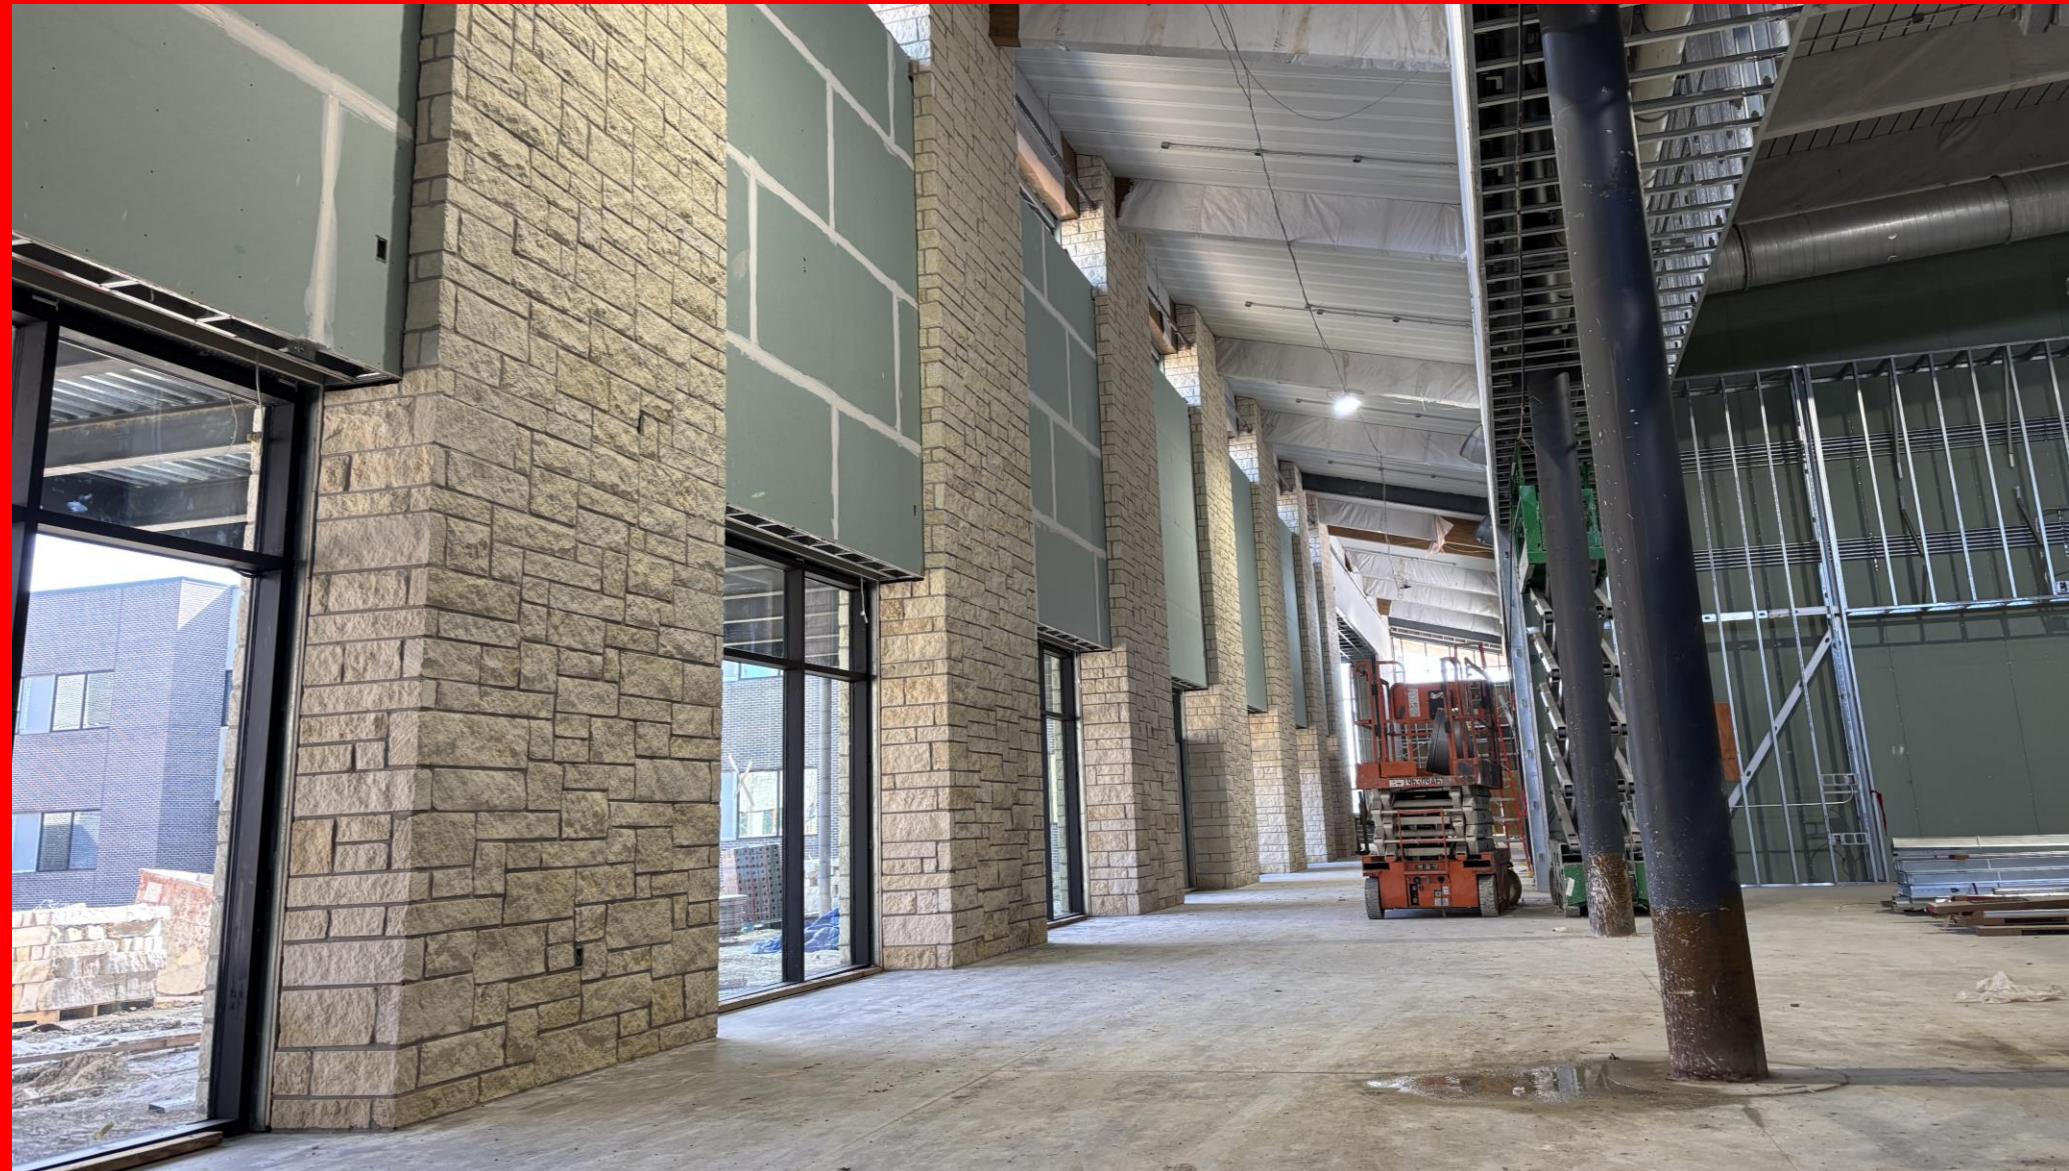

Collaboration Space



Library



Gymnasium



Concessions



Look Ahead

- Wall and Floor Finishes
- Install Millwork & Casework
- MEP Trim Out
- Permanent Power & Gas Connection



Key Milestones

Key Milestone Tracking


Town Permit	December 20, 2024
Structural Steel Completion	October 2025
Entire Building Dried-In	January 2026
Interior Finishes	Winter/Spring 2026
Substantial Completion	July 2026



Michael Ball Elementary School

February 2026 Update

Overall Site

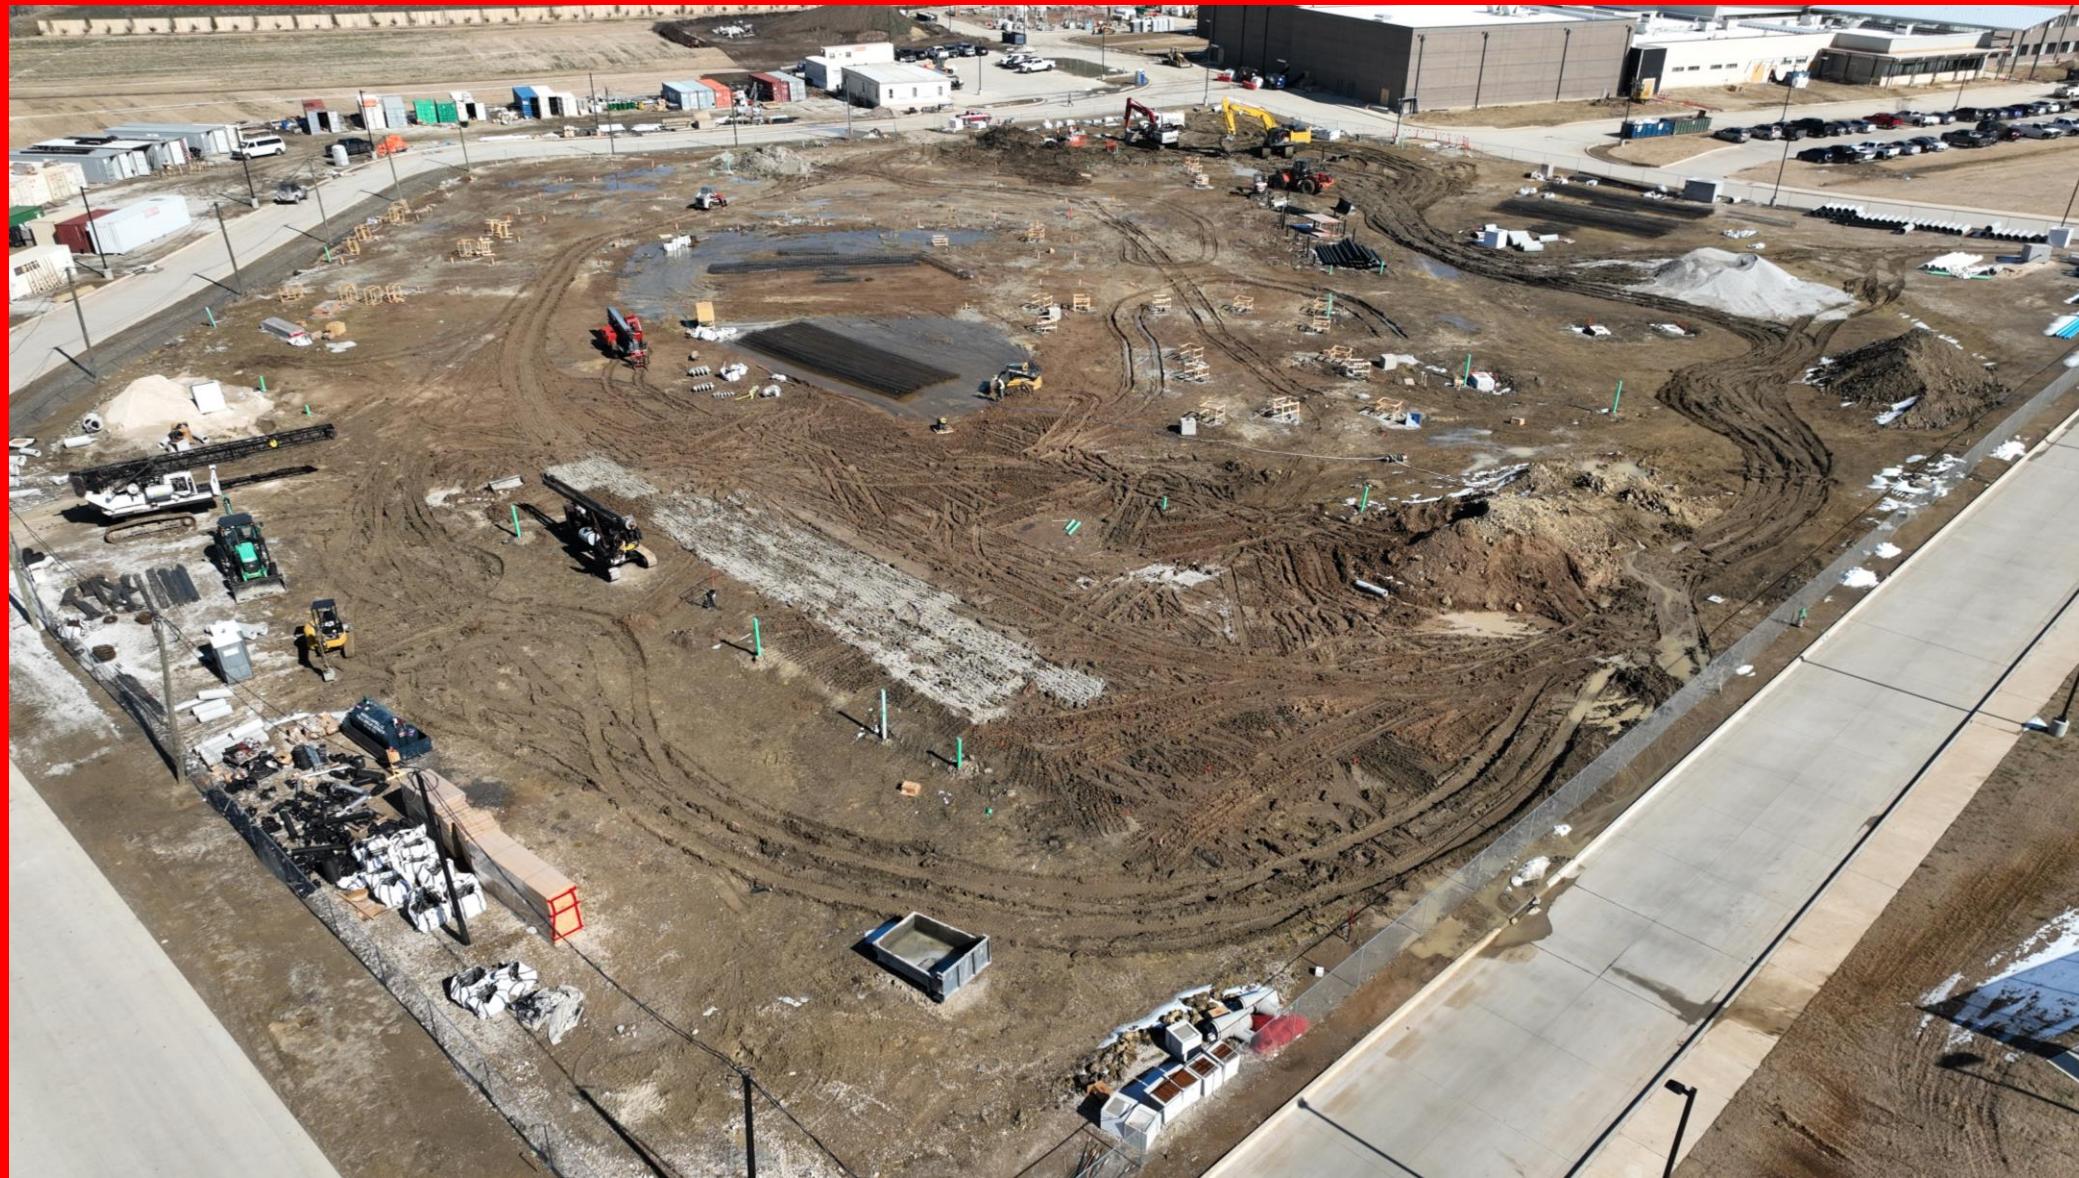

Unground Utilities



Look Ahead

- Complete Underground Utilities
- Grade Beams & Foundations
- Steel Erection



Key Milestones

Key Milestone Tracking

Town Permit	October 8, 2025
Mobilization	November 2025
Steel Erection Complete	May 2026
Substantial Completion	February 2027

