

SOUTH SAN ANTONIO INDEPENDENT SCHOOL DISTRICT

Agenda Item Summary

Meeting Date: October 12, 2022

Agenda Section: Presentation

Agenda Item Title: Current status of construction projects at West Campus Phase IV and the

Veterans Memorial

From: Andy A. Rocha – Executive Director of Operations, PBK and Marksman

Construction

Description: The Board of Trustees will be given a brief presentation on the status of the West

Campus Phase IV projects and the Veterans Memorial Project at South San H.S.

Recommendation: Presentation only

Funding Budget Code and Amount: Maintenance Tax Note

Mr. Henry Yzaguirre South San Antonio Independent School District 1450 Gillette Blvd San Antonio, TX 78224 VIA: E-mail



RE: UPDATE REPORT ON VETERANS MEMORIAL AND WEST CAMPUS HIGH SCHOOL PHASE IV PROJECTS

Dear Mr. Henry Yzaguirre:

Below is a report detailing the work that is currently under way for the Veterans Memorial at South San High Antonio High School and the Phase IV Renovations at West Campus High School.

Veterans Memorial

- Building permit was issued on October 3rd, 2022.
- PBK has been reviewing and responding to Submittals and pre-construction documents since the contract was signed in September.
- Mobilization by the Marksmen General Contractor will occur on November 17th, 2022.
- The estimated Substantial Completion date is March 22nd, 2022.

West Campus Phase IV - Cafeteria Package


- Currently under permitting process with the city.
- The city-required Preliminary Plan Review has been scheduled for October 17th at their Development Services Department offices.
- PBK has been reviewing and responding to Submittals and pre-construction documents since the contract was signed in September.
- Once permit is released, Marksmen will provide a detailed project schedule.

West Campus Phase IV - Kitchen, Athletics, Media Center Package


- Issue for Construction set of drawings and specifications will be issued on October 21st, 2022.
- Drawings will be sent to Marksmen General Contractors for an estimate of construction which will be presented to the Board for approval.

We look forward to continuing working with you and the district.



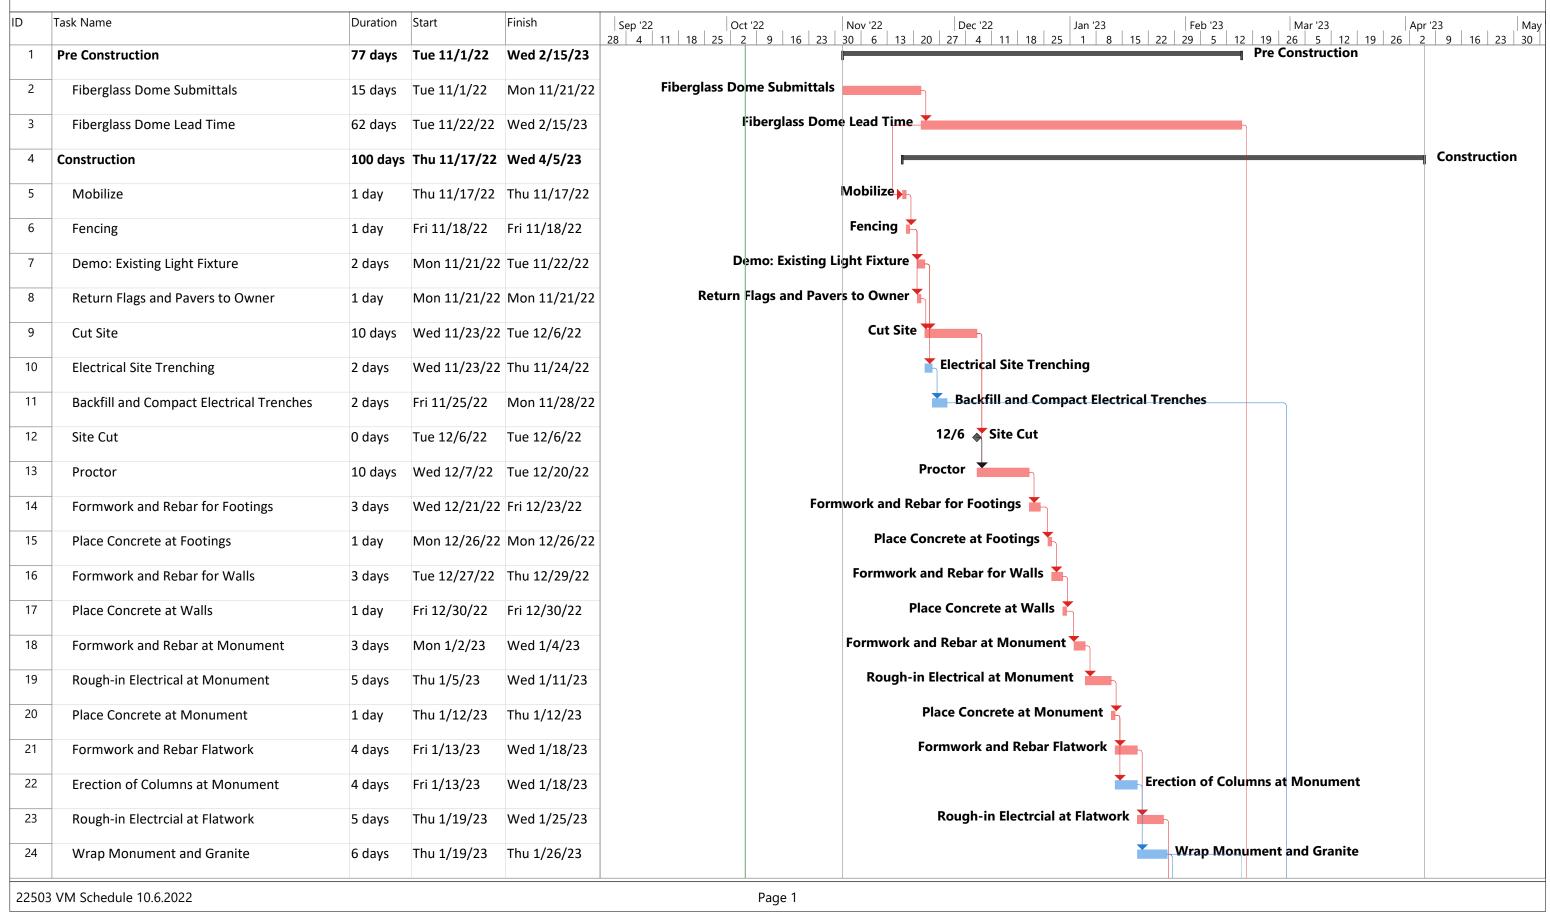



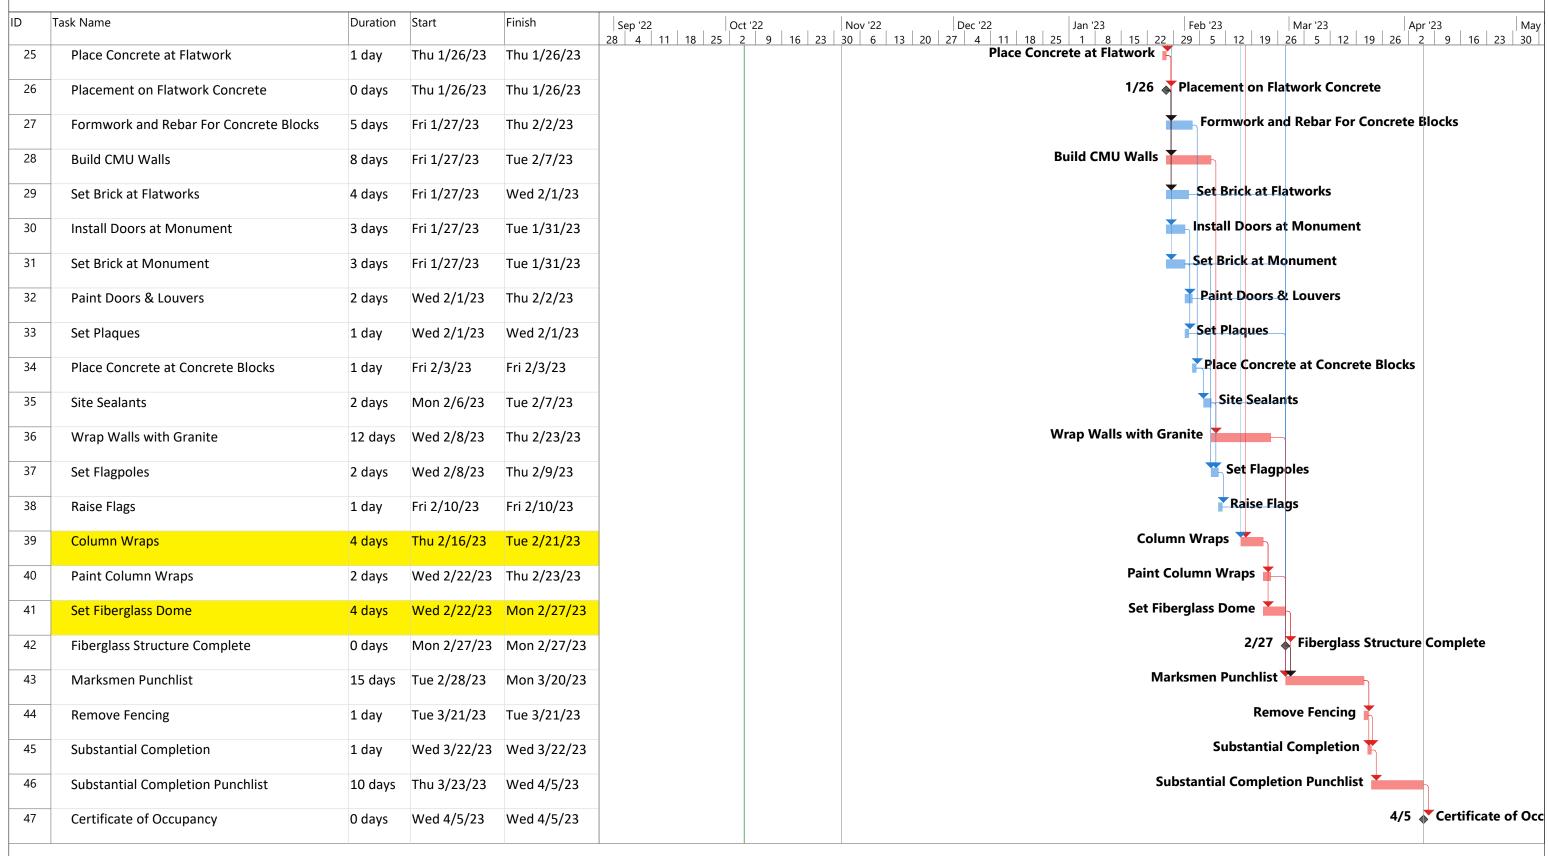

22503 VM Schedule 10.6.2022 Page 2
