DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

Construction Report

November 2022

Active Construction Timeline



Facility	Phase of Development	Construction Commencing	Construction Completion
Calhoun Middle Replacement Campus	Under Construction	Fall 2022	Summer 2024
LaGrone Academy Additions and Renovations	Under Construction	Spring 2022	Summer 2023
Carrico Athletic Complex Renovations	Complete	Spring 2021	Summer 2022
Newton Rayzor Elementary Replacement Campus	Under Construction	Fall 2022	Summer 2024
Transportation East Facility	Under Construction	Spring 2022	Early 2023
Cheek Middle School	Under Construction	Spring 2021	Summer 2023

Construction, Planning & Growth

Calhoun Middle School

November 2022

Prepared by:



2018 Bond Authorization Architects – Corgan & Associates

Contractor – Balfour Beatty Move In – Summer 2024





2018 Bond Authorization Architects – Corgan & Associates

Contractor – Balfour Beatty Move In – Summer 2024





2018 Bond Authorization
Architects – Corgan &
Associates
Contractor – Balfour Beatty
Move In – Summer 2024

Tasks completed previous 90 days:

- Project Started Aug. 8, 2022
- Asbestos Abatement on Existing Building
- Selective Interior Demo & Waste Removal
- Remove Inside Utilities
- Clearing & Grading Site



2018 Bond Authorization Architects – Corgan & Associates

Contractor – Balfour Beatty Move In – Summer 2024





2018 Bond Authorization Architects – Corgan & Associates

Contractor – Balfour Beatty Move In – Summer 2024





2018 Bond Authorization Architects – Corgan & Associates

Contractor – Balfour Beatty
Move In – Summer 2024

Upcoming tasks:

- Install New Utilities & Walls in Existing Buildings
- Construct New Building Pads
- Drill & Pour Piers
- Roof Existing Buildings
- Set Forms & Pour Grade Beams
- Install New HVAC, Electrical, & Plumbing in Existing Remodeled Buildings
- Install Underground Utilities in New Building Pad



2018 Bond Authorization

Architects - Corgan & Associates

Contractor – Balfour Beatty Move In – Summer 2024



DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

LaGrone Advanced Technical Center

November 2022

Prepared by:



2018 Bond Authorization
Architects – VLK
Contractor – Steele & Freeman Inc.

Move In - Spring 2023





2018 Bond Authorization Architects – VLK

Contractor – Steele & Freeman Inc.

Move In - Spring 2023

Tasks completed previous 90 days:

Cosmetology & Culinary Areas

- Framing, In-Wall, & Overhead Mechanical Work
- Flooring & Light Fixtures
- Set New RTU's
- Patched Existing Roof

New Addition

- Drilled Piers, Poured Grade Beams & Slabs
- Erected Steel
- Fire Proofed Structural Steel
- Tied in Tower Roofing Over Existing Building



2018 Bond Authorization
Architects – VLK
Contractor – Steele & Freeman
Inc.

Move In - Spring 2023





2018 Bond Authorization

Architects – VLK

Contractor – Steele & Freeman
Inc.

Move In - Spring 2023

Upcoming tasks:

Cosmetology & Culinary Install:

- Mod-U-Serve Line, Kitchen Equip, Wall Panels & Power to RTU's
- Life Safety Devices
- Tie in Kitchen Hoods
- Lab Specialty Items & Turnover to DISD

New Addition Install:

- Roof, Decking, Screens
- Exterior Framing/Sheathing, Waterproofing, Exterior Metal Panels
- Storefronts, Rainscreen System, Fire Suppression
- Interior Framing & Door Frames



2018 Bond Authorization
Architects – VLK
Contractor – Steele & Freeman
Inc.

Move In - Spring 2023





2018 Bond Authorization Architects – VLK Contractor – Steele & Freeman Inc.

Move In - Spring 2023

DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS


Construction, Planning & Growth

Carrico Stadium


November 2022

Prepared by:




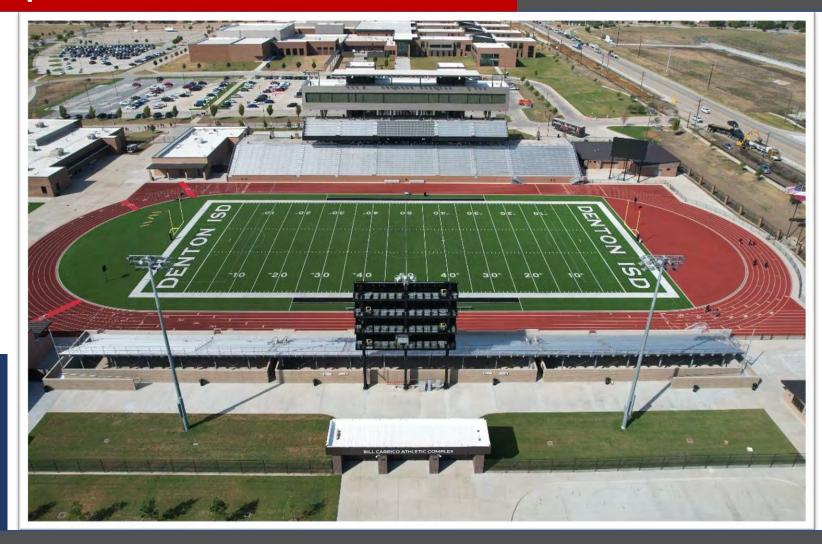




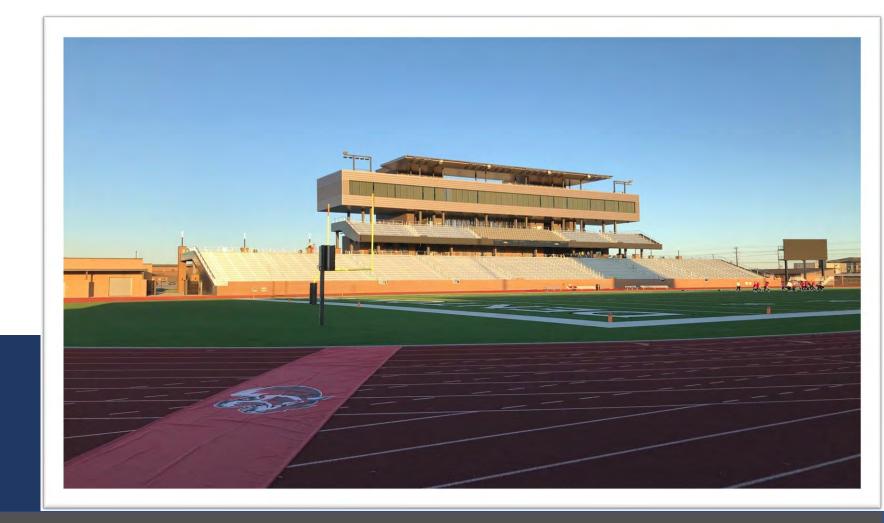



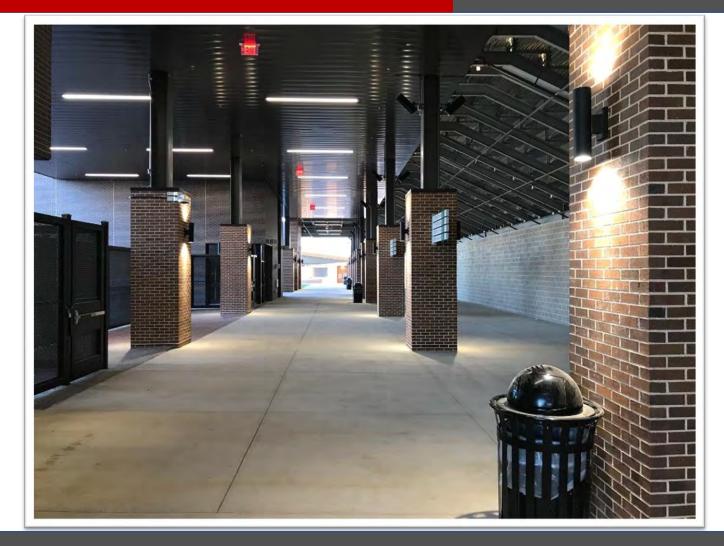



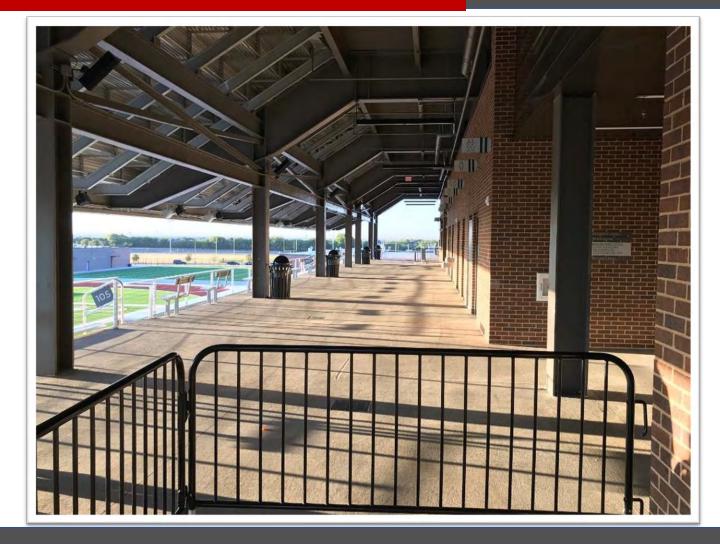







2018 Bond Authorization

Architects – VLK Architects

Contractor - Balfour Beatty Construction

CARRICO STADIUM OCT. 2022

Construction, Planning & Growth


Newton Rayzor Elementary School

November 2022

Prepared by:



2018 Bond Authorization
Architects – Corgan & Associates
Contractor – Balfour Beatty
Move In – Summer 2024

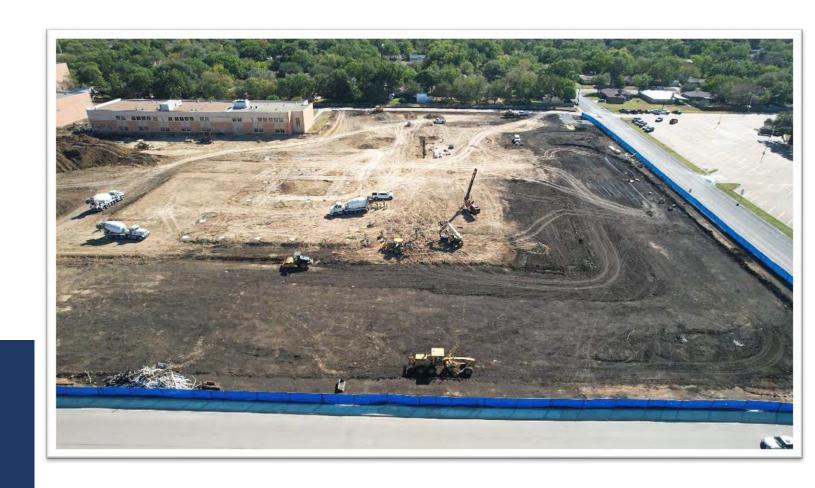



2018 Bond Authorization

Architects – Corgan & Associates

Contractor – Balfour Beatty


Move In – Summer 2024

Last 90 days tasks:

- Project Started Aug. 8, 2022
- Demo of Baseball Field & Existing Structures
- Removed Existing Parking Lot, Cleared & Graded Site, Topsoil Being Stored on Open Space at Existing Newton Rayzor Site.
- Constructed the Building Pad
- Drilled & Poured all Concrete Building Piers



2018 Bond Authorization
Architects – Corgan & Associates
Contractor – Balfour Beatty
Move In – Summer 2024

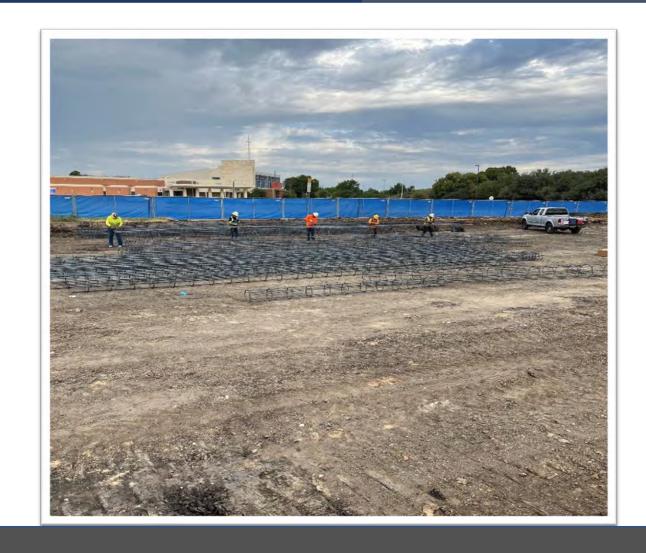



2018 Bond Authorization

Architects – Corgan & Associates

Contractor – Balfour Beatty

Move In – Summer 2024

Upcoming Tasks:

- Set Forms & Pour Grade Beams
- Relocate Existing Sanitary Sewer Line
- Install New Storm Sewer in Crescent Street
- Forming & Pouring Grade Beams
- Install Underground Utilities
- Onsite Utilities
- Set Forms & Reinforcement for Building Slab



2018 Bond Authorization
Architects – Corgan & Associates
Contractor – Balfour Beatty
Move In – Summer 2024





2018 Bond Authorization
Architects – Corgan & Associates
Contractor – Balfour Beatty
Move In – Summer 2024





2018 Bond Authorization Architects – Corgan & Associates

Contractor – Balfour Beatty Move In – Summer 2024

NEWTON RAYZOR ELEMENTARY REPLACEMENT CAMPUS OCTOBER 2022

DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

Transportation East Facility

November 2022

Prepared by:

Denton Transportation Center East



2018 Bond Authorization
Architects – Corgan & Associates
Contractor – Steele & Freeman Inc.
Move In – Fall 2022



Denton Transportation Center East



2018 Bond Authorization
Architects – Corgan & Associates
Contractor – Steele & Freeman Inc.
Move In – Fall 2022





Denton Transportation Center East



2018 Bond Authorization
Architects – Corgan & Associates
Contractor – Steele & Freeman Inc.
Move In – Fall 2022

Tasks completed previous 90 days:

- Water Proofing
- Brick Masonry
- Interior Texture & Painting
- Overhead Work
- Wash System Equipment Set in the Bay & Mechanical Room



2018 Bond Authorization
Architects – Corgan & Associates
Contractor – Steele & Freeman
Inc.

Move In - Fall 2022





2018 Bond Authorization
Architects – Corgan & Associates
Contractor – Steele & Freeman
Inc.

Move In - Fall 2022





2018 Bond Authorization
Architects – Corgan & Associates
Contractor – Steele & Freeman Inc.
Move In – Fall 2022


Upcoming tasks:

- Interior Finishes
- FF&E Move in
- Commissioning & Startup
- Punch Work
- Landscaping



2018 Bond Authorization
Architects – Corgan & Associates
Contractor – Steele & Freeman
Inc.

Move In - Fall 2022

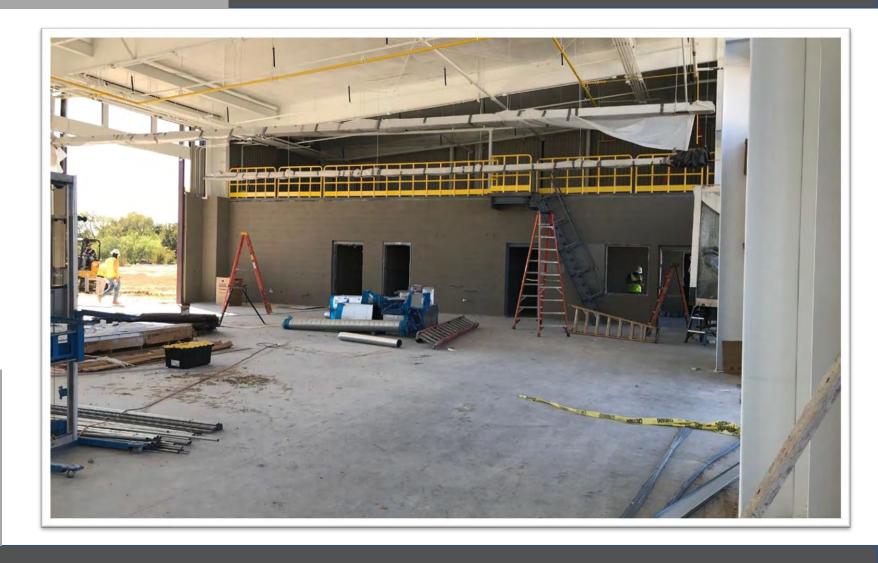



2018 Bond Authorization
Architects – Corgan & Associates
Contractor – Steele & Freeman Inc.
Move In – January 2023

Construction, Planning & Growth

PAT CHEEK MIDDLE SCHOOL CAMPUS

November 2022

Prepared by:




2018 Bond Authorization
Architects – Corgan Architects
Contractor – Northstar Builders
Move In – Summer 2023






2018 Bond Authorization
Architects – Corgan Architects
Contractor – Northstar
Builders

Move In – Summer 2023

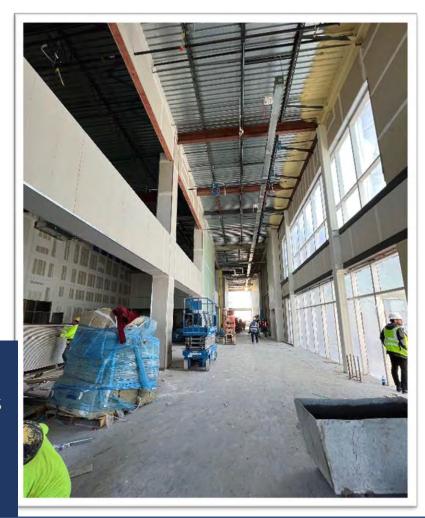

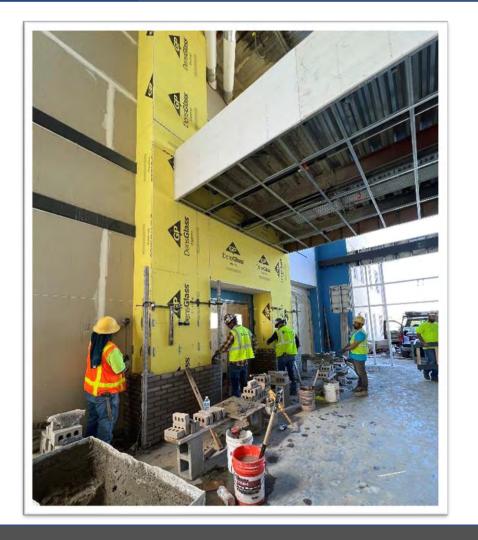




2018 Bond Authorization
Architects – Corgan Architects
Contractor – Northstar
Builders
Move In – Summer 2023

Tasks completed previous 90 days:

- Completed ICF Walls, Structural Steel, Masonry Veneer and roofing
- Completed Exterior Stud Framing and Exterior Windows
- Completed Interior Framing & Sheetrock areas A, B & F
- Completed MEP Overhead areas A, B & F
- Completed Walk In Freezer, Coolers and Exhaust Hoods in Kitchen
- Completed Tape, Bed, Texture and Paint area A 1st and 2nd Floor
- Complete Foundations for Concession, Storage Buildings and Sport Lighting at Football Field



2018 Bond Authorization
Architects – Corgan Architects
Contractor – Northstar
Builders
Move In – Summer 2023

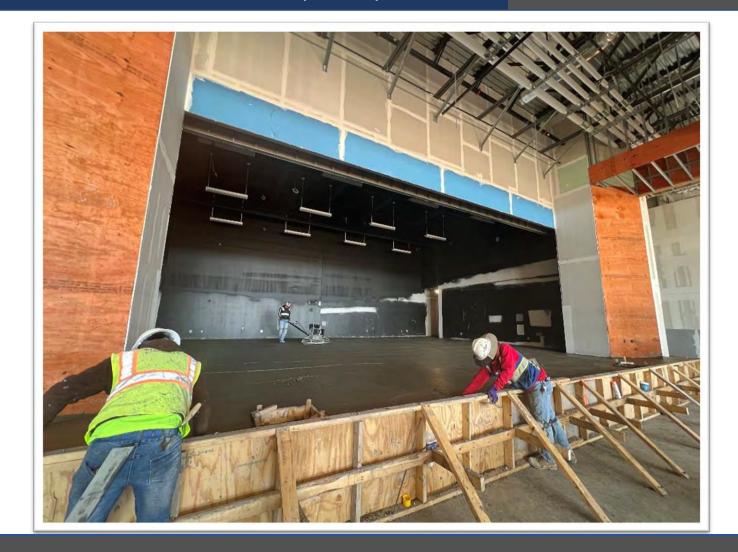



2018 Bond Authorization
Architects – Corgan Architects
Contractor – Northstar
Builders

Move In – Summer 2023

Upcoming Tasks:

- Complete / Punch Area A 1^{st,} 2nd Floor & Area F
- Set Kitchen Equipment
- Interior Framing and Sheetrock Areas C & D
- Hang Athletic Equipment, Paint in Gyms, Gym Floors & Gym Bleachers
- Complete Storefront and Glazing at Courtyards
- MEP Overhead areas C&D
- Ceramic Tile areas C, D, E & Stairs
- Interior Guard Rails
- CMU Structure, Masonry Veneer, Roofing & Canopy for Concession Building
- Install Flat Work, Install Bleachers, Press Box, Erect Metal Storage Building, Football Field & Track
- Sidewalks, Landscape & Irrigation at the Building




2018 Bond Authorization

Architects – Corgan Architects

Contractor – Northstar

Builders

Move In – Summer 2023

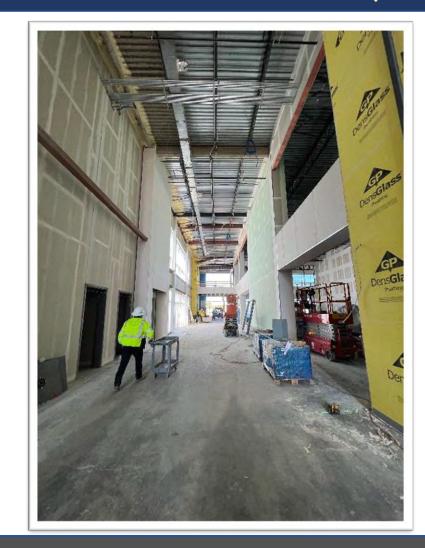





2018 Bond Authorization

Architects – Corgan Architects

Contractor – Northstar

Builders

Move In – Summer 2023

CHEEK MIDDLE SCHOOL OCT. 2022

DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Maintenance & Operations

Controls, MEP, Fire Alarm & Vestibule Projects

November 2022

Controls, MEP, Fire Alarm & Vestibule Projects



2018 Bond Authorization Maintenance

Facility	HVAC Controls	Access Control	Mechanical RTUs	Fire Alarm	Secure Vestibule
Ann Windle	Complete	Complete	Complete	In Progress	Design
Borman	In Progress	In Progress	Complete	N/A	N/A
Crownover	In Progress	In Progress	Complete	In Progress	N/A
Davis School	In Progress	In Progress	Complete	Complete	Complete
EP Rayzor	Complete	Complete	Complete	In Progress	N/A
Evers Park	In Progress	In Progress	Complete	In Progress	N/A
Ginnings	Complete	Complete	Complete	In Progress	N/A
Hodge	In Progress	In Progress	Complete	N/A	N/A

Controls, MEP, Fire Alarm & Vestibule Projects



2018 Bond Authorization Maintenance

Facility	HVAC Control	Access Control	Mechanical RTUs	Fire Alarm	Secure Vestibule
Houston	In Progress	In Progress	Complete	In Progress	N/A
McNair	In Progress	In Progress	Complete	N/A	N/A
Old Technology / Communications	In Progress	In Progress	Complete	Complete	N/A
Pecan Creek	In Progress	In Progress	Complete	In Progress	N/A
Providence	In Progress	Complete	N/A	In Progress	N/A
Rivera	In Progress	In Progress	Complete	In Progress	N/A
Service Center Annex	In Progress	In Progress	Complete	Complete	N/A
WS Ryan	In Progress	In Progress	Complete	Complete	N/A

DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Maintenance & Operations

Questions?
