



Collin College

October 2025 Monthly Report

2023-2030 Master Plan Phase I
Collin County Community College District

Project Number: 60726232

November 10, 2025

Quality Information

Prepared by**Nuria Cortes**Nuria Cortes
Program Controls Manager**Reviewed by****Melissa Perette**Melissa Perette
Assistant Program Director**Approved By****Tim Smith**Tim Smith
Program Director

Revision History

Revision	Revision date	Details	Authorized	Name	Position
First Publication	November 6, 2025	October '25 Report	Yes	Tim Smith	Program Director

Distribution List

# Hard Copies	PDF Required	Association / Company Name
	1	Dr. Neil Matkin / Collin College
	1	Dr. Bill King / Collin College
	1	Chris Eyle / Collin College

Prepared for:

Collin County Community College District
3452 Spur 399
Suite 327
McKinney, TX 75069

Prepared by:

Nuria Cortes
Program Controls Manager
E: ncortes.aecom@collin.edu

AECOM
13355 Noel Road
4th Floor
Dallas TX, 75240
aecom.com

Copyright © 2025 by AECOM

All rights reserved. No part of this copyrighted work may be reproduced, distributed, or transmitted in any form or by any means without the prior written permission of AECOM.

Table of Contents

1.	Introduction	5
2.	Executive Summary	5
3.	Program Summary	6
3.1	Program Schedule	6
3.2	Program Budget	7
3.3	Current Personnel Estimate	7
4.	Project Summary	8
5	Completed Items	13
5.1	General Program	13
5.2	Procurement	13
5.3	Design	13
5.4	Pre-Construction	13
5.5	Construction	13
5.6	Acceptance and Close-Out	14
6	Pending Items	14
6.1	General Program	14
6.2	Procurement	14
6.3	Design	14
6.4	Pre-Construction	14
6.5	Construction	14
6.6	Acceptance and Close-Out	15
7	Progress Pictures	16
7.1	Plano Campus Renovations	16
7.2	Health Science Center	17
7.3	CHEC	18
7.4	Courtyard Center	19

1. Introduction

AECOM is currently managing 5 projects in this program. The total budget for the entire program is \$240,333,508.36, which includes 2 projects that AECOM is not managing.

On February 27, 2024, the Board of Trustees granted the District President authority to enter into and negotiate a contract with AECOM Technical Services, Inc. (AECOM) to provide Program Management Services for the Collin College 2023 Master Plan Program. On May 3, 2024, Collin College and AECOM executed the Collin contract for program management services. As part of these services, AECOM will deliver a monthly report to provide status and progress of key aspects of the Program.

2. Executive Summary

Completed and Pending Items

- Plano Campus – Roof work continues. Courtyard slab to be poured in the first week of November. Science labs, Theater select Restrooms and Dining, Commercial Music has work continuing. Demolition has started in the Welcome Center. Terrazzo work begins in front entry.
- Courtyard Center – Certificate of Occupancy has been received for the whole building. Punchlist items are being completed.
- CHEC – On the first floor, carpet and door frames have been installed at the new Foundation area and old iCollin area. On the second floor, door frames were installed at Institutional Research new offices. On the third floor, painting was completed, door frames were installed, and lighting was installed. Fourth floor muddying and painting is ongoing. Plumbing and electrical has is ongoing.
- Health Science Center – Concrete pours are complete for the building. Steel erection began at end of October. CM completed onboarding all subcontractors for the project and refining scopes by trade.
- Wylie CTE – 100% Construction Documents received 10-12-25. Prebid RFI's and Addendums have been issued. Bids are due 11-06-25.

Items of close attention

- No items of close attention at this time

Budget Summary

- \$159,748,596.46 of the \$240,333,508.36 has been committed to-date in the form of contracts with various vendors.
- \$58,590,197.47 of the \$159,748,596.46 committed amount has been expended to-date.

3. Program Summary

3.1 Program Schedule

Project	Scope of Work	2024												2025												2026												2027																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										
		January	February	March	April	May	June	July	August	September	October	November	December	January	February	March	April	May	June	July	August	September	October	November	December	January	February	March	April	May	June	July	August	September	October	November	December																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
Plano Campus	Renovations & Upgrades																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															</

Planning & Programming

Design & Construction Documents

Construction


Final Completion & Close-Out


We Are Here

3.2 Program Budget

Cost Summary							
Budget Group	Original Budget	Current Budget	Commitments	Approved Changes	Total Commitments	Pending Commitments	Expended to Date
Construction, Equipment & Furnishings	\$157,491,962.00	\$197,052,751.00	\$94,743,686.31	\$45,617,740.82	\$140,361,427.13	\$351,117.14	\$46,035,222.36
Contingency	\$22,203,853.00	\$19,432,851.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
Investigation, Testing & Verification	\$2,847,939.00	\$3,309,483.00	\$1,485,042.00	\$5,115.00	\$1,490,157.00	\$4,094.00	\$391,937.18
Management, Design & Pre-Construction	\$17,145,727.36	\$20,078,376.36	\$16,984,594.01	\$822,870.00	\$17,807,464.01	\$0.00	\$12,163,037.93
Miscellaneous	\$393,015.00	\$460,047.00	\$85,642.32	\$3,906.00	\$89,548.32	\$1,144.92	\$0.00
Total	\$200,082,496.36	\$240,333,508.36	\$113,298,964.64	\$46,449,631.82	\$159,748,596.46	\$356,356.06	\$58,590,197.47

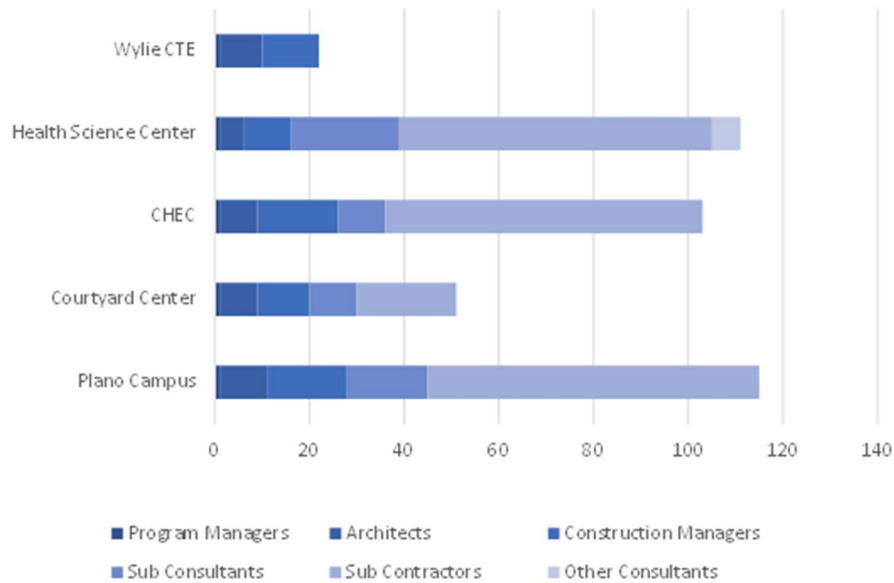

3.3 Current Personnel Estimate



It is estimated that the Program Managers, Architects, Construction Managers, Sub-Consultants, and Sub-Contractors, under contract with Collin College for the 2023 Master Plan Programs, have 402 employees contributing to the program's progress.

4. Project Summary

Courtyard Renovation



<div>Project Name</div> <div>Courtyard Renovation</div>		<div>COLLIN COLLEGE</div> <div></div>		<div>Schedule</div> <table><thead><tr><th>Activity</th><th>Baseline Finish</th><th>Planned Finish</th><th>Actual Finish</th></tr></thead><tbody><tr><td>BOT Approval of Construction Delivery Method</td><td>1/26/2024</td><td>1/26/2024</td><td>1/26/2024</td></tr><tr><td>BOT Approval of Recommended A/E</td><td>1/26/2024</td><td>1/26/2024</td><td>1/26/2024</td></tr><tr><td>BOT Approval of Program Manager</td><td>2/27/2024</td><td>2/27/2024</td><td>2/27/2024</td></tr><tr><td>Architect Mobilized</td><td>5/17/2024</td><td>5/17/2024</td><td>5/17/2024</td></tr><tr><td>BOT Approval of Recommended CMAR</td><td>5/26/2024</td><td>5/26/2024</td><td>5/28/2024</td></tr><tr><td>100% CDs Complete</td><td>11/1/2024</td><td>10/10/2024</td><td>10/10/2024</td></tr><tr><td>GMP Submittal</td><td>12/1/2024</td><td>11/22/2024</td><td>11/22/2024</td></tr><tr><td>BOT Approval of GMP</td><td>12/10/2024</td><td>12/10/2024</td><td>12/10/2024</td></tr><tr><td>Obtain Building Permit</td><td>12/13/2024</td><td>12/13/2024</td><td>1/16/2025</td></tr><tr><td>Contractor Mobilized</td><td>12/20/2024</td><td>12/20/2024</td><td>1/20/2025</td></tr><tr><td>Substantial Completion</td><td>7/15/2025</td><td>8/18/2025</td><td>8/18/2025</td></tr><tr><td>Final Completion</td><td>8/1/2025</td><td>9/10/2025</td><td>10/8/2025</td></tr><tr><td>Student Occupancy</td><td>8/26/2025</td><td>8/26/2025</td><td>9/2/2025</td></tr></tbody></table>					Activity	Baseline Finish	Planned Finish	Actual Finish	BOT Approval of Construction Delivery Method	1/26/2024	1/26/2024	1/26/2024	BOT Approval of Recommended A/E	1/26/2024	1/26/2024	1/26/2024	BOT Approval of Program Manager	2/27/2024	2/27/2024	2/27/2024	Architect Mobilized	5/17/2024	5/17/2024	5/17/2024	BOT Approval of Recommended CMAR	5/26/2024	5/26/2024	5/28/2024	100% CDs Complete	11/1/2024	10/10/2024	10/10/2024	GMP Submittal	12/1/2024	11/22/2024	11/22/2024	BOT Approval of GMP	12/10/2024	12/10/2024	12/10/2024	Obtain Building Permit	12/13/2024	12/13/2024	1/16/2025	Contractor Mobilized	12/20/2024	12/20/2024	1/20/2025	Substantial Completion	7/15/2025	8/18/2025	8/18/2025	Final Completion	8/1/2025	9/10/2025	10/8/2025	Student Occupancy	8/26/2025	8/26/2025	9/2/2025
Activity	Baseline Finish	Planned Finish	Actual Finish																																																													
BOT Approval of Construction Delivery Method	1/26/2024	1/26/2024	1/26/2024																																																													
BOT Approval of Recommended A/E	1/26/2024	1/26/2024	1/26/2024																																																													
BOT Approval of Program Manager	2/27/2024	2/27/2024	2/27/2024																																																													
Architect Mobilized	5/17/2024	5/17/2024	5/17/2024																																																													
BOT Approval of Recommended CMAR	5/26/2024	5/26/2024	5/28/2024																																																													
100% CDs Complete	11/1/2024	10/10/2024	10/10/2024																																																													
GMP Submittal	12/1/2024	11/22/2024	11/22/2024																																																													
BOT Approval of GMP	12/10/2024	12/10/2024	12/10/2024																																																													
Obtain Building Permit	12/13/2024	12/13/2024	1/16/2025																																																													
Contractor Mobilized	12/20/2024	12/20/2024	1/20/2025																																																													
Substantial Completion	7/15/2025	8/18/2025	8/18/2025																																																													
Final Completion	8/1/2025	9/10/2025	10/8/2025																																																													
Student Occupancy	8/26/2025	8/26/2025	9/2/2025																																																													
<div>Project Name</div> <div>Courtyard Renovation</div>		<div>Project Number</div> <div>PJ1065</div>		<div>Scope Description</div> <div>* Renovations of the Courtyard Center</div> <div>* The Renovations include:</div> <div>- New Cosmetology Space</div> <div>- Relocate and expand Esthetician Space</div> <div>- New Medical Message space</div> <div>- Remodel of 4th floor for Information Technology and Police</div>																																																												
<div>Project Type</div> <div>Renovation</div>		<div>Project Phase</div> <div>Construction</div>																																																														
<div>Project Manager</div> <div>Melissa Perette</div>	<div>Contractor/CM</div> <div>Skanska</div>	<div>Architect</div> <div>IN2 Architecture</div>																																																														
<div>Project Directory</div> <table><thead><tr><th>Company</th><th>Project Role</th></tr></thead><tbody><tr><td>AECOM Technical Services, Inc.</td><td>Program Manager</td></tr><tr><td>Collin College</td><td>Owner</td></tr><tr><td>Skanska</td><td>Construction Manager-at-Risk</td></tr><tr><td>IN2 Architecture</td><td>A/E</td></tr><tr><td>RWB Consulting Engineers</td><td></td></tr></tbody></table>							Company	Project Role	AECOM Technical Services, Inc.	Program Manager	Collin College	Owner	Skanska	Construction Manager-at-Risk	IN2 Architecture	A/E	RWB Consulting Engineers																																															
Company	Project Role																																																															
AECOM Technical Services, Inc.	Program Manager																																																															
Collin College	Owner																																																															
Skanska	Construction Manager-at-Risk																																																															
IN2 Architecture	A/E																																																															
RWB Consulting Engineers																																																																
<div>Progress Summary</div> <table><thead><tr><th>Status Date</th><th>Notes</th></tr></thead><tbody><tr><td>10/31/2025</td><td>Certificate of Occupancy has been received for the whole building. Punchlist items are being completed.</td></tr></tbody></table>							Status Date	Notes	10/31/2025	Certificate of Occupancy has been received for the whole building. Punchlist items are being completed.																																																						
Status Date	Notes																																																															
10/31/2025	Certificate of Occupancy has been received for the whole building. Punchlist items are being completed.																																																															

Cost Summary							
Budget Group	Original Budget	Current Budget	Commitments	Approved Changes	Total Commitments	Pending Commitments	Expended to Date
Construction, Equipment & Furnishings	\$4,991,556.00	\$5,222,037.00	\$4,999,577.35	\$251,369.00	\$5,250,946.35	\$0.00	\$3,729,449.82
Contingency	\$294,481.00	\$50,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
Investigation, Testing & Verification	\$82,073.00	\$82,073.00	\$72,151.00	\$0.00	\$72,151.00	\$0.00	\$38,674.80
Management, Design & Pre-Construction	\$696,100.00	\$710,100.00	\$690,736.36	\$5,000.00	\$695,736.36	\$0.00	\$486,224.20
Miscellaneous	\$4,551.00	\$4,551.00	\$3,597.50	\$0.00	\$3,597.50	\$0.00	\$0.00
Total	\$6,068,761.00	\$6,068,761.00	\$5,766,062.21	\$256,369.00	\$6,022,431.21	\$0.00	\$4,254,348.82



CHEC Renovation

Project Name							
CHEC Renovation							
Project Name		Project Number					
CHEC Renovation		PJ1066					
Project Type	Project Phase						
Renovation	Construction						
Project Manager	Contractor/CM	Architect					
Melissa Perette	Skanska	IN2 Architecture					
Project Directory							
Company	Project Role						
AECOM Technical Services, Inc.	Program Manager						
Collin College	Owner						
IN2 Architecture	A/E						
Skanska	A/E						
RWB Consulting Engineers							
Scope Description							
*Renovations Collin Higher Education Center - Renovations of selected spaces on 1st, 2nd, 3rd and 4th floor.							
Schedule							
Activity	Baseline Finish	Planned Finish	Actual Finish				
BOT Approval of A/E Procurement Method	1/26/2024	1/26/2024	1/26/2024				
BOT Approval of Construction Delivery Method	1/26/2024	1/26/2024	1/26/2024				
BOT Approval of Recommended A/E	1/26/2024	1/26/2024	1/26/2024				
BOT Approval of Program Manager	2/27/2024	2/27/2024	2/27/2024				
Architect Mobilized	5/17/2024	5/17/2024	5/17/2024				
BOT Approval of Recommended CMAR	5/26/2024	5/26/2024	5/28/2024				
100% CDs Complete	11/1/2024	2/14/2025	2/14/2025				
GMP Submittal	12/1/2024	2/20/2025	2/20/2025				
BOT Approval of GMP	12/10/2024	3/25/2025	3/25/2025				
Obtain Building Permit	12/20/2024	4/16/2025	4/21/2025				
Contractor Mobilized	1/6/2025	4/17/2025	4/21/2025				
Substantial Completion	4/1/2026	4/24/2026					
Final Completion	5/1/2026	5/26/2026					
Progress Summary							
Status Date	Notes						
10/31/2025	On the first floor, carpet and door frames have been installed at the new Foundation area and old iCollin area. On the second floor, door frames were installed at Institutional Research new offices. On the third floor, painting has been completed, door frames were installed and lighting was installed. Fourth floor muddying and painting is ongoing. Plumbing and electrical has is ongoing.						
Cost Summary							
Budget Group	Original Budget	Current Budget	Commitments	Approved Changes	Total Commitments	Pending Commitments	Expended to Date
Construction, Equipment & Furnishings	\$7,172,040.00	\$7,172,040.00	\$7,477,415.49	(\$537.00)	\$7,476,878.49	\$35,168.00	\$2,881,153.79
Contingency	\$562,950.00	\$543,950.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
Investigation, Testing & Verification	\$117,927.00	\$117,927.00	\$121,960.00	\$0.00	\$121,960.00	\$0.00	\$36,273.00
Management, Design & Pre-Construction	\$860,348.36	\$879,348.36	\$844,348.36	\$5,000.00	\$849,348.36	\$0.00	\$600,956.90
Miscellaneous	\$6,540.00	\$6,540.00	\$2,400.00	\$0.00	\$2,400.00	\$0.00	\$0.00
Total	\$8,719,805.36	\$8,719,805.36	\$8,446,123.85	\$4,463.00	\$8,450,586.85	\$35,168.00	\$3,518,383.69

Plano Renovation

<div>Project Name</div> <div>Plano Renovation</div>			<div></div>		<div>Schedule</div> <table><thead><tr><th>Activity</th><th>Baseline Finish</th><th>Planned Finish</th><th>Actual Finish</th><th></th></tr></thead><tbody><tr><td>BOT Approval of Construction Delivery Method</td><td>1/26/2024</td><td>1/26/2024</td><td>↑</td><td>1/26/2024 ✓</td></tr><tr><td>BOT Approval of Recommended A/E</td><td>1/26/2024</td><td>1/26/2024</td><td>↑</td><td>1/26/2024 ✓</td></tr><tr><td>BOT Approval of Program Manager</td><td>2/27/2024</td><td>2/27/2024</td><td>↑</td><td>2/27/2024 ✓</td></tr><tr><td>BOT Approval of Recommended CMAR</td><td>3/26/2024</td><td>3/26/2024</td><td>↑</td><td>3/26/2024 ✓</td></tr><tr><td>Architect Mobilized</td><td>4/19/2024</td><td>4/19/2024</td><td>↑</td><td>4/19/2024 ✓</td></tr><tr><td>GMP 1 Construction Documents Submittal</td><td>7/26/2024</td><td>8/2/2024</td><td>↓</td><td>8/2/2024 ✓</td></tr><tr><td>BOT Approval of GMP 1</td><td>9/24/2024</td><td>9/24/2024</td><td>↑</td><td>9/24/2024 ✓</td></tr><tr><td>GMP 2 Construction Documents Submittal</td><td>10/21/2024</td><td>9/19/2024</td><td>↑</td><td>9/20/2024 ✓</td></tr><tr><td>BOT Approval of GMP 2</td><td>12/10/2024</td><td>12/10/2024</td><td>↑</td><td>12/10/2024 ✓</td></tr><tr><td>Obtain Building Permit</td><td>12/13/2024</td><td>1/13/2025</td><td>↓</td><td>1/30/2025 ✓</td></tr><tr><td>Contractor Mobilized</td><td>12/20/2024</td><td>12/20/2024</td><td>↑</td><td>12/20/2024 ✓</td></tr><tr><td>Substantial Completion</td><td>6/1/2026</td><td>7/30/2026</td><td>↓</td><td></td></tr><tr><td>Final Completion</td><td>7/21/2026</td><td>8/6/2026</td><td>↓</td><td></td></tr><tr><td>Student Occupancy</td><td>8/17/2026</td><td>8/17/2026</td><td>↑</td><td></td></tr></tbody></table>					Activity	Baseline Finish	Planned Finish	Actual Finish		BOT Approval of Construction Delivery Method	1/26/2024	1/26/2024	↑	1/26/2024 ✓	BOT Approval of Recommended A/E	1/26/2024	1/26/2024	↑	1/26/2024 ✓	BOT Approval of Program Manager	2/27/2024	2/27/2024	↑	2/27/2024 ✓	BOT Approval of Recommended CMAR	3/26/2024	3/26/2024	↑	3/26/2024 ✓	Architect Mobilized	4/19/2024	4/19/2024	↑	4/19/2024 ✓	GMP 1 Construction Documents Submittal	7/26/2024	8/2/2024	↓	8/2/2024 ✓	BOT Approval of GMP 1	9/24/2024	9/24/2024	↑	9/24/2024 ✓	GMP 2 Construction Documents Submittal	10/21/2024	9/19/2024	↑	9/20/2024 ✓	BOT Approval of GMP 2	12/10/2024	12/10/2024	↑	12/10/2024 ✓	Obtain Building Permit	12/13/2024	1/13/2025	↓	1/30/2025 ✓	Contractor Mobilized	12/20/2024	12/20/2024	↑	12/20/2024 ✓	Substantial Completion	6/1/2026	7/30/2026	↓		Final Completion	7/21/2026	8/6/2026	↓		Student Occupancy	8/17/2026	8/17/2026	↑	
Activity	Baseline Finish	Planned Finish	Actual Finish																																																																																	
BOT Approval of Construction Delivery Method	1/26/2024	1/26/2024	↑	1/26/2024 ✓																																																																																
BOT Approval of Recommended A/E	1/26/2024	1/26/2024	↑	1/26/2024 ✓																																																																																
BOT Approval of Program Manager	2/27/2024	2/27/2024	↑	2/27/2024 ✓																																																																																
BOT Approval of Recommended CMAR	3/26/2024	3/26/2024	↑	3/26/2024 ✓																																																																																
Architect Mobilized	4/19/2024	4/19/2024	↑	4/19/2024 ✓																																																																																
GMP 1 Construction Documents Submittal	7/26/2024	8/2/2024	↓	8/2/2024 ✓																																																																																
BOT Approval of GMP 1	9/24/2024	9/24/2024	↑	9/24/2024 ✓																																																																																
GMP 2 Construction Documents Submittal	10/21/2024	9/19/2024	↑	9/20/2024 ✓																																																																																
BOT Approval of GMP 2	12/10/2024	12/10/2024	↑	12/10/2024 ✓																																																																																
Obtain Building Permit	12/13/2024	1/13/2025	↓	1/30/2025 ✓																																																																																
Contractor Mobilized	12/20/2024	12/20/2024	↑	12/20/2024 ✓																																																																																
Substantial Completion	6/1/2026	7/30/2026	↓																																																																																	
Final Completion	7/21/2026	8/6/2026	↓																																																																																	
Student Occupancy	8/17/2026	8/17/2026	↑																																																																																	
<div>Project Name</div> <div>Plano Renovation</div>			<div>Project Number</div> <div>PJ1064</div>		<div>Scope Description</div> <div>* Renovations to the Plano Campus</div> <div>* The Renovation includes:</div> <div>- Roof Replacement</div> <div>- Expanding Science Labs</div> <div>- Renovation and Expanding Health Sciences</div> <div>- Renovation in various other areas</div>																																																																															
<div>Project Type</div> <div>Renovation</div>		<div>Project Phase</div> <div>Construction</div>																																																																																		
<div>Project Manager</div> <div>Tim Smith</div>	<div>Contractor/CM</div> <div>Skanska</div>	<div>Architect</div> <div>IN2 Architecture</div>																																																																																		
<div>Project Directory</div> <table><thead><tr><th>Company</th><th>Project Role</th></tr></thead><tbody><tr><td>AECOM Technical Services, Inc.</td><td>Program Manager</td></tr><tr><td>Collin College</td><td>Owner</td></tr><tr><td>Skanska</td><td>Construction Manager-at-Risk</td></tr><tr><td>IN2 Architecture</td><td>A/E</td></tr><tr><td>BAi, LLC</td><td></td></tr><tr><td>Dunaway</td><td></td></tr><tr><td>Foodservice Design Professional</td><td></td></tr><tr><td>MATSON DRISCOLL & DAMICO LLP</td><td></td></tr><tr><td>Price Consulting, Inc.</td><td></td></tr><tr><td>RWB Consulting Engineers</td><td></td></tr></tbody></table>					Company	Project Role	AECOM Technical Services, Inc.	Program Manager	Collin College	Owner	Skanska	Construction Manager-at-Risk	IN2 Architecture	A/E	BAi, LLC		Dunaway		Foodservice Design Professional		MATSON DRISCOLL & DAMICO LLP		Price Consulting, Inc.		RWB Consulting Engineers		<div>Progress Summary</div> <table><thead><tr><th>Status Date</th><th>Notes</th></tr></thead><tbody><tr><td>10/31/2025</td><td>Plano Campus, Roof work continues. Courtyard slab to be pour first week in November Science labs, Theater select Restrooms and Dining, Commercial Music has work continuing. Demolition has started in the Welcome Center. Terrazzo work beginning in front entry.</td></tr></tbody></table>					Status Date	Notes	10/31/2025	Plano Campus, Roof work continues. Courtyard slab to be pour first week in November Science labs, Theater select Restrooms and Dining, Commercial Music has work continuing. Demolition has started in the Welcome Center. Terrazzo work beginning in front entry.																																																	
Company	Project Role																																																																																			
AECOM Technical Services, Inc.	Program Manager																																																																																			
Collin College	Owner																																																																																			
Skanska	Construction Manager-at-Risk																																																																																			
IN2 Architecture	A/E																																																																																			
BAi, LLC																																																																																				
Dunaway																																																																																				
Foodservice Design Professional																																																																																				
MATSON DRISCOLL & DAMICO LLP																																																																																				
Price Consulting, Inc.																																																																																				
RWB Consulting Engineers																																																																																				
Status Date	Notes																																																																																			
10/31/2025	Plano Campus, Roof work continues. Courtyard slab to be pour first week in November Science labs, Theater select Restrooms and Dining, Commercial Music has work continuing. Demolition has started in the Welcome Center. Terrazzo work beginning in front entry.																																																																																			
<div>Cost Summary</div> <table><thead><tr><th>Budget Group</th><th>Original Budget</th><th>Current Budget</th><th>Commitments</th><th>Approved Changes</th><th>Total Commitments</th><th>Pending Commitments</th><th>Expended to Date</th></tr></thead><tbody><tr><td>Construction, Equipment & Furnishings</td><td>\$62,835,304.00</td><td>\$74,193,298.00</td><td>\$68,918,893.21</td><td>\$1,626,402.82</td><td>\$70,545,296.03</td><td>\$315,949.14</td><td>\$29,558,536.51</td></tr><tr><td>Contingency</td><td>\$2,372,401.00</td><td>\$1,008,102.00</td><td>\$0.00</td><td>\$0.00</td><td>\$0.00</td><td>\$0.00</td><td>\$0.00</td></tr><tr><td>Investigation, Testing & Verification</td><td>\$1,150,911.00</td><td>\$1,359,240.00</td><td>\$591,949.00</td><td>\$5,115.00</td><td>\$597,064.00</td><td>\$4,094.00</td><td>\$196,316.25</td></tr><tr><td>Management, Design & Pre-Construction</td><td>\$6,895,542.00</td><td>\$8,078,310.00</td><td>\$6,987,542.26</td><td>(\$10,000.00)</td><td>\$6,977,542.26</td><td>\$0.00</td><td>\$5,195,494.90</td></tr><tr><td>Miscellaneous</td><td>\$305,272.00</td><td>\$361,050.00</td><td>\$79,644.82</td><td>\$3,906.00</td><td>\$83,550.82</td><td>\$1,144.92</td><td>\$0.00</td></tr><tr><td>Total</td><td>\$73,559,430.00</td><td>\$85,000,000.00</td><td>\$76,578,029.29</td><td>\$1,625,423.82</td><td>\$78,203,453.11</td><td>\$321,188.06</td><td>\$34,950,347.66</td></tr></tbody></table>								Budget Group	Original Budget	Current Budget	Commitments	Approved Changes	Total Commitments	Pending Commitments	Expended to Date	Construction, Equipment & Furnishings	\$62,835,304.00	\$74,193,298.00	\$68,918,893.21	\$1,626,402.82	\$70,545,296.03	\$315,949.14	\$29,558,536.51	Contingency	\$2,372,401.00	\$1,008,102.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	Investigation, Testing & Verification	\$1,150,911.00	\$1,359,240.00	\$591,949.00	\$5,115.00	\$597,064.00	\$4,094.00	\$196,316.25	Management, Design & Pre-Construction	\$6,895,542.00	\$8,078,310.00	\$6,987,542.26	(\$10,000.00)	\$6,977,542.26	\$0.00	\$5,195,494.90	Miscellaneous	\$305,272.00	\$361,050.00	\$79,644.82	\$3,906.00	\$83,550.82	\$1,144.92	\$0.00	Total	\$73,559,430.00	\$85,000,000.00	\$76,578,029.29	\$1,625,423.82	\$78,203,453.11	\$321,188.06	\$34,950,347.66																					
Budget Group	Original Budget	Current Budget	Commitments	Approved Changes	Total Commitments	Pending Commitments	Expended to Date																																																																													
Construction, Equipment & Furnishings	\$62,835,304.00	\$74,193,298.00	\$68,918,893.21	\$1,626,402.82	\$70,545,296.03	\$315,949.14	\$29,558,536.51																																																																													
Contingency	\$2,372,401.00	\$1,008,102.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00																																																																													
Investigation, Testing & Verification	\$1,150,911.00	\$1,359,240.00	\$591,949.00	\$5,115.00	\$597,064.00	\$4,094.00	\$196,316.25																																																																													
Management, Design & Pre-Construction	\$6,895,542.00	\$8,078,310.00	\$6,987,542.26	(\$10,000.00)	\$6,977,542.26	\$0.00	\$5,195,494.90																																																																													
Miscellaneous	\$305,272.00	\$361,050.00	\$79,644.82	\$3,906.00	\$83,550.82	\$1,144.92	\$0.00																																																																													
Total	\$73,559,430.00	\$85,000,000.00	\$76,578,029.29	\$1,625,423.82	\$78,203,453.11	\$321,188.06	\$34,950,347.66																																																																													

Health Science Center

<div>Project Name</div> <div>Health Science Center</div>			<div>COLLIN COLLEGE</div> <div></div>		<div>Schedule</div> <table><thead><tr><th>Activity</th><th>Baseline Finish</th><th>Planned Finish</th><th>Actual Finish</th></tr></thead><tbody><tr><td>BOT Approval of Rec. A/E & CMAR Firms</td><td>3/26/2024</td><td>3/26/2024</td><td><div><div></div><div></div><div></div></div>3/26/2024</td></tr><tr><td>Architect Mobilized</td><td>4/30/2024</td><td>4/30/2024</td><td><div><div></div><div></div><div></div></div>4/30/2024</td></tr><tr><td>Programming</td><td>7/30/2024</td><td>8/15/2024</td><td><div><div></div><div></div><div></div></div>8/15/2024</td></tr><tr><td>Schematic Design</td><td>9/30/2024</td><td>10/4/2024</td><td><div><div></div><div></div><div></div></div>10/4/2024</td></tr><tr><td>Design Development Completion</td><td>12/20/2024</td><td>12/20/2024</td><td><div><div></div><div></div><div></div></div>12/18/2024</td></tr><tr><td>GMP 1 Package Issuance</td><td>12/22/2024</td><td>12/18/2024</td><td><div><div></div><div></div><div></div></div>12/18/2024</td></tr><tr><td>GMP 1 Package Bidding</td><td>1/15/2025</td><td>1/24/2025</td><td><div><div></div><div></div><div></div></div>1/24/2025</td></tr><tr><td>BOT Approval of GMP 1</td><td>2/25/2025</td><td>2/25/2025</td><td><div><div></div><div></div><div></div></div>2/25/2025</td></tr><tr><td>Contractor Mobilized</td><td>2/26/2025</td><td>5/1/2025</td><td><div><div></div><div></div><div></div></div>5/2/2025</td></tr><tr><td>GMP 2 - 100% CDs Bidding</td><td>3/28/2025</td><td>2/28/2025</td><td><div><div></div><div></div><div></div></div>2/28/2025</td></tr><tr><td>Foundations Complete</td><td>4/30/2025</td><td>9/11/2025</td><td><div><div></div><div></div><div></div></div>8/27/2025</td></tr><tr><td>GMP 2 - 100% CDs Issuance</td><td>5/12/2025</td><td>6/9/2025</td><td><div><div></div><div></div><div></div></div>6/19/2025</td></tr><tr><td>BOT Approval of GMP 2</td><td>5/31/2025</td><td>5/27/2025</td><td><div><div></div><div></div><div></div></div>5/27/2025</td></tr><tr><td>Structures Complete</td><td>2/28/2026</td><td>12/3/2025</td><td><div><div></div><div></div><div></div></div></td></tr><tr><td>Interior Finish-Out Complete</td><td>7/15/2026</td><td>9/16/2026</td><td><div><div></div><div></div><div></div></div></td></tr><tr><td>Substantial Completion</td><td>7/31/2026</td><td>11/30/2026</td><td><div><div></div><div></div><div></div></div></td></tr><tr><td>Temporary CO</td><td>8/7/2026</td><td>10/31/2026</td><td><div><div></div><div></div><div></div></div></td></tr><tr><td>Final CO</td><td>8/14/2026</td><td>11/30/2026</td><td><div><div></div><div></div><div></div></div></td></tr><tr><td>Final Completion</td><td>8/31/2026</td><td>12/11/2026</td><td><div><div></div><div></div><div></div></div></td></tr><tr><td>Owner Occupancy</td><td>8/31/2026</td><td>1/19/2027</td><td><div><div></div><div></div><div></div></div></td></tr><tr><td>Student Occupancy</td><td>8/31/2026</td><td>1/19/2027</td><td><div><div></div><div></div><div></div></div></td></tr></tbody></table>					Activity	Baseline Finish	Planned Finish	Actual Finish	BOT Approval of Rec. A/E & CMAR Firms	3/26/2024	3/26/2024	<div><div></div><div></div><div></div></div> 3/26/2024	Architect Mobilized	4/30/2024	4/30/2024	<div><div></div><div></div><div></div></div> 4/30/2024	Programming	7/30/2024	8/15/2024	<div><div></div><div></div><div></div></div> 8/15/2024	Schematic Design	9/30/2024	10/4/2024	<div><div></div><div></div><div></div></div> 10/4/2024	Design Development Completion	12/20/2024	12/20/2024	<div><div></div><div></div><div></div></div> 12/18/2024	GMP 1 Package Issuance	12/22/2024	12/18/2024	<div><div></div><div></div><div></div></div> 12/18/2024	GMP 1 Package Bidding	1/15/2025	1/24/2025	<div><div></div><div></div><div></div></div> 1/24/2025	BOT Approval of GMP 1	2/25/2025	2/25/2025	<div><div></div><div></div><div></div></div> 2/25/2025	Contractor Mobilized	2/26/2025	5/1/2025	<div><div></div><div></div><div></div></div> 5/2/2025	GMP 2 - 100% CDs Bidding	3/28/2025	2/28/2025	<div><div></div><div></div><div></div></div> 2/28/2025	Foundations Complete	4/30/2025	9/11/2025	<div><div></div><div></div><div></div></div> 8/27/2025	GMP 2 - 100% CDs Issuance	5/12/2025	6/9/2025	<div><div></div><div></div><div></div></div> 6/19/2025	BOT Approval of GMP 2	5/31/2025	5/27/2025	<div><div></div><div></div><div></div></div> 5/27/2025	Structures Complete	2/28/2026	12/3/2025	<div><div></div><div></div><div></div></div>	Interior Finish-Out Complete	7/15/2026	9/16/2026	<div><div></div><div></div><div></div></div>	Substantial Completion	7/31/2026	11/30/2026	<div><div></div><div></div><div></div></div>	Temporary CO	8/7/2026	10/31/2026	<div><div></div><div></div><div></div></div>	Final CO	8/14/2026	11/30/2026	<div><div></div><div></div><div></div></div>	Final Completion	8/31/2026	12/11/2026	<div><div></div><div></div><div></div></div>	Owner Occupancy	8/31/2026	1/19/2027	<div><div></div><div></div><div></div></div>	Student Occupancy	8/31/2026	1/19/2027	<div><div></div><div></div><div></div></div>
Activity	Baseline Finish	Planned Finish	Actual Finish																																																																																														
BOT Approval of Rec. A/E & CMAR Firms	3/26/2024	3/26/2024	<div><div></div><div></div><div></div></div> 3/26/2024																																																																																														
Architect Mobilized	4/30/2024	4/30/2024	<div><div></div><div></div><div></div></div> 4/30/2024																																																																																														
Programming	7/30/2024	8/15/2024	<div><div></div><div></div><div></div></div> 8/15/2024																																																																																														
Schematic Design	9/30/2024	10/4/2024	<div><div></div><div></div><div></div></div> 10/4/2024																																																																																														
Design Development Completion	12/20/2024	12/20/2024	<div><div></div><div></div><div></div></div> 12/18/2024																																																																																														
GMP 1 Package Issuance	12/22/2024	12/18/2024	<div><div></div><div></div><div></div></div> 12/18/2024																																																																																														
GMP 1 Package Bidding	1/15/2025	1/24/2025	<div><div></div><div></div><div></div></div> 1/24/2025																																																																																														
BOT Approval of GMP 1	2/25/2025	2/25/2025	<div><div></div><div></div><div></div></div> 2/25/2025																																																																																														
Contractor Mobilized	2/26/2025	5/1/2025	<div><div></div><div></div><div></div></div> 5/2/2025																																																																																														
GMP 2 - 100% CDs Bidding	3/28/2025	2/28/2025	<div><div></div><div></div><div></div></div> 2/28/2025																																																																																														
Foundations Complete	4/30/2025	9/11/2025	<div><div></div><div></div><div></div></div> 8/27/2025																																																																																														
GMP 2 - 100% CDs Issuance	5/12/2025	6/9/2025	<div><div></div><div></div><div></div></div> 6/19/2025																																																																																														
BOT Approval of GMP 2	5/31/2025	5/27/2025	<div><div></div><div></div><div></div></div> 5/27/2025																																																																																														
Structures Complete	2/28/2026	12/3/2025	<div><div></div><div></div><div></div></div>																																																																																														
Interior Finish-Out Complete	7/15/2026	9/16/2026	<div><div></div><div></div><div></div></div>																																																																																														
Substantial Completion	7/31/2026	11/30/2026	<div><div></div><div></div><div></div></div>																																																																																														
Temporary CO	8/7/2026	10/31/2026	<div><div></div><div></div><div></div></div>																																																																																														
Final CO	8/14/2026	11/30/2026	<div><div></div><div></div><div></div></div>																																																																																														
Final Completion	8/31/2026	12/11/2026	<div><div></div><div></div><div></div></div>																																																																																														
Owner Occupancy	8/31/2026	1/19/2027	<div><div></div><div></div><div></div></div>																																																																																														
Student Occupancy	8/31/2026	1/19/2027	<div><div></div><div></div><div></div></div>																																																																																														
<div>Project Name</div> <div>Health Science Center</div>			<div>Project Number</div> <div>PJ1067</div>		<div>Scope Description</div> <div>Construction of new Health Science Center, Frisco, Texas</div> <div>The building will be: 3 stories totaling 116,902 square feet 82,593 square feet to be finished out, 34,309 square feet to remain shell New Programs: MLT Radiography Cath Lab Nuclear Med CT Technology MRI Technology Programs Moving or Expanding: Nursing Diagnostic Sonography (program move from McKinney) Physical Therapy Assistant Health Professions Interdisciplinary Spaces: AR/VR Lab space Healthcare Simulation space</div>																																																																																												
<div>Project Type</div> <div>New</div>		<div>Project Phase</div> <div>Construction</div>																																																																																															
<div>Project Manager</div> <div>Penny Busch</div>	<div>Contractor/CM</div> <div>McCarthy Building Comp...</div>	<div>Architect</div> <div>PBK Architects, Inc.</div>																																																																																															
<div>Project Directory</div> <table><thead><tr><th>Company</th><th>Project Role</th></tr></thead><tbody><tr><td>JQ Engineering (IMEG)</td><td>Structural Engineer</td></tr><tr><td>AECOM Technical Services, Inc.</td><td>Program Manager</td></tr><tr><td>Collin College</td><td>Owner</td></tr><tr><td>RWB Consulting Engineers</td><td>MEP</td></tr><tr><td>CCA Landscape Architects, Inc.</td><td>Landscape Architect</td></tr><tr><td>McCarthy Building Companies, Inc.</td><td>Construction Manager-at-Risk</td></tr><tr><td>RLK Engineering</td><td>Civil Engineer</td></tr><tr><td>PBK Architects, Inc.</td><td>A/E</td></tr><tr><td>PBK</td><td></td></tr></tbody></table>					Company	Project Role	JQ Engineering (IMEG)	Structural Engineer	AECOM Technical Services, Inc.	Program Manager	Collin College	Owner	RWB Consulting Engineers	MEP	CCA Landscape Architects, Inc.	Landscape Architect	McCarthy Building Companies, Inc.	Construction Manager-at-Risk	RLK Engineering	Civil Engineer	PBK Architects, Inc.	A/E	PBK																																																																										
Company	Project Role																																																																																																
JQ Engineering (IMEG)	Structural Engineer																																																																																																
AECOM Technical Services, Inc.	Program Manager																																																																																																
Collin College	Owner																																																																																																
RWB Consulting Engineers	MEP																																																																																																
CCA Landscape Architects, Inc.	Landscape Architect																																																																																																
McCarthy Building Companies, Inc.	Construction Manager-at-Risk																																																																																																
RLK Engineering	Civil Engineer																																																																																																
PBK Architects, Inc.	A/E																																																																																																
PBK																																																																																																	
<div>Progress Summary</div> <table><thead><tr><th>Status Date</th><th>Notes</th></tr></thead><tbody><tr><td>10/31/2025</td><td>CM completed onboarding all subcontractors for the project and refining scopes by trade.</td></tr><tr><td>10/31/2025</td><td>Concrete pours are complete for the building.</td></tr><tr><td>10/31/2025</td><td>Steel erection began at the end of October.</td></tr></tbody></table>					Status Date	Notes	10/31/2025	CM completed onboarding all subcontractors for the project and refining scopes by trade.	10/31/2025	Concrete pours are complete for the building.	10/31/2025	Steel erection began at the end of October.																																																																																					
Status Date	Notes																																																																																																
10/31/2025	CM completed onboarding all subcontractors for the project and refining scopes by trade.																																																																																																
10/31/2025	Concrete pours are complete for the building.																																																																																																
10/31/2025	Steel erection began at the end of October.																																																																																																
<div>Cost Summary</div> <table><thead><tr><th>Budget Group</th><th>Original Budget</th><th>Current Budget</th><th>Commitments</th><th>Approved Changes</th><th>Total Commitments</th><th>Pending Commitments</th><th>Expended to Date</th></tr></thead><tbody><tr><td>Construction, Equipment & Furnishings</td><td>\$47,793,062.00</td><td>\$63,833,786.00</td><td>\$13,347,800.26</td><td>\$43,740,506.00</td><td>\$57,088,306.26</td><td>\$0.00</td><td>\$9,866,082.24</td></tr><tr><td>Contingency</td><td>\$1,987,031.00</td><td>\$1,066,438.00</td><td>\$0.00</td><td>\$0.00</td><td>\$0.00</td><td>\$0.00</td><td>\$0.00</td></tr><tr><td>Investigation, Testing & Verification</td><td>\$777,028.00</td><td>\$777,028.00</td><td>\$420,227.00</td><td>\$0.00</td><td>\$420,227.00</td><td>\$0.00</td><td>\$125,185.38</td></tr><tr><td>Management, Design & Pre-Construction</td><td>\$5,212,227.00</td><td>\$6,092,097.00</td><td>\$5,244,227.03</td><td>\$822,870.00</td><td>\$6,067,097.03</td><td>\$0.00</td><td>\$4,379,121.19</td></tr><tr><td>Miscellaneous</td><td>\$44,652.00</td><td>\$44,652.00</td><td>\$0.00</td><td>\$0.00</td><td>\$0.00</td><td>\$0.00</td><td>\$0.00</td></tr><tr><td>Total</td><td>\$55,814,000.00</td><td>\$71,814,001.00</td><td>\$19,012,254.29</td><td>\$44,563,376.00</td><td>\$63,575,630.29</td><td>\$0.00</td><td>\$14,370,388.81</td></tr></tbody></table>									Budget Group	Original Budget	Current Budget	Commitments	Approved Changes	Total Commitments	Pending Commitments	Expended to Date	Construction, Equipment & Furnishings	\$47,793,062.00	\$63,833,786.00	\$13,347,800.26	\$43,740,506.00	\$57,088,306.26	\$0.00	\$9,866,082.24	Contingency	\$1,987,031.00	\$1,066,438.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	Investigation, Testing & Verification	\$777,028.00	\$777,028.00	\$420,227.00	\$0.00	\$420,227.00	\$0.00	\$125,185.38	Management, Design & Pre-Construction	\$5,212,227.00	\$6,092,097.00	\$5,244,227.03	\$822,870.00	\$6,067,097.03	\$0.00	\$4,379,121.19	Miscellaneous	\$44,652.00	\$44,652.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	Total	\$55,814,000.00	\$71,814,001.00	\$19,012,254.29	\$44,563,376.00	\$63,575,630.29	\$0.00	\$14,370,388.81																																	
Budget Group	Original Budget	Current Budget	Commitments	Approved Changes	Total Commitments	Pending Commitments	Expended to Date																																																																																										
Construction, Equipment & Furnishings	\$47,793,062.00	\$63,833,786.00	\$13,347,800.26	\$43,740,506.00	\$57,088,306.26	\$0.00	\$9,866,082.24																																																																																										
Contingency	\$1,987,031.00	\$1,066,438.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00																																																																																										
Investigation, Testing & Verification	\$777,028.00	\$777,028.00	\$420,227.00	\$0.00	\$420,227.00	\$0.00	\$125,185.38																																																																																										
Management, Design & Pre-Construction	\$5,212,227.00	\$6,092,097.00	\$5,244,227.03	\$822,870.00	\$6,067,097.03	\$0.00	\$4,379,121.19																																																																																										
Miscellaneous	\$44,652.00	\$44,652.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00																																																																																										
Total	\$55,814,000.00	\$71,814,001.00	\$19,012,254.29	\$44,563,376.00	\$63,575,630.29	\$0.00	\$14,370,388.81																																																																																										

5 Completed Items

5.1 General Program

- Facilities Meeting were held on October 6th, 13th, 20th, and 29th

5.2 Procurement

- No Procurement items were completed at this time

5.3 Design

- Wylie CTE, Air Gas (for welding) design review meeting was held between Collin College, Page Southerland and AECOM on October 3rd.
- Wylie CTE, 100% Construction Documents were received from Page Southerland on October 12th.
- Wylie CTE, Skanska conducted a Pre-Bid meeting that was held between Skanska, Page Southerland, AECOM, and interested subcontractors on October 15th.
- Wylie CTE, Page Southerland issued Addendum 1 and Skanska posted for interested bidders on October 15th.
- Wylie CTE, Page Southerland conducted an interior and exterior fly-through presentation for Dr. Matkin and the Cabinet members on October 17th.
- Wylie CTE, Page Southerland issued Addendum 2 and Skanska posted for interested bidders on October 28th.
- Health Science Center, PBK issued the construction drawings for the additional two X-Ray units and the RF unit.

5.4 Pre-Construction

- Health Science Center, McCarthy completed the subcontractor contacts and on-boarding for the project.

5.5 Construction

- Plano Campus provost meetings were held between Collin College, AECOM, and Skanska on October 1st, 7th, 8th, 14th, 15th, 21st, 22nd, 28th, and 29th
- Plano Campus OAC meetings were held on October 2nd, 9th, 16th, 23rd, and 30th
- CHEC OAC meetings were held on October 2nd, 9th, 16th, 23rd, and 30th
- Courtyard Center OAC meetings were held on October 2nd and 9th
- Courtyard Center Renovations and JOC Commissioning meeting was held on October 16th
- Plano Campus, Meeting to walk the H and I Lab layout was held between Collin College, AECOM, IN2, and Skanska on October 6th
- Courtyard Center, Final Certificate of Occupancy was received by the City of Plano on October 8th.
- CHEC Phase 2 to 3 Transition and Carpet/Paint meeting was held between Collin College, AECOM, and Skanska on October 15th and 22nd
- Plano Campus, meeting to review tile at Daletile showroom was held between AECOM, IN2, Skanska, and OneSource Floors on October 16th
- Plano Campus, Theater railing design meeting was held between AECOM, IN2, and Skanska on October 17th
- Courtyard Center Financial Close Out Discussion meeting was held between Collin College, Skanska and AECOM on October 21st

- Plano Campus, meeting on the Audio Visual Extron computer needs for Science labs was held between Collin College and AECOM on October 23rd
- Plano Campus, bookstore temporary location meeting was held between Collin College, AECOM, IN2, and Barnes and Noble on October 24th
- Plano Campus, toilet accessories meeting was held between Collin College, AEOM, and Skanska was held on October 27th
- Plano Campus, mock-up for glass railing meeting was held between AECOM, IN2, Skanska, and Viva Railings on October 28th
- Plano Campus, A&P technology review was held between Collin College, AECOM, and The Brass Effect on October 28th
- Health Science Center, Concrete placement for the building was completed.
- Health Science Center, Fireline expansion and modifications were completed with city approval.

5.6 Acceptance and Close-Out

- No Acceptance and Close-Out items were completed at this time

6 Pending Items

6.1 General Program

- No General Program items are pending at this time

6.2 Procurement

- Health Science Center, design team obtaining proposal for physicist to complete a shielding report for the RF room.
- Health Science Center, Mock MRI proposal has been obtained. Procurement pending board approval and then PO issuance.

6.3 Design

- Wylie CTE, Bids due November 6th
- Health Science Center, Dance studio courtyard revisions to landscape is into the City of Frisco for review and approval.

6.4 Pre-Construction

- No Pre-Construction items are pending at this time

6.5 Construction

- Plano Campus, Roof work continues. Courtyard slab to be poured first week in November. Science labs, Theater select Restrooms and Dining, Commercial Music has work continuing. Demolition has started in the Welcome Center. Terrazzo work begins in front entry.
- Health Science Center, structural steel erection is nearing complete on the west end of the building with all roofing structural steel to follow.
- Health Science Center, temporary lighting is installed on first floor and to follow for second level as remainder of shoring and pans are removed.
- Health Science Center, priority wall layout to begin with wall framing to be in progress by the end of November.

- Health Science Center, mechanical, electrical, and plumbing trades coordinating and moving forward with the install of main system runs.
- Courtyard Center, final punch list items to be completed and financial close out.
- CHEC, Phase 2 carpet installation, paint, door installation on levels 1-3. Hard lid ceilings, final paint, carpet, plumbing and final electrical installation pending on level 4.

6.6 Acceptance and Close-Out

- No Acceptance and Close-out Items are pending at this time

7 Progress Pictures

7.1 Plano Campus Renovations



Courtyard




Courtyard




Restroom Tile



Science Labs Casework

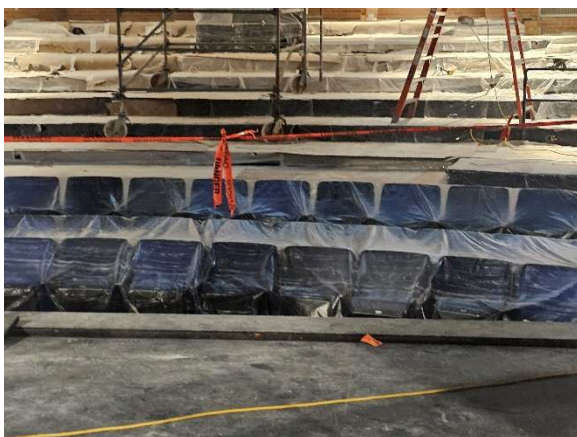


Theater Seating

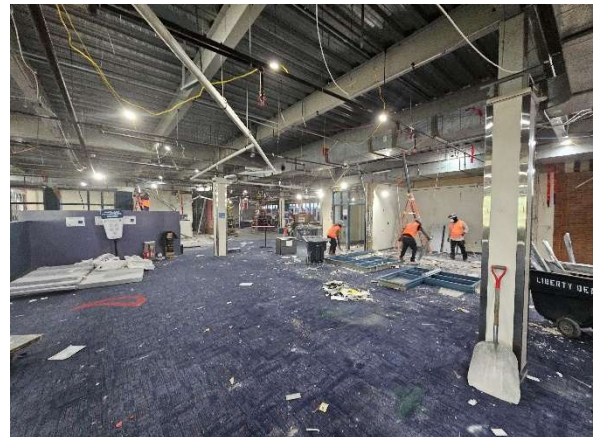

Welcome Center Demo

7.2 Health Science Center

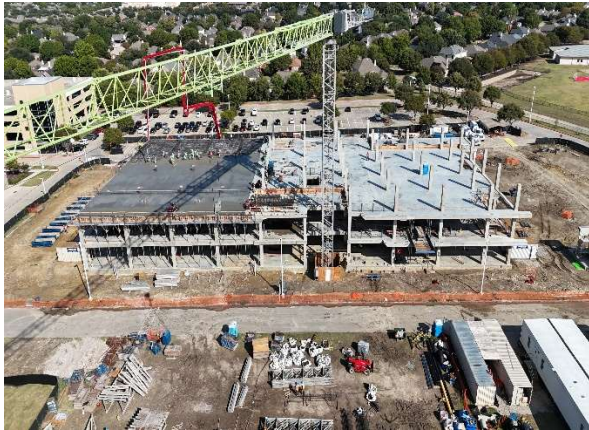

View to North



View to Northwest



View to Southwest



Overhead View

7.3 CHEC



1st Floor – New Foundation Offices



1st Floor – Foundation Reception Area



3rd Floor – Business Offices



4th floor – Presidential Suite Offices

7.4 Courtyard Center



1st Floor – Cosmetology Reception



2nd Floor – Medical Massage Reception



4th Floor – Emergency Management Conference



2nd floor – Esthetician Lab Reception
