

ALEDO ISD 2019 BOND UPDATE



Board Meeting

October 18, 2021

ANNETTA ELEMENTARY SCHOOL COST SUMMARY TO DATE



Project: Annetta Elementary (Elementary School No. 6)

Grades: K-5

Capacity: 889

Bond 2019 Estimate: \$35,858,000.00

Budget: \$38,358,000.00 (Includes cost for Learners Lane – NCTCOG partnership)

Amount Spent To Date: \$37,751,018.76

Phase Completion: **planning, design, procurement, construction**, warranty

Square Footage: 107,391

Date Open: August 2021

ANNETTA ELEMENTARY SCHOOL SCHEDULE UPDATE



- Schedule Update:
 - Temporary Certificate of Occupancy (TCO) Issued – 8-17-21
 - TCO inspection items wrapping up – 10-18-21
 - Water Well - Letter of Conveyance items wrapping up – 11-5-21
 - WWTP Building Completion - 10-15-21
 - WWTP Aeration Field – TBD
 - Punch List item work on-going

ANNETTA ELEMENTARY SCHOOL SCHEDULE UPDATE – CON'T.



- Schedule Update, Con't:
 - Playground Equipment – Installation complete
 - Playground Open Items: Teacher benches, 5-12 sod
 - Landscape Work Complete by 9-20-21
 - Punch Walks complete (building, landscape, civil, structural)

ANNETTA ELEMENTARY SCHOOL
FRONT OF SCHOOL – 10-15-21



ANNETTA ELEMENTARY SCHOOL
OFFICE ENTRANCE – 10-15-21



ANNETTA ELEMENTARY SCHOOL DEDICATION PLAQUE – 10-15-21



**ANNETTA
ELEMENTARY SCHOOL**
2021



BOARD OF TRUSTEES

MR. HOYT HARRIS	PRESIDENT
MS. JENNIFER LOFTIN	VICE PRESIDENT
MR. FORREST COLLINS	SECRETARY
MR. DAVID LEAR	TRUSTEE
MS. JESSICA BROWN	TRUSTEE
MS. JENNIFER TAYLOR	TRUSTEE
MS. JULIE TURNER	TRUSTEE

ADMINISTRATION

DR. SUSAN K. BOHN SUPERINTENDENT OF SCHOOLS

ARCHITECT



GENERAL CONTRACTOR

S & P

**SATTERFIELD & PONTIKES
CONSTRUCTION, INC.**

ANNETTA ELEMENTARY SCHOOL
5-12 PLAYGROUND – 10-15-21



ANNETTA ELEMENTARY SCHOOL
2-5 PLAYGROUND – 10-15-21



ANNETTA ELEMENTARY SCHOOL
WASTE-WATER TREATMENT BUILDING PROGRESS – 10-15-21



ANNETTA ELEMENTARY SCHOOL

WASTE-WATER TREATMENT FIELD PREP PROGRESS – 10-15-21



MCANALLY MIDDLE SCHOOL COST SUMMARY TO DATE



Project: McAnally Middle School (Middle School No. 2)

Grades: 6-8

Capacity: 1,449

Bond 2019 Estimate: \$62,501,000.00

Budget: \$53,747,575.25

Amount Spent To Date: \$48,413,913.65

Phase Completion: **planning, design, procurement, construction**, warranty

Square Footage: 181,009


Date Open: August 2022

MCANALLY MIDDLE SCHOOL SCHEDULE UPDATE



- Substantial completion date – 6-29-22
 - Critical Path Schedule ~1 week behind
 - Parking lot work on-going – working towards building
 - Block work on-going
 - Area 1 roof work beginning week of 10-18-21
 - Tri-County Electric permanent meter set week of 10-18-21
 - Storm Shelter tilt wall erection beginning week of 10-18-21

MCANALLY MIDDLE SCHOOL SITE PLAN – PLAN NORTH

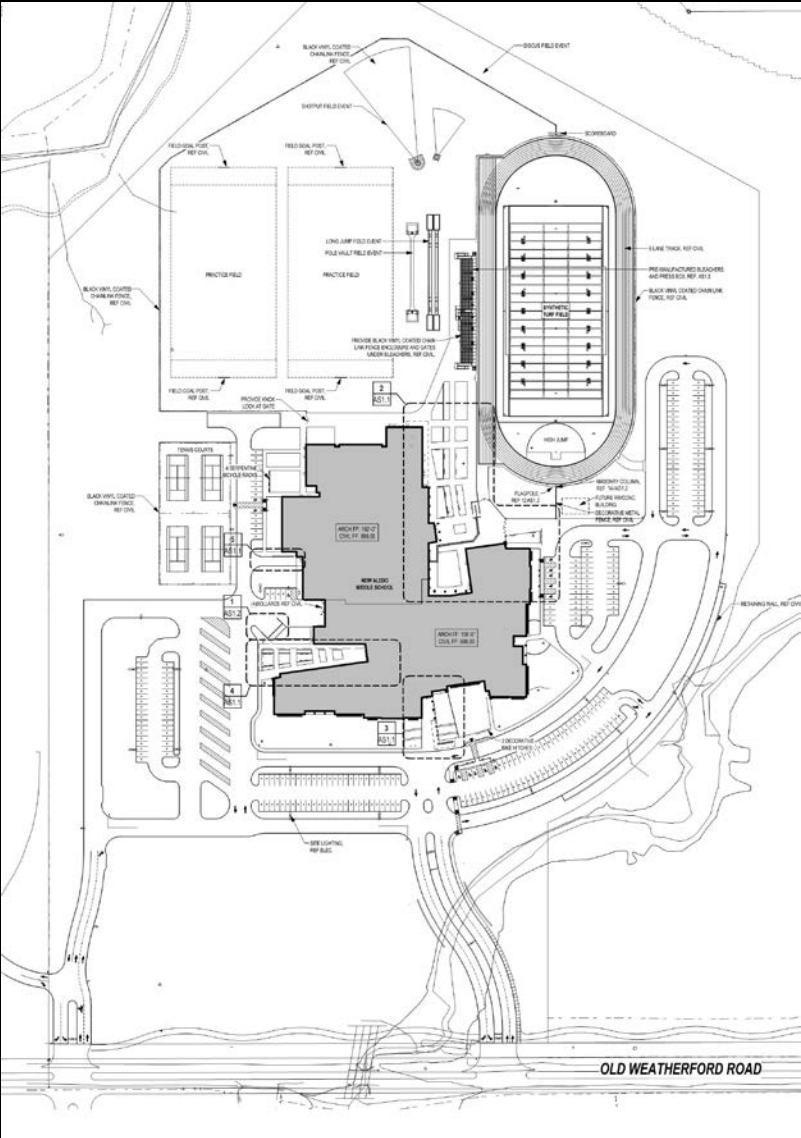

MCANALLY MIDDLE SCHOOL
AERIAL VIEW, FRONT – 10-15-21



MCANALLY MIDDLE SCHOOL AERIAL VIEW, FRONT OF SCHOOL – 10-15-21



MCANALLY MIDDLE SCHOOL
AERIAL VIEW, EAST OF SCHOOL – 10-15-21




MCANALLY MIDDLE SCHOOL
AERIAL VIEW, SOUTH OF SCHOOL – 10-15-21



MCANALLY MIDDLE SCHOOL
PERFORMING ARTS BLOCK WORK – 10-15-21



MCANALLY MIDDLE SCHOOL
AREA 1 PROGRESS – 10-15-21

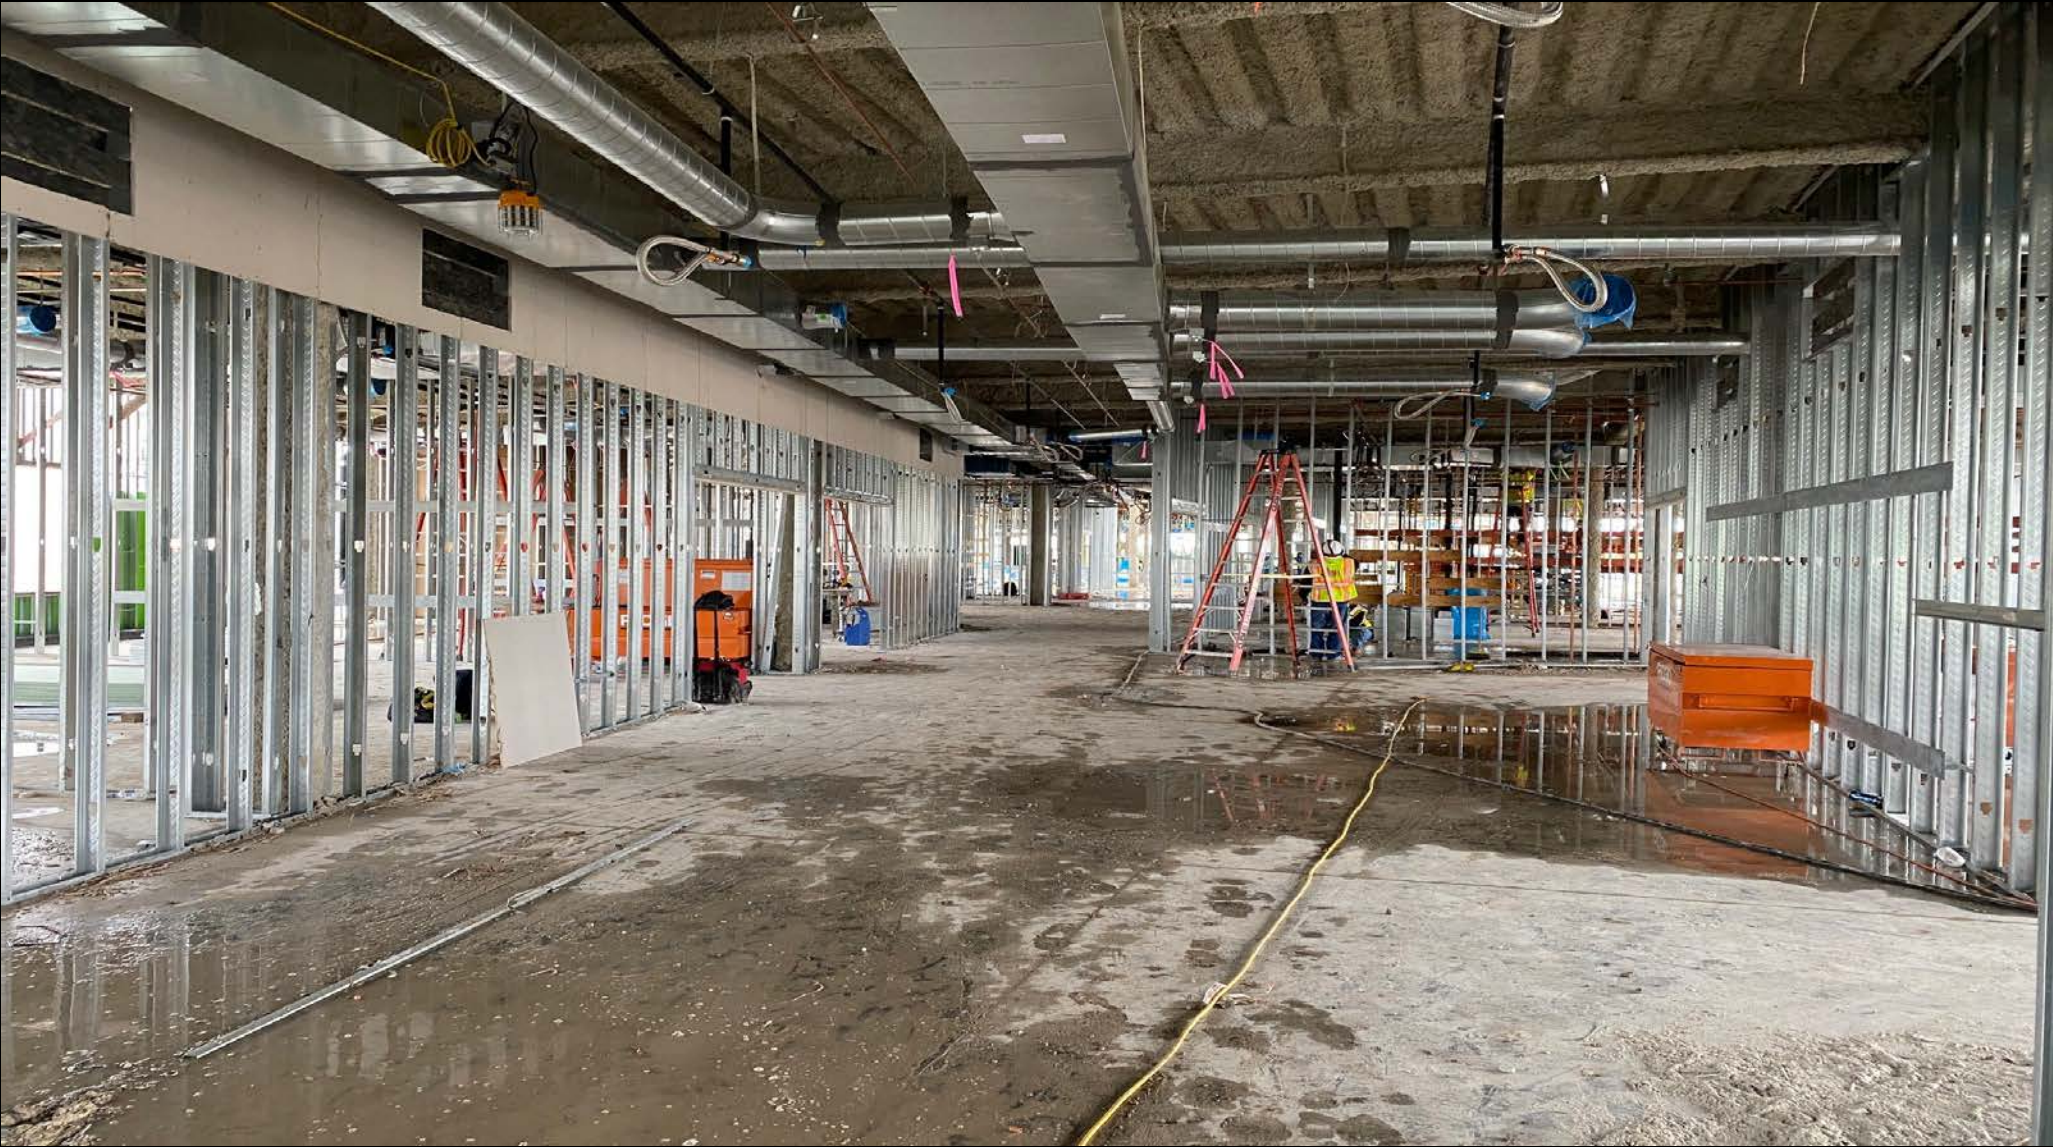

MCANALLY MIDDLE SCHOOL MATERIALS STORAGE – 10-15-21



ALEDO MIDDLE SCHOOL COST SUMMARY TO DATE



Project: Aledo Middle School Expansion/Renovation

Grades: 6-8

Capacity: 1,449

Bond 2019 Estimate: \$33,446,000.00

Budget: \$37,184,779.41

Amount Spent To Date: \$35,918,038.07

Phase Completion: **planning, design, procurement, construction**, warranty

Square Footage: 183,927

Date Open: August 2022

ALEDO MIDDLE SCHOOL SCHEDULE UPDATE



- SUBSTANTIAL COMPLETION DATE – 9-30-22
 - Abatement in 600 Wing completed on 9-30-21
 - Construction in 600 Wing begins on 10-1-21
 - Moved into (3) new science rooms on 9-24-21
 - Moved out of 500 Wing on 9-24-21
 - Abatement in 500 Wing completed on 10-13-21
 - Construction began in 500 Wing on 10-14-21

ALEDO MIDDLE SCHOOL NEW ADMINISTRATION FOUNDATION PROGRESS – 10-15-21




ALEDO MIDDLE SCHOOL NEW CTE LAB FOUNDATION PROGRESS – 10-15-21



ALEDO MIDDLE SCHOOL NEW LOCKER ROOM FOUNDATION PROGRESS – 10-15-21



ALEDO MIDDLE SCHOOL
STORM SHELTER INTERIOR PROGRESS – 10-15-21

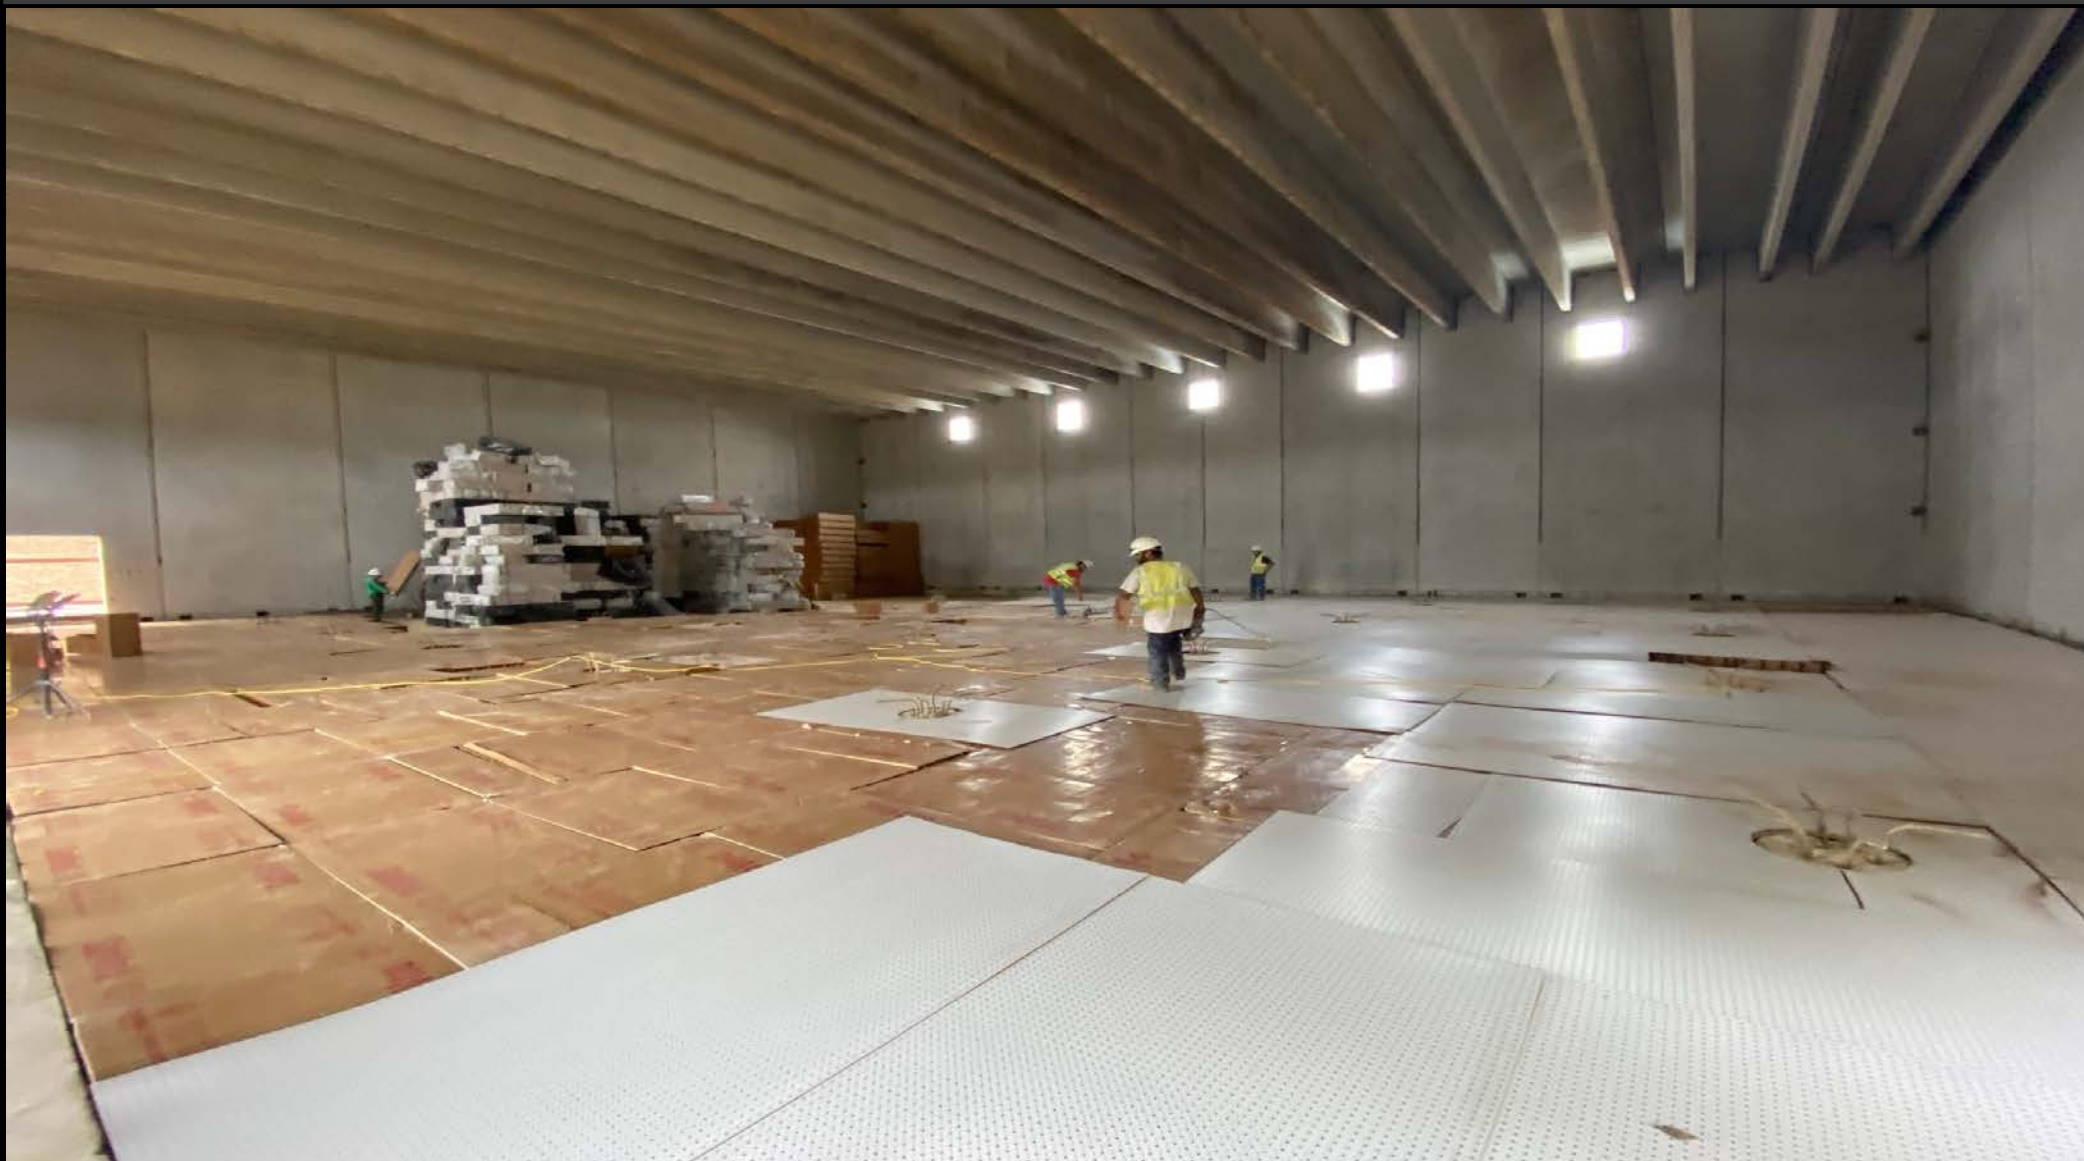

ALEDO MIDDLE SCHOOL STORM SHELTER INTERIOR PROGRESS – 10-15-21



ALEDO MIDDLE SCHOOL NEW CONNECTOR CORRIDOR FRAMEWORK – 10-15-21



ALEDO MIDDLE SCHOOL UPPER LIBRARY SPACE – 9-24-21



ALEDO MIDDLE SCHOOL
LOWER LIBRARY SPACE – 9-24-21



ALEDO MIDDLE SCHOOL
LOWER LIBRARY SPACE – 10-15-21



ALEDO MIDDLE SCHOOL
LOWER LIBRARY SPACE – 10-15-21



ALEDO MIDDLE SCHOOL
NEW SCIENCE LAB STOREFRONT— 9-24-21



ALEDO MIDDLE SCHOOL
NEW SCIENCE LAB FURNITURE – 9-24-21



ALEDO MIDDLE SCHOOL NEW SCIENCE LAB FURNITURE – 9-24-21



ALEDO MIDDLE SCHOOL
NEW SCIENCE LAB STORAGE AREA – 10-15-21



ALEDO MIDDLE SCHOOL
SCIENCE LAB CORRIDOR – 9-24-21



ALEDO MIDDLE SCHOOL
NEW KITCHEN WORK ACCESS – 10-15-21



ALEDO MIDDLE SCHOOL
NEW KITCHEN PROGRESS— 10-15-21



ALEDO MIDDLE SCHOOL NEW KITCHEN PROGRESS – 10-15-21



ALEDO MIDDLE SCHOOL
500 HALL ABATEMENT WORK – 10-15-21



ALEDO MIDDLE SCHOOL
500 HALL ABATEMENT WORK – 10-15-21



ALEDO MIDDLE SCHOOL
500 HALL ABATEMENT WORK – 10-15-21



(NEW) VANDAGRIFF ELEMENTARY SCHOOL
COST SUMMARY TO DATE



Project: McAnally Intermediate Conversion to Elementary School

Grades: K-5

Capacity: 800

Bond 2019 Estimate: \$9,611,000.00

Budget: \$9,493,583.68

Amount Spent To Date: \$8,148,122.80

Phase Completion: **planning, design, procurement, construction**, warranty

Square Footage: 103,866

Date Open: August 2022

(NEW) VANDAGRIFF ELEMENTARY SCHOOL SCHEDULE UPDATE



- Wrapping up finish details in front office area
- Wrapping up Music and Choir spaces
- Work on new 5th grade wing on-going
- Storm shelter work on-going
- Re-visiting phasing based on available swing space and material delivery schedules

(NEW) VANDAGRIFF ELEMENTARY SCHOOL



(NEW) VANDAGRIFF ELEMENTARY SCHOOL FLOOR PLAN



PRK



LEGEND

- ADMINISTRATION
- CAFETERIA
- CIRCULATION
- CLASSROOM
- FOOD SERVICES
- LIBRARY
- MUSIC, FINE ARTS
- PE, ATHLETICS
- SPECIAL ED
- SUPPORT

McANALLY INTERMEDIATE SCHOOL CONVERSION
ALEDO INDEPENDENT SCHOOL DISTRICT

NEW COMPOSITE FLOOR PLAN



(NEW) VANDAGRIFF ELEMENTARY SCHOOL
STORM SHELTER AREA – 10-15-21



(NEW) VANDAGRIFF ELEMENTARY SCHOOL MUSIC ROOM PROGRESS – 10-15-21



(NEW) VANDAGRIFF ELEMENTARY SCHOOL
ART ROOM PLUMBING WORK – 10-15-21



(NEW) VANDAGRIFF ELEMENTARY SCHOOL
5TH GRADE COLLAB CORRIDOR – 10-15-21



(NEW) VANDAGRIFF ELEMENTARY SCHOOL
5TH GRADE CLASSROOM TYPICAL – 10-15-21



EARLY CHILDHOOD ACADEMY (ECA) SCHEDULE



- PROJECT SCHEDULE
 - November 2021 – Design presentation to Board
 - December 2021 – Issue Drawings
 - December 2021 - Bidding
 - January 2022 – Board Approval (NTP)
 - February 2022 – August 2022 Construction

QUESTIONS?



Questions?
