



# Bloomington School District 13

## Districtwide Referendum Program

Board Report | February 23, 2026

**BULLEY &  
ANDREWS**

# Safety & Manpower



**WESTFIELD MIDDLE  
SCHOOL**



**ERICKSON  
ELEMENTARY SCHOOL**



**DUJARDIN  
ELEMENTARY SCHOOL**

## SAFETY

# of Safety Orientations	35	25	0
# of Incidents	0	0	0
# of Recordables	0	0	0

## Manpower

# Trades	10	5	0
Avg. Daily Manpower	8.2	6	0
Total MHs Worked to Date	3566.5	494	0

# Progress Photos



WESTFIELD MIDDLE  
SCHOOL

**BULLEY &  
ANDREWS**



Dec 24<sup>th</sup>, 8am



Dec 26<sup>th</sup>, 1pm



Jan 3<sup>rd</sup>, 1:30pm



Feb 9<sup>th</sup>, 2026



Feb 16<sup>th</sup>, 2026

# Submittal & RFI Summary



**WESTFIELD MIDDLE  
SCHOOL**



**ERICKSON  
ELEMENTARY SCHOOL**



**DUJARDIN  
ELEMENTARY SCHOOL**

## SUBMITTALS

Total Submittal	144	131	71
Total Open	32	25	26
Total Closed	107	106	45

## RFIs

Total Submittal	39	24	10
Total Open	3	8	6
AVG Return Time	5 Days	5 Days	5 Days



**WESTFIELD MIDDLE  
SCHOOL**



**ERICKSON  
ELEMENTARY SCHOOL**



**DUJARDIN  
ELEMENTARY SCHOOL**

## INSPECTIONS

Total Complete	5	2	0
Total Passed	5	2	0
Scheduled Next Month	12	10	0

# Progress Photos




ERICKSON  
ELEMENTARY SCHOOL

**BULLEY &  
ANDREWS**




# Schedule

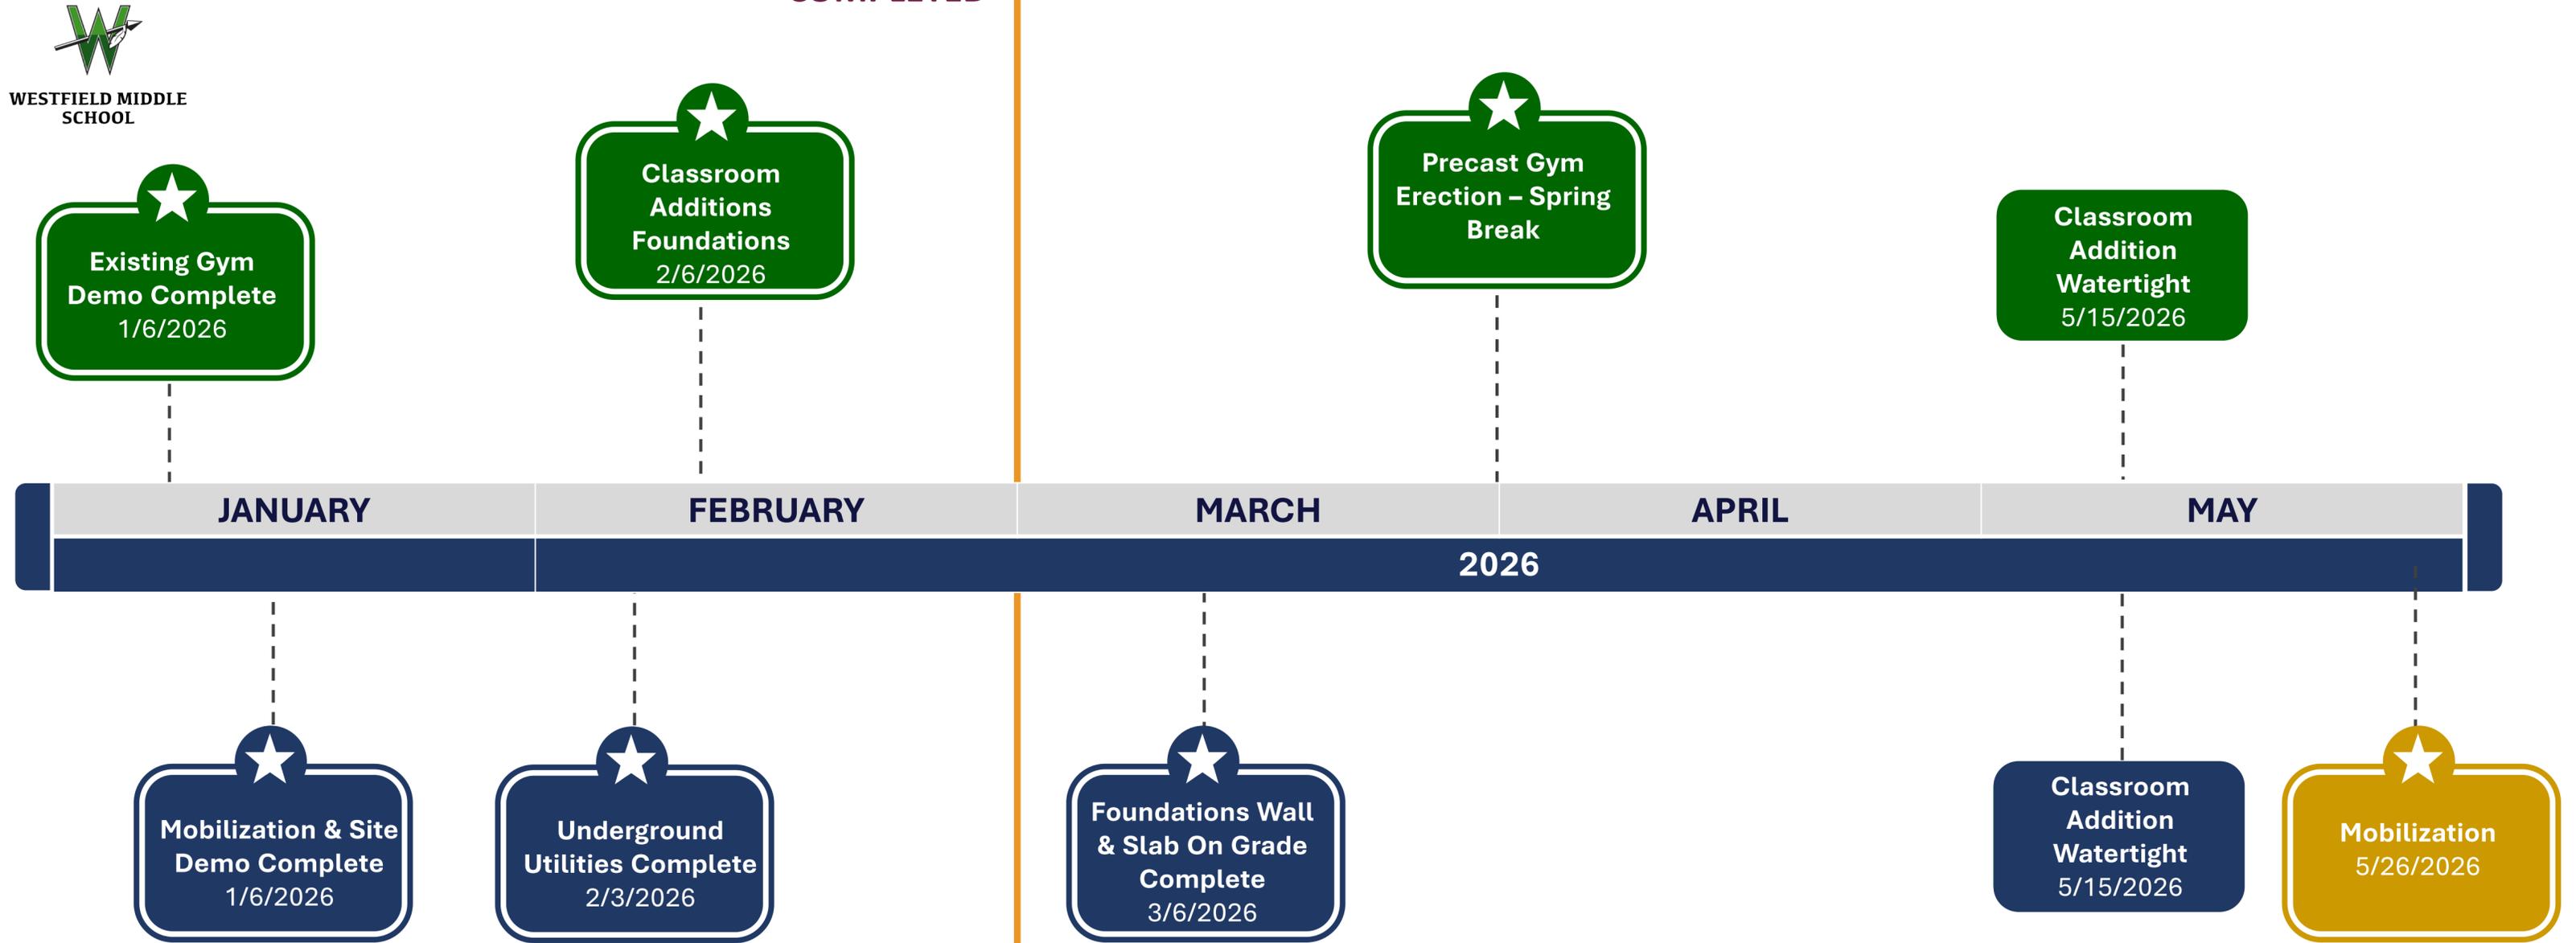

ERICKSON  
ELEMENTARY SCHOOL



DUJARDIN  
ELEMENTARY SCHOOL



# Overall Progress vs. Baseline



**WESTFIELD MIDDLE  
SCHOOL**



**ERICKSON  
ELEMENTARY SCHOOL**



**DUJARDIN  
ELEMENTARY SCHOOL**



COMING SUMMER 2026

Despite the January cold snap, both projects are on schedule compared to the bid schedule.



Behind  
Schedule



On Schedule



Ahead of  
Schedule

# Finances



WESTFIELD MIDDLE SCHOOL



ERICKSON ELEMENTARY SCHOOL



DUJARDIN ELEMENTARY SCHOOL

**BULLEY & ANDREWS**

	Description	Original Budget	Updated Budget	Projected Cost	Under (Over) Budget	Committed Cost	Invoiced To Date
<b>Professional Services</b>	Design & Engineering	\$2,900,000	\$2,900,000	\$2,900,000	\$0 0.0%	\$2,850,000 98.3%	\$2,360,464 82.82%
	Quality & Material Testing	\$116,243	\$116,243	\$126,000	-\$9,757 -8.4%	\$126,000 108.4%	\$32,738 26.0%
	Commissioning	\$77,496	\$77,496	\$67,000	\$10,496 13.5%	\$57,700 74.5%	\$0 0.0%
	<b>Total</b>	<b>\$3,093,739</b>	<b>\$3,093,739</b>	<b>\$3,093,000</b>	<b>\$739 0.0%</b>	<b>\$3,033,700 98.1%</b>	<b>\$2,393,202 78.9%</b>
<b>Direct to Owner</b>	Moving & Storage	\$193,740	\$193,740	\$193,740	\$0 0.0%	\$0 0.0%	\$0 0.0%
	Temporary Facilities	\$0	\$24,313	\$24,313	\$0 0.0%	\$24,313 100.0%	\$0 0.0%
	Furniture & Equipment	\$1,302,987	\$1,302,987	\$1,302,987	\$0 0.0%	\$0 0.0%	\$0 0.0%
	Bond & Insurance Costs	\$135,000	\$135,000	\$135,000	\$0 0.0%	\$127,060 94.1%	\$86,678 68.2%
	Miscellaneous	\$100,000	\$100,000	\$100,000	\$0 0.0%	\$0 0.0%	\$0 0.0%
	<b>Total</b>	<b>\$1,731,727</b>	<b>\$1,756,040</b>	<b>\$1,756,040</b>	<b>\$0 0.0%</b>	<b>\$151,373 8.6%</b>	<b>\$86,678 57.3%</b>
<b>Construction</b>	Westfield Middle	\$21,935,743	\$21,935,743	\$21,935,743	\$0 0.0%	\$21,935,743 100.0%	\$1,421,935.00 6.5%
	DuJardin Elementary	\$8,559,853	\$8,559,853	\$8,559,853	\$0 0.0%	\$8,559,853 100.0%	\$547,754.85 6.4%
	Erickson Elementary	\$8,252,302	\$8,252,302	\$8,252,302	\$0 0.0%	\$8,252,302 100.0%	\$243,353.41 2.9%
	<b>Total</b>	<b>\$38,747,898</b>	<b>\$38,747,898</b>	<b>\$38,747,898</b>	<b>\$0 0.0%</b>	<b>\$38,747,898 100.0%</b>	<b>\$2,213,043 5.7%</b>
<b>Owners Contingency</b>	<b>Total</b>	<b>\$937,636</b>	<b>\$913,324</b>	<b>\$914,063</b>			
<b>GRAND TOTAL</b>		<b>\$44,511,000</b>	<b>\$44,511,000</b>	<b>\$44,511,000</b>		<b>\$41,932,971 94.2%</b>	<b>\$4,692,923 11.2%</b>
