

Status of Bond Projects
8/7/12 Governing Board Meeting

President Boros, Board Members, Mr. Nelson,
Current Project Update:

I. HEALTH, SAFETY, AND SECURITY

A. Transportation Offices:

Construction is complete.

The new transportation and food service offices are complete and occupied. The realignment of the bus yard is also complete and in use.

This project was completed on schedule and on budget.



South Bus Yard (from Pastime Rd)



North Bus Yard (exit at Roger Rd.)

II. INSTRUCTIONAL SPACE / PORTABLE REPLACEMENT

A. Amphitheater Middle School Addition / Remodel:

Design is complete and construction documents have been submitted to the city for plan review and permitting. A Guaranteed Maximum Price is being prepared by CORE Construction and will be presented to the Governing Board at the August 21 board meeting. At the conclusion of tonight's update, Mr. Frank Slingerland of BWS Architecture will give a fly through presentation of the project.

B. Canyon Del Oro High School Addition / Remodel:

Construction is 50% complete.

A detailed progress update will be presented at tonight's meeting as this project is moving so fast it is difficult to project an accurate completion schedule at the date of this report.

CDO project is on schedule and on budget.



Administration Exterior – Storm Water
Drainage Improvements




Administration Interior Finish Application



New MDF on North Elevation of F Bldg



New MDF Interior Prior to Equipment
Installation

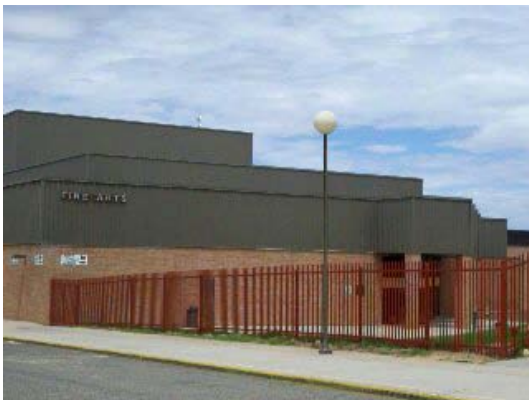

Inner Campus Security Fence



New J-3 Student Restrooms



New North Gym Restrooms



C Bldg Addition –
Underground and Stem Walls



South Gym Repainted



Team Rooms & Locker Rooms Renovated



MPR South Elevation



MPR North Elevation



Kitchen Renovation

C. Canyon Del Oro Stadium Renovation:

The stadium renovation work is 95% complete.

All bleacher and light pole painting, field event venues, paving, irrigation, and sod installation are complete. Final touches and punch list corrections are ongoing.

The stadium repair project is on schedule and on budget.



Re-Painted Bleachers and Light Poles



New Sod and Asphalt



Shot Put Venue Preparation



Long Jump Runway Preparation

D. Copper Creek Classroom Renovation / IT Re-cabling:

Construction is complete.

The campus has been completely re-cabled. New IDF's are complete and in use. All accordion classroom walls have been replaced and the campus is ready for fall semester start.

Copper Creek re-cabling project was completed on schedule and on budget.



New Computer Lab



Library Smart Board Prep and Re-Cabling



Typical Re-cabled Classroom with Accordion Wall Replaced

E. Amphitheater High School Renovations:

Schematic design is complete and Design Development drawings have been started.

F. Holaway Elementary Classroom Addition:

Schematic design is complete and Design Development drawings have been started.

G. Rio Vista Elementary Classroom Addition:

Schematic design drawings are being prepared.

H. Nash Elementary Library Renovation:

There is an architecture vendor recommendation on tonight's consent agenda for Governing Board review and approval. If approved, programming and design will start immediately.

III. TRANSPORTATION

27 New Busses have been received, tested, and are ready for service.

15 are full size transit busses and 12 are mid-size. 6 of the 12 mid-size busses are equipped with wheel chair lifts for special needs students.

