

PROJECT UPDATE

JUNE 2025

TOM BANSCHBACH MIDDLE SCHOOL



OVERALL SITE



EXTERIOR PROGRESS



INTERIOR PROGRESS

CONSTRUCTION STATUS

SITE WORK


- TRACK AND FIELD WORK CONTINUES
- TENNIS COURT UNDERWAY
- LIGHT POLE BASES NEAR COMPLETE

BUILDING

- RTUs SET
- STRUCTURAL STEEL COMPLETE
- ELEVATED SLABS COMPLETE

LOOKING FORWARD

- EXTERIOR WATERPROOFING AND GLAZING INSTALL CONTINUES
- EIFS BEGINS @ MAIN ENTRY
- BUILDING DRIED-IN

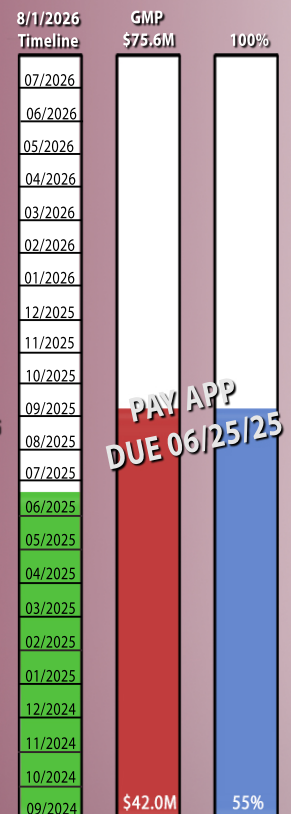


PROJECT UPDATE

JUNE 2025

ADMIN & WAREHOUSE BUILDINGS



OVERALL SITE

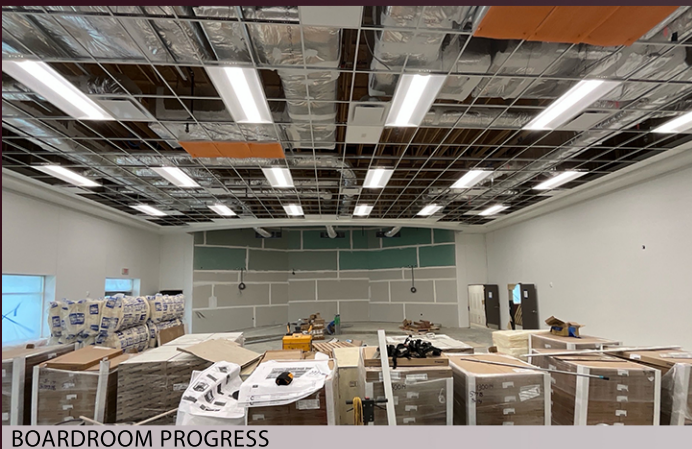

BOARDROOM PROGRESS



WAREHOUSE PROGRESS


CONSTRUCTION STATUS

BUILDING

- INTERIOR FINISHES CONTINUE
- PERMANENT POWER ON AT ADMIN
- INTERIOR DOORS INSTALLED AT ADMIN
- MASONRY VENEER AT WAREHOUSE COMPLETE

LOOKING FORWARD

- FINAL PAINT AT ADMIN
- ELECTRICAL AND LOW VOLTAGE TRIMOUT AT WAREHOUSE

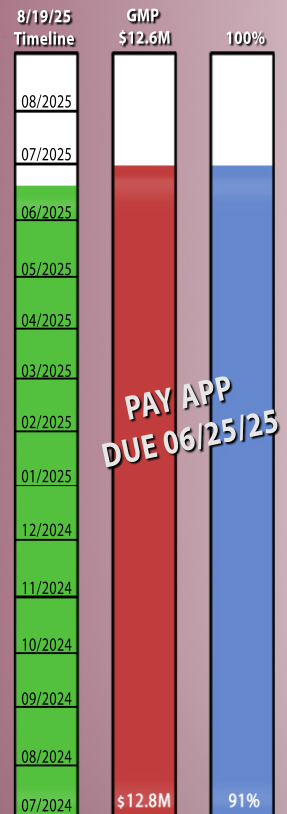

PROJECT UPDATE

JUNE 2025

CARRELL ELEMENTARY SCHOOL



OVERALL SITE



FINAL FIRST FLOOR SLAB POUR



STRUCTURAL STEEL PROGRESS

CONSTRUCTION STATUS

SITE WORK


- SUBGRADE PREP COMPLETE FOR BUS DROPOFF LANE

BUILDING

- FINAL FIRST FLOOR SLAB POUR COMPLETE
- STRUCTURAL STEEL INSTALL BEGAN

LOOKING FORWARD

- COMPLETION OF FOUNDATIONS
- JOIST/DECK INSTALL FOR FIRST FLOOR ROOFS & SECOND FLOOR

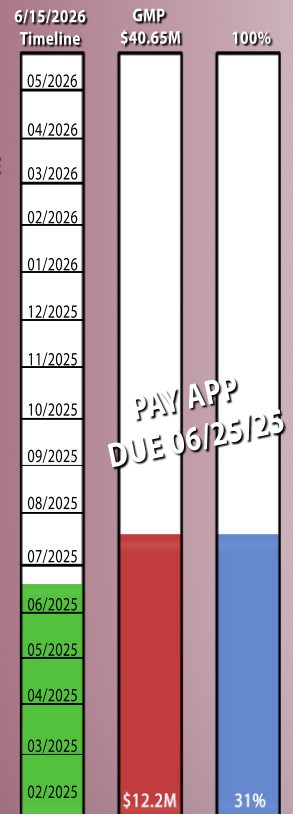

PROJECT UPDATE

JUNE 2025

JACKIE HENDRICKS STADIUM EXPANSION



CONSTRUCTION STATUS

BUILDING

- PRESS BOX STEEL COMPLETE
- CONCESSIONS/RESTROOMS PLUMBING AND ELECTRICAL ROUGHS COMPLETE
- GRANDSTAND AND FIELD HOUSE STEEL IN PROGRESS

LOOKING FORWARD

- LIGHT GAUGE WALL INSTALL AT FIELD HOUSE
- EXTERIOR SHEATHING & WATERPROOFING AT FIELD HOUSE
- BEGIN MASONRY VENEER AT CONCESSIONS/RESTROOMS

