

PROJECT UPDATE

APRIL 2024

GREEN ELEMENTARY SCHOOL



VIEW LOOKING NORTH



TYPICAL CLASSROOM



MEDIA CENTER

CONSTRUCTION STATUS

SITE WORK


- FINAL GRADES - PAVEMENT CLEANING
- LANDSCAPING SOON

BUILDING

- MASONRY CLEANING
 - CARPET IN CLASSROOMS
- NEARING COMPLETION
- KITCHEN EQUIP START UP

LOOKING FORWARD

- ABOVE CEILING INSPECTIONS CONTINUES
- DOOR HARDWARE
- CONTRACTOR PUNCHLIST OCCURING
- ARCHITECT/OWNER PUNCHLIST WALKS

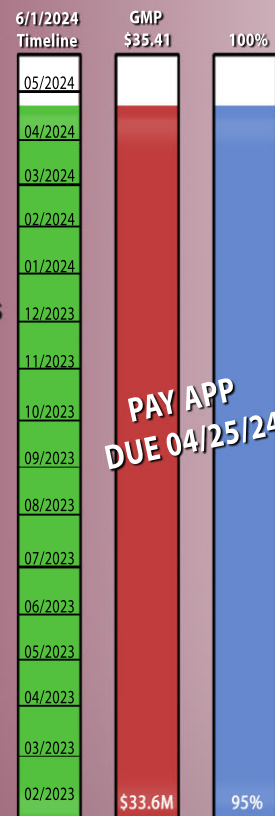

PROJECT UPDATE

APRIL 2024

JAMES ELEMENTARY SCHOOL



Lorem Ipsum



KITCHEN EQUIPMENT



FRONT ENTRY RECEPTION

CONSTRUCTION STATUS

SITE WORK


- FENCING IN NEXT 2 WKS
- FINAL GRADING

BUILDING

- FINAL SWITCHGEAR SET
- OVERHEAD INSPECTIONS
- MILLWORK INSTALLATION
- GYM FLOOR COMPLETE

LOOKING FORWARD

- RTU TEST AND BALANCE
- CEILING TILE INSTALLATION
- PUNCHLIST INSPECTIONS
- EXTERIOR FLATWORK

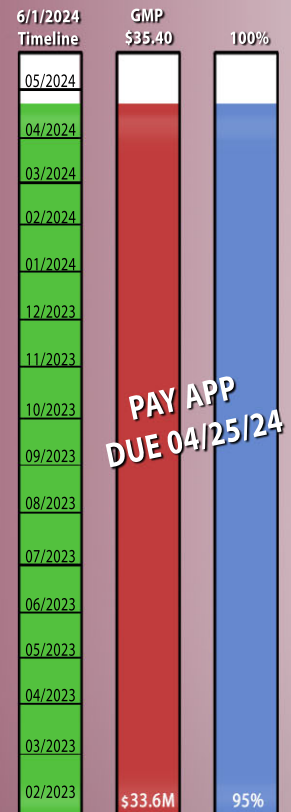

PROJECT UPDATE

APRIL 2024

LOVELADY HIGH SCHOOL ADDITION



NEW WALK TO BOORMAN LN



TYPICAL CLASSROOM



RESTROOM FIXTURES & PARTITIONS

CONSTRUCTION STATUS

SITE WORK


- Flatwork installation for walks

BUILDING WORK

- Ceiling tile installaion
- Masonry cleaning and sealing

Looking Ahead

- Test & Balance
- Overhead inspections
- Corrior VCT
- Contractor Punchlists

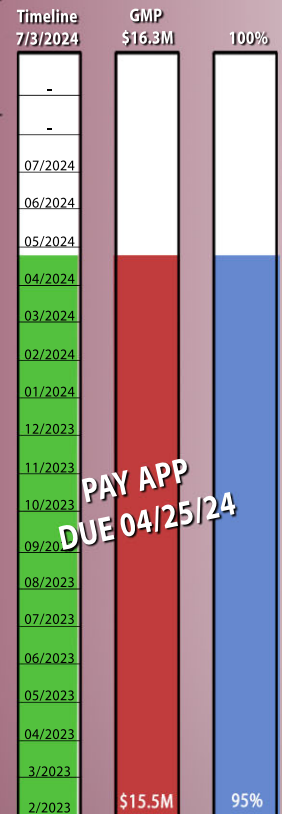

PROJECT UPDATE

APRIL 2024

PERKINS EARLY CHILDHOOD & JAGUAR DAYCARE



VIEW LOOKING SOUTH



STEEL INSTALLATION, COLD FORM METAL STUDS & DRIVES



STORM SHELTER CONSTRUCTION

CONSTRUCTION STATUS

SITE WORK

- DROP-OFF PAVING CONTINUES

BUILDING

- STEEL COLUMNS AND JOISTS
- SLAB POURS
- STORM SHELTER ICF FORMS
- PLUMBING IN KITCHEN

LOOKING FORWARD

- SUBMITTALS AND SHOP DRAWINGS
- PRE-CONSTRUCTION COORDINATION MTGS
- COLD FORM STUD FRAMING

