

School Board Update September 17, 2024



PROJECT IMPLEMENTATION

BOND 2023

SEPTEMBER 17, 2024

ECTOR COUNTY ISD MIDDLE SCHOOL



Design

Procurement

CONSTRUCTION UPDATE

DESIGN

- Received the 50% Construction Documents on 8/30/2024
- Estimates from Teinert and Gallagher due on 9/25/2024

ON-SITE ACTIVITY

 Geo-technical boring completed. Draft report has been received. Final report due on 9/20/2024.

COST SUMMARY				
Budget	\$ 120,000,000			
Encumbrance	\$ 5,600,318			
Actual	\$ 2,730,541			
Available	\$ 111,669,141			
Percentage Complete:	2%			





WWW.GALLAGHERTX.COM


Construction

SEPTEMBER 17, 2024

4

ECTOR COUNTY ISD

CAREER & TECHNOLOGIES CENTER

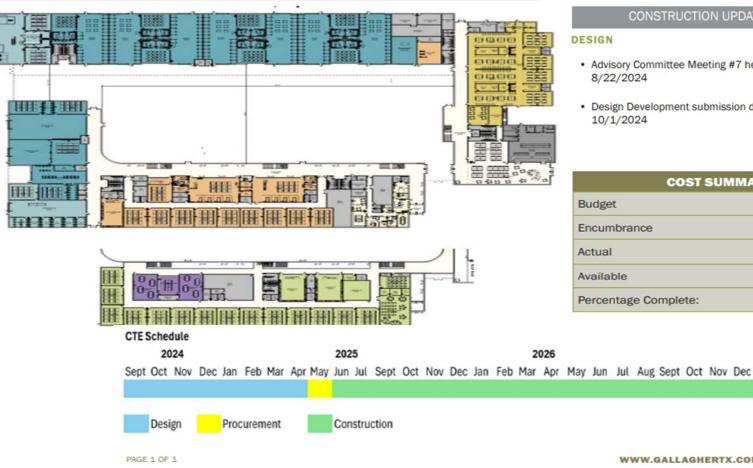

CONSTRUCTION UPDATE

- · Advisory Committee Meeting #7 held on 8/22/2024
- · Design Development submission due on 10/1/2024

COST SUMMARY				
Budget	\$ 80,000,000			
Encumbrance	\$ 5,160,733			
Actual	\$ 890,112			
Available	\$ 73,949,155			
Percentage Complete:	1%			

Q

GALLAGHER

WWW.GALLAGHERTX.COM

TLC – Educational Specifications Addendum



Educational Specifications Addendum

Transition Learning Center

Submitted: September 11, 2024





Parkhill Architecture Projects

- Parkhill has met multiple times over the last month with ECISD staff:
 - o Ag Farm
 - o Permian Auditorium
 - o JROTC Facility
 - Transportation Facility
- Parkhill & Operations working with City of Odessa to understand ordinances affecting construction.
- Parkhill & ECISD staff evaluating site options



Ag Farm

- Land Survey and Geotechnical Evaluation Underway
- Parkhill Architects will provide samples of past projects:
 - Lubbock ISD Ag Educ. Facility 40,000 sq ft. (2022)
 - Lubbock ISD Animal Barn 15,500 sq ft (under construction)
 - L-CISD Ag Educ. Facility -15,000 sq ft (2014)
 - L-CISD Ag Educ. Facility 27,000 sq ft (2020)
 - Plains ISD Ag. Educ. Facility 15,000 sq ft (2013)



Middle School Bleacher Replacement

- Bonham MS:
- $\circ~$ Bowie MS:
- Crockett MS:
- Ector MS:
- Nimitz MS:
- Wilson & Young MS:
- Cobalt Blue Deep Violet Crimson Red Cobalt Blue Blue Dusk Black











ECISD Bond 2023 Costs by Project as of 9/11/2024




Project Name	Project	Purchase Orders Encumbrance	Paid	Remaining Available	Percentage Complete
	Budget		Actual		
MIDDLE SCHOOL	120,000,000	5,600,318	2,730,541	111,669,141	2%
PRIORITY 1&2 ITEMS	117,783,000	5,090,723	441,446	112,250,831	0%
HS/CTE CENTER	80,000,000	5,160,733	890,112	73,949,155	1%
TRANSPORTATION FACILITY	35,000,000	1,480,500	94,500	33,425,000	0%
AUDITORIUM RENO-PHS	12,500,000	725,156	71,719	11,703,125	1%
TECHNOLOGY-PA, BELL, CLOCK, FA S	10,000,000			10,000,000	0%
LAND PURCHASE	9,000,000	131,314	835,008	8,033,678	9%
TRANSITION LEARNING CENTER	8,000,000	370,500	19,500	7,610,000	0%
AG FARM BUILDINGS-CTE	7,500,000	360,141	5,484	7,134,375	0%
TECHNOLOGY ITEMS-SURVEILLANCE	6,000,000	3,458,327	1,447,995	1,093,678	24%
FINE ARTS INSTRUMENTS	3,665,000	487,568	838,602	2, <mark>338,8</mark> 30	23%
TECH ITEMS-FLT PNL BDS,AV EQP	3,500,000		3,422,512	77,488	98%
TECHNOLOGY - PHONE SYS	2,500,000			2,500,000	0%
TRANSPORTATION BUSES	2,450,000		Ĩ	2,450,000	0%
JROTC FACILITY	1,500,000	96,257	7,805	1,395,938	1%
TECHNOLOGY ITEMS - AV EQUIP	1,500,000			1,500,000	0%
ATH-MS GYM BLEACHERS	1,000,000	845,158		154,842	0%
MS UNIF-BAND&MARIACHI	685,000		6 2	685,000	0%
ATH-BB & TENNIS LIGHTS-OHS	650,000	42,000	558,000	50,000	86%
ATH-MS TENNIS COURT RESURFACE	480,000	40,121	216,826	223,053	45%
ATH-BASEBALL LIGHTING-PHS	400,000	80,799	319,200	1	80%
MS PERFORMANCE RISERS	150,000	-	30,948	119,052	21%
Totals	424,263,000	\$ 23,969,615	\$ 11,930,198	\$ 388,363,187	
Percent	100%	6%	3%	92%	

FUTURE ACTIONS

BOND 2023

Priority 1 & 2 Items – Electrical Projects Planning

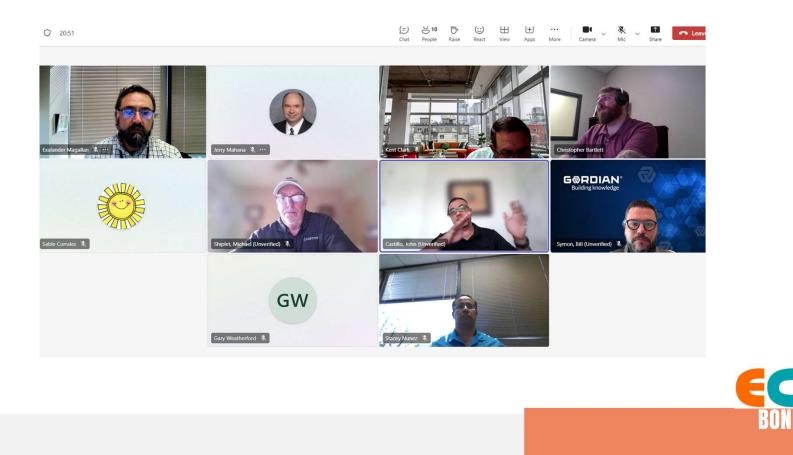

Advisory Committees

Advisory Committees continue to develop for these projects:

- o Ag Farm
- o JROTC Facilities
- Permian High School Auditorium Renovation
- Transition Learning Center
- o New Middle School
- New CTE High School



THANK YOU

