



WAUNAKEE COMMUNITY MIDDLE SCHOOL - PROJECT UPDATE


MAY 7, 2024

AGENDA

- BETHEL CIRCLE PROJECT BID RESULTS
- MIDDLE SCHOOL PROJECT BID RESULTS
- MIDDLE SCHOOL SUBCONTRACTOR AWARDS



BUDGET BREAKDOWN - \$175 MILLION

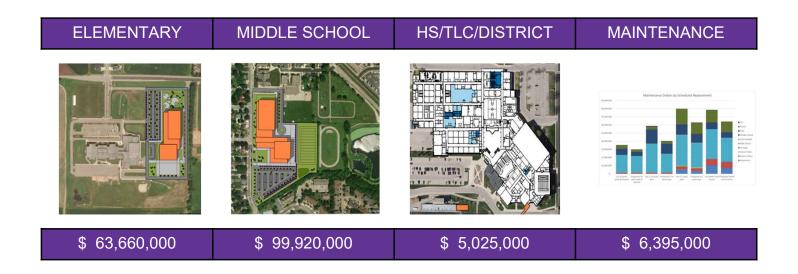



WCSD MIDDLE SCHOOL - BID RESULTS UPDATE

DESCRIPTION	MAY 2024
CONSTRUCTION	\$ 84,539,820
CONTINGENCY	\$ 3,580,180
SOFT COSTS	\$ 11,700,000
TOTAL	\$ 99,920,000



- Included items previously identified as alternates
 - O Track resurfacing, outdoor classroom, lockers, cellular repeater system, full height tile
- Includes budget for solar panels



WCSD MIDDLE SCHOOL NEXT STEPS

- JUNE 2024
 - FINAL GUARANTEED MAXIMUM PRICE (GMP)
 - MULTIPLE SUBCONTRACTOR BID AWARDS
 - MOBILIZATION ON SITE
- JULY 2024
 - REMAINING SUBCONTRACTOR BID AWARDS
 - BUILDING DEMOLITION
 - NEW BUILDING FOUNDATION



MIDDLE SCHOOL BID AWARDS

SUBCONTRACTOR BID AWARDS

REBAR SUPPLY

CONCRETE REDI-MIX SUPPLY

FIRE PROTECTION

HATCH BUILDING SUPPLY


ADVANCED CONCRETE

HOOPER CORPORATION

***SEE SEPARATE ATTACHMENT FOR BID TABULATIONS



DISTRICT OFFICE SCOPE OF WORK

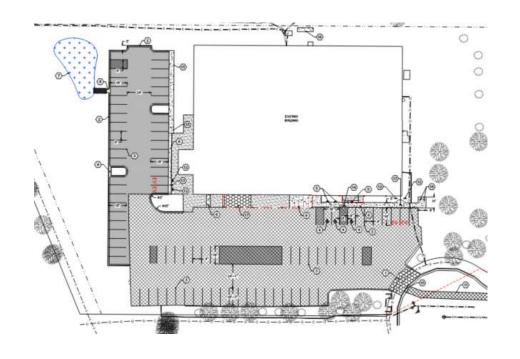






DISTRICT OFFICE WORK

- 2024 WORK TARGET BUDGET \$615,000
 - OFFICE MODIFICATIONS
 - PARKING LOT REPLACEMENT/ADDITION
- FINAL BID RESULTS \$629,000
 - O INCLUDES ELECTRIC VEHICLE CHARGING ROUGH-IN
 - INCLUDES ADDITIONAL OFFICES/RECORDS SPACE
 - VOGEL BROS. SUPERVISION/MANAGEMENT INCLUDED IN HIGH SCHOOL GMP
- APPROVAL TO PROCEED AT \$615,000 WITH VALUE ENGINEERING PROCESS TO REACH TARGET (VOGEL/EUA/WCSD ADMINISTRATION)
- ASK FOR ADMINISTRATION APPROVAL FOR SUBCONTRATORS AWARDS
 - WILL PROVIDE FINAL LISTING IN JUNE



OFFICE



