

ROOF PROGRESS REPORT THROUGH 07-25-2025

Contact:	Keri Hacker (507) 273-2689 khacker@tremcoinc.com
Inspector:	Thomas Fritz Jr (507) 606-2861 tfritzjr2128@gmail.com
Project Manager:	Mike Kerker (319)-277-9355 mike@blackhawkroof.com
Contractor:	Black Hawk Roof Company
Foreman: (Translator)	Angel Palofox (817)-441-3919

Areas of Work: Roof Area #4, 8A, and 10

- 1-½" isocyanurate insulation board mechanically attached over existing insulation board
- ¼" prime coverboard adhered in low-rise adhesive over insulation
- 60 mil KEE fleece-backed membrane adhered in membrane adhesive
- ½" HD iso coverboard adhered in low-rise adhesive over existing insulation
- 45 mil KEE fleece-backed membrane adhered in membrane adhesive
- Removed ballast from roof


Notes:

- Sheet metal installation to begin after the flashing detail is complete

Issues and Corrections:

- Exposed detail work identified, and repair made


Project Maps:

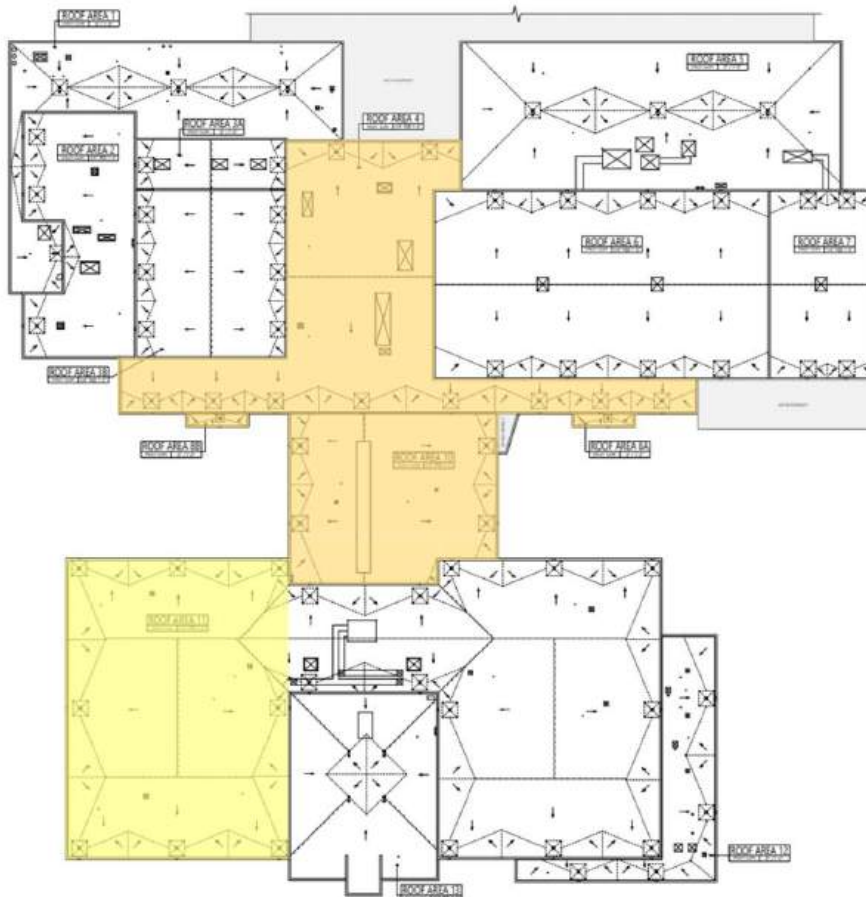

Roof Area 100% Completed



Roof Area primarily completed



Roof Area started

ROOF PROGRESS REPORT THROUGH 07-25-2025


ROOFING SCHEDULE		
ROOF AREA	STATUS	SCHEDULE
#4	90% COMPLETE	WEEK OF 7/21
#8A	90% COMPLETE	WEEK OF 7/21
#8B	90% COMPLETE	WEEK OF 7/21
#10	90% COMPLETE	WEEK OF 7/21
#11	10% COMPLETE	WEEK OF 7/28
#12	INCOMPLETE	TBD
#13	INCOMPLETE	TBD

ROOF PROGRESS REPORT THROUGH 07-25-2025




Roof edge detail exposed and not fastened on Roof
Area #10

ROOF PROGRESS REPORT THROUGH 07-25-2025

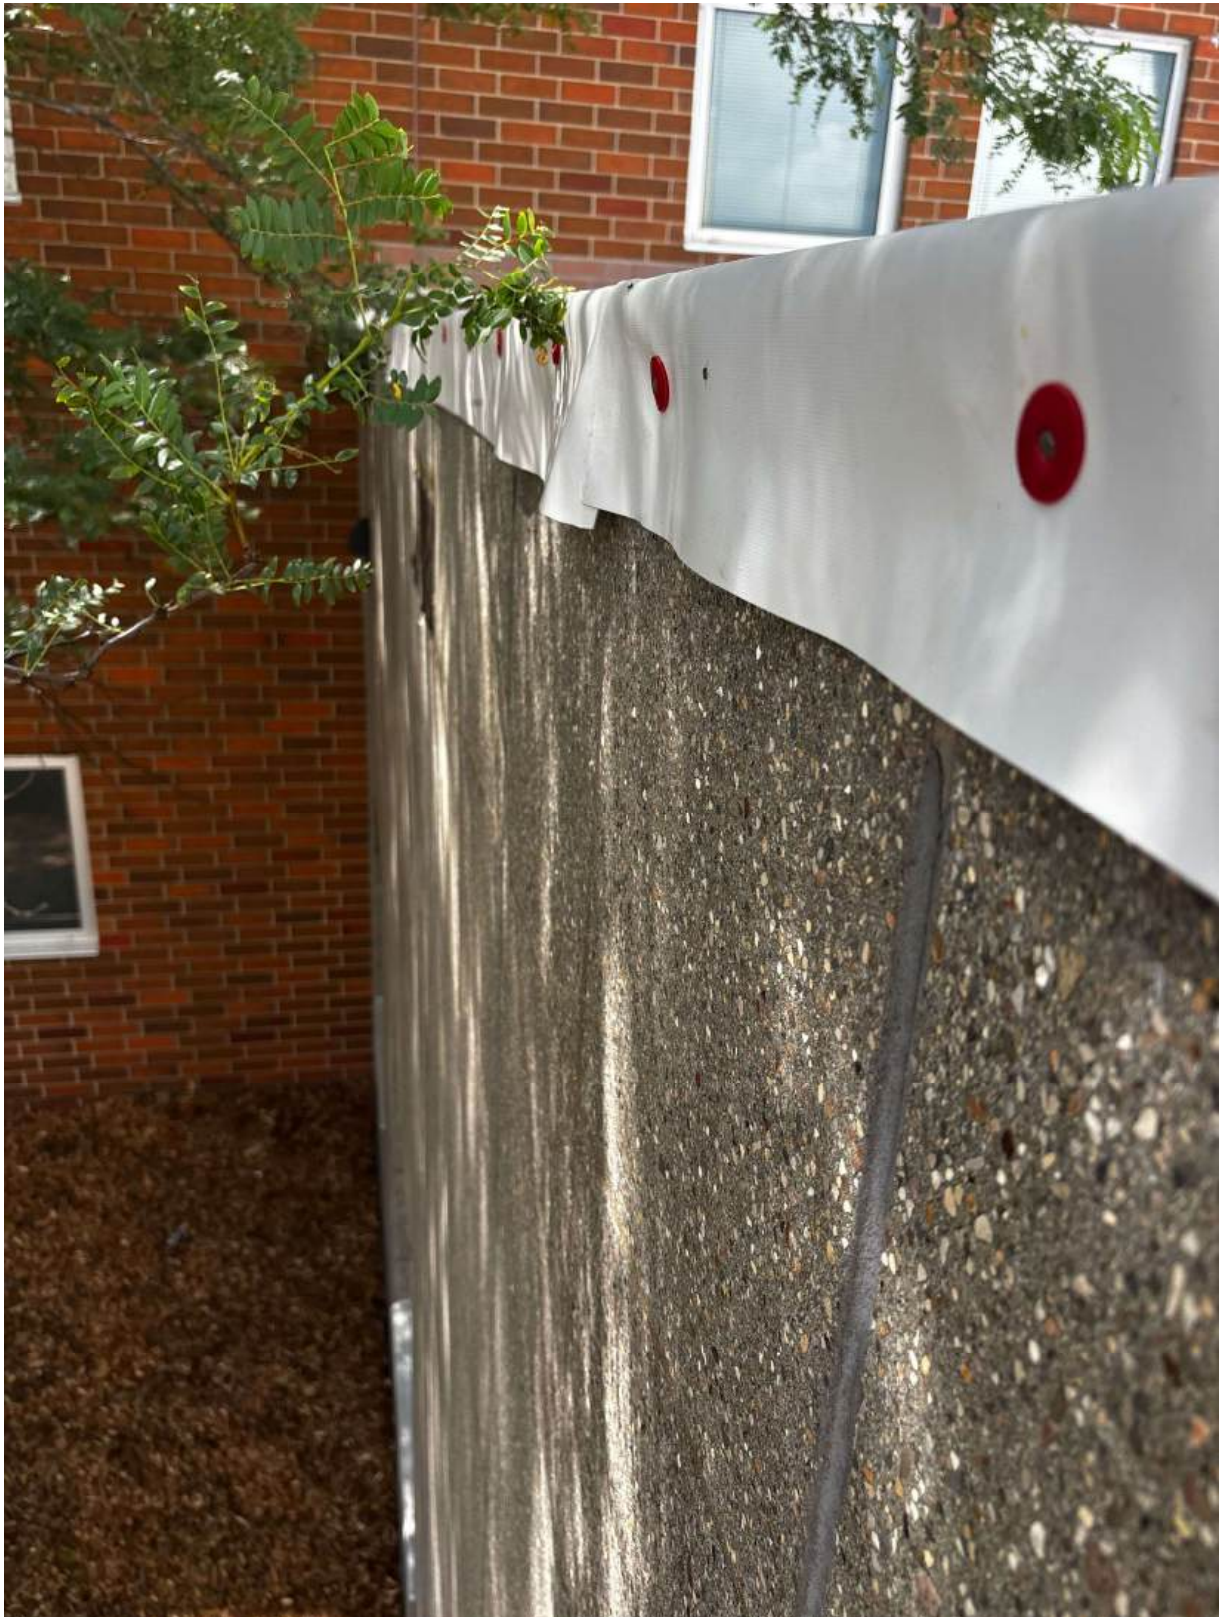

Fastened roof edge detail with nail and rubber washer on perimeter of Roof Area #10

ROOF PROGRESS REPORT THROUGH 07-25-2025

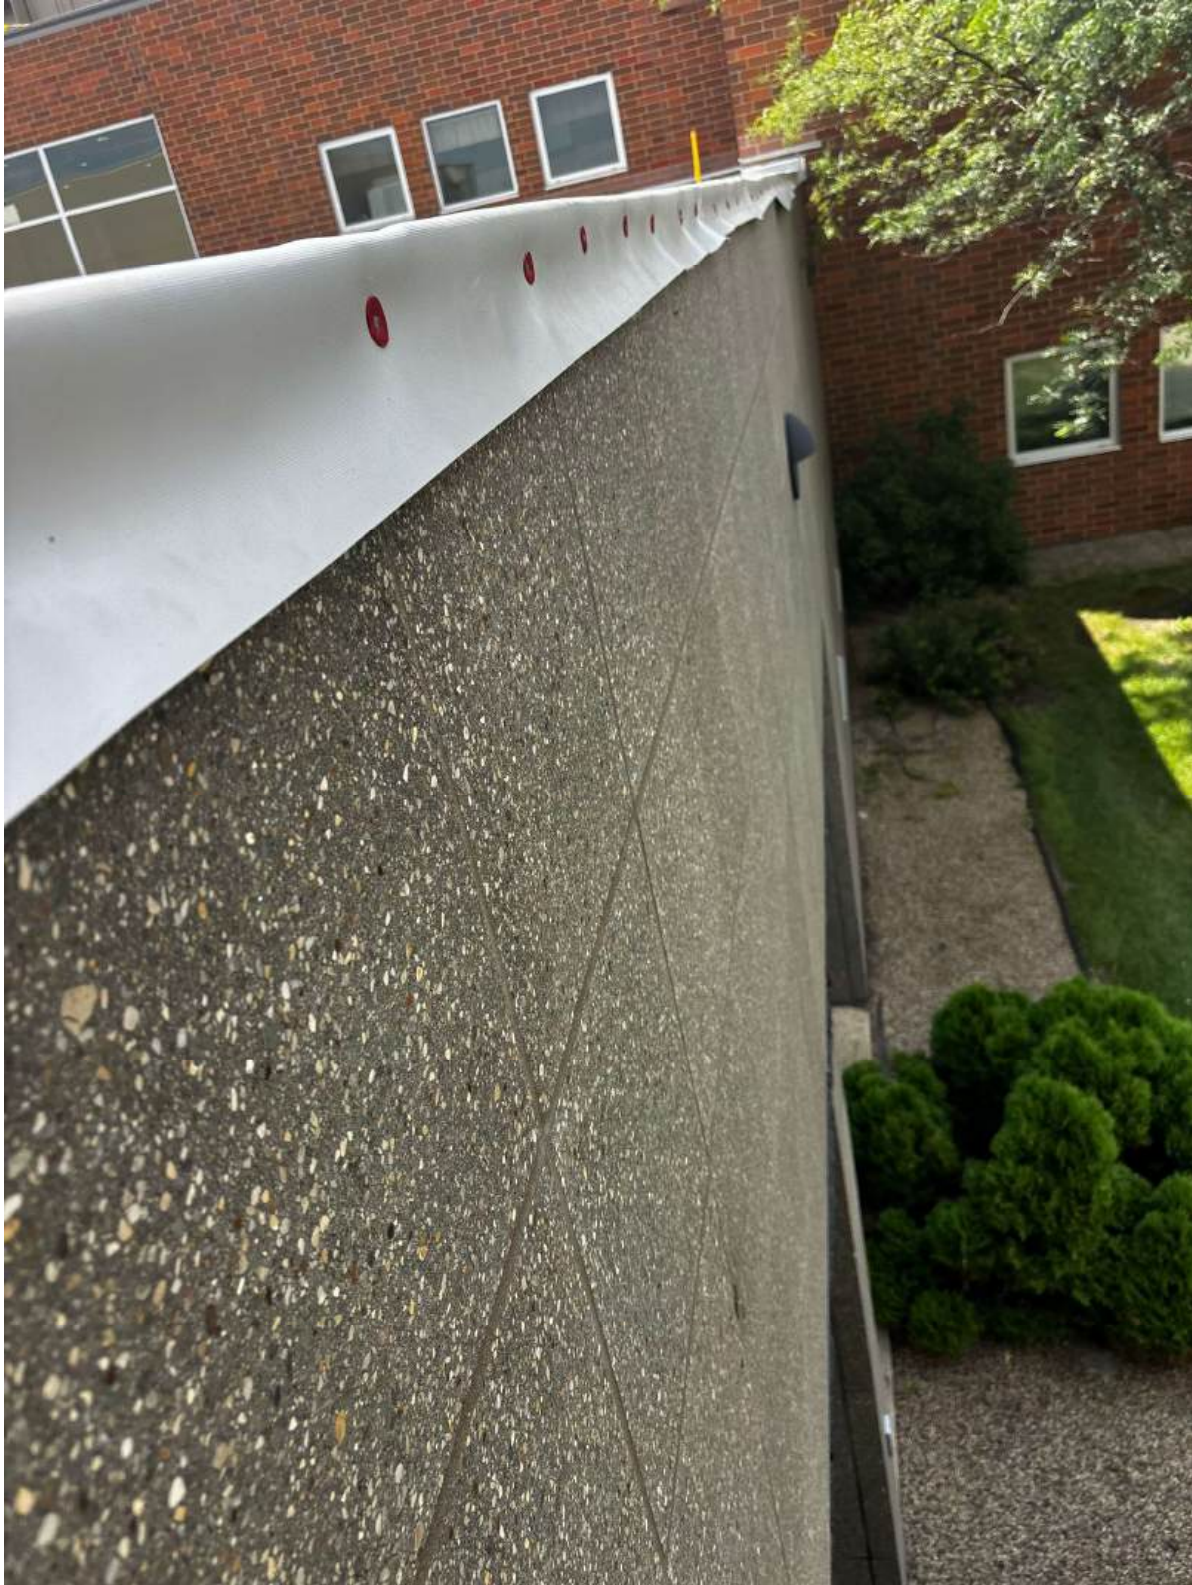

Fastened roof edge detail with nail and rubber washer on perimeter of Roof Area #10

ROOF PROGRESS REPORT THROUGH 07-25-2025



Roof edge detail exposed awaiting progress

ROOF PROGRESS REPORT THROUGH 07-25-2025



Roof edge detail: heat welded KEE membrane to seal exposed area

ROOF PROGRESS REPORT THROUGH 07-25-2025



Removed Ballast from Roof Area #11

ROOF PROGRESS REPORT THROUGH 07-25-2025



Removed Ballast from Roof Area #11

ROOF PROGRESS REPORT THROUGH 07-25-2025



Overview of Roof Area #4

ROOF PROGRESS REPORT THROUGH 07-25-2025



KEE membrane flashing sealed with termination bar
and caulk

ROOF PROGRESS REPORT THROUGH 07-25-2025



Overview of Roof Area #8B

ROOF PROGRESS REPORT THROUGH 07-25-2025



2" from sump perimeter to allow for optimal
drainage

ROOF PROGRESS REPORT THROUGH 07-25-2025



KEE membrane flashing sealed with termination bar
and caulk

ROOF PROGRESS REPORT THROUGH 07-25-2025



Drain and Sump Detail: KEE membrane is sealed to ensure watertight connection around drain.

ROOF PROGRESS REPORT THROUGH 07-25-2025



Overview of Roof Area #4

ROOF PROGRESS REPORT THROUGH 07-25-2025



Fastened roof edge detail with nail and rubber washer on perimeter of Roof Area #4 - Wall will be covered in Metal Wall Panels by sheet metal crew

ROOF PROGRESS REPORT THROUGH 07-25-2025



Roof-to-wall detail awaiting sheet metal installation

ROOF PROGRESS REPORT THROUGH 07-25-2025



Curb awaiting sheet metal installation
