




Construction Report

September 2026

Presented by Jerry Jackman

**Capital
Improvements
completed this
summer:**

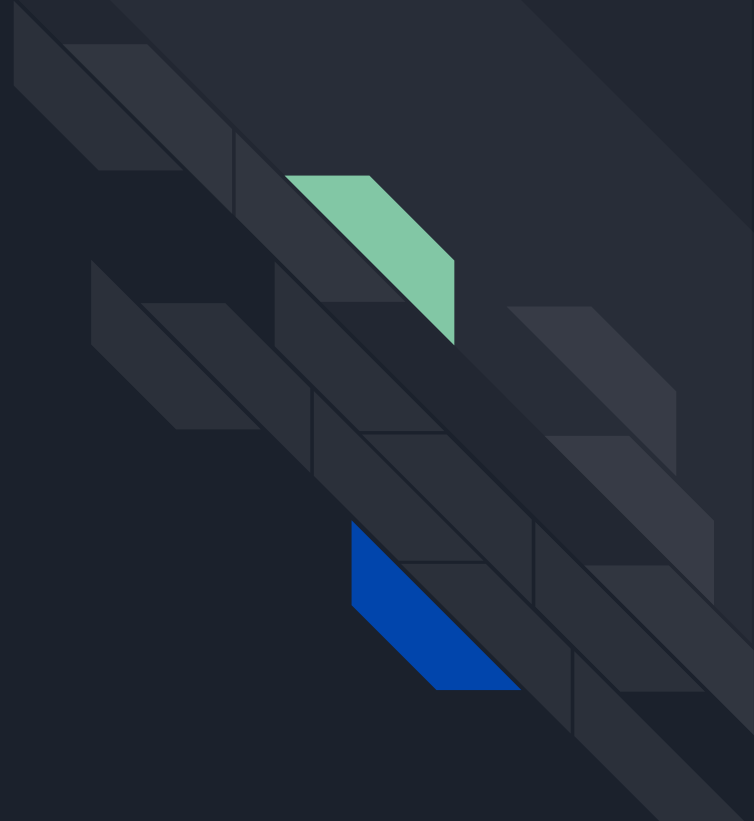

Summer Capital Improvements

01

Roof Replacement

Completed full roof replacements to TMC and on the classroom towers of BEHS

02


Refinished Floors

Sanded, sealed, and polished gym floors to pristine condition.



Locations


BEHS, BRHS, & BRMS

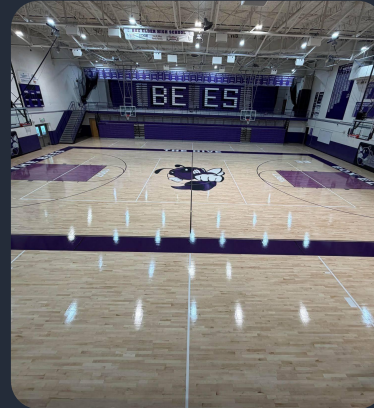

03

Bleacher Upgrade

Removed outdated structures and installed modern, safer seating.

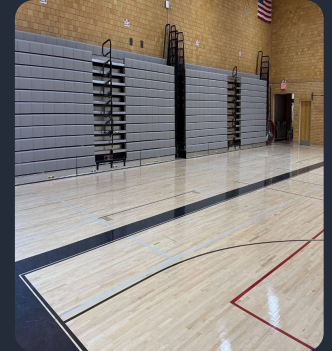

Locations

BRMS Gym

Summer Capital Improvements

04

Parking Lot Improvements

Resurfaced some areas and seal coated several parking lots.


Locations

- Harris, Garland, & Park Valley
- Snowville & Willard

05

Computer Room Remodel

Removed tiered seating, replaced carpet and added some cabinetry.

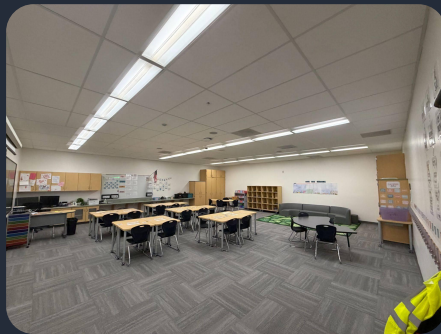

Locations

TMC & Garland

Summer Capital Improvements

06

Dishwashers Added

Added new commercial dishwashers to upgrade cafeteria facilities.

Locations

- BRHS
- ACHI
- TMC

07

Portables Moved

Moved and set up portables to Fielding.



08

Rigging & Curtains

Abated fire curtains and replaced rigging at BEHS and BRHS.



09

Sewer Line Repair

Repaired critical sewer lines.


Locations

- BRMS
- Lake View

10

The prep work for the playgrounds at Century, North Park, and McKinley is complete. Parts will be delivered on the 8th and 9th and all five will be completed by the end of September!

**New construction
update.**

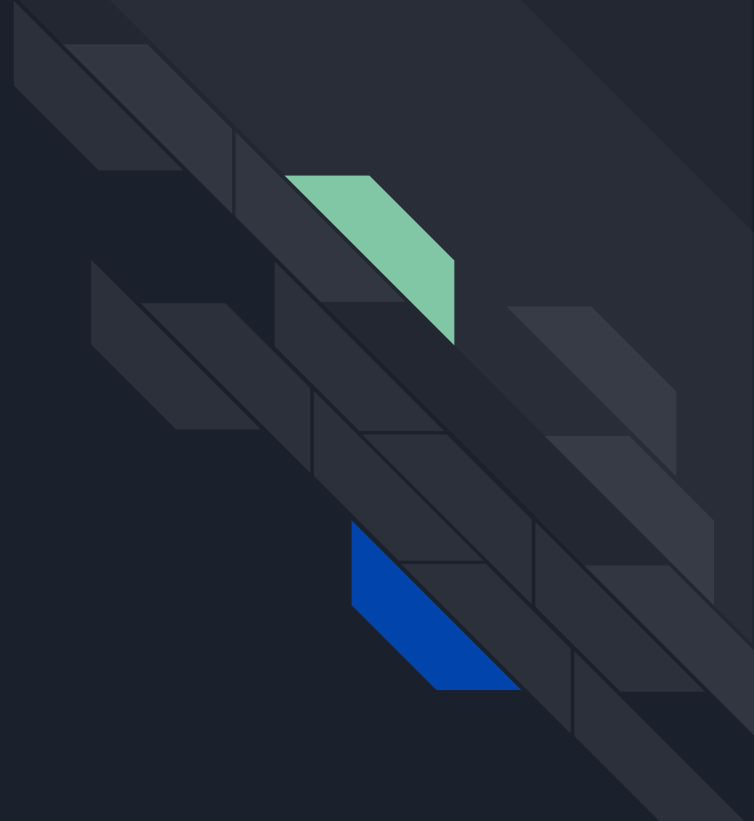

Construction Update Discovery

01 Interior & Utilities

Removed ceiling. Hot water lines inside are done. Cold water and Fire sprinklers are underway.

02 Foundation & Framing

Footings are almost done and some foundation walls are framed up.

03 Upcoming Milestones

Hope to start masonry by the end of September.



Construction Update

New Elementary in Tremonton

01 Surcharge is still happening

Things have settled approximately 2 hundredths of an inch so hoping to go till the beginning of October and then push to end the surcharge and get started on that side of the building.

02 Received approval to start on North side

Submitting for rebar and should start digging footings in three weeks. Should put water hookup in at the same time

03 Starting today, looking at 18 Month build

Hoping to finish in less, but March 2028 is the conservative completion date.

