




Construction Update

School Board Meeting - October 12, 2026

Communication Structure

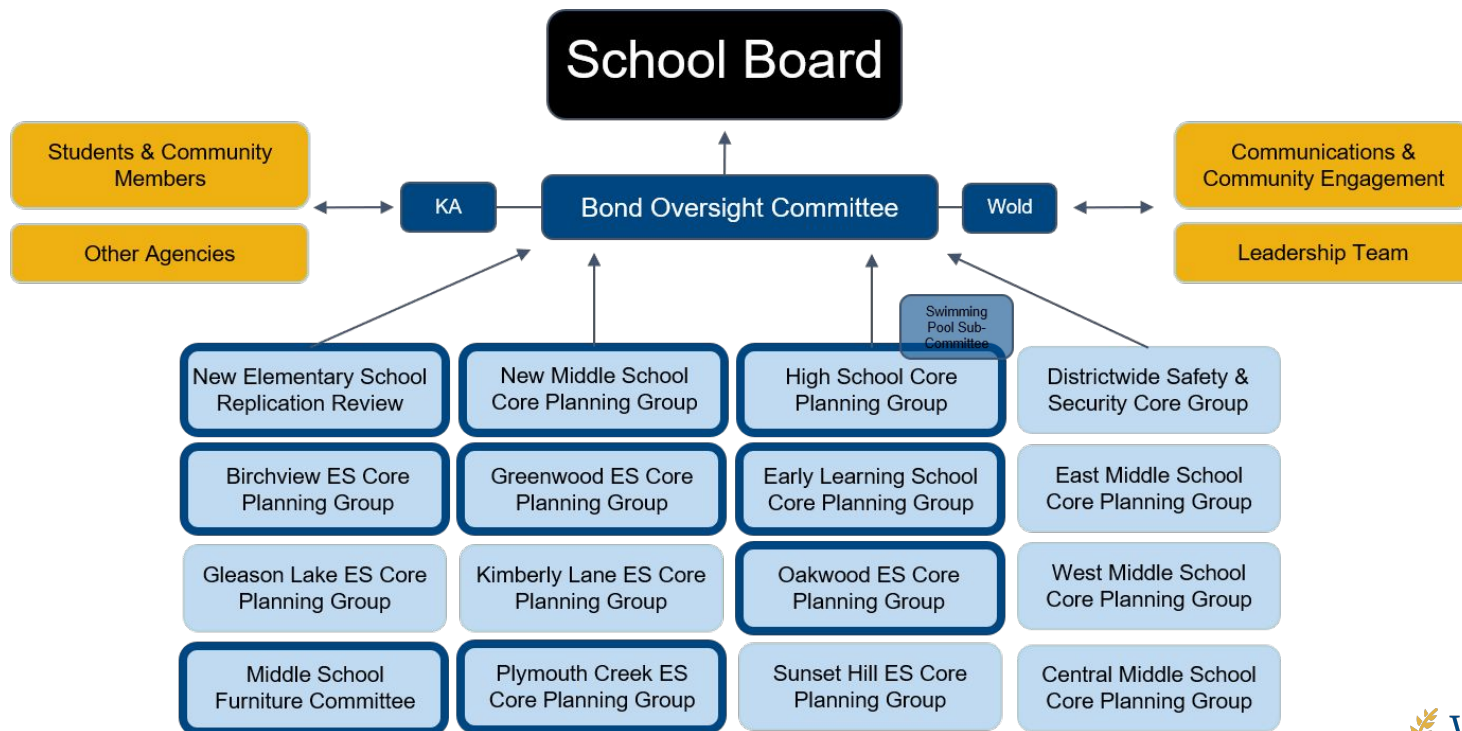

Strategic Partners



Design Team

Key Partners

- Wold Architects & Engineers
- Kraus-Anderson Construction Company
- Bolton & Menk



City of Plymouth

Joint Initiatives

- Wayzata High School Campus
- Plymouth Creek Site Safety



City of Medina

Site Development

- Site for Elementary #10 & Middle School #4
- Highway 55 Traffic Study

Middle School #4

Core Planning Group

7 Meetings Completed

Spanning June 15th through September 25th

School Tours

Completed on June 25th

User Groups

15 User Group Teams

School-level representation

1st Meetings

Completed October 6th & 8th

2nd Meetings

Scheduled for week of October 26th

Elementary School #10

Replication Review

Meetings Ongoing

Building and district administrators

Site Layout (along with MS #4)

City of Medina

Infrastructure to support both district & city

Other Agencies

MN Department of Transportation (Highway 55)

Hennepin County (Hamel Road)

Railroad

High School Addition



Core Planning Group

Scheduled Meetings

First meeting completed October 6th

5 more every two weeks through December 15th



City of Plymouth

Coordinated Site Planning

Playing fields realignment

Parking & infrastructure

Status of Other Projects

Birchview Elementary School

Addition to add full Kitchen

- Through core planning process and into user input meetings

Greenwood Elementary School

Renovation to add full Kitchen

- Through core planning process and into user input meetings

Plymouth Creek Elementary School

Site Improvements

- Preliminary planning stages with City of Plymouth

Status of Other Projects, continued

Oakwood Elementary & Early Learning School

2nd Level Build-Out & Various Renovations

- Through core planning process and nearing the completion of user input meetings

Middle School Furniture

Furniture Refresh & Asset Addition

- Through core planning process and classroom pilot furniture is on order. User input to follow pilot in Spring 2027

Notable Next Steps

- Continue through core planning & user input groups
 - New elementary school, new middle school, high school addition, Birchview, Greenwood, Plymouth Creek, Oakwood/Early Learning, & middle school furniture
- Agreement & approval of high school campus design
 - Surveys, soil borings, permits, wetland delineation, etc.
 - Finalize timelines & construction schedule
- Initiate swimming pool sub-committee
- Conduct traffic studies
 - Medina site, high school & Plymouth Creek



Questions?
