

# Aledo ISD Board Update 2023 Bond Progress

December 16, 2024



**2023**  
**BOND**  
Aledo Independent School District



Elementary School #7

\$59,800,00



High School Addition/Repurpose

\$20,200,00



AHS/DNG Furniture

\$5,000,000



Transportation

\$4,500,000



Land (to include tracts for additional high school facilities)

\$17,800,000



Safety & Security

\$5,000,000



Technology

\$6,500,000



Facility Maintenance

\$5,000,000

**TOTAL BOND PACKAGE:**

**\$123,800,000**

# McKinney Elementary School- ES#7

Grades: K-5

Capacity: 889

Budget: \$59,800,000.00

Amount Obligated To Date: \$54,114,153.10

Phase Completion: **planning, design, procurement, construction**, warranty

Square Footage: 106,180

Date To Open: August 2024

# McKinney Elementary School- ES#7

- **Construction**
  - Substantially complete.
    - Punch list
    - Contractor demobilization
    - Site concrete
    - HVAC balancing
  - Close out
    - January target

# AHS Repurpose and Additions

Grades: 9-12

Capacity: 3,000

Budget: \$20,200,000.00

Amount Obligated To Date: \$19,193,201.89


Phase Completion: **planning, design, procurement**, construction, warranty

Date To Open: August 2024

# AHS Repurpose and Additions

- Construction
  - AHS Reno
    - Substantially complete.
    - Punch list ongoing.
  - Steve Wood Complex
    - Hardened CMU 99% complete.
    - Structural steel is 90%.
    - Roof decking is being installed.
  - AG Barn Addition
    - Sheet metal walls complete.
    - Insulation and roofing complete.

# Steve Wood Complex

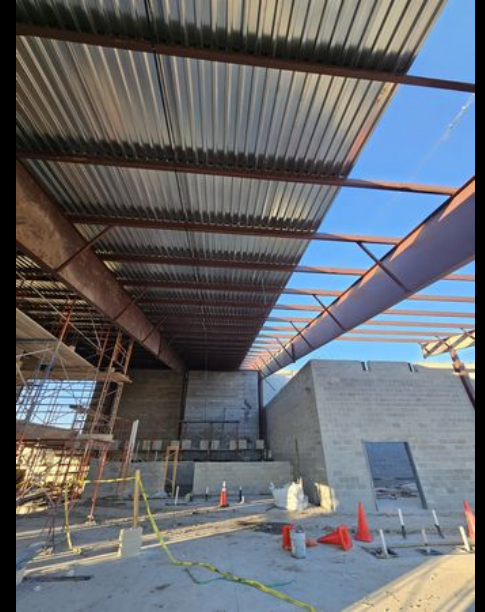

# Steve Wood Complex





# Ag Barn Addition

