

DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

Construction Report

August 2024

Active Construction Timeline



Facility	Phase of Development	Move In Date
Hill Elementary School	Under Construction	TBD
Reeves Elementary School	Under Construction	Summer 2025
Denton High School Multipurpose	Under Construction	Summer 2025
Braswell High School Multipurpose & Additions	Under Construction	Summer 2025
Guyer High School Multipurpose & Ag Facility	Under Construction	Fall 2025
Ryan High Renovation & Multipurpose	Awaiting Permit	TBD
Crownover Middle School Track & Field	Under Construction	December 2024
Myers Middle School Track & Field	Under Construction	December 2024
Rodriguez Middle School Track & Field	Under Construction	December 2024

Completed Projects



Facility	Phase of Development	Move In Date
Evers Park Elementary School Renovation	Completed	August 2024
Alexander Elementary School Renovation	Completed	August 2024
Blanton Elementary School Renovation	Completed	August 2024
Nelson Elementary School Renovation	Completed	August 2024
Strickland Middle School Renovation	Completed	August 2024
Fred Moore Day Nursery School Roof Replacement	Completed	August 2024

Future Project Timeline



Facility	Phase of Development	Construction Commencing	Move In Date
High School #5	Permitting / Board Approval	October 2024	TBD
Harpool Middle School Track & Field	Planning and Design	December 2024	TBD
Navo Middle School Track & Field	Planning and Design	December 2024	TBD
Strickland Middle School Track & Field	Planning and Design	December 2024	TBD
McMath Middle School Track & Field	Planning and Design	TBD	TBD



DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

Reeves Elementary School

August 2024










Tasks completed previous 90 days:

- Geo wells completed.
- Fire lanes completed.
- Drilling foundation piers/piles completed.
- Grade beams
- Under slab utilities
- Slab on grade
- Began erecting steel

Upcoming Tasks:

- Parking/Paving to be completed
- Foundations/slab to be completed
- Structural steel erection
- Storm shelter to be completed
- Roofing will begin
- Framing & Mechanical, Electrical,
 Plumbing rough in is ongoing



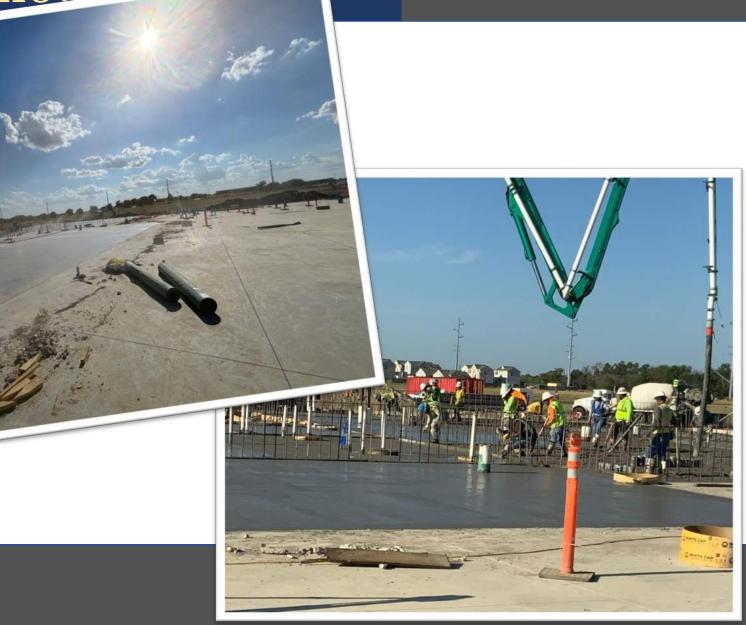







DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

Crownover, Myers & Rodriguez Middle School Turf & Track

August 2024

Prepared by:





2023 Bond Authorization
Architects – Corgan
Contractor – BWC
Completion – August 2024



Myers Middle School



2023 Bond Authorization
Architects – Corgan
Contractor – BWC
Completion – August 2024





DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

Denton High School Multipurpose Facility

August 2024



Tasks completed previous 90 days:


- Completed Site Utilities
- Sod and removed temporary fencing from practice field
- Installed Field drainage systems
- Building Piers installed
- Set and poured grade beams
- Building Installation

2023 Bond Authorization
Architects – VLK Architects
Contractor – BWC
Move In – August 2025

Upcoming tasks:

- Complete Steel Building Erection
- Install Roof Frame, Decking and Wall Panels
- Remaining Grade Beam and Slab on Grade
- Metal Framing and Mechanical, Electrical, Plumbing Rough in.
- Practice Field Drainage and Field Preparation



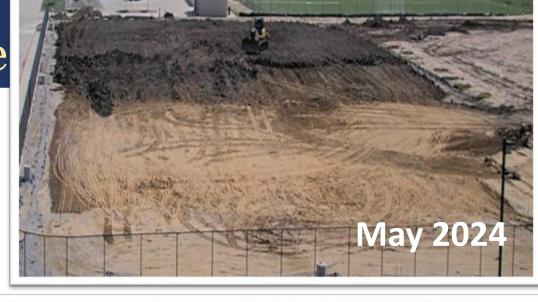

2023 Bond Authorization
Architects – VLK Architects
Contractor – BWC
Move In – August 2025






2023 Bond Authorization **Architects – VLK Architects Contractor – BWC** Move In – August 2025





2023 Bond Authorization
Architects – VLK Architects
Contractor – BWC
Move In – August 2025

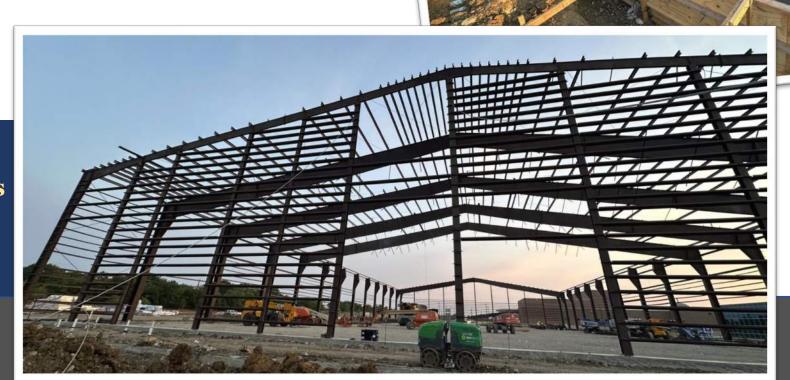

DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

Evers Park Elementary School

August 2024

Prepared by:







2023 Bond Authorization
Architects – Corgan
Contractor – Balfour Beatty
Move In – August 2025

Tasks completed previous 90 days:

- Renovation and remodel of interior and exterior of existing building.
- Vinyl flooring, carpet, tile wainscot, and wood drop in ceilings in hallways, collaboration areas, library, and cafe.
- New tile ceilings throughout the building
- Millwork and cabinetry in all spaces.
- Extensive remodel of library spaces adding a reading nook area and maker spaces
- New windows throughout the building and entry vestibule.
- Ballistic film is applied to glass in all sensitive areas of the building.
- New fire alarm, access controls, security system, lighting controls and panic buttons installed.
- Courtyard renovation with shade canopy, artificial turf, raised beds, and stone seating areas
- New playground with artificial turf fall area.
- Extensive landscaping and irrigation renovation using native grasses and drought tolerant plants.
- Renovation of HVAC system throughout the building.

Prepared by:




2023 Bond Authorization
Architects – Corgan
Contractor – Balfour Beatty
Move In – August 2025

Upcoming Tasks:

- Continue with punch list items
- Installation of glass partition wall between library and maker space
- Install new chillers and air handlers to complete HVAC renovation
- Complete fit and finish of millwork
- Replace temporary doors and hardware





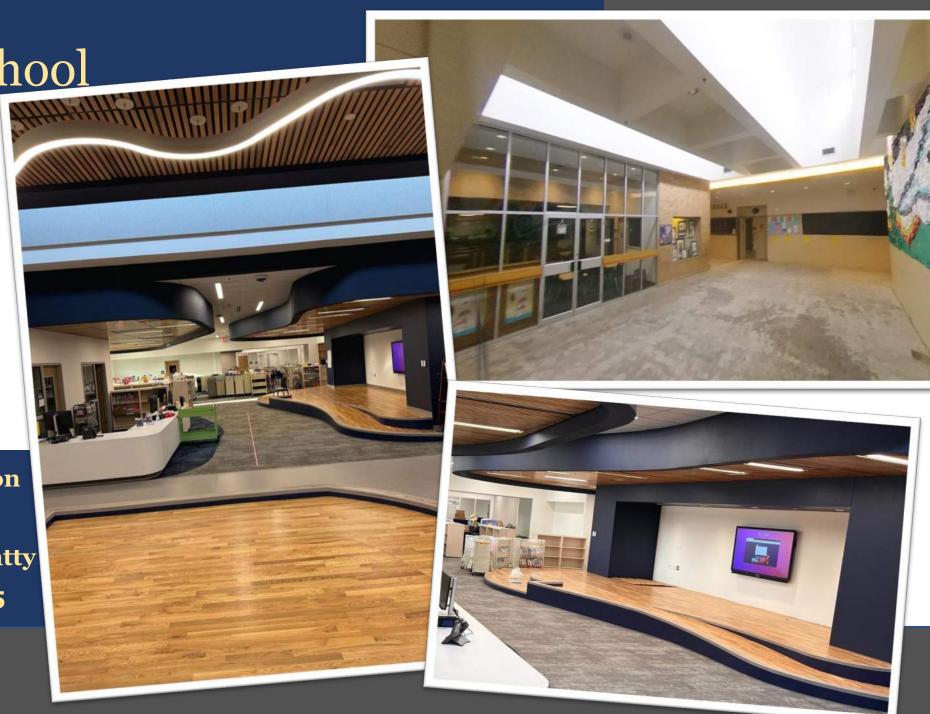









DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth












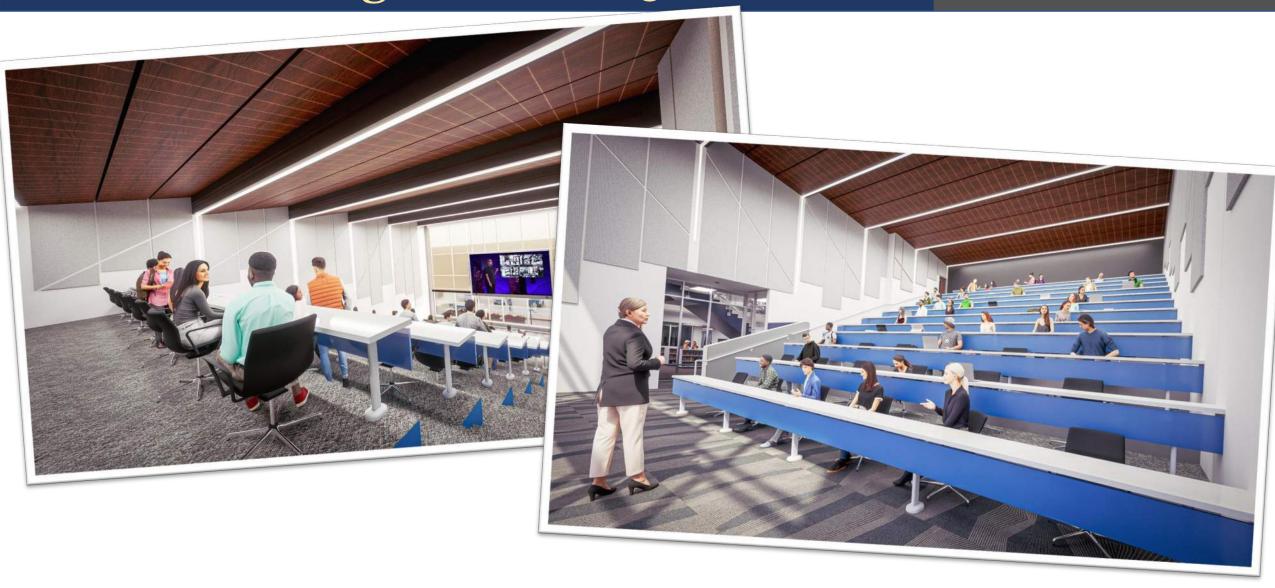















DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

Borman Elementary School

August 2024

Prepared by:















