

Status of Bond Projects  
8/8/17 Governing Board Meeting

President Grant, Board Members, Mr. Jaeger  
Current Project Update:

**I. INNOVATION ACADEMY**

A. New Elementary School:  
Punch list item work is ongoing site-wide



Center Campus



Solar Array and Canopy's

**Innovation Academy Is Complete  
On Time and On Budget**

## II. Keeling Elementary

### A. Design & Renovation

Roof punch work is scheduled for 7/31

Electrostatic wrought iron painting was 50% complete the week of 7/24

Exterior painting and sealing of buildings including door & window frames is scheduled for completion 8/4

IT cabling upgrades are ongoing



Keeling Blue



Roof at Keeling Annex



Keeling Administration Roof

### **III. Amphitheater High**

#### **A. Renovation and Renewal**

Tennis court concrete slabs and enclosures are complete

Fencing around tennis courts began 7/24 and substantial completion is expected by August 18th

200, 300 & 400 classrooms are complete with punch work ongoing in hallways including cove base and floor stencils

HVAC punch work is ongoing

Football Stadium: visitor bleacher dirt work and compaction are complete, bleachers arrived the morning of 7/24, installation scheduled for 3 weeks

Building 700 renovations: floor grinding and polishing is ongoing, ceiling grid and lighting is ongoing, millwork installation was scheduled for the week of 7/24, wrought iron is ongoing

Chiller P.O. (SFB) has been issued, demo was scheduled to begin 7/24

Estimated completion is 8/7/17




Tennis Court Post-tension Work



Building 700 Renovation



Grinding Classroom Concrete Floor

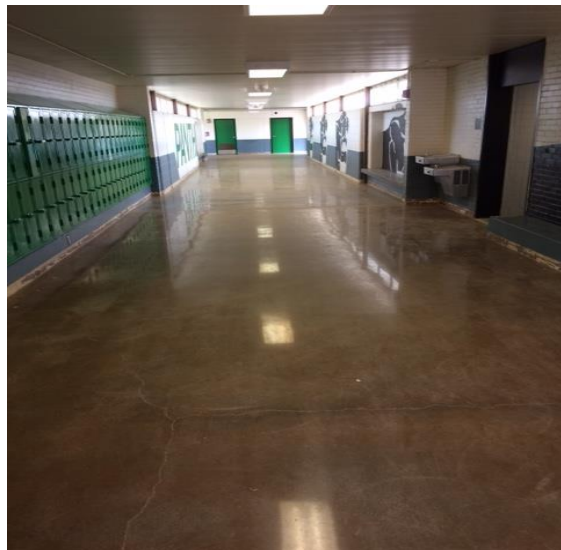

Polished Concrete Floor



## IV. Canyon Del Oro

### A. Renovation and Renewal

D building – HVAC is complete and inspection was scheduled for 7/24, installation of ceiling grid and tiles is complete, locker painting is complete  
LED lighting in halls and classrooms is 98% complete as of 7/24

Punch walk was scheduled for 7/26

E building – Complete


F building – Complete

R building – Complete

G building – Complete

South gym – Complete

North gym – Lighting is ongoing

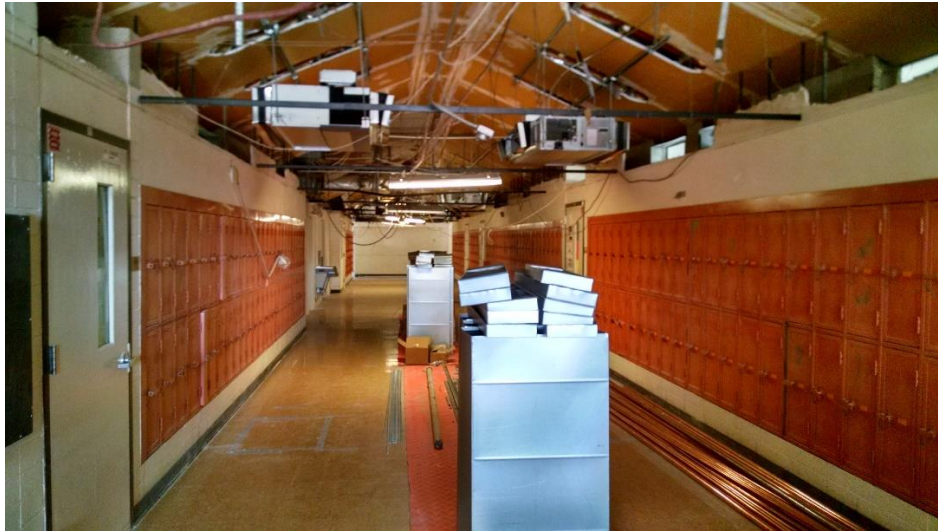

D Building HVAC Work



South Gym Padding and Painting

## **V. Ironwood Ridge**

### **A. Renovation and Renewal**

Lighting upgrade is ongoing

Buildings A, B, C & D are complete (sensors are being programmed)

Building E is ongoing

Buildings F and G to follow

This is night work from 4.00pm until 2:00am

Gym roof and Gym block walls are with the SFB

## **VI. Sand Volleyball**

### **A. Design**

Proposed site locations have been delivered to the Athletic Director

Design will be complete 4 weeks after locations are confirmed

Pre-design walks were completed with Breckenridge Architecture at all three High Schools
