



ISD #726
Becker Public Schools

CS
Weekly Update


Nov 10, 2022

Transportation Building

Week Ending Nov 11th, 2022

- Area Steel structure Set
- Area B Steel Starts
- Site meeting with Sumre and Midco
- Sub Grade prepping for Aprons

Steel erection progress on Area A and starting on B

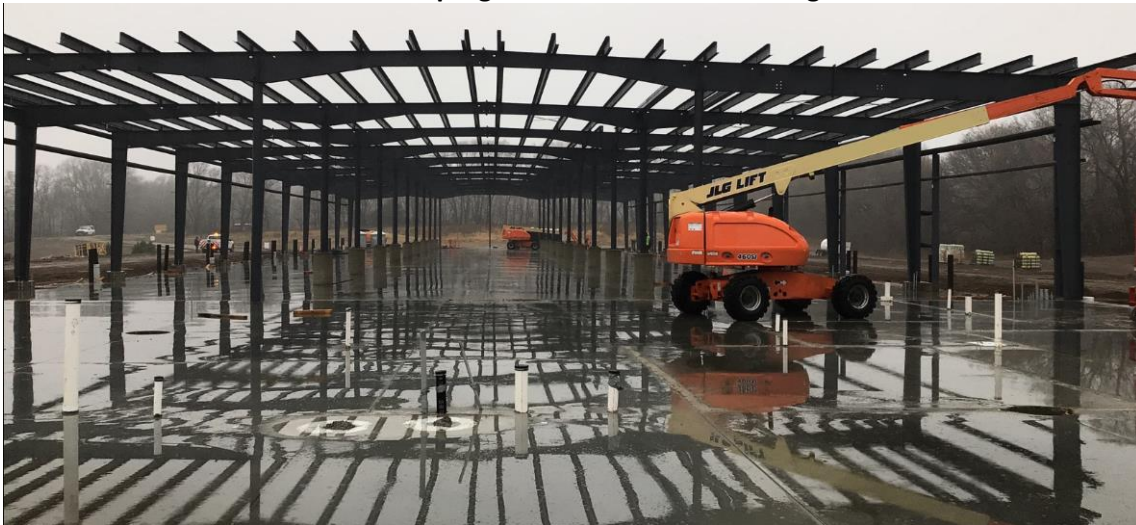

Temporary Power set up and Connexus was out to the site to prepare for Transformer



Week Ending Nov 17th, 2022

- Apron prep work and pours
- Fire Protection Rebid
- Area B steel continues
- Road and parking sitework continues
