

# Argyle Stadium

## September 2025 Update

# Site Photos





# Site Photos





# Site Photos





# Site Photos






# Site Photos





# Site Photos

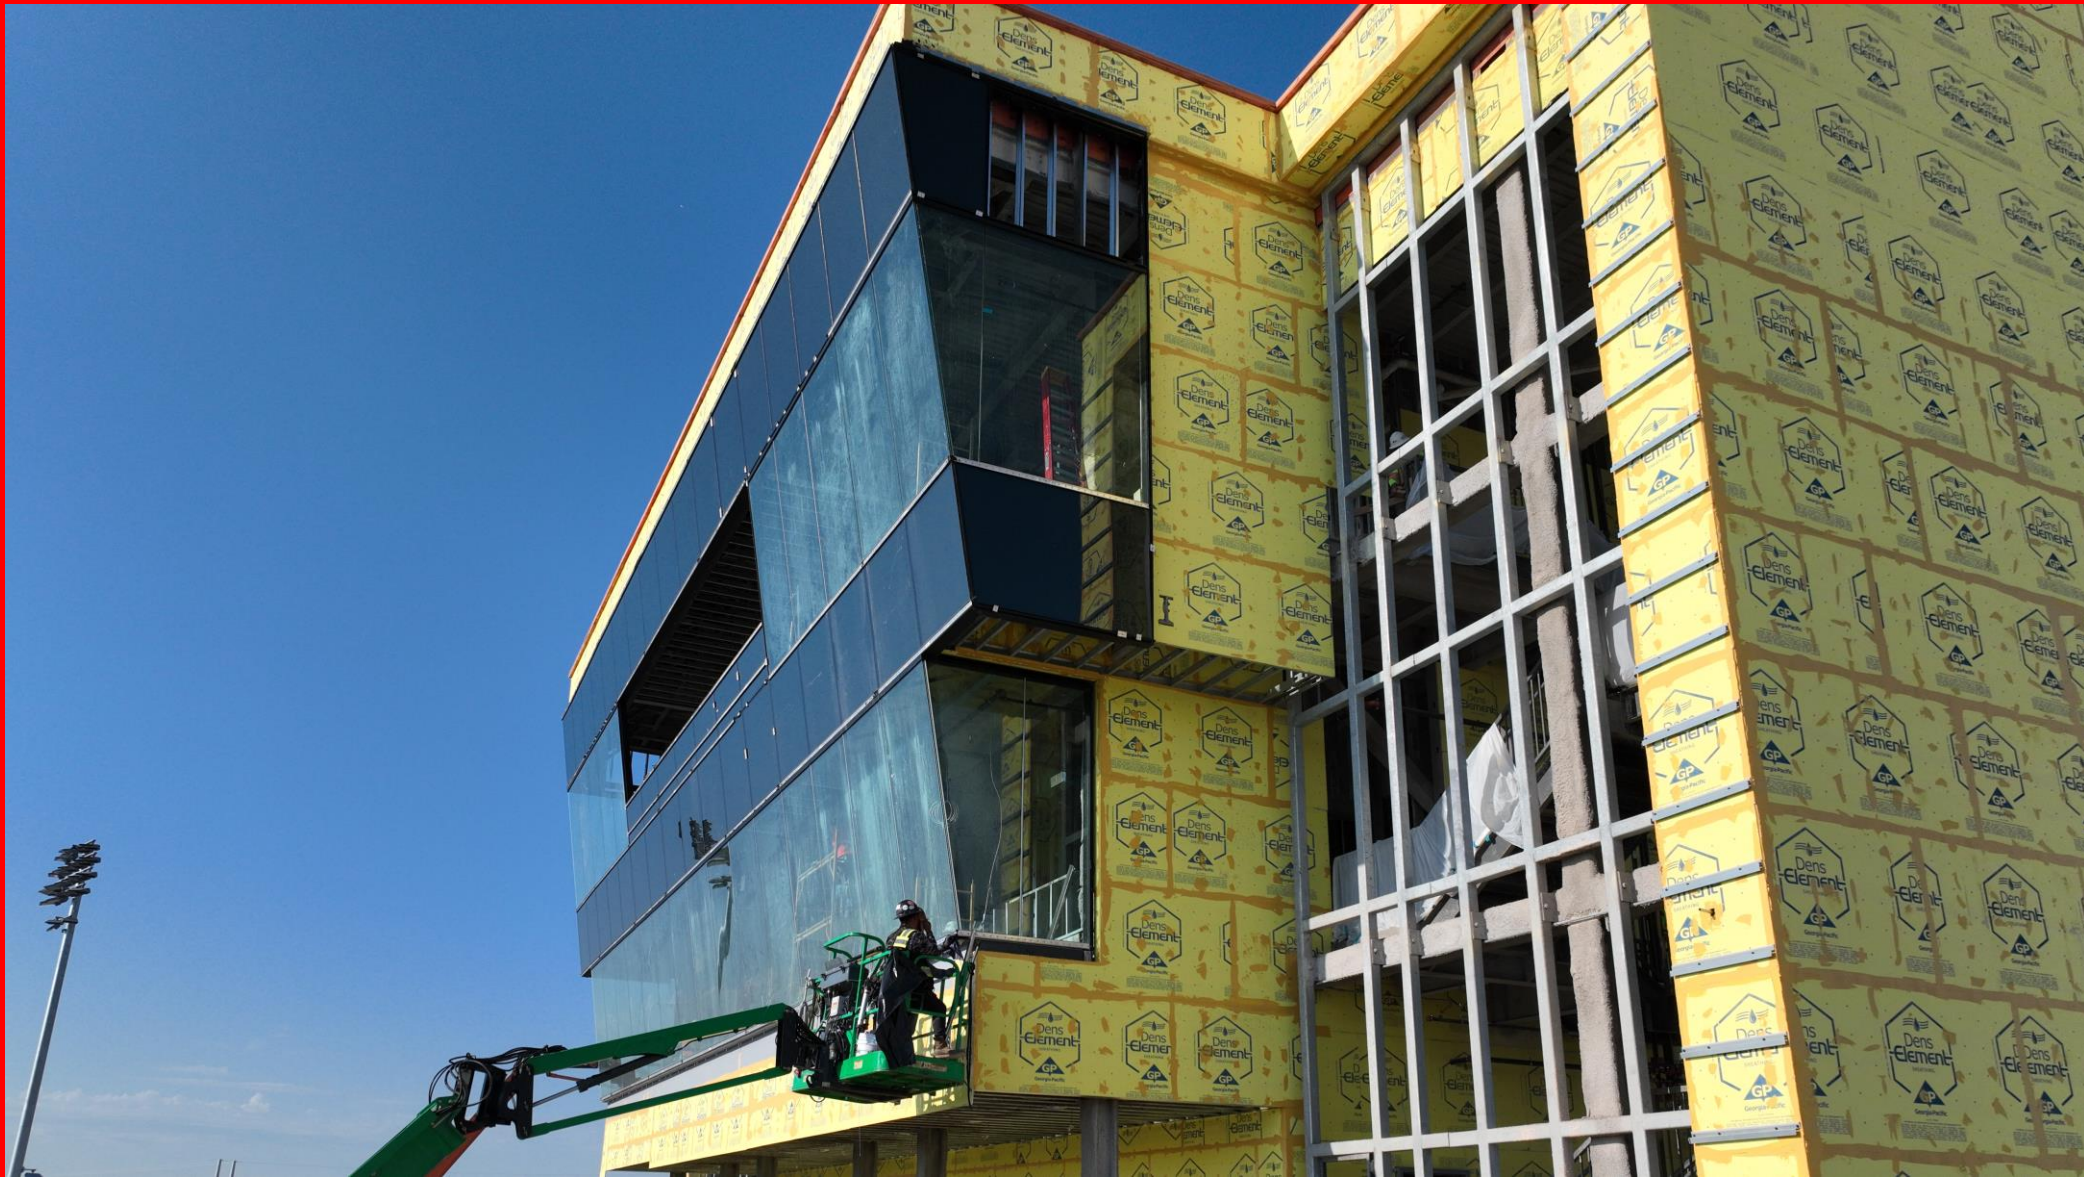



# Site Photos





# Look Ahead

- Install LEDs on Video Board  
Mid-September
- Install of Home Grandstands
- Dry-In Press Box
- Install Metal Panels at  
Press Box





# Key Milestones

## Key Milestone Tracking

Town Permit Field Event Locations	September 5, 2024 January 1, 2025
Press Box Erection Begins IAC Erection Begins	March 2025 Spring 2025
Visitor Grandstand Install Home Grandstand Install	Spring 2025 Summer/Fall 2025
Substantial Completion	November 2025





A large, stylized, dark red letter 'A' logo is centered in the background. It has a thick, blocky design with a slight curve to the right side of the vertical strokes.

# Middle School

# September 2025 Update



# Site Photos





# Site Photos





# Site Photos





# Site Photos





# Site Photos





# Site Photos





# Site Photos





# Look Ahead

- Bleacher Install at Sports Field
- RTU Install Early October
- Permanent Gas Connection
- Permanent Power Connection
- Site Preparations for ES #5





# Key Milestones

## Key Milestone Tracking

Town Permit	December 20, 2024
Grading Completion	November 2024
Structural Steel Completion	September 2025
Substantial Completion	July 2026

