



A Professional Project Management Firm



La Vernia ISD

2023 Bond – Project Status Update

PRESENTED BY: **AG|CM, INC. & BARTLETT COCKE**
July 21, 2025

Bartlett Cocke – Weekly Reports

Week of July 4th –
Primary School




Admin Renovations



Parking Lot Expansion

Bartlett Cocke – Weekly Reports

Week of July 4th –
Intermediate School

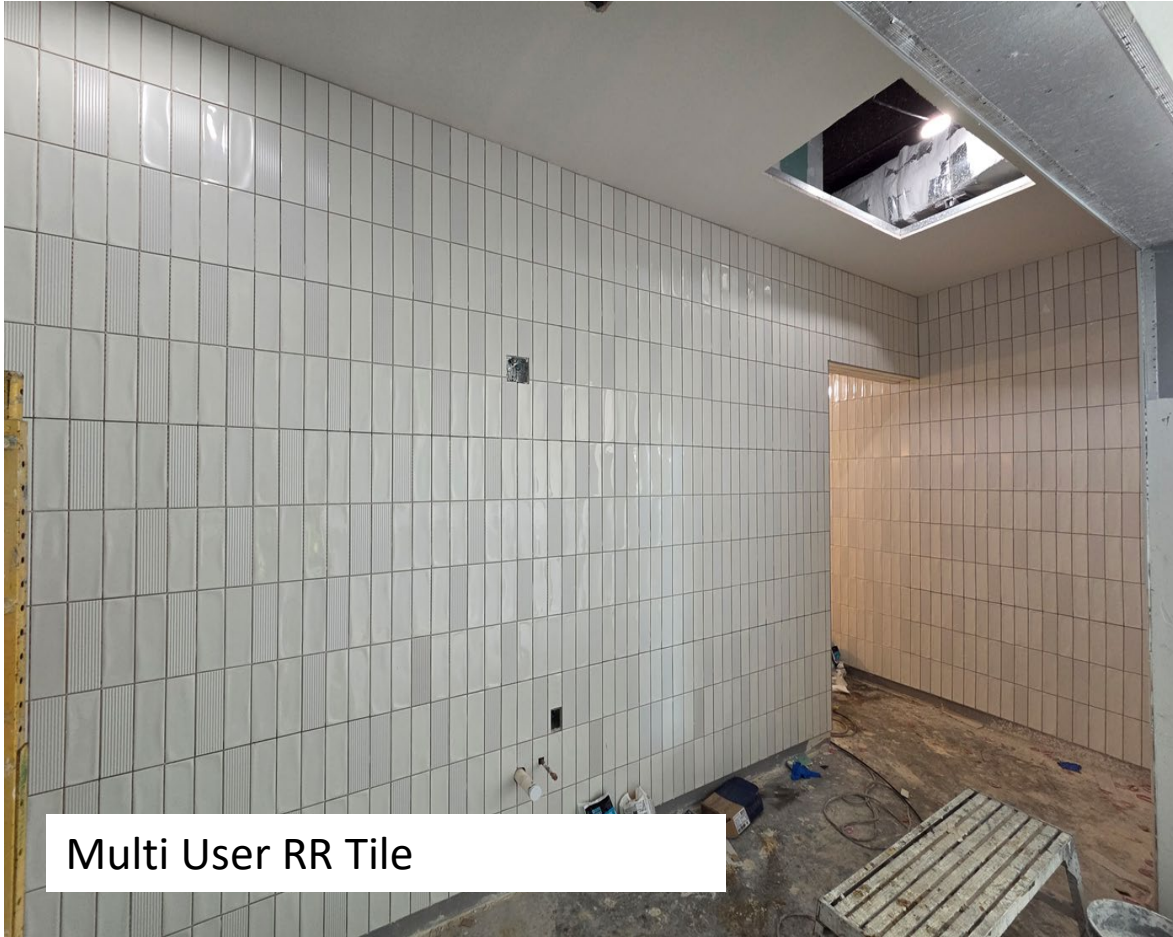

Bartlett Cocke – Weekly Reports

Week of July 4th –
Junior High School




Cafeteria Tie-In Brick
Removal



Demo and Haul off

Bartlett Cocke – Weekly Reports

Week of July 11th
Primary School

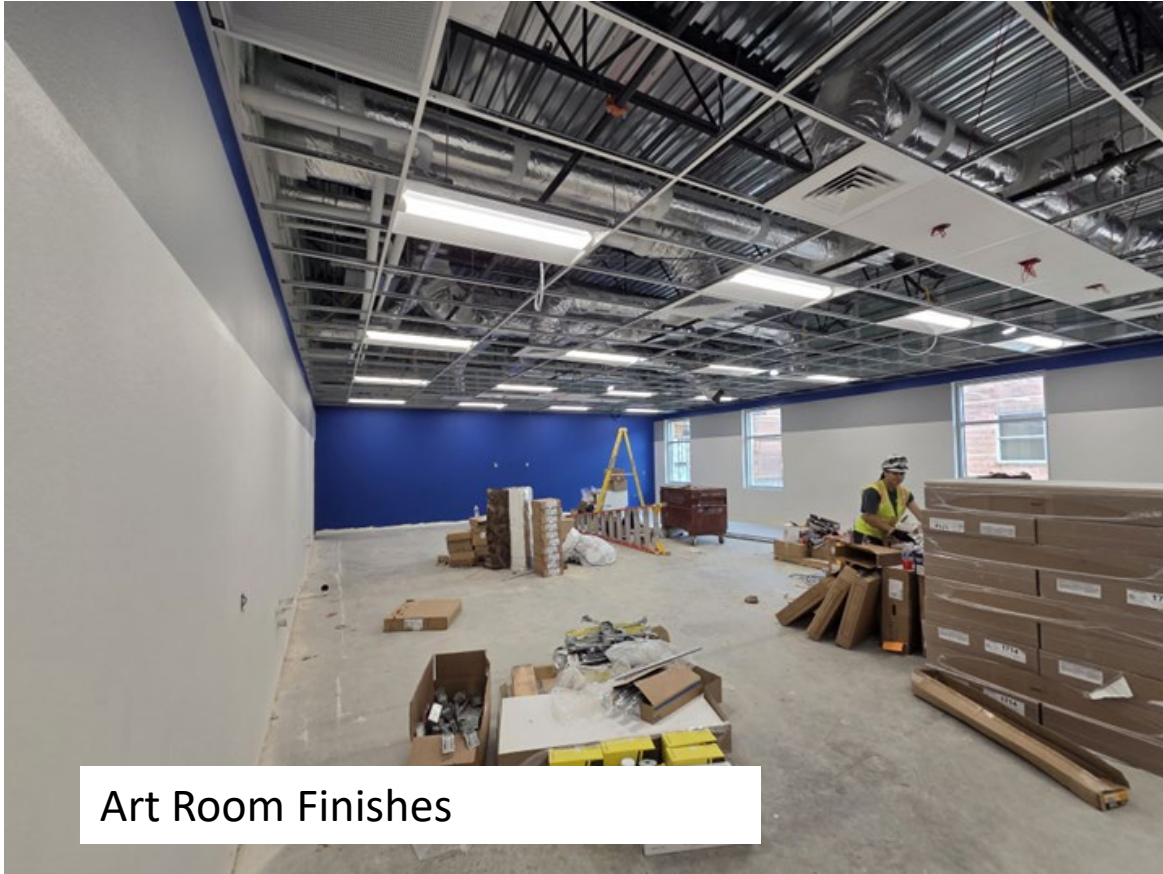

Art Room Finishes




Utilities at Courtyard and Playground

Bartlett Cocke – Weekly Reports

Week of July 11th
Intermediate School



Demo of Gym Addition Wall

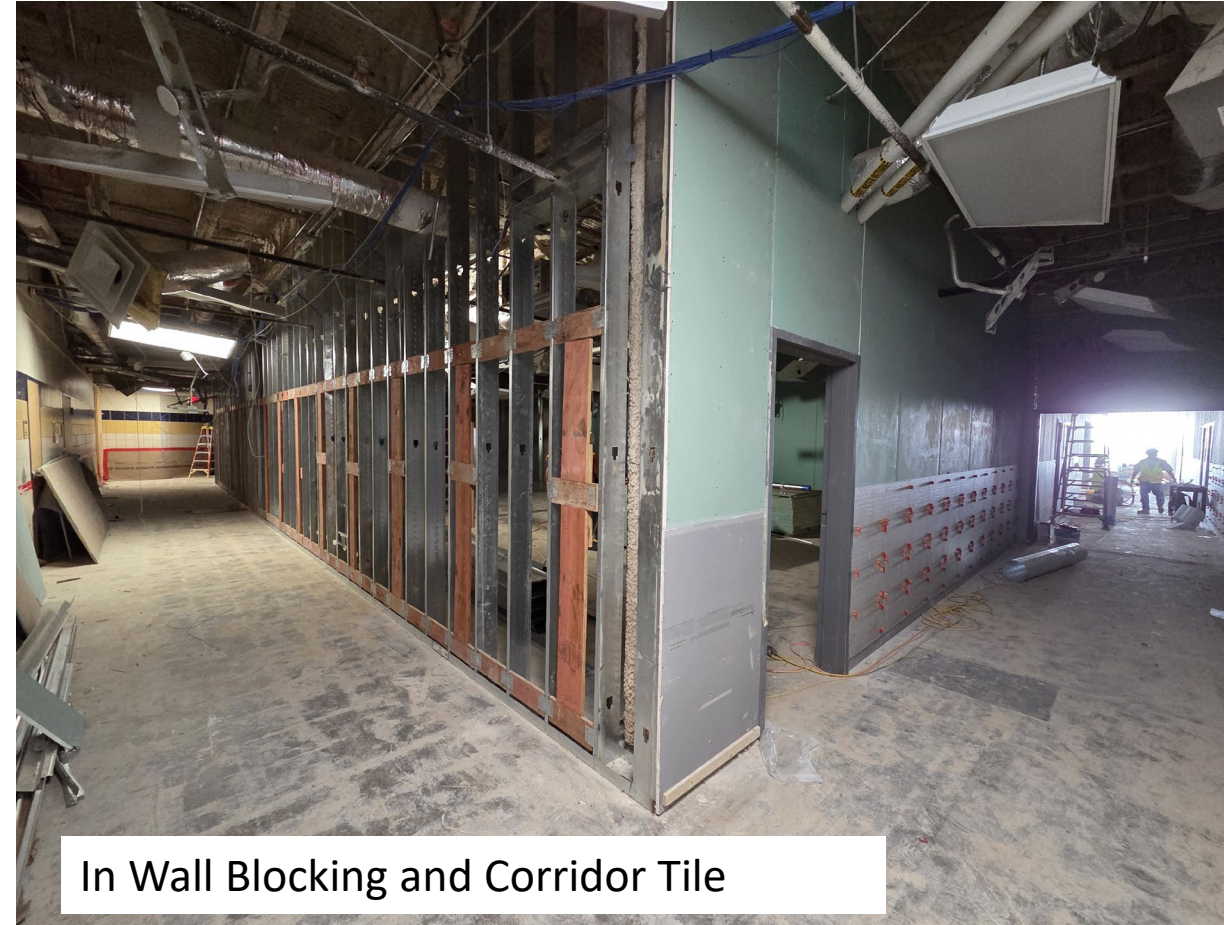

In Wall Blocking and Corridor Tile

Bartlett Cocke – Weekly Reports

Week of July 11th
Primary and Intermediate



Primary – Library Addition



Intermediate – Roof Top Units

Bartlett Cocke – Weekly Reports

Critical Path Activities

- Continue with Finishes at Primary
- Switch over to Permanent Power at Primary
- Electrical Services at Intermediate
- Restart of Utilities and Foundation Pad at HS
- Utilities at JR HS
- Rerouting of Services GVEC/FELPS/TX Gas



Project Highlight – Intermediate School Chiller

New Two Pipe Chiller has been
Installed 6/30/2025

**Originally scheduled to be
replaced Summer 2026

