

Bond Construction Update

Lee Raspberry
Director of Construction & Planning
January 28, 2025



2021 Bond Projects

Bastrop & Cedar Creek Middle School Weight Rooms

- New MS Weight Rooms - approx. 2,100 SF
- Storefront glass due March 2025
- **99% Complete**








2023 Projects

Adelton Elementary

- Schedule: June 2024 – June 2025
- New 105,000 SF Schools
- ES#10 in Design Phase
- On Schedule

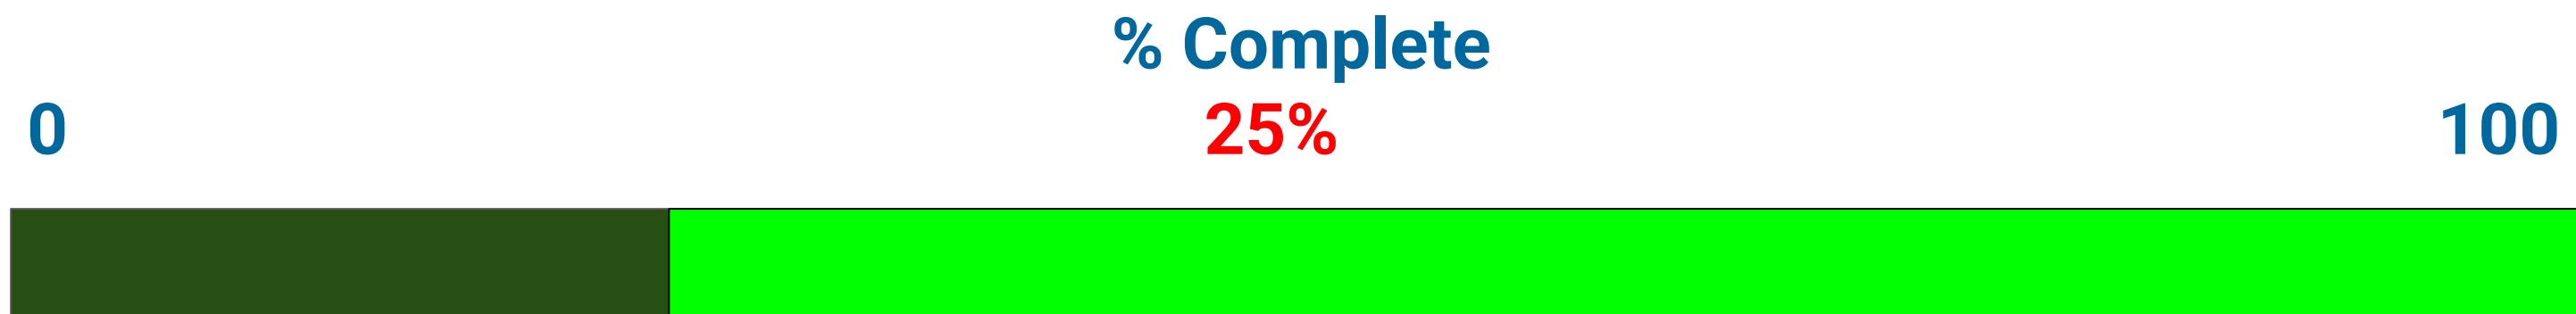



Bastrop Independent School District | January 28,

2025






Bastrop Independent School District | January 28,

2025





**Bastrop Independent School District | January 28,
2025**

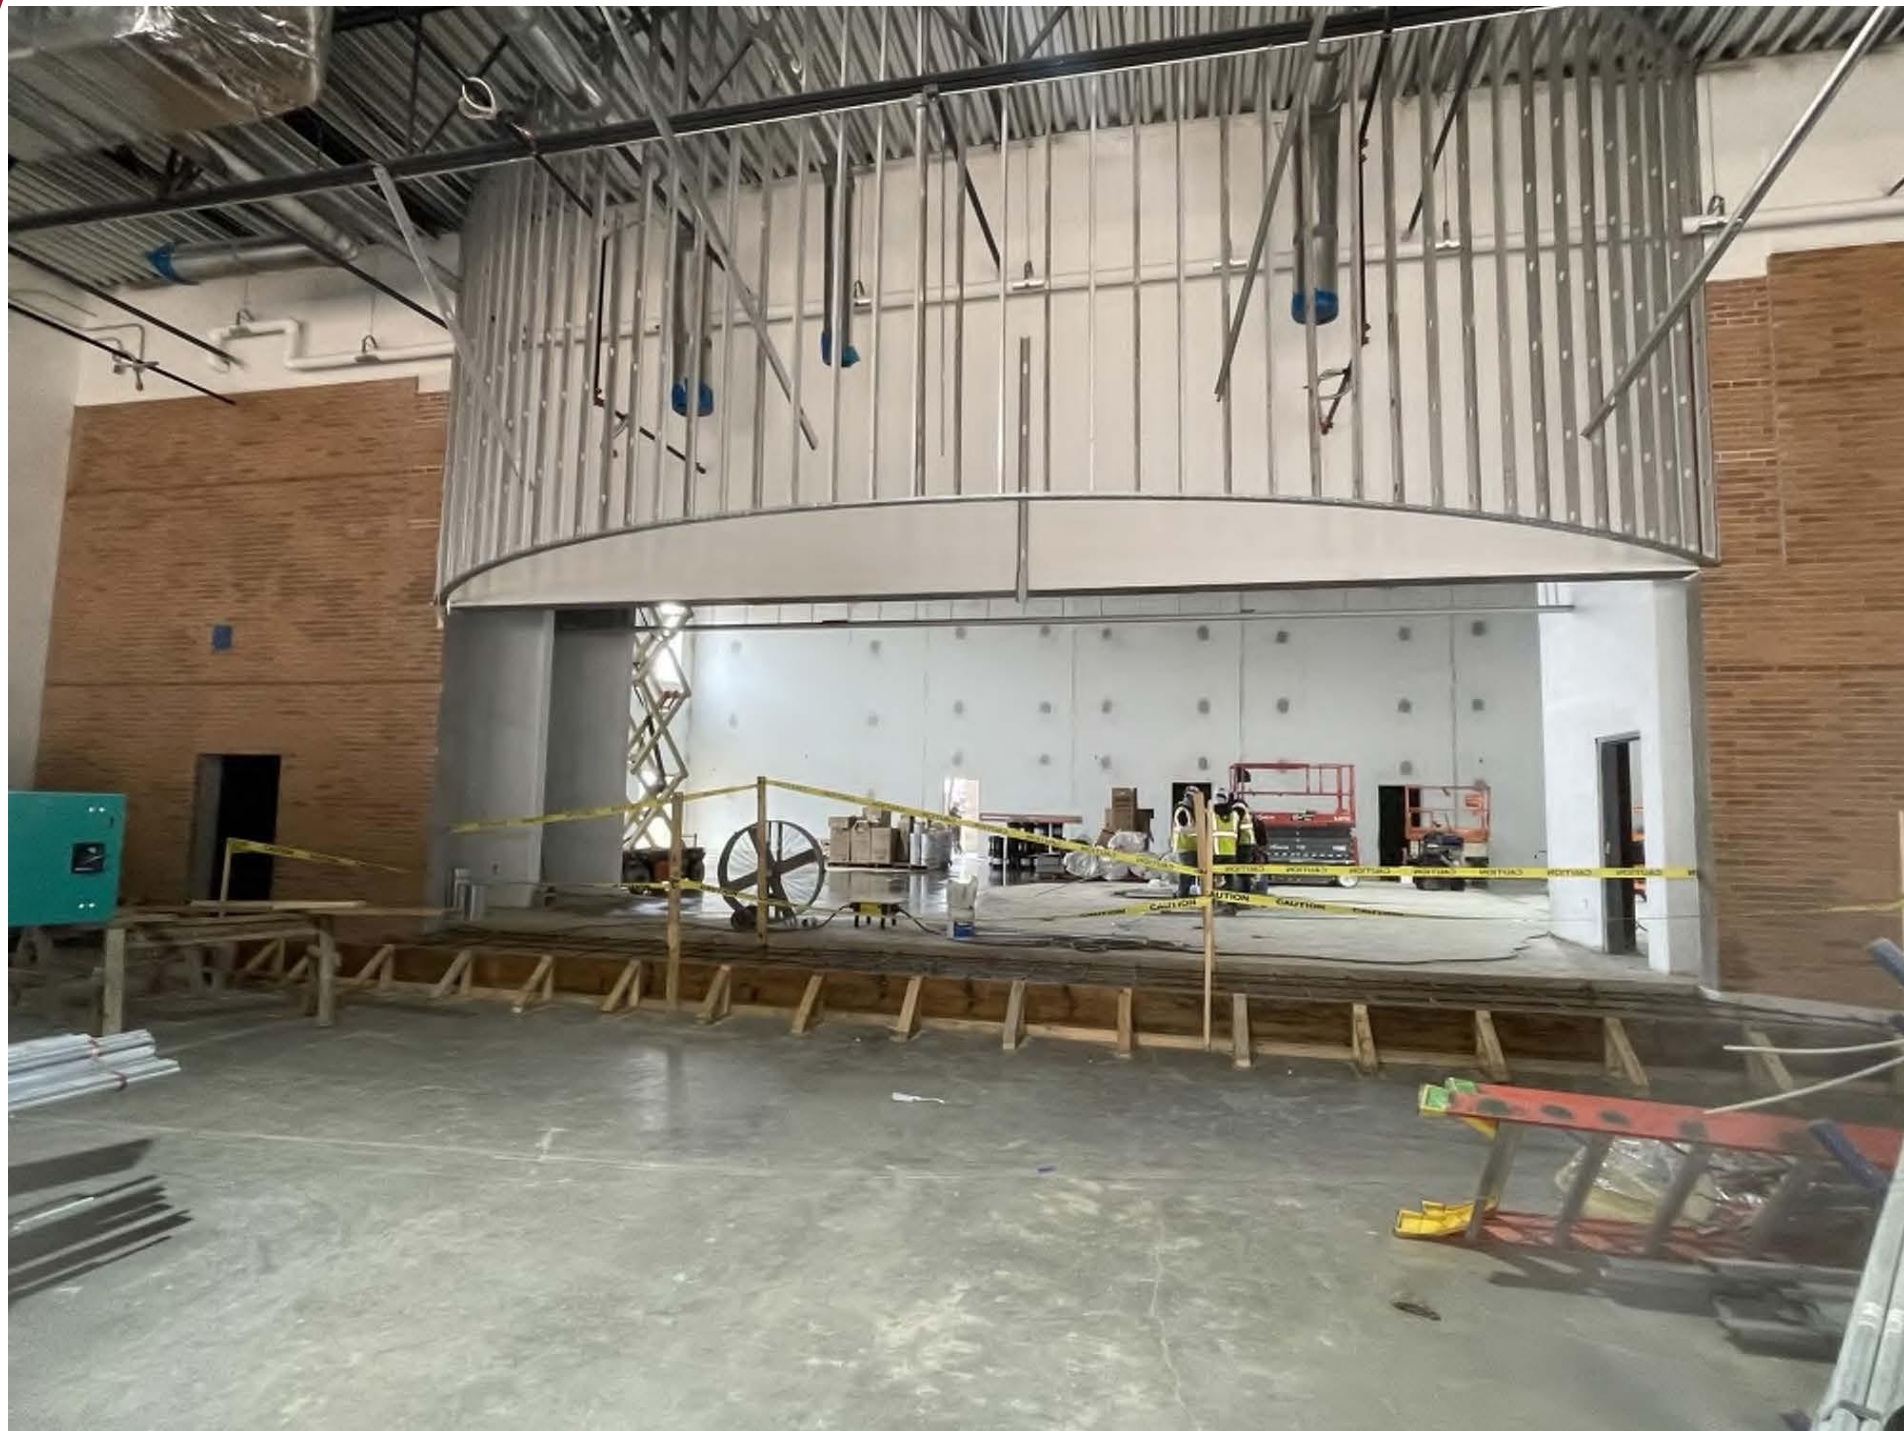

**Bastrop Independent School District | January 28,
2025**

ES #10 (Silverleaf Development)

- New 105,000 SF School currently in design phase





Bastrop High School

- New classroom wing & continued renovations
- Schedule: Feb. 2025 - Dec. 2026
- Approximately 30,000 SF classroom addition
- Currently in Design Development phase
- On Schedule







Bastrop Independent School District | January 28,


2025





New Police and Operations Facility

- Schedule: Jan. 2025 – Feb. 2026
- Approximately 55,000 SF Multi-Use Facility
- Permitting Complete - Construction to begin January 2025.

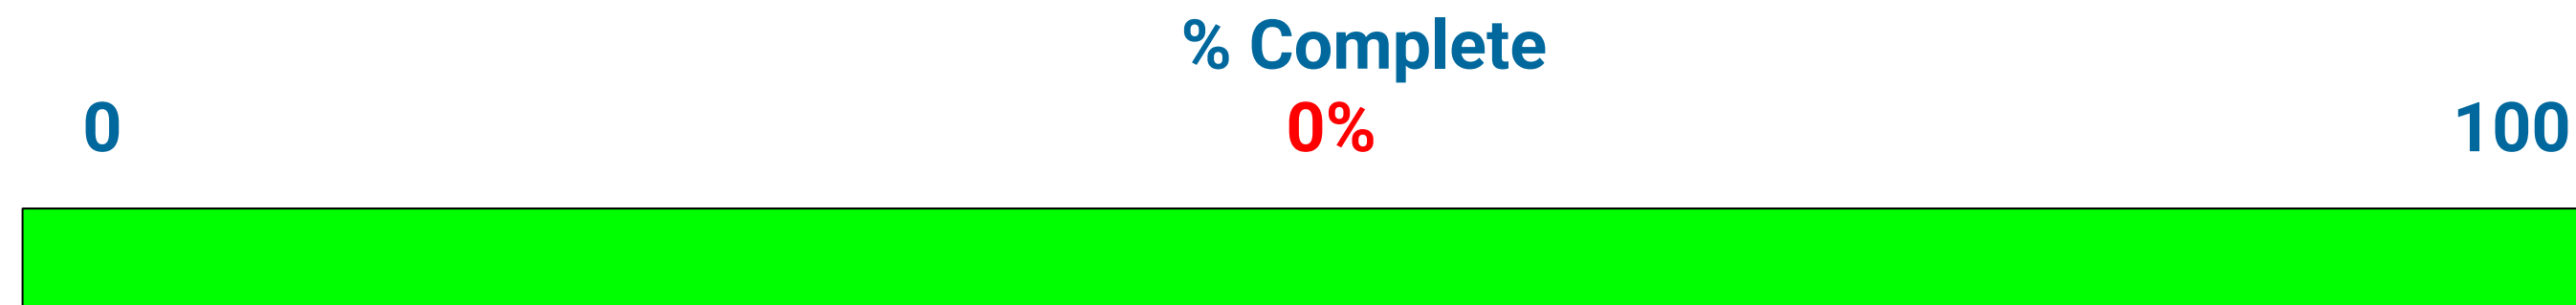

POLICE AND OPERATIONS CENTER
MAIN ENTRY PERSPECTIVE



Mina Elementary Rebuild

- Schedule: Feb. 2025 – Mar. 2026
- Approximately 35,500 SF Facility
- Demo/Make Safe to begin Dec. 2025
- **On Schedule**



% Complete
2%




0

100




Bastrop & Cedar Creek MS Additions

- Schedule: Dec. 2024 – Dec. 2025
- Approximately 21,000 SF additions
- Make Safe & Utility Relocate Underway
- BMS Library & Cafe flooring complete
- **On Schedule**

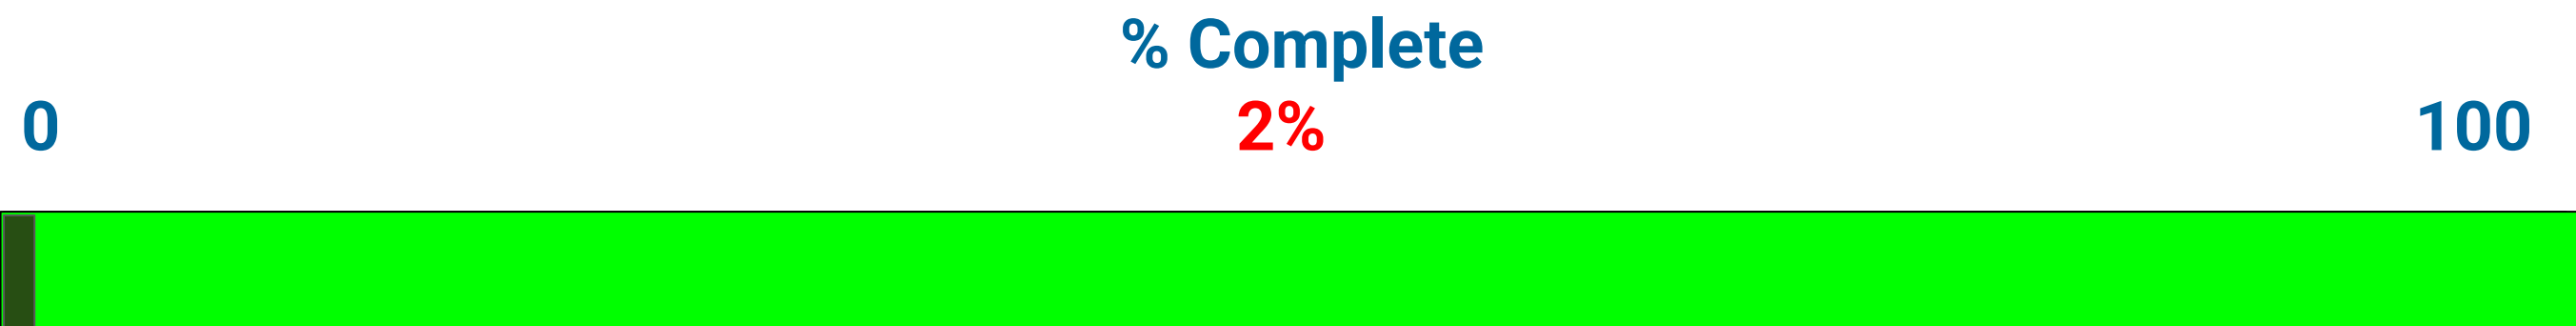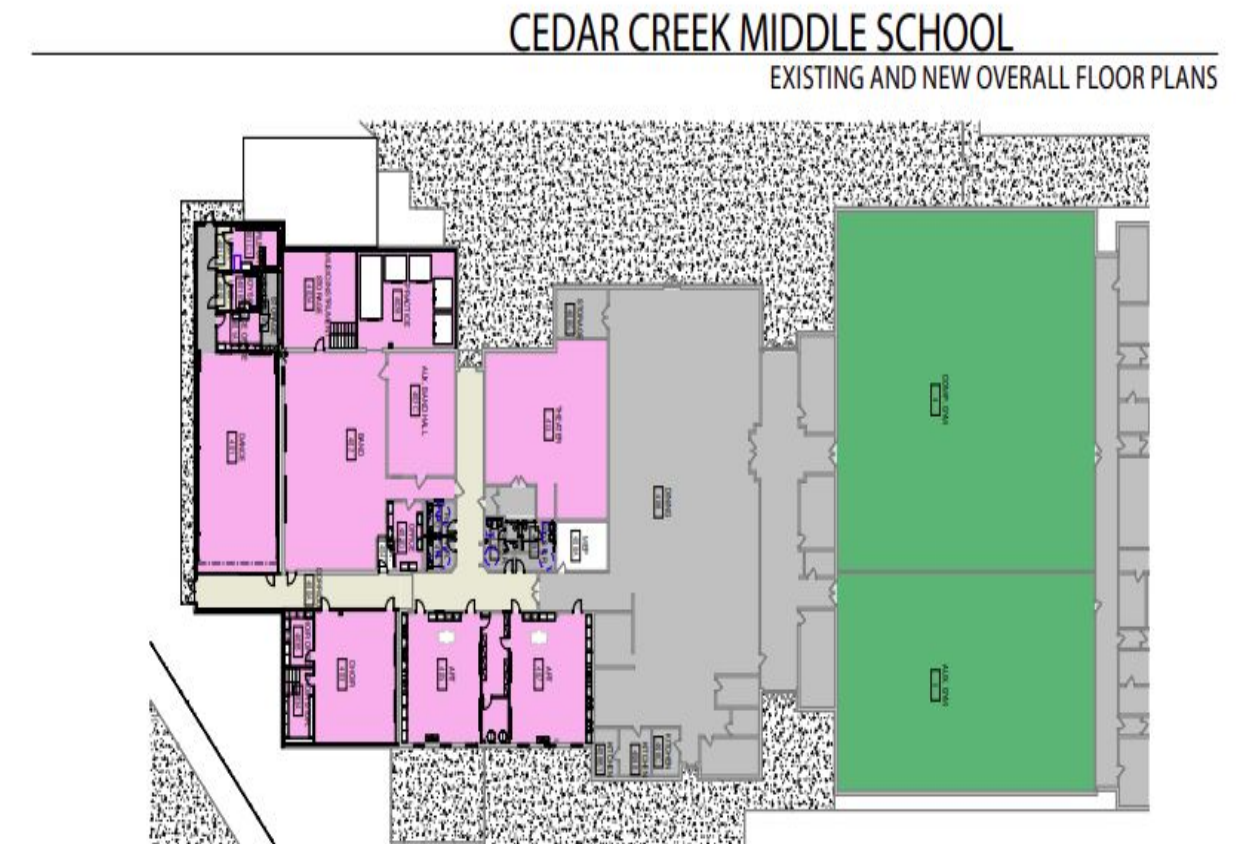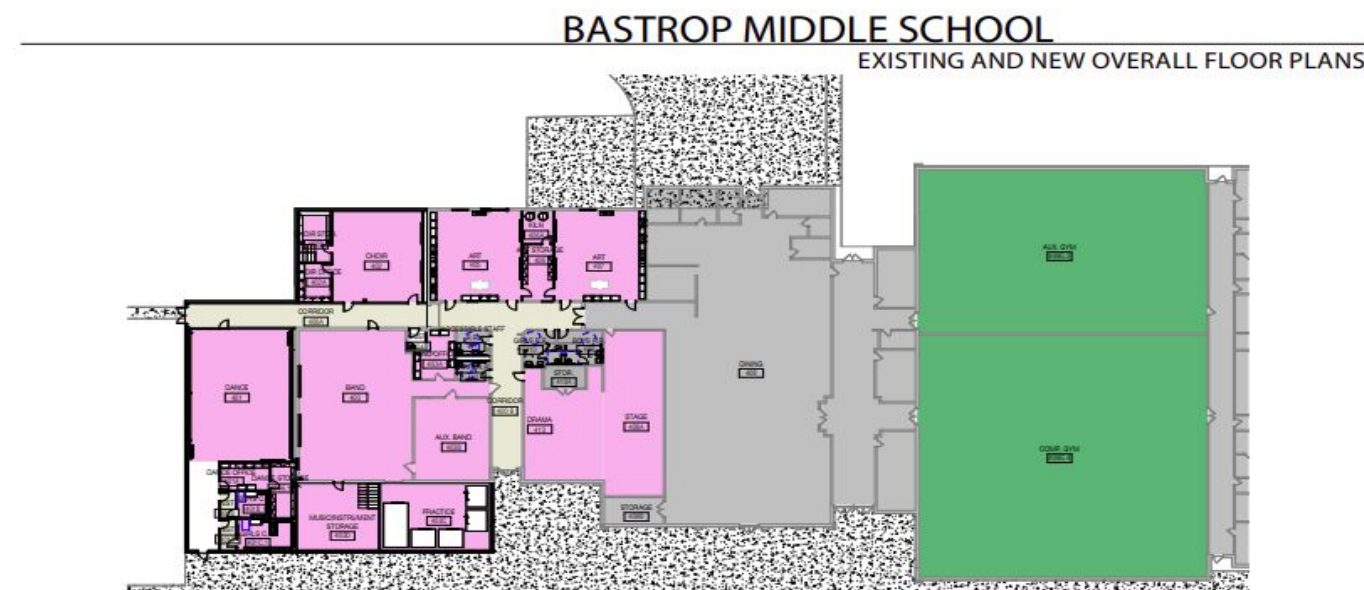

Riverside MS Renovations

- Schedule: Oct. 2024 – Dec. 2025
- Approximately 60,000 SF addition
- 1st phase of interior renovation complete
- Gym & Fine Arts additions underway
- On Schedule

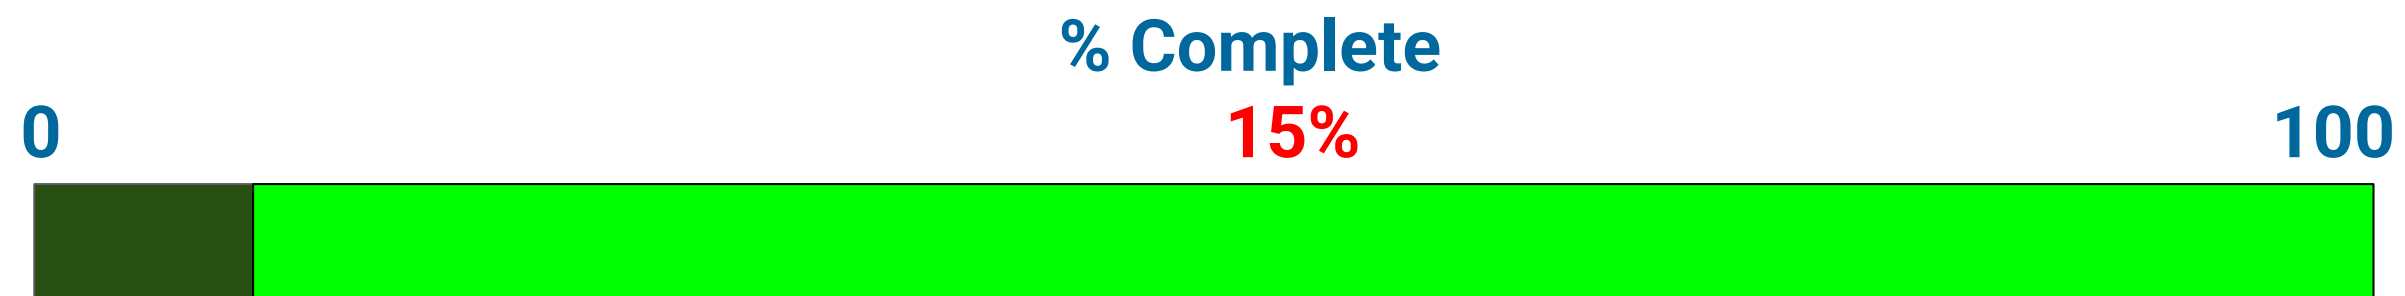




Bastrop Independent School District | January 28,

2025




Creekside MS Renovations

- Schedule: Oct. 2024 – Dec. 2025
- Approximately 60,000 SF addition
- 1st phase of interior renovation complete
- Gym & Fine Arts additions underway
- On Schedule

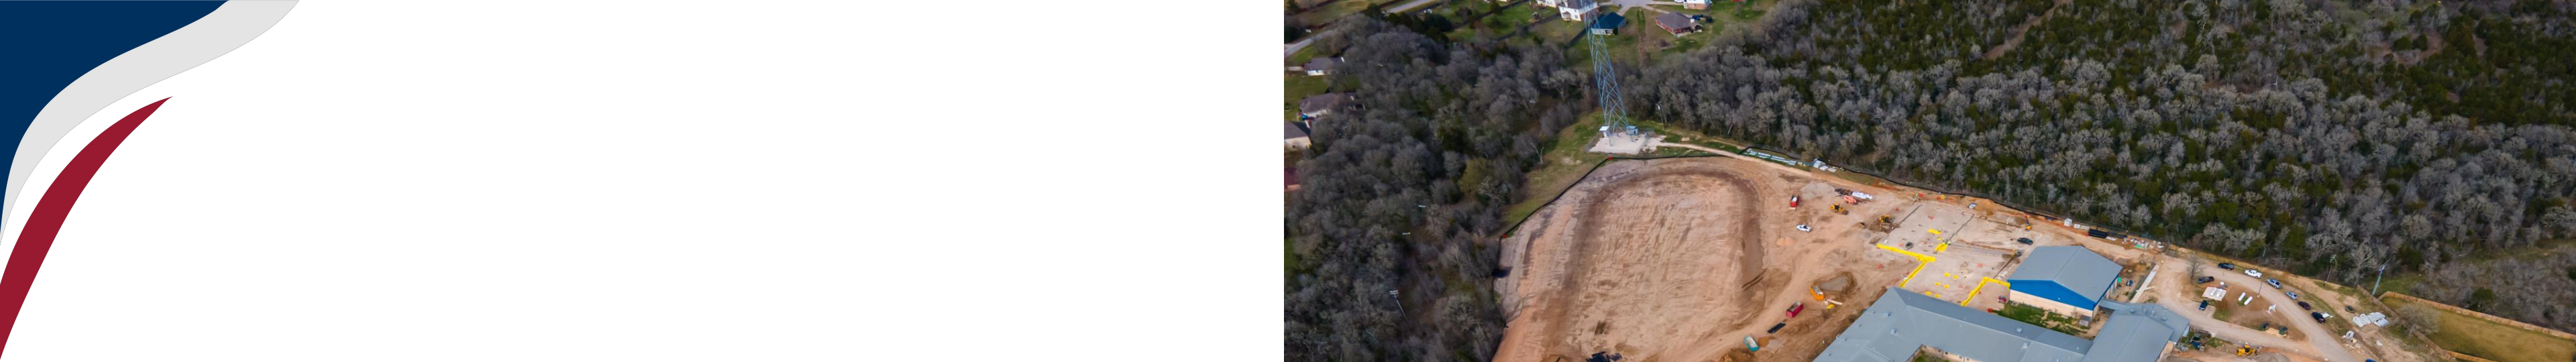

Cedar Creek HS Classroom Addition

- Schedule: Sept. 2024 – Nov. 2025
- Approximately 30,500 SF addition
- Building pad & piers underway
- Utility package complete
- On Schedule

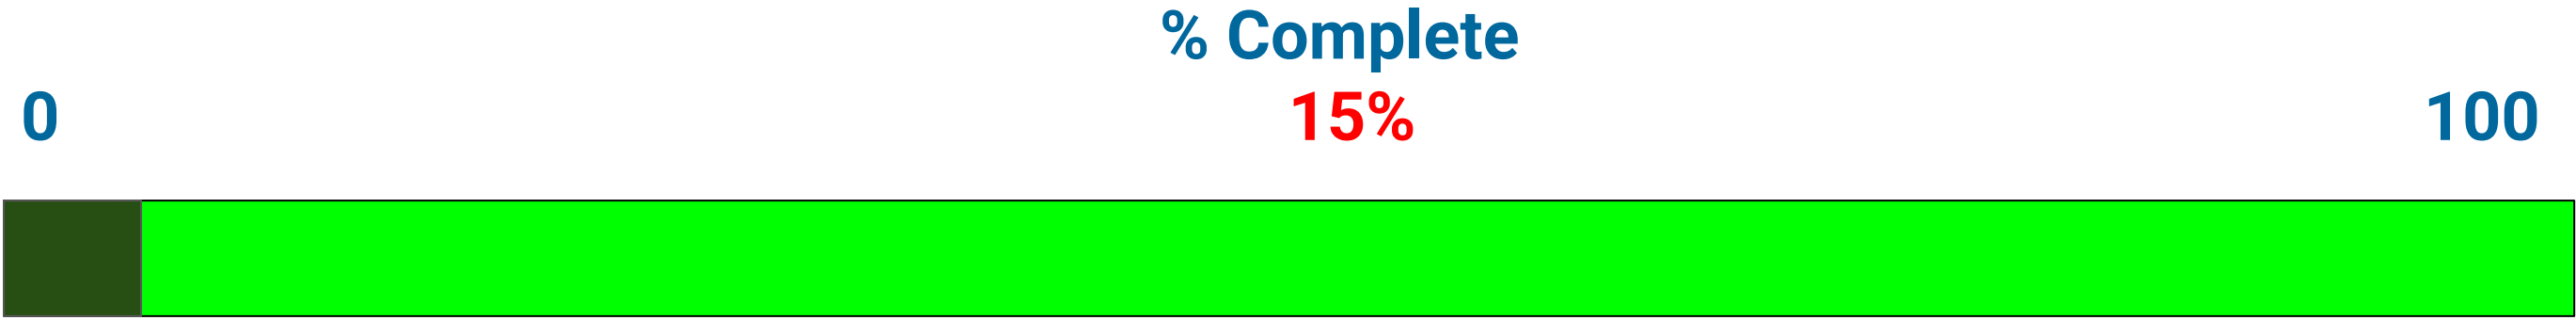



THANK YOU!

Are there any questions?

