

DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

Construction Report

August 2022

Prepared by: Brandon Boyter Executive Director of Construction, Planning & Growth



DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

Denton High School

August 2022

Prepared by: Brandon Boyter Executive Director of Construction, Planning & Growth



Project – 01 2018 Bond Authorization Architects – VLK Architects Contractor – Northstar Builders



DENTON HIGH SCHOOL MAIN ENTRY 6-22-22



Project – 01 2018 Bond Authorization Architects – VLK Architects Contractor – Northstar Builders



DENTON HIGH SCHOOL MAIN ENTRY 8-1-22



Project – 01 2018 Bond Authorization Architects – VLK Architects Contractor – Northstar Builders

Tasks completed previous 90 days:

- Bronco Way & Sidewalks Installed
- 95% Landscaping & Irrigation Installed
- District WAN installed
- Classroom Furniture, Office Furniture installed
- Technology systems have been installed
- System trainings are ongoing
- First Responder Radio Repeater System Installed
- HVAC Commissioning is ongoing



Project – 01 2018 Bond Authorization Architects – VLK Architects Contractor – Northstar Builders



DENTON HIGH SCHOOL REAR AERIAL



Project – 01 2018 Bond Authorization Architects – VLK Architects Contractor – Northstar Builders



DENTON HIGH TENNIS COURTS & BB, SB FIELDS



Project – 01 2018 Bond Authorization Architects – VLK Architects Contractor – Northstar Builders



DENTON HIGH FOOTBALL FIELD & TRACK AERIAL



Project – 01 2018 Bond Authorization Architects – VLK Architects Contractor – Northstar Builders





Project – 01 2018 Bond Authorization Architects – VLK Architects Contractor – Northstar Builders





Project – 01 2018 Bond Authorization Architects – VLK Architects Contractor – Northstar Builders






Project – 01 2018 Bond Authorization Architects – VLK Architects Contractor – Northstar Builders





Project – 01 2018 Bond Authorization Architects – VLK Architects Contractor – Northstar Builders

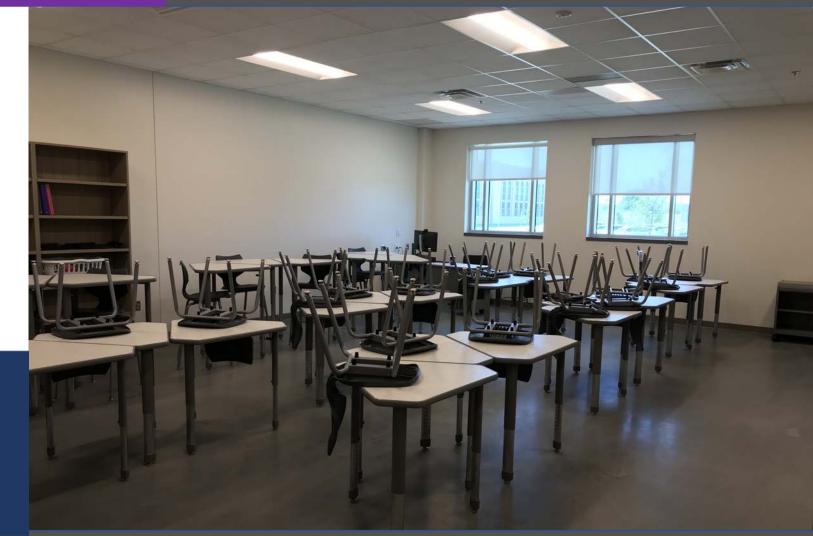



Project – 01 2018 Bond Authorization Architects – VLK Architects Contractor – Northstar Builders





Project – 01 2018 Bond Authorization Architects – VLK Architects Contractor – Northstar Builders



CLICK TO IMAGE TO OPEN VIDEO



Project – 01 2018 Bond Authorization Architects – VLK Architects Contractor – Northstar Builders

FIRST DAY OF **SCHOOL FOR STUDENTS** AUGUST 11,2022



DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

Transportation East Facility

August 2022

Prepared by: Brandon Boyter Executive Director of Construction, Planning & Growth

Center East



Project – 02 2018 Bond Authorization Architects – Corgan Contractor – Steele & Freeman Inc. Move In – Fall 2022



ADMINISTRATIVE OFFICES AND MECHANIC SHOP

Center East



Project – 02 2018 Bond Authorization Architects – Corgan Contractor – Steele & Freeman Inc. Move In – Fall 2022



MECHANIC SHOP AND ADMINISTRATIVE OFFICES

Center East



Project – 02 2018 Bond Authorization Architects – Corgan Contractor – Steele & Freeman Inc. Move In – Fall 2022



AUTOMATIC BUS WASH



Project – 02 2018 Bond Authorization Architects – Corgan Contractor – Steele & Freeman Inc. Move In – Fall 2022



STEEL FRAMING OF THE MECHANIC SHOP



Project – 02 2018 Bond Authorization Architects – Corgan Contractor – Steele & Freeman Inc. Move In – Fall 2022

Tasks completed previous 90 days:

- Administrative Area building envelope has been installed.
- Interior Framing of Administrative Area is Complete.
- Completed Plumbing & Electrical Rough in, Administrative Building
- Preparing for installation of Retaining Walls
- Metal Building for the Mechanic Shop Has been Erected



Project – 02 2018 Bond Authorization Architects – Corgan Contractor – Steele & Freeman Inc. Move In – January 2023



CLICK IMAGE TO OPEN VIDEO



Project – 02

2018 Bond Authorization

Architects – Corgan

Contractor – Steele & Freeman Inc.

Move In – Fall 2022

Upcoming tasks:

- Installing Building Envelope on Mechanic Shop & Bus Wash
- Electrical, Plumbing & HVAC Completion on Administrative Building
- Retaining Walls
- MEP Rough in on both Mechanic Shop and Bus Wash
- Light Pole Install
- Fence Install



DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

PAT CHEEK MIDDLE SCHOOL CAMPUS

August 2022

Prepared by: Brandon Boyter Executive Director of Construction, Planning & Growth



Project – 24 2018 Bond Authorization Architects – Corgan Architects Contractor – Northstar Builders Move In – Summer 2023



PREVIOUS AERIAL OF PAT CHEEK MIDDLE SCHOOL



Project – 24 2018 Bond Authorization Architects – Corgan Architects Contractor – Northstar Builders Move In – Summer 2023



8-1-22 AERIAL OF PAT CHEEK MIDDLE SCHOOL



Project – 24 2018 Bond Authorization Architects – Corgan Architects Contractor – Northstar Builders

Move In – Summer 2023



PAT CHEEK MIDDLE SCHOOL MAIN ENTRY



Project – 24

2018 Bond Authorization Architects – Corgan Architects Contractor – Northstar Builders Move In – Summer 2023

Tasks completed previous 90 days:

- ICF areas E, C and D
- Structural Steel Erection Areas E, F, C & D
- Second Floor Concrete Placement Area A
- Metal Stud Framing Area A & F
- MEP Overhead Rough-In Area A & F
- Exterior Masonry area A
- Exterior Windows area A
- Roofing areas B and A

Project – 24 2018 Bond Authorization Architects – Corgan Architects Contractor – Northstar Builders Move In – Summer 2023



CLICK PICTURE TO OPEN VIDEO



Project – 24

2018 Bond Authorization Architects – Corgan Architects Contractor – Northstar Builders Move In – Summer 2023

Upcoming and Ongoing Tasks:

- Roof Drains are Being Installed
- Interior Framing is Ongoing Throughout the Building
- Tile is Being Installed in First Floor Bathrooms
- Electrical Rough In Is Being Installed
- Geothermal Wells are Being Plumbed Into the Building
- Interior Geothermal Piping is Being Flushed
- Fire Sprinkler Lines are being Installed
- Building Envelope Water Proofing is Being Installed
- Brick Veneer is Being Installed on Exterior
- Site Lighting along Denton Way is Being Installed



DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

Braswell High School

August 2022

Prepared by: Brandon Boyter Executive Director of Construction, Planning & Growth
























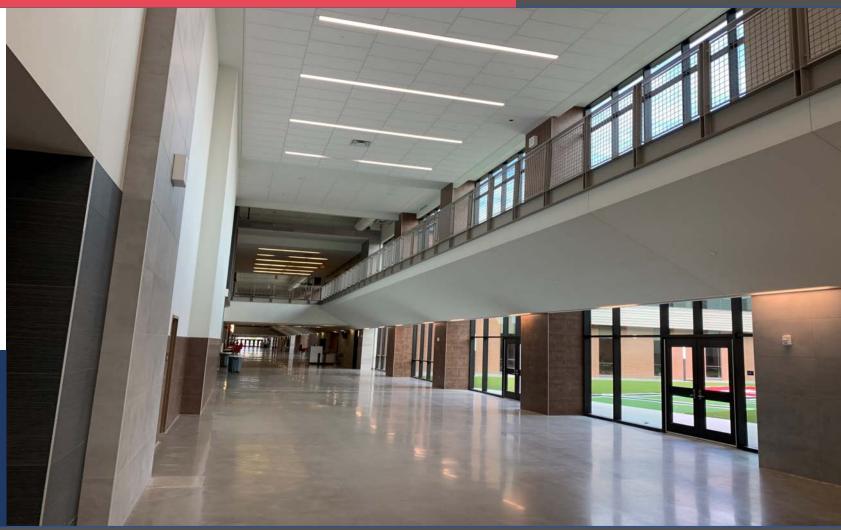



Classroom Addition Ongoing Work:

• Complete landscaping, Complete Interior Vinyl Wall Graphics, Cafeteria Fabric Wall Baffles.



2018 Bond Authorization

Architects – VLK Architects

Contractor – Balfour Beatty Construction



CLICK PICTURE TO OPEN VIDEO



DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS


Construction, Planning & Growth

Carrico Stadium

August 2022

Prepared by: Brandon Boyter Executive Director of Construction, Planning & Growth



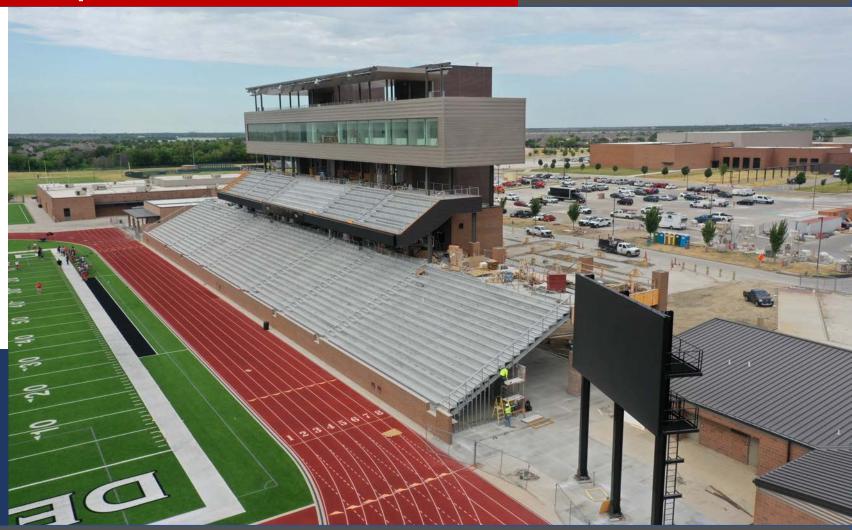




2018 Bond Authorization Architects – VLK Architects Contractor – Balfour Beatty Construction

Tasks completed previous 90 days:

- <u>Stadium</u> Visitor Entrance Flatwork Pavement, Home Side Roofs, Remaining Curtain Wall, Interior Finishes, Mill-Work, Doors, Frames & Hardware, Kitchen Equipment for both concession areas, Light fixtures
- <u>Auxiliary Buildings</u> Flatwork Pavement, Permanent Power, Fire Alarm Connections and Testing, Mechanical equipment start up and commissioning. **Temporary Certificate of** Occupancy achieved.
- <u>Site</u> 60 Yard Practice Field Turf Install (substantial completion date: 6/22/22), Southeast Practice Field Addition of SOD and Irrigation.



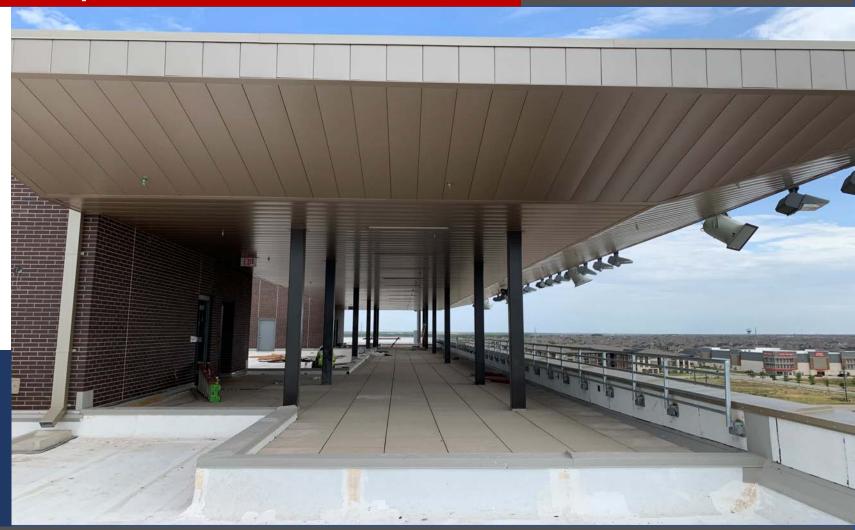












2018 Bond Authorization

Architects – VLK Architects

Contractor – Balfour Beatty Construction

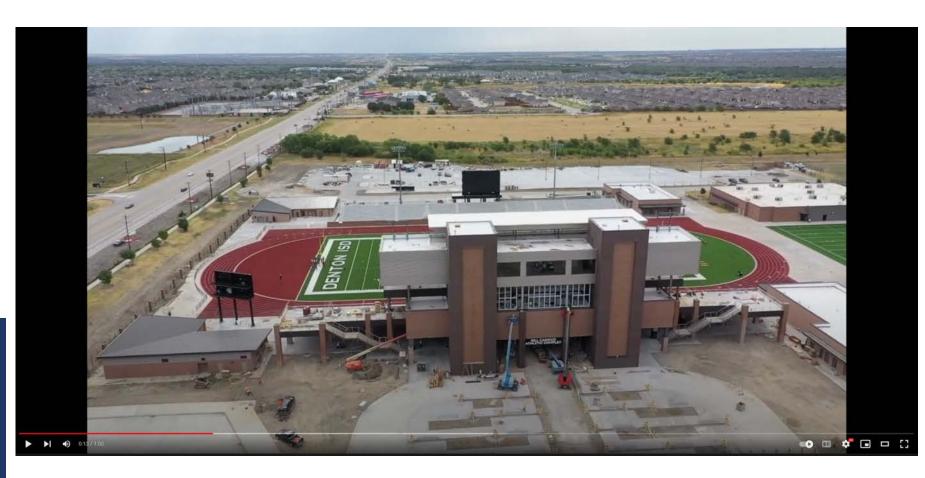

CLICK PICTURE TO OPEN VIDEO



Architects – VLK Architects Contractor – Balfour Beatty Construction

2018 Bond Authorization

Upcoming tasks:

- Stadium Complete Technology Rough-In and Start Up, Complete Elevators, Complete Exterior Metal Panels, Landscaping, Site Lighting & Controls, MEP System Commissioning, Punchlist.
- Auxiliary Buildings Punchlist, MEP Commissioning, Health Inspection for new concessions,
- Site Complete Southeast practice field sod (held up due to new sewer line), Stripe and Landscape around west parking and east parking lots.



DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

LaGrone Advanced Technical Center

August 2022

Prepared by: Brandon Boyter Executive Director of Construction, Planning & Growth



Project – 02 2018 Bond Authorization Architects – VLK Contractor – Steele & Freeman Inc. Move In – Spring 2023





Project – 02 2018 Bond Authorization Architects – VLK Contractor – Steele & Freeman Inc. Move In – Spring 2023





Project – 02 2018 Bond Authorization Architects – VLK Contractor – Steele & Freeman Inc. Move In – Spring 2023





Project – 02 2018 Bond Authorization Architects – VLK Contractor – Steele & Freeman Inc. Move In – Spring 2023



CLICK PICTURE TO OPEN VIDEO



DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

Sandbrock Ranch Elementary School

August 2022

Prepared by: Brandon Boyter Executive Director of Construction, Planning & Growth





























2018 Bond Authorization

Architects – Pfluger Architects

Contractor – Balfour Beatty

Move In – Summer 2022

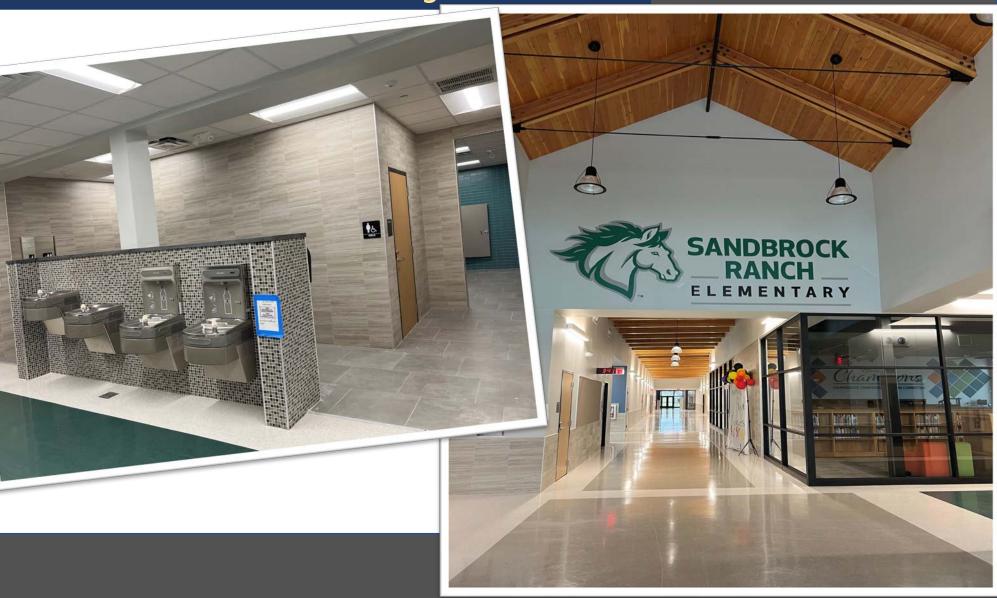



2018 Bond Authorization

Architects – Pfluger Architects

Contractor – Balfour Beatty

Move In – Summer 2022



CLICK PICTURE TO OPEN VIDEO



2018 Bond Authorization Architects – Pfluger Architects Contractor – Balfour Beatty Move In – Summer 2022

Doors open for Students 8-11-22



DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Maintenance & Operations

Controls, MEP, Fire Alarm & Vestibule Projects

August 2022

Prepared by: Paul Andress, Executive Director or Operations

Controls, MEP, Fire Alarm & Vestibule Projects



2018 Bond Authorization

Maintenance

Facility	HVAC Control	Access Control	Mechanical RTUs	Fire Alarm	Secure Vestibule
Ann Windle	Complete	Complete	Complete	In Progress	Design
Borman	In Progress	In Progress	Complete	NA	NA
Crownover	In Progress	In Progress	Complete	In Progress	NA
Davis School	In Progress	In Progress	Complete	Complete	Complete
EP Rayzor	Complete	Complete	Complete	In Progress	NA
Evers	In Progress	In Progress	Complete	In Progress	NA
Ginnings	Complete	Complete	Complete	In Progress	NA
Hodge	In Progress	In Progress	Complete	NA	NA

Controls, MEP, Fire Alarm & Vestibule Projects



2018 Bond Authorization

Maintenance

	Facility	HVAC Control	Access Control	Mechanical RTUs	Fire Alarm	Secure Vestibule
	Houston	In Progress	In Progress	Complete	In Progress	NA
	McNair	In Progress	In Progress	Complete	NA	NA
	Old Technology / Communications	In Progress	In Progress	Complete	Complete	NA
	Pecan Creek	In Progress	In Progress	Complete	In Progress	NA
	Providence	In Progress	Complete	ΝΑ	In Progress	NA
	Rivera	In Progress	In Progress	Complete	In Progress	NA
	Service Center Annex	In Progress	In Progress	Complete	Complete	NA
	WS Ryan	In Progress	In Progress	Complete	Complete	NA



DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Maintenance & Operations

Questions?
