

Minidoka County School District  
**Monthly Maintenance Report**  
August 8, 2017

July 10th - 112 New Requests  
88 Work in Progress  
38 Complete  
10011 Closed Work Orders


Aug. 8th - 126 New Requests  
116 Work in Progress  
22 Complete  
10069 Closed Work Orders

**Maintenance Department Updates**


**Current Projects:**

**DSC Roofing Project**

- 1) Roofing project to replace 3 areas of sloped roofing is designed and ready for bidding. Bidding to take place late spring. Advertise for bid April 19 & 26. Bid opening was May 4<sup>th</sup>. Replace and construct cat walk for servicing HVAC equipment on roof. Contracts being issued. Pre-construction meeting was held on July 7th. Work to begin on July 17<sup>th</sup>.

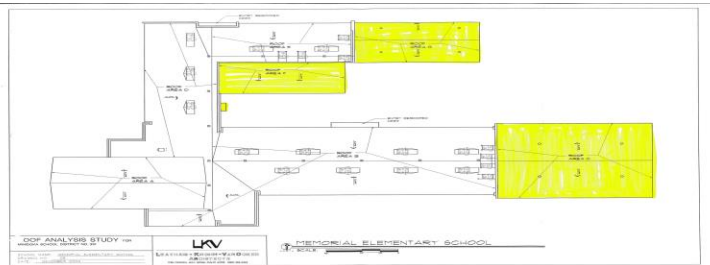


- 2) DSC Office Remodel – Complete



Minidoka County School District  
**Monthly Maintenance Report**  
August 8, 2017

**Minico**

- 1) Irrigation Pump Project Relocation- Advanced Irrigation Solutions is designing the relocation of Minico's turbine pump. This is being relocated because MID is dropping the water level in the ditch. In design. Plans complete and under review. Specs reviewing making ready to bid.

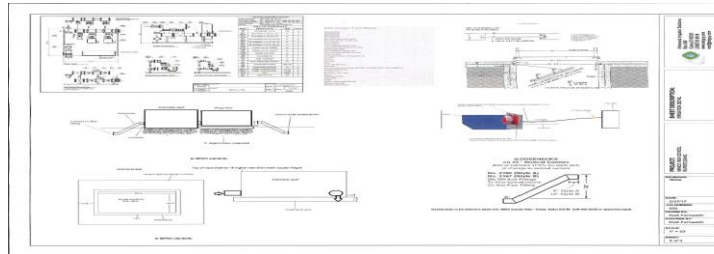

- 2) Bleachers are ordered. Electric panel change out over Spring Break. Delivery date is in July 13th- Removed old bleachers at the close of school. New support wall installed & electrical being installed. Bleachers installed and complete.

**Before**



**After**




Minidoka County School District  
**Monthly Maintenance Report**

August 8, 2017

**3) Minico Flooring - Complete  
Before**



**After**





**4) All Gym Floors Being Refinished**



**5) New Computer Lab – Finishing up.**



**6) Ag Teachers Offices – Complete  
Before**




**After**



Minidoka County School District  
**Monthly Maintenance Report**  
August 8, 2017

**Maintenance Building**

Before. Project taken a backseat to construction in schools. Project on hold until summer work is complete.

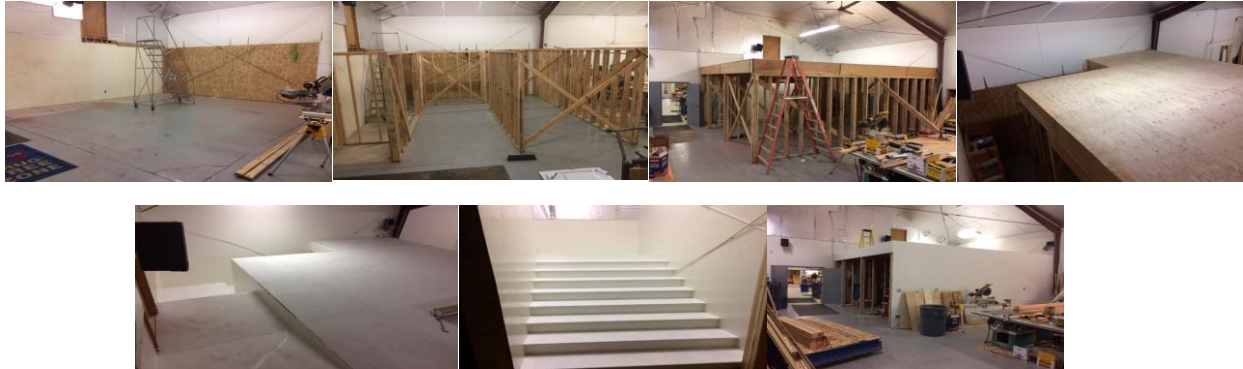

**Food Service Building**

Project on hold until summer work is complete.



**Heyburn**

- 1) Flooring  
Before



After - 100% of carpet installed in classrooms. Tiled floors to follow after school starts. It will be done after hours & weekends. A classroom or two at a time. Hallways to follow.

