



A LEGENCE Company



# ISD #726 – BECKER AREA PUBLIC SCHOOLS REFERENDUM PROJECTS

Progress Update  
August 2<sup>nd</sup>, 2023



# **Agenda:**

Progress Update

Q&A

# Transportation Building Project Update

- Through all inspector walkthroughs
- District has full access of the facility
- Final concrete sealer is being installed
- Misc. items remain



# Middle School & High School Project Update



## Middle School Project Update

### South Addition (Turnover is contingent on storm windows)

- Ceilings will be padded out after above ceiling electrical inspection
- Terrazzo contractor has started hallway work
- Misc. installations taking place in classroom areas
- Exterior work is ongoing
- Waiting on storm windows
- Ala Carte finishes are being installed
- Music Room is complete



### North Addition (Turnover tentatively August 21<sup>st</sup>)

- Metal panel work has started
- Ceilings are being padded out
- Carpet will be starting Thursday
- Final inspections in the next week and a half
- Exterior work is ongoing



## High School Project Update

- HS Office (Turnover tentatively August 21<sup>st</sup>)
- CTE (Turnover tentatively August 28th)
- FACS (Turnover tentatively August 28th)
- Mechanical and Electrical Rough-ins are wrapping up in all areas
- Painting starting soon

# Middle School & High School Project Update





# Middle School & High School Project Update



# Multi-Purpose Field Project Update

- Finishing Turf Install
- Fence installation and final cleaning of surfaces to follow
- Scoreboard installation is tentatively August 30th






# Multi-Purpose Field Project Update



# Intermediate Renovations Project





# Intermediate Renovations Project

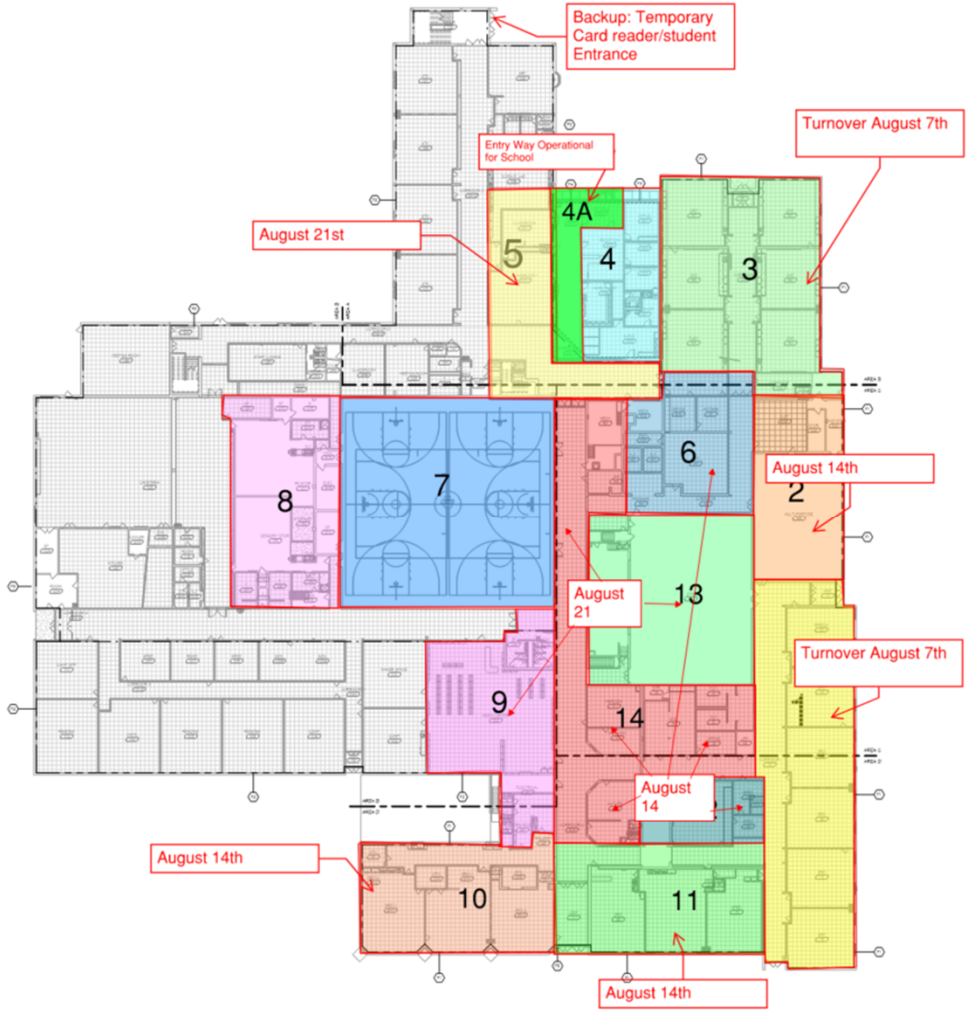

# Intermediate Renovations Project



# Primary/ECFE Additions & Renovations Project





# Primary/ECFE Additions & Renovations Project

## **Main Entry Addition(Turnover September 15<sup>th</sup>)**



- Steel Installation is ongoing
- Concrete slabs are being poured
- Exterior enclosure to begin once steel is complete

## **ECFE**

- Steel install is ongoing
- Exterior framing is ongoing
- MEP rough-ins are ongoing
- Footings and foundations for the link are being installed.



# Primary/ECFE Additions & Renovations Project



# Primary/ECFE Additions & Renovations Project







# Q&A



A LEGENCE Company
