





# SUMMER 2022

## ADA SITE WORK UPGRADES

- ramps & stairs
- landscaping
- parking

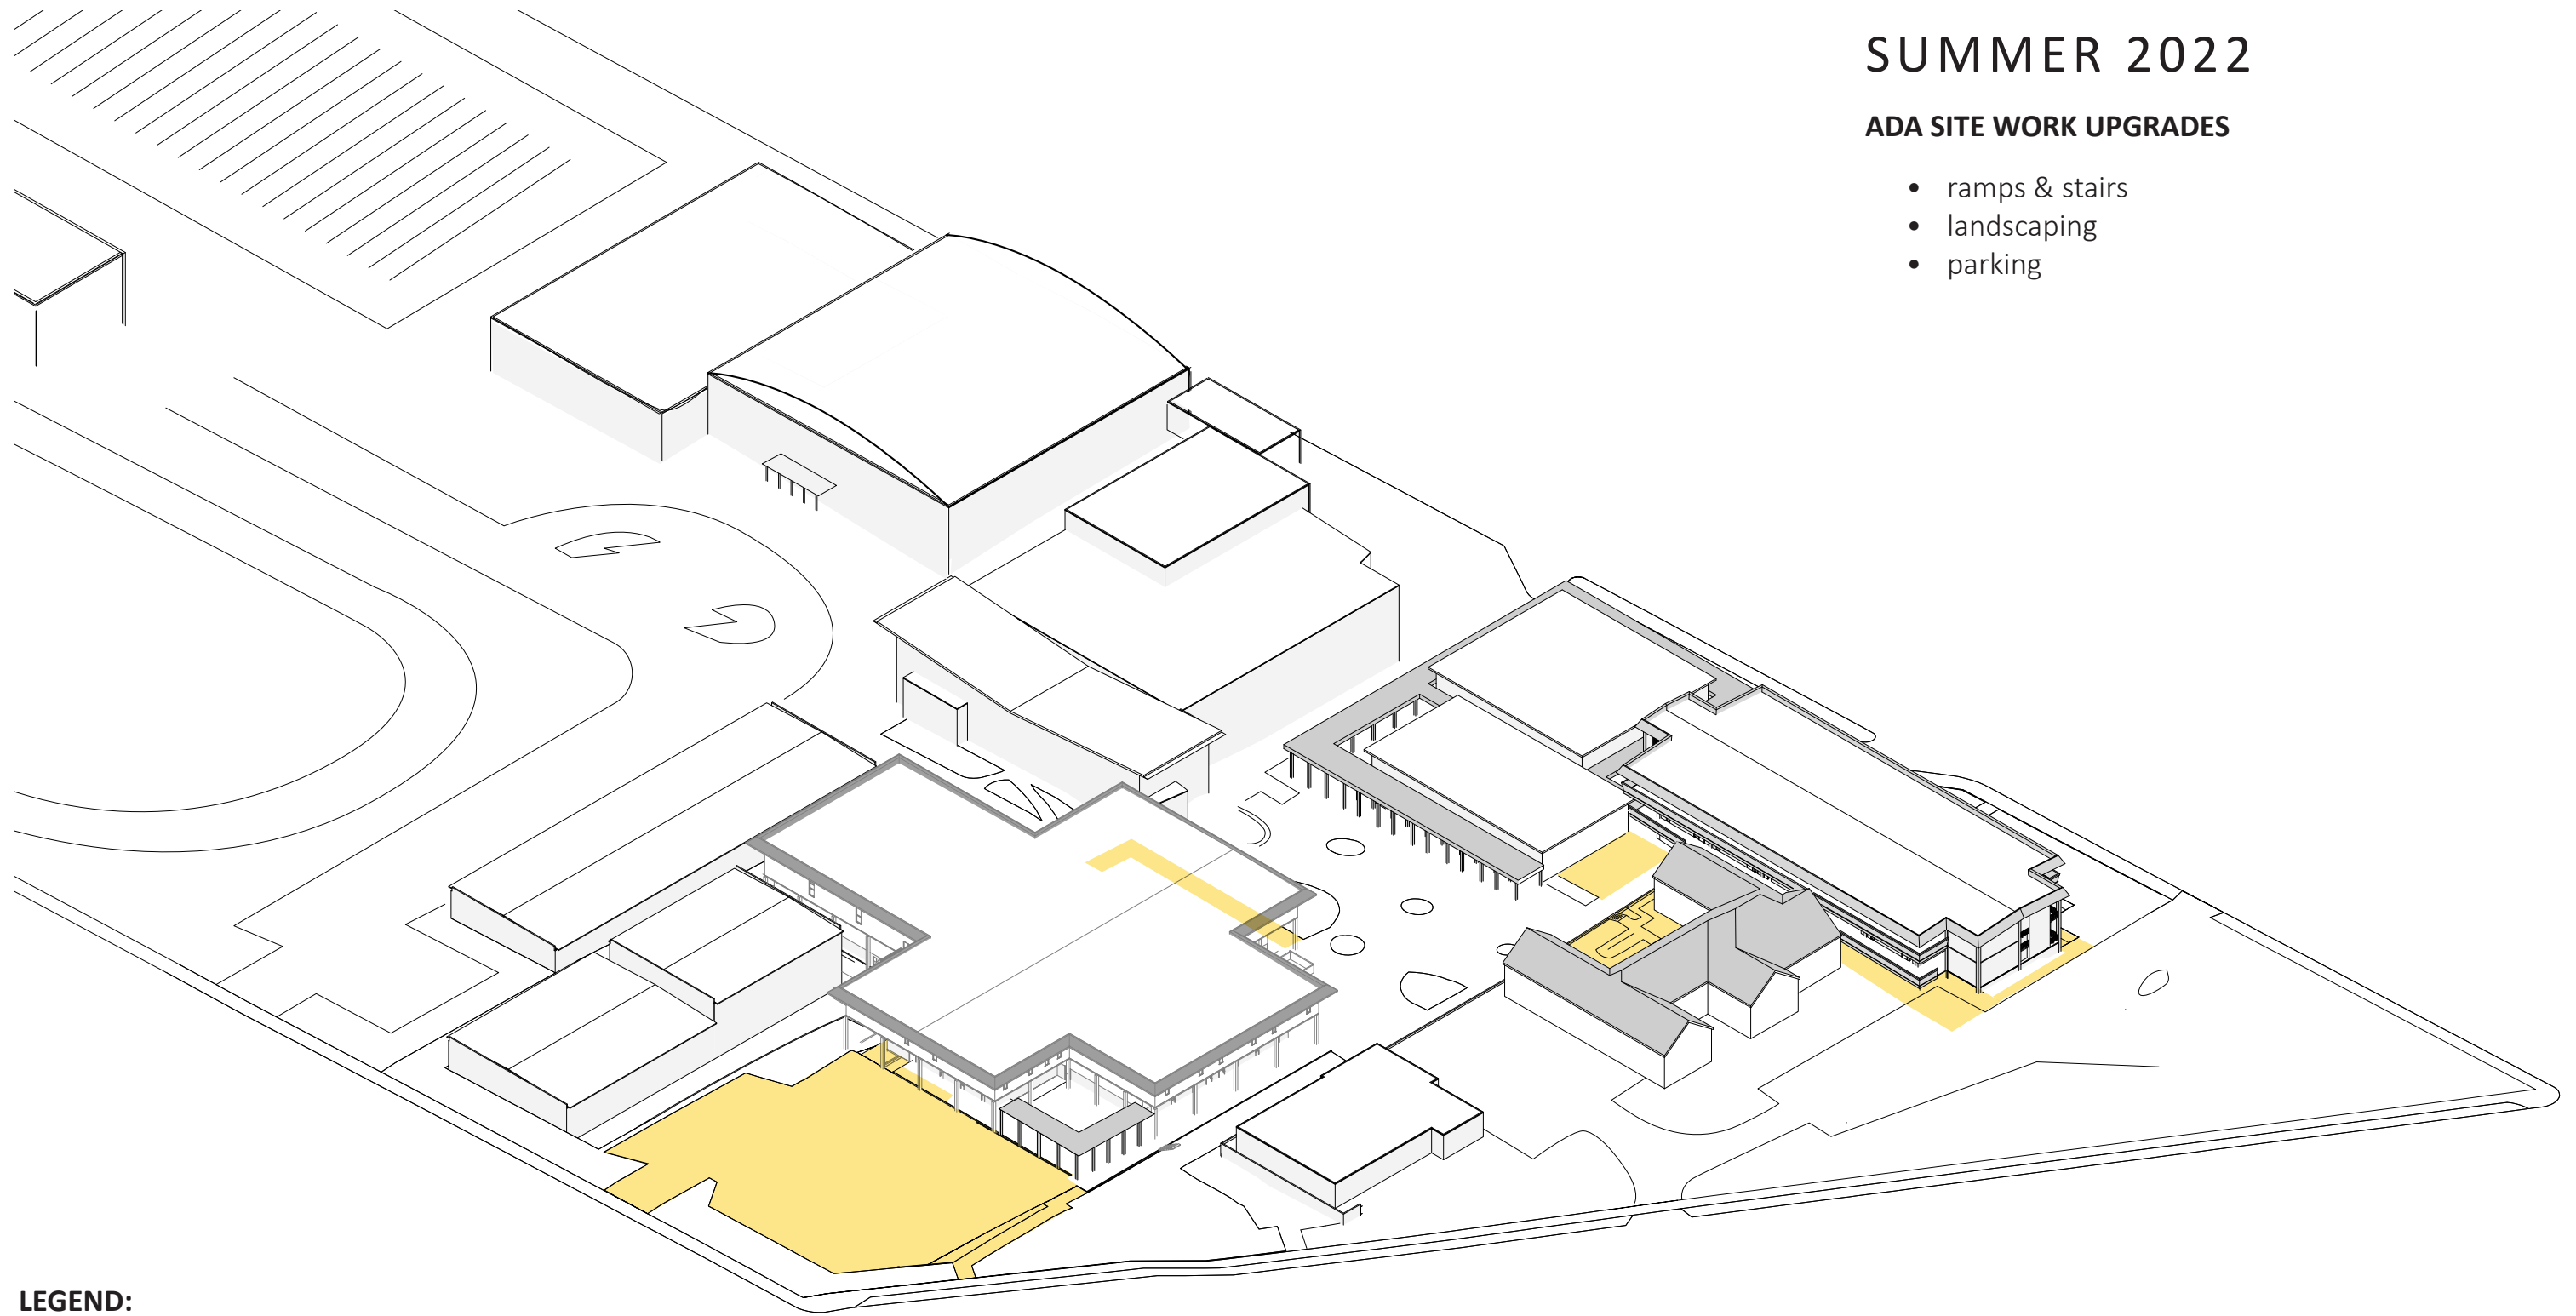

### LEGEND:

-  site work
-  building structure & systems
-  fire alarm



NO ANIMALS  
NO ALCOHOL  
NO GOLFING  
NO MOTORIZED  
VEHICLES  
STRICTLY  
ENFORCED  
ORS 144.205

  
NO DOGS


























# SPRING-SUMMER 2023

## HUMANITIES BUILDING




- abatement / demolition
- seismic structural retrofit- level 1
- elevator / restroom addition

## SCIENCE BUILDING STAIRS

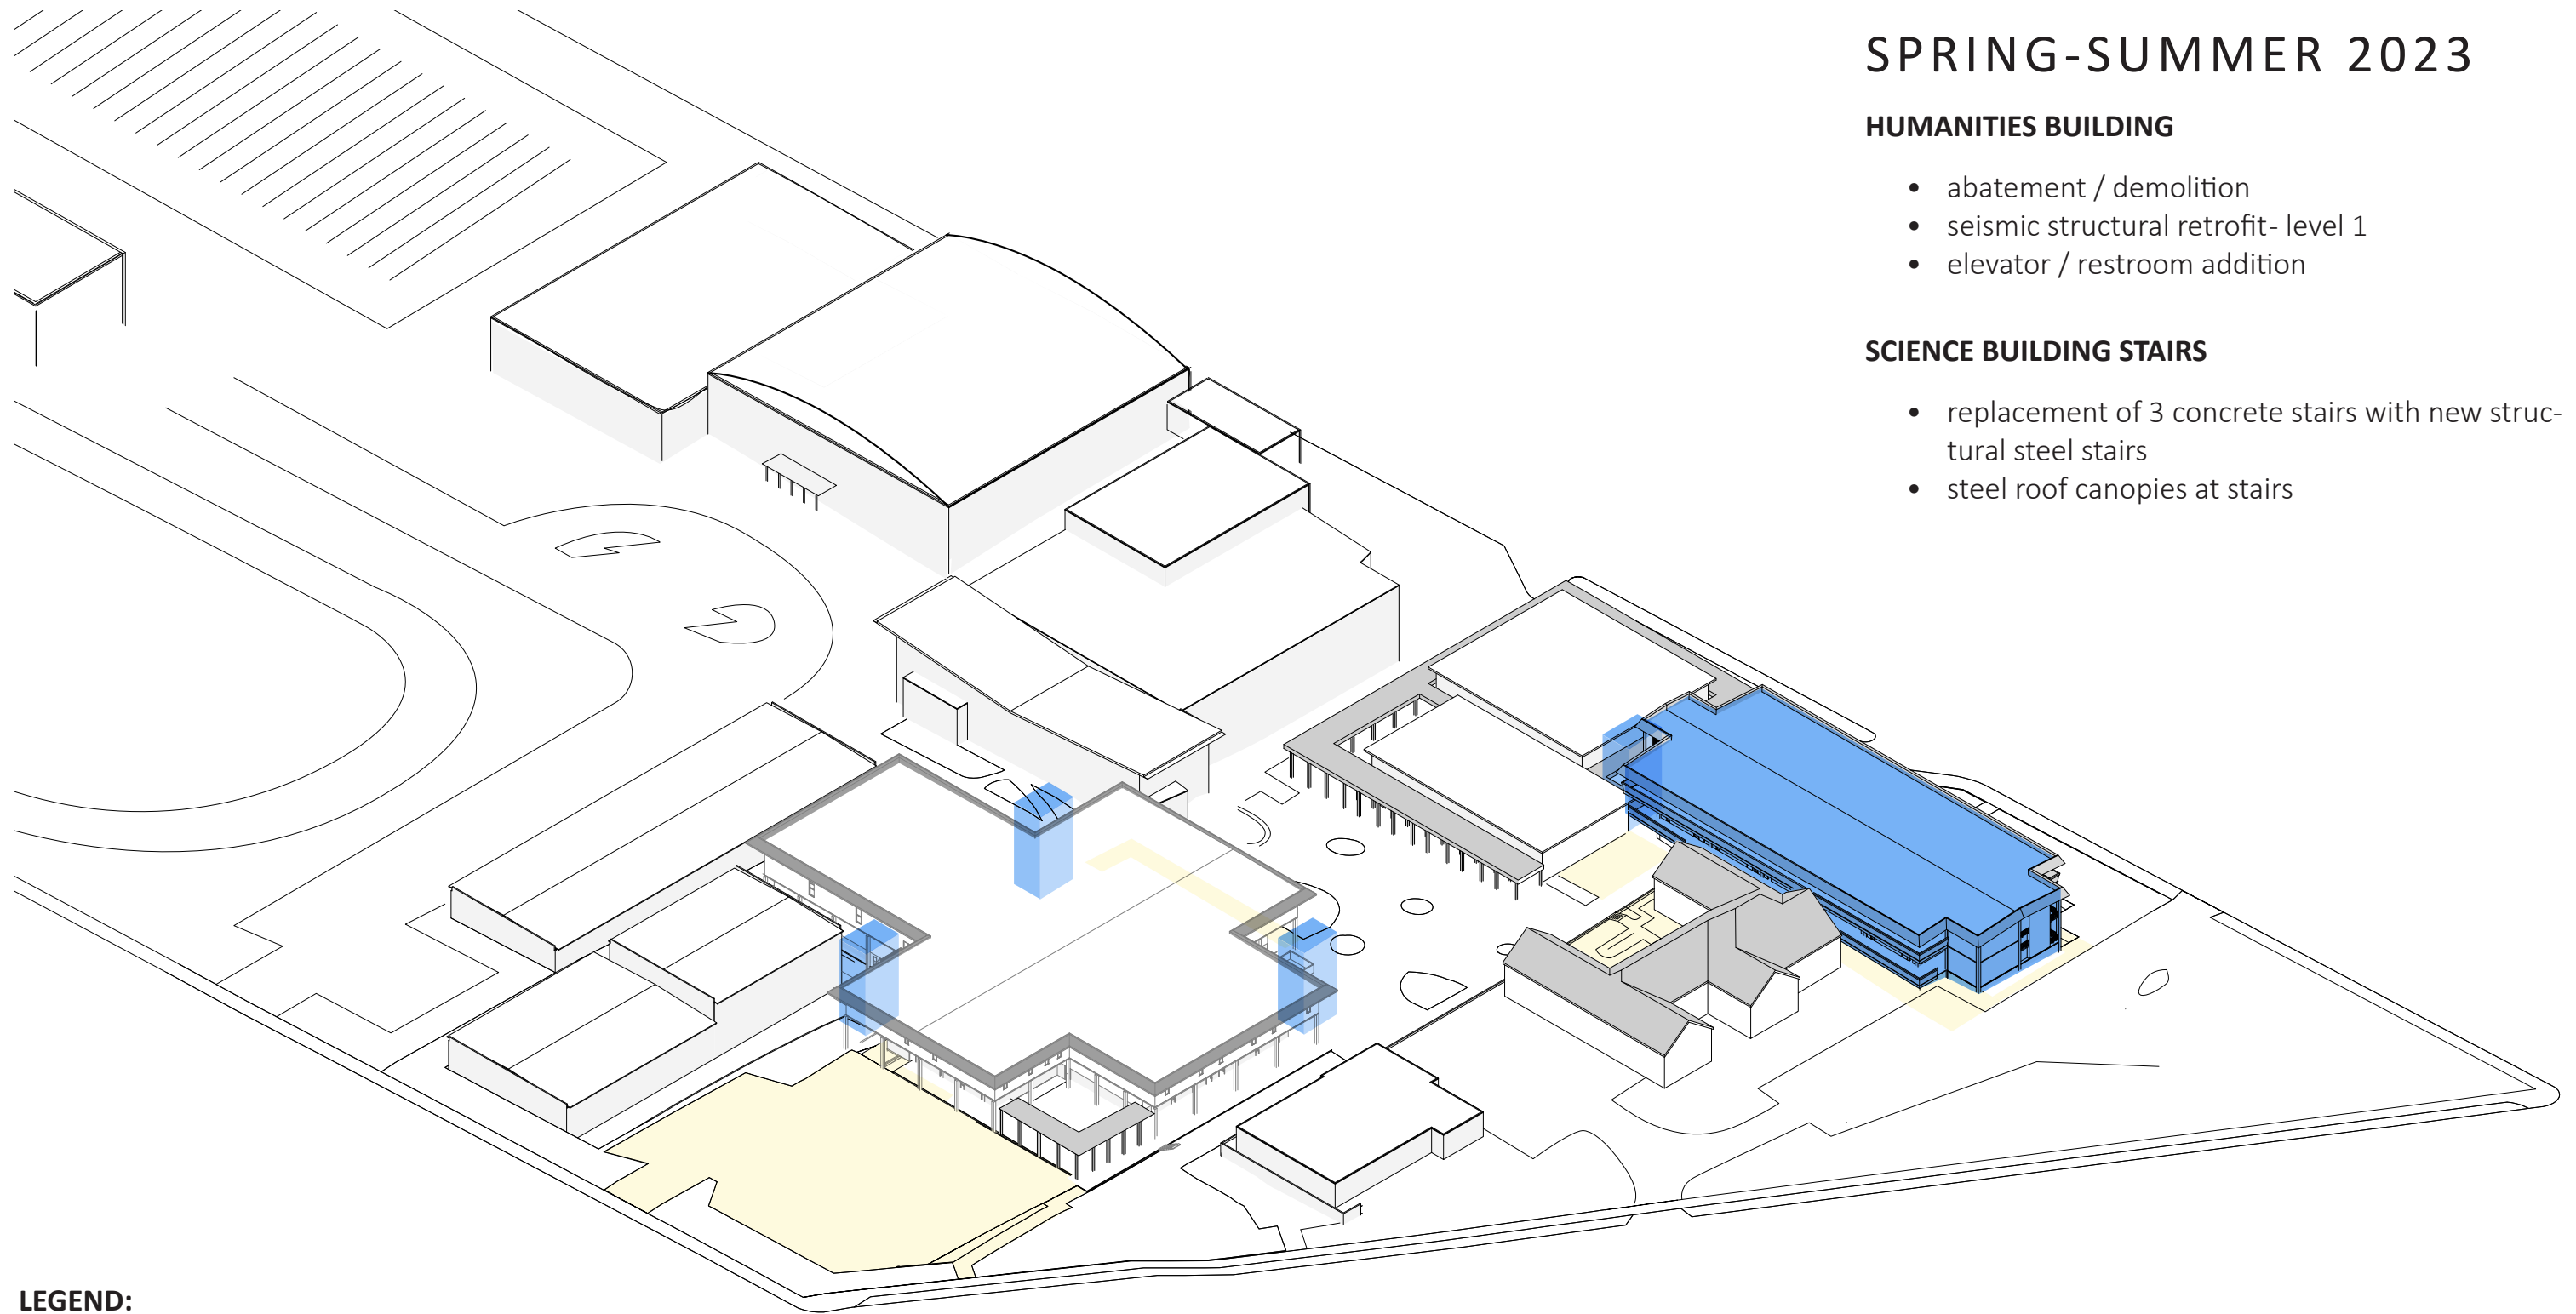- replacement of 3 concrete stairs with new structural steel stairs
- steel roof canopies at stairs




### LEGEND:

-  site work
-  building structure & systems
-  fire alarm







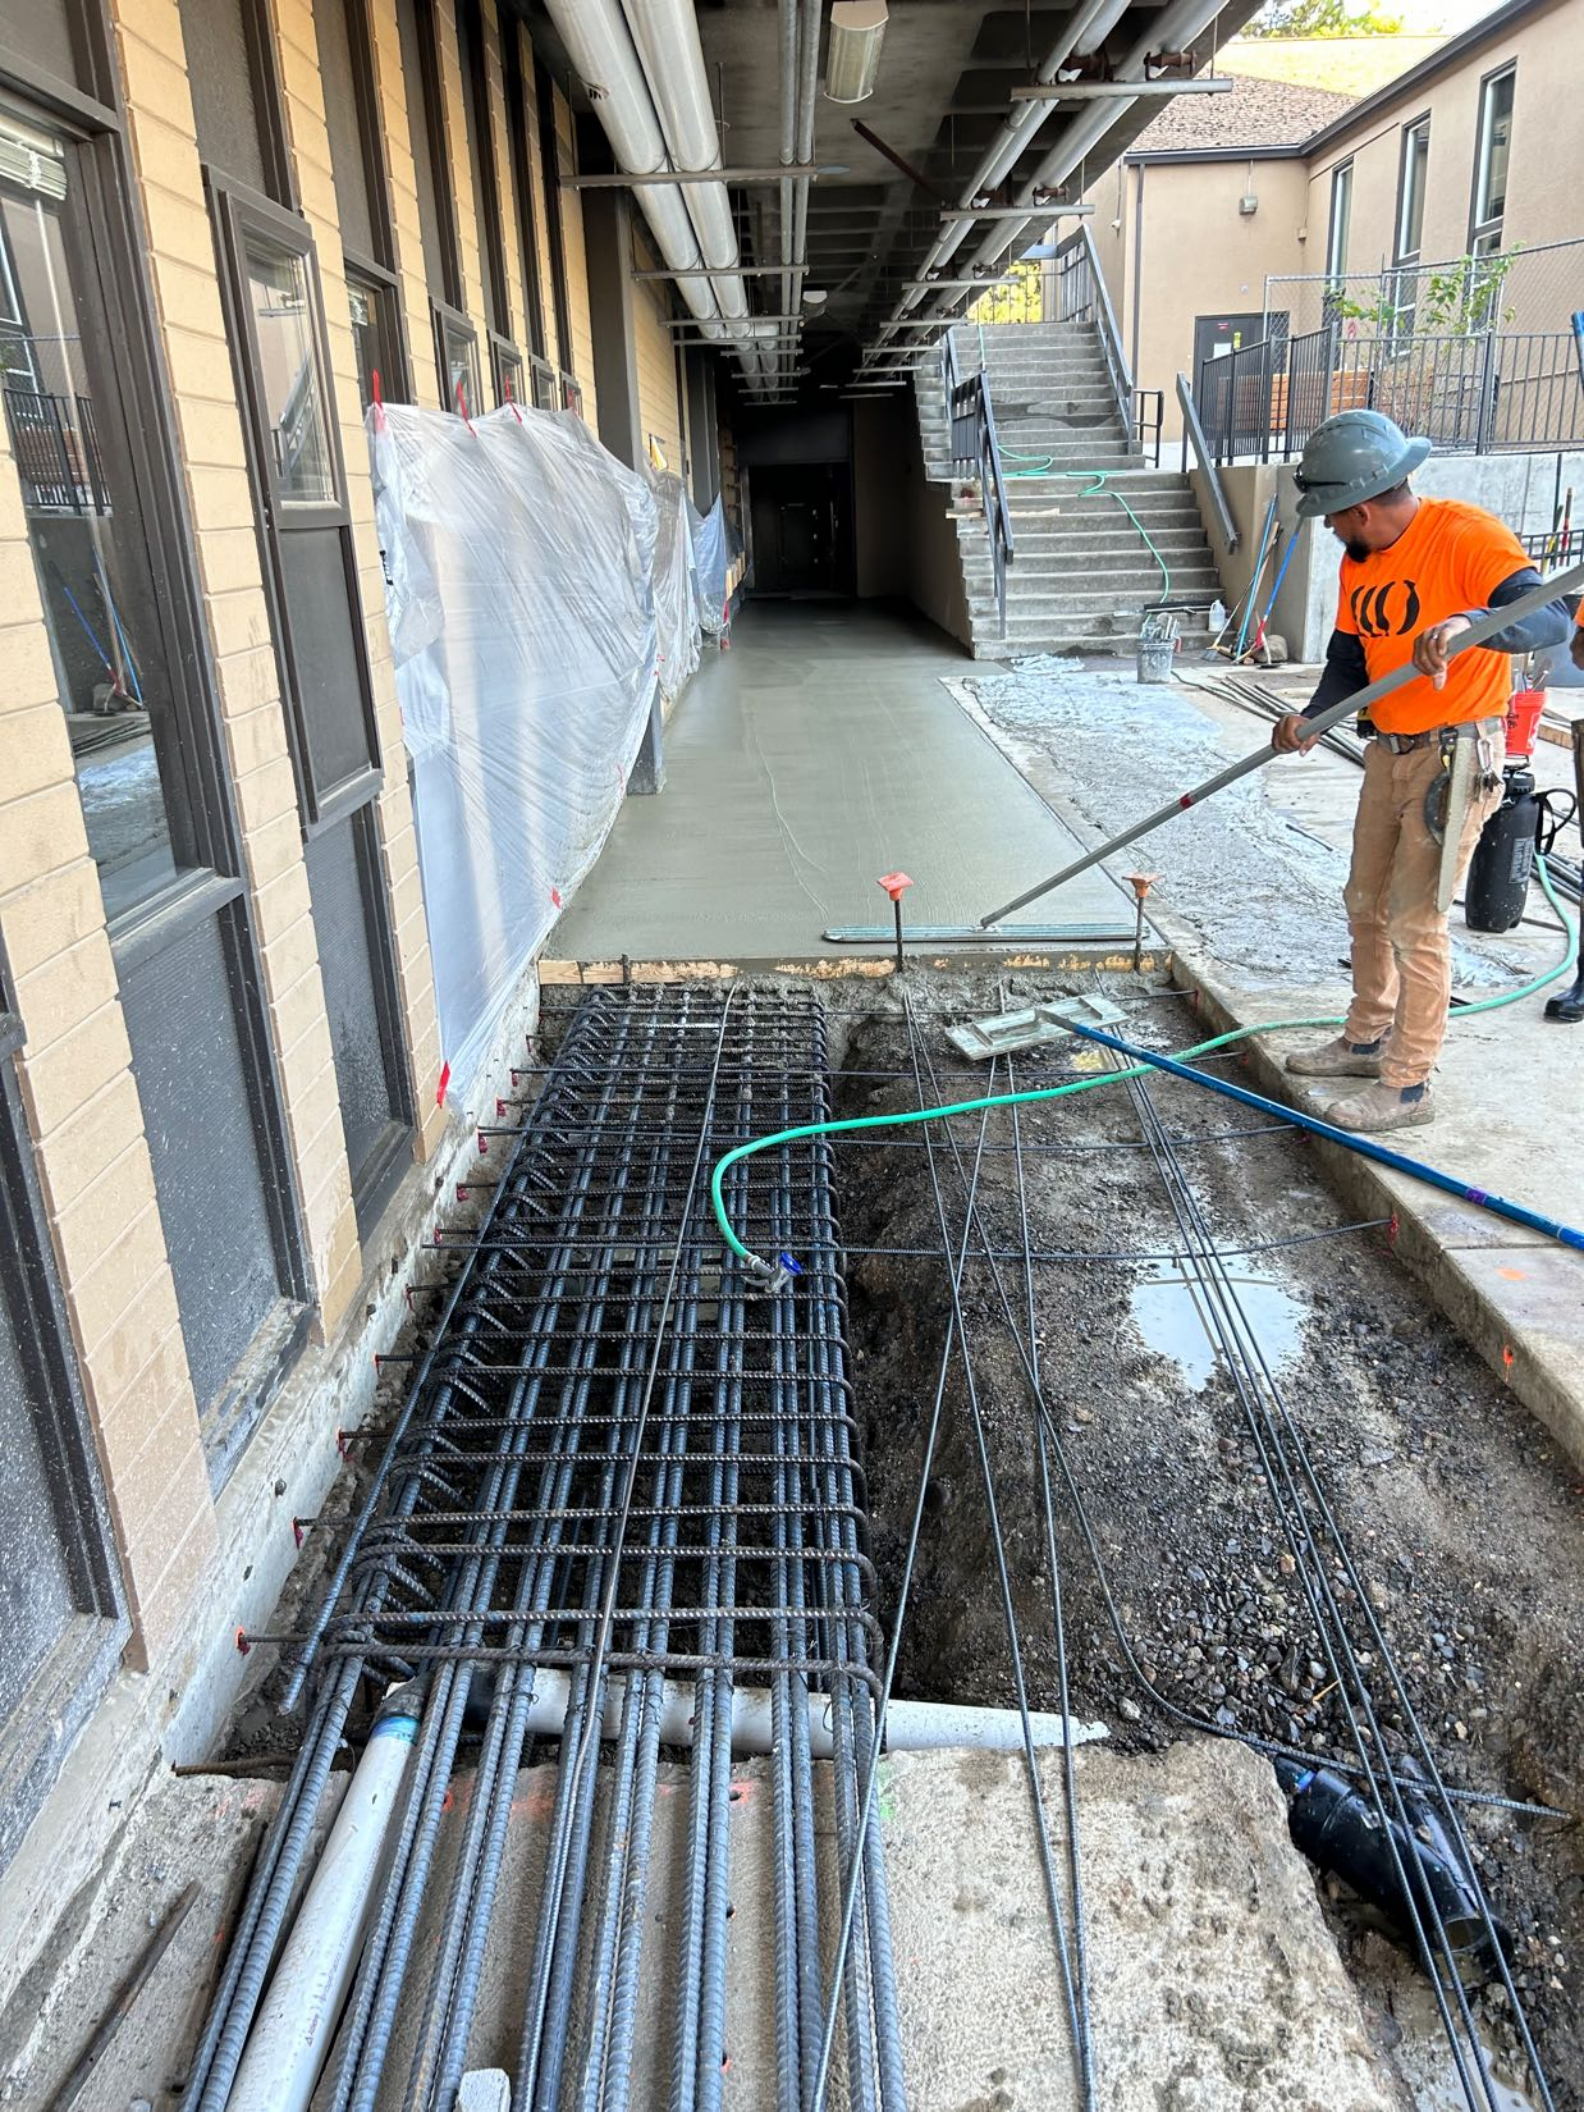














































Good! BAD  
← →

7308







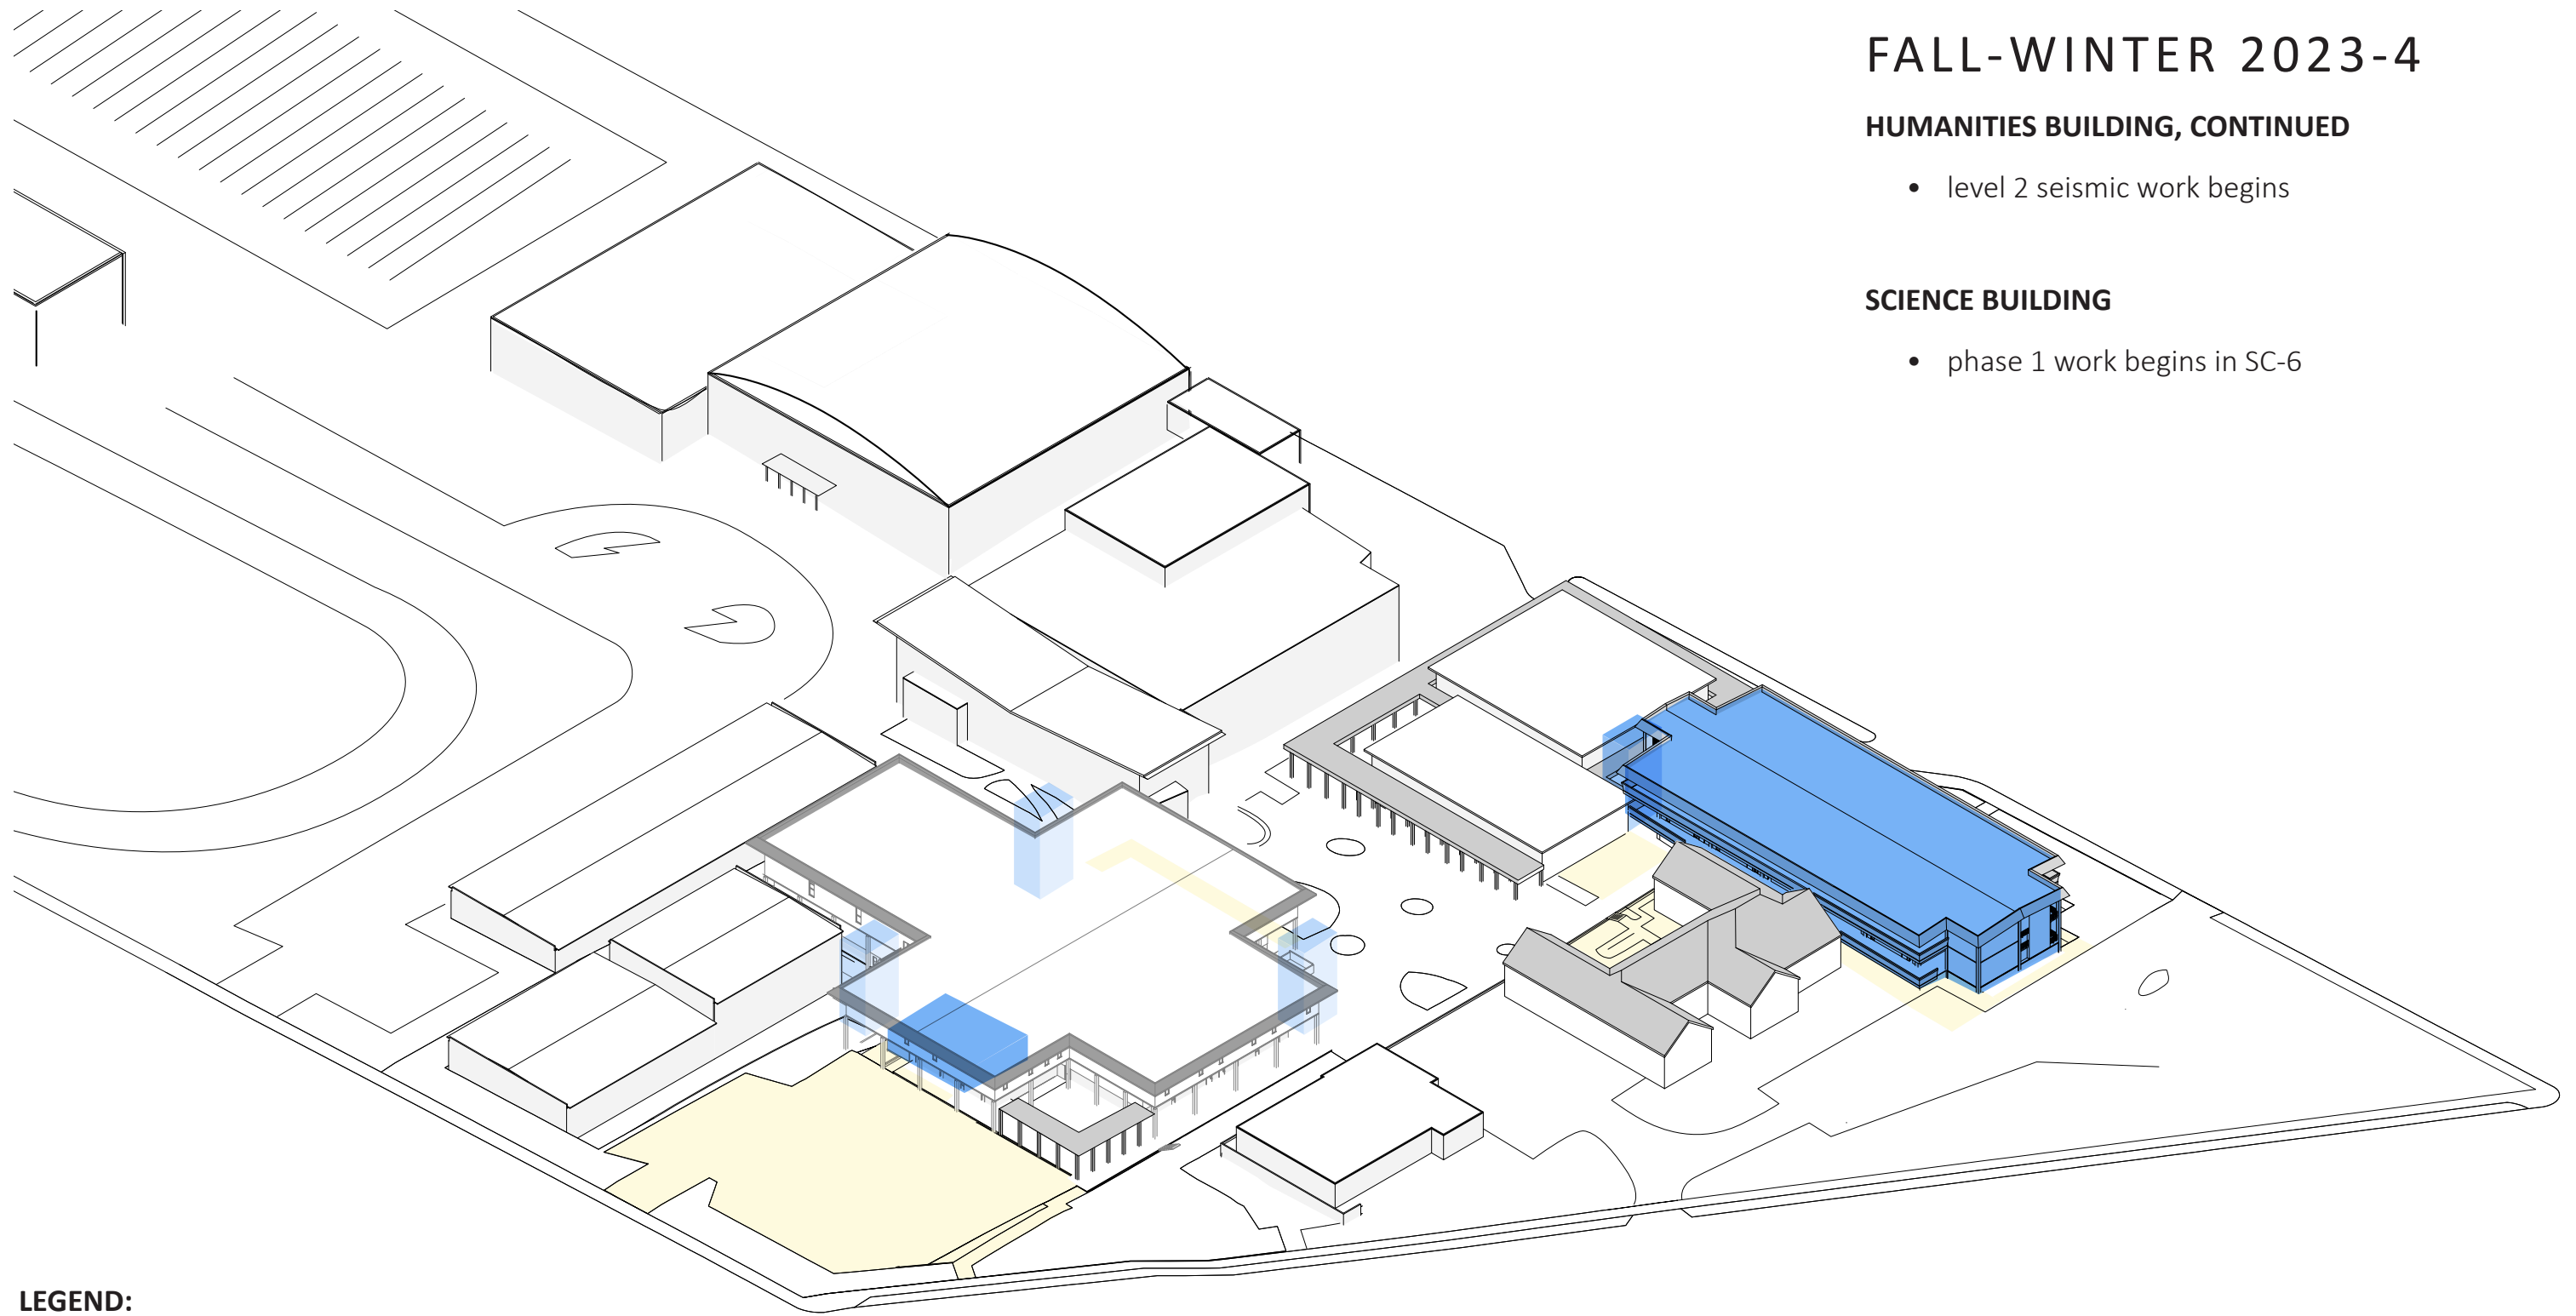

# FALL-WINTER 2023-4




## HUMANITIES BUILDING, CONTINUED

- level 2 seismic work begins

## SCIENCE BUILDING

- phase 1 work begins in SC-6

### LEGEND:

-  site work
-  building structure & systems
-  fire alarm





































DANGER

AHS Science














nVent  
HOFFMAN



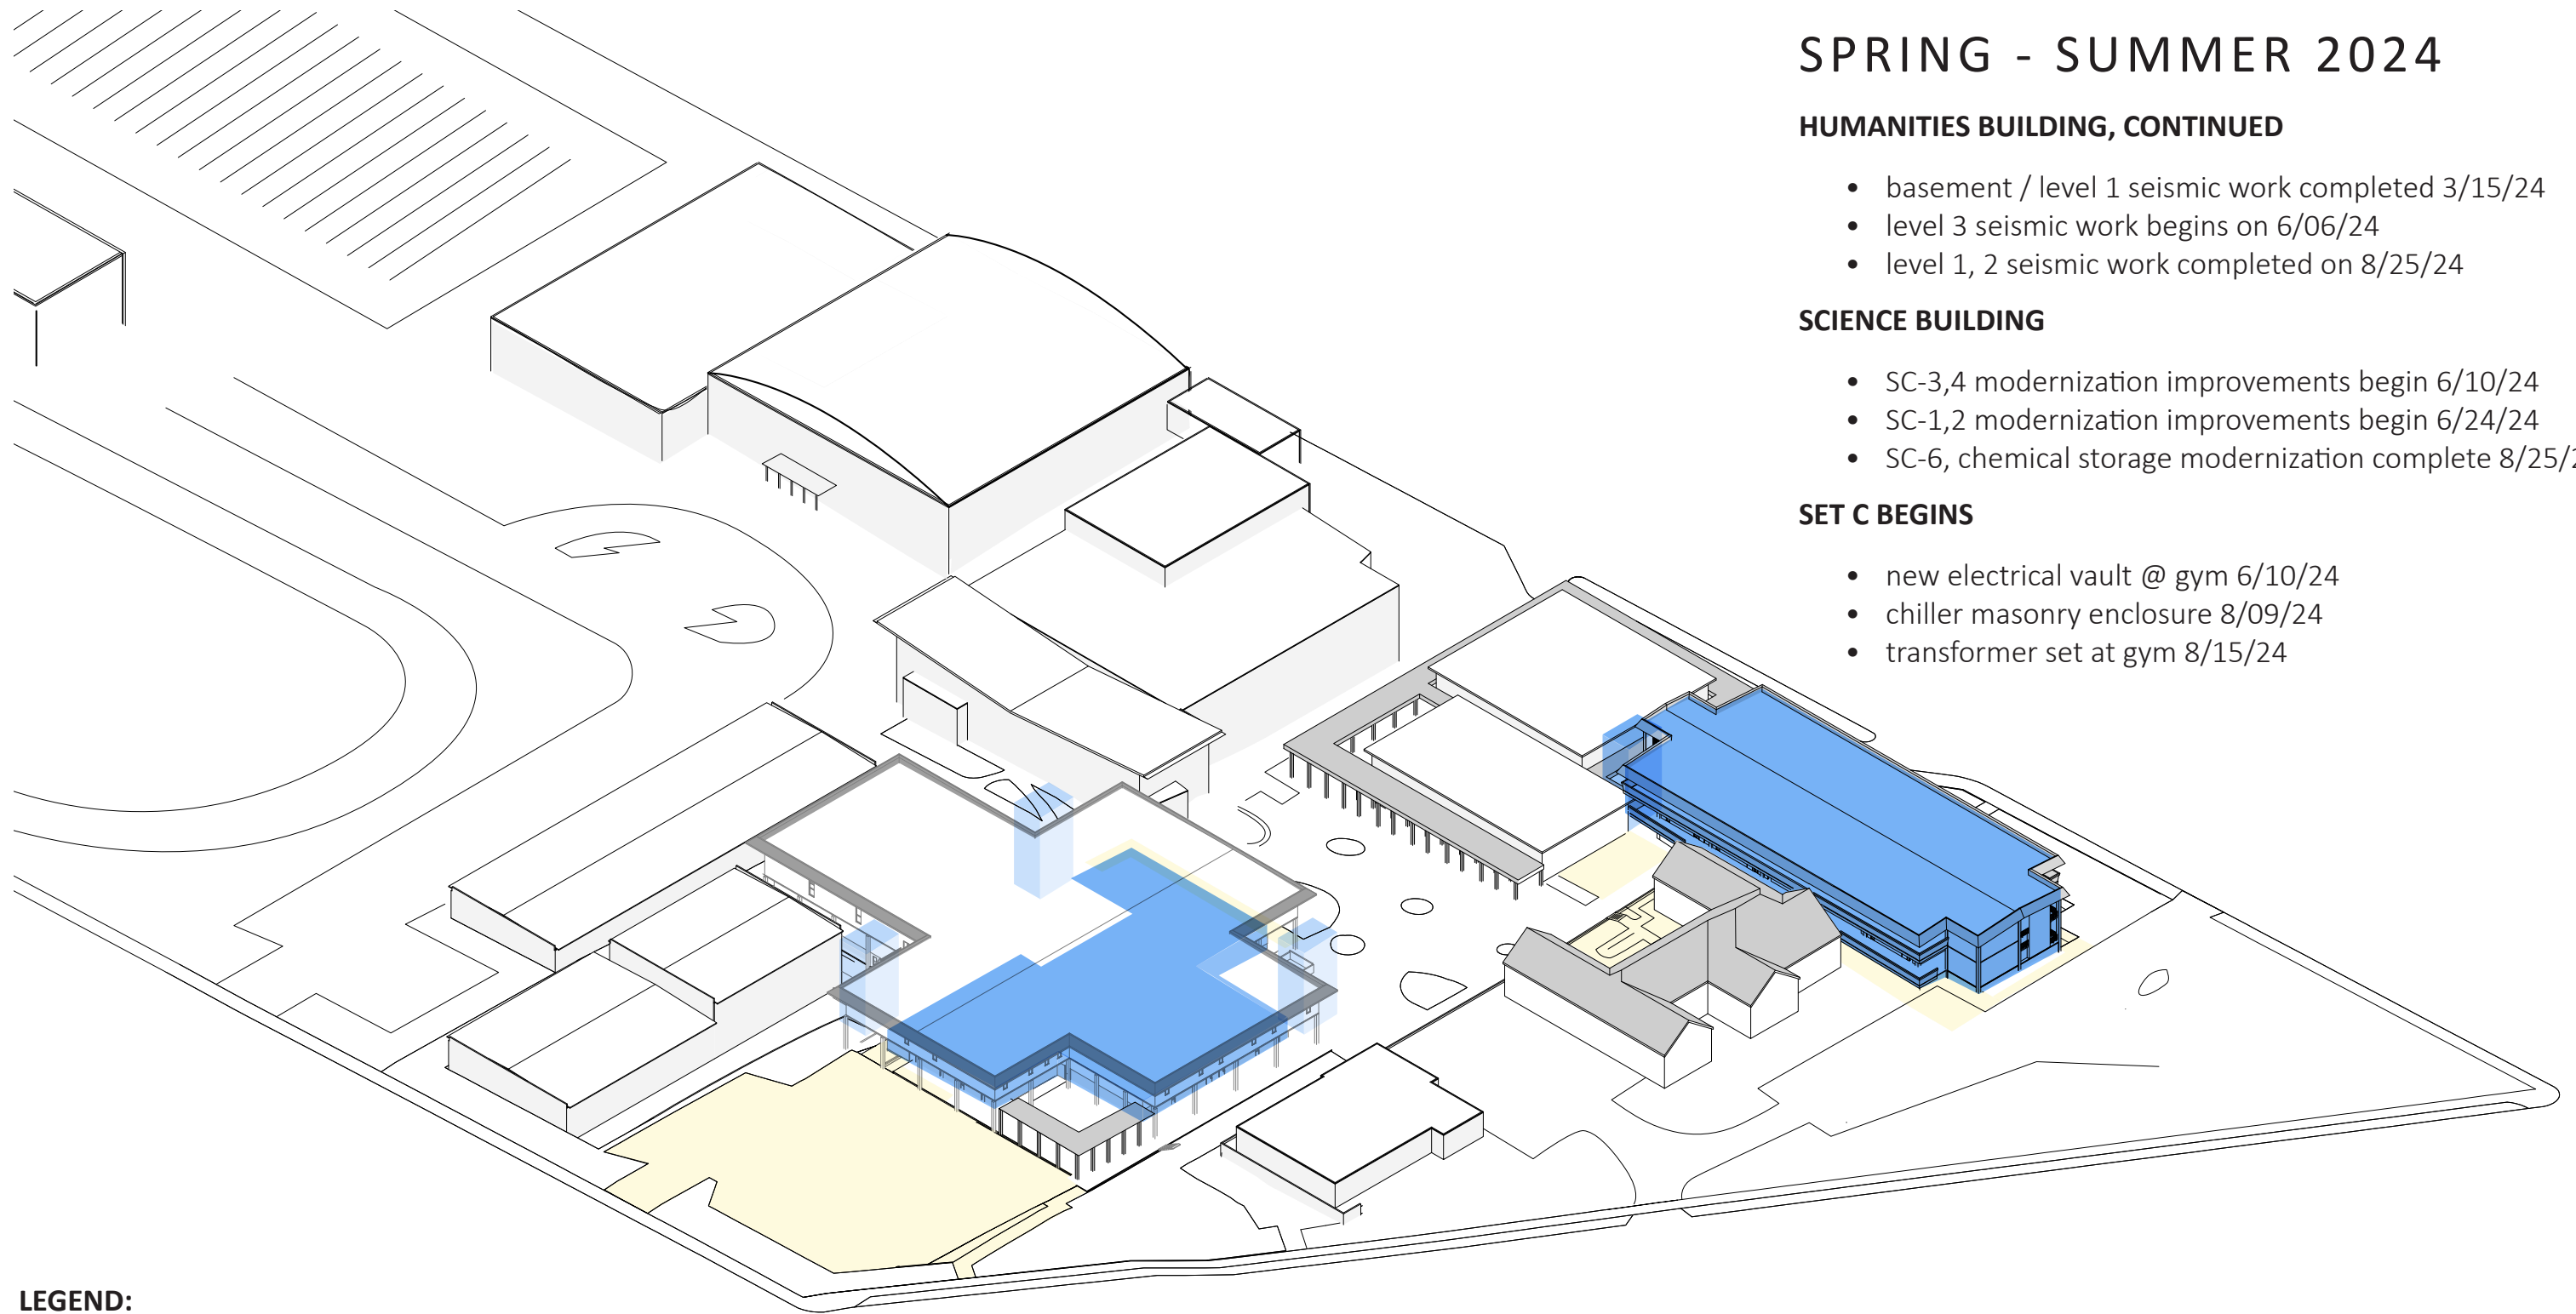

# SPRING - SUMMER 2024

## HUMANITIES BUILDING, CONTINUED

- basement / level 1 seismic work completed 3/15/24
- level 3 seismic work begins on 6/06/24
- level 1, 2 seismic work completed on 8/25/24

## SCIENCE BUILDING

- SC-3,4 modernization improvements begin 6/10/24
- SC-1,2 modernization improvements begin 6/24/24
- SC-6, chemical storage modernization complete 8/25/24


## SET C BEGINS

- new electrical vault @ gym 6/10/24
- chiller masonry enclosure 8/09/24
- transformer set at gym 8/15/24


### LEGEND:

- site work
- building structure & systems
- fire alarm




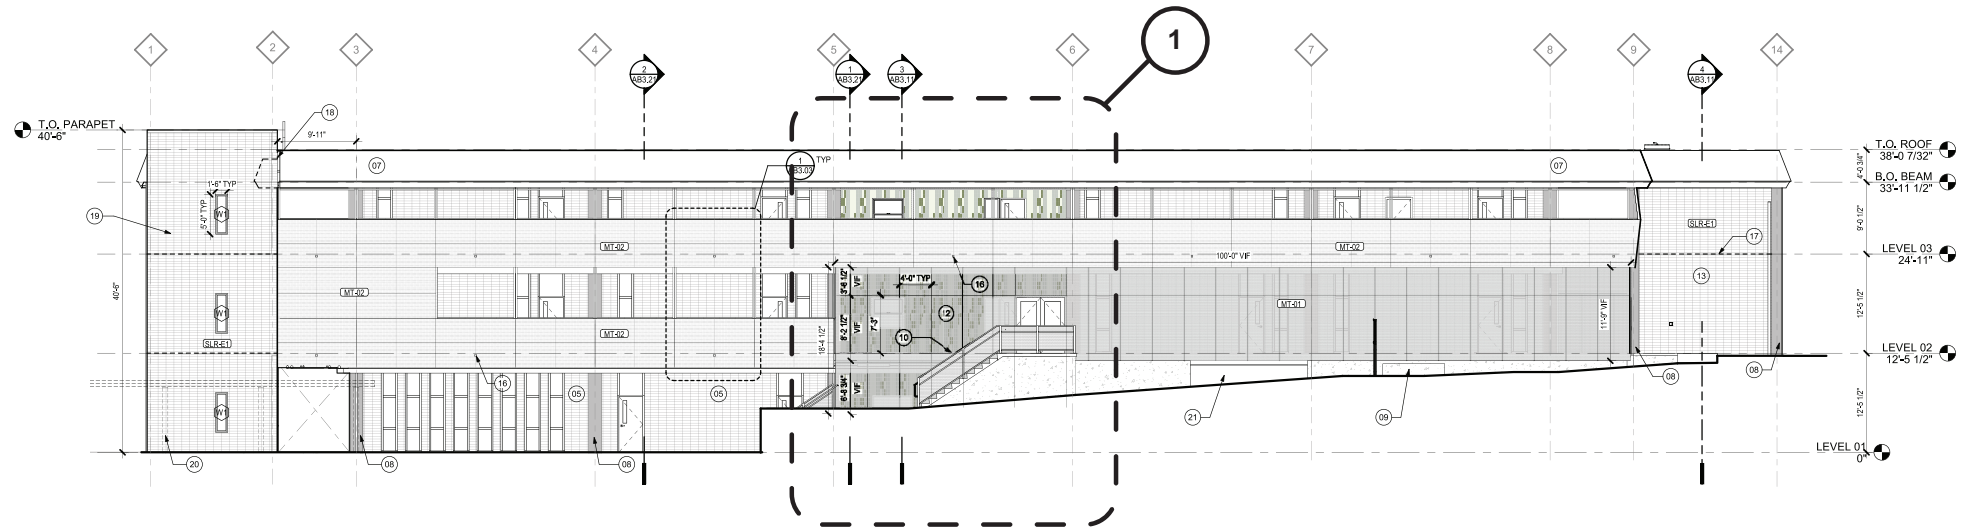


**HUMANITIES - WEST BUILDING ELEVATION**

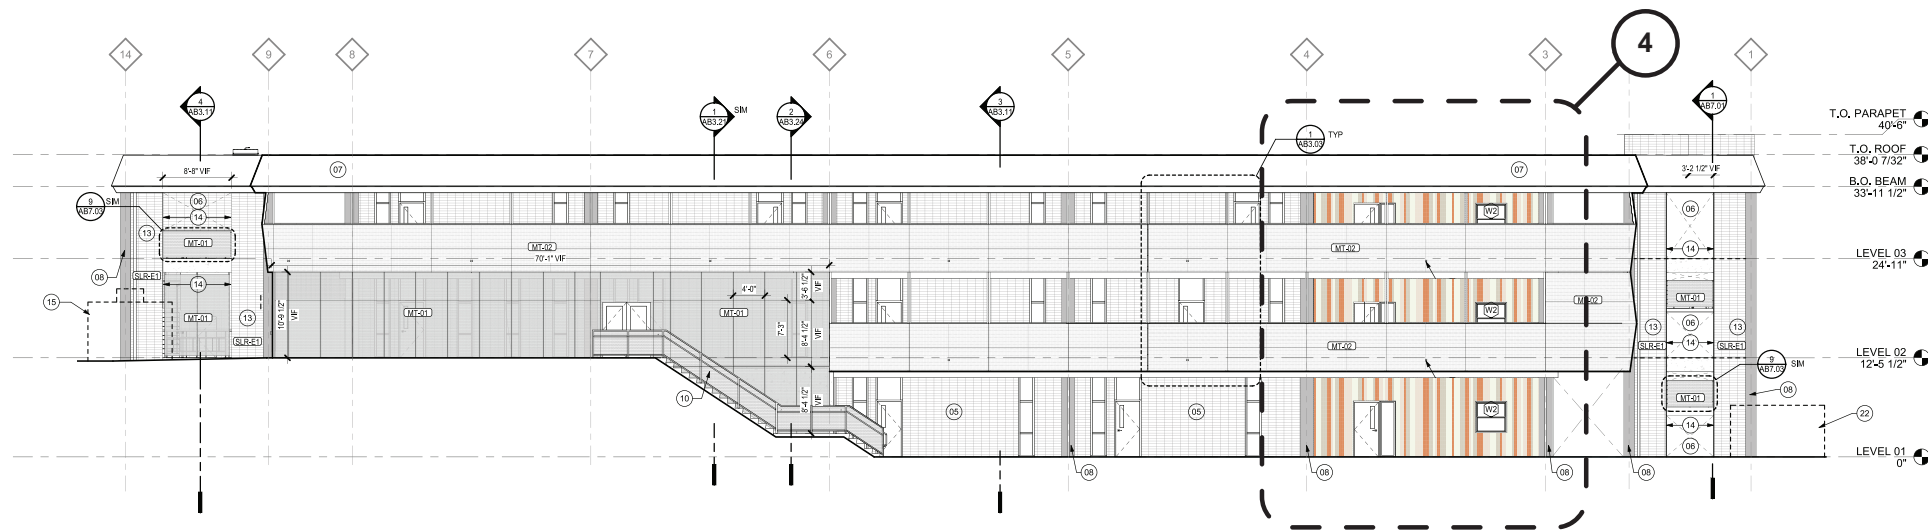

**HUMANITIES - EAST BUILDING ELEVATION**

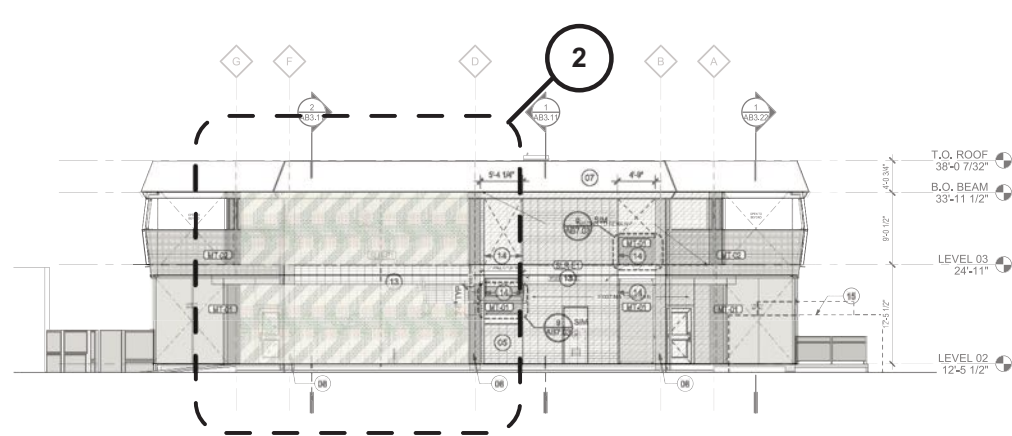

**HUMANITIES - SOUTH CORRIDOR (LOOKING NORTH)**  
(TILE NOT VISIBLE FROM THE EXTERIOR)

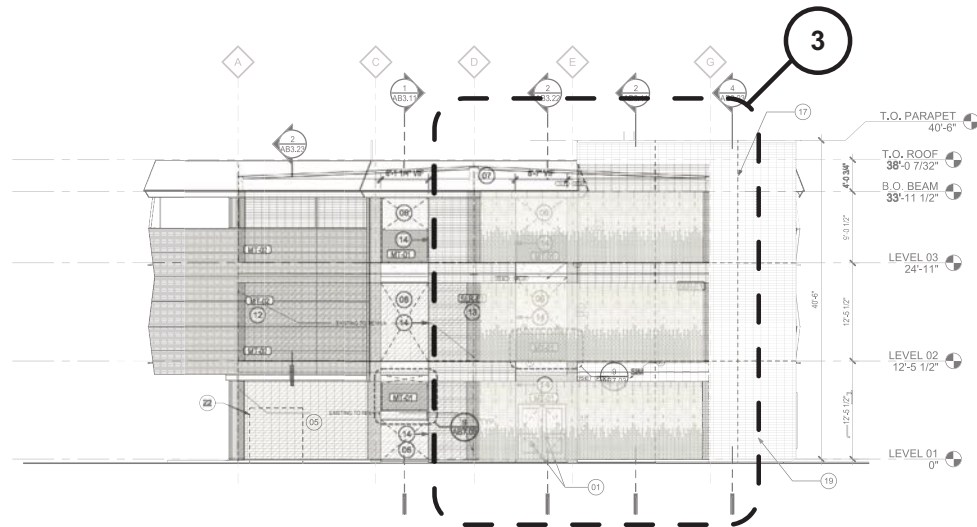

**HUMANITIES - NORTH CORRIDOR (LOOKING SOUTH)** (TILE NOT VISIBLE FROM THE EXTERIOR)

# HUMANITIES TILE MOSAIC

## DESIGN TIMELINE:

- **2021-09-30**- Mosaic tiles are supplied to the Planning department as an updated submittal.
- **2021-11-29** - Coordination on mosaic designs w/ Max Malcomb, Maryetta Jacques.
- **2023-05-23**- Drawings are submitted to the City for building permit review. Mosaic tiles are included as proposed.
- **2023-05-26**- Project review with AHS leadership class; Student approval of Mosaic designs.
- **2023-09-01**- As a cost saving measure, KNO proposes to use the tile manufacturer's standard color range of tiles, rather than the specified architectural tiles. Refer to COR #3. Cost savings of \$47k
- **2023-11-10**- KNO provides new tile samples to arkitek and the construction team.
- **2023-11-13**- arkitek distributes updated renderings of mosaic tile walls with alternate tiles.
- **2023-11-16**- After regular OAC meeting, arkitek reviews updated tiles with Steve Mitzel and AHS student body president and vice-president, Hank Stringer/Noah Cott.
- **2023-11-20**- arkitek distributes new updated renderings of mosaic tile walls with new accent tiles.
- **2023-11-20**- AHS Admin, Bond Administration approves updated tile selection at AHS OAC meeting.
- **2023-12-07**- COR #3 is approved
- **2024-05-31**- arkitek reviews site-built 2nd floor murals with AHS leadership class; receives approval.
- **2024-06-07**- arkitek distributes Humanities historical package to George Kramer; Tile referenced as historical period appropriate finish for SHPO.









PRECISION  
ELECTRIC

CROSSSTEP





PRECISION ELECTRI

2nd FLOOR PLAN  
1/2" = 1'-0"  
DATE: 1/15/11

















**Justrite**  
FLAMMABLE  
KEEP FIRE AWAY  
INFLAMMABLE  
INFLAMMABLE









United Rentals



















innotech  
KINDERTROOST  
innotech-kindertroost.nl




















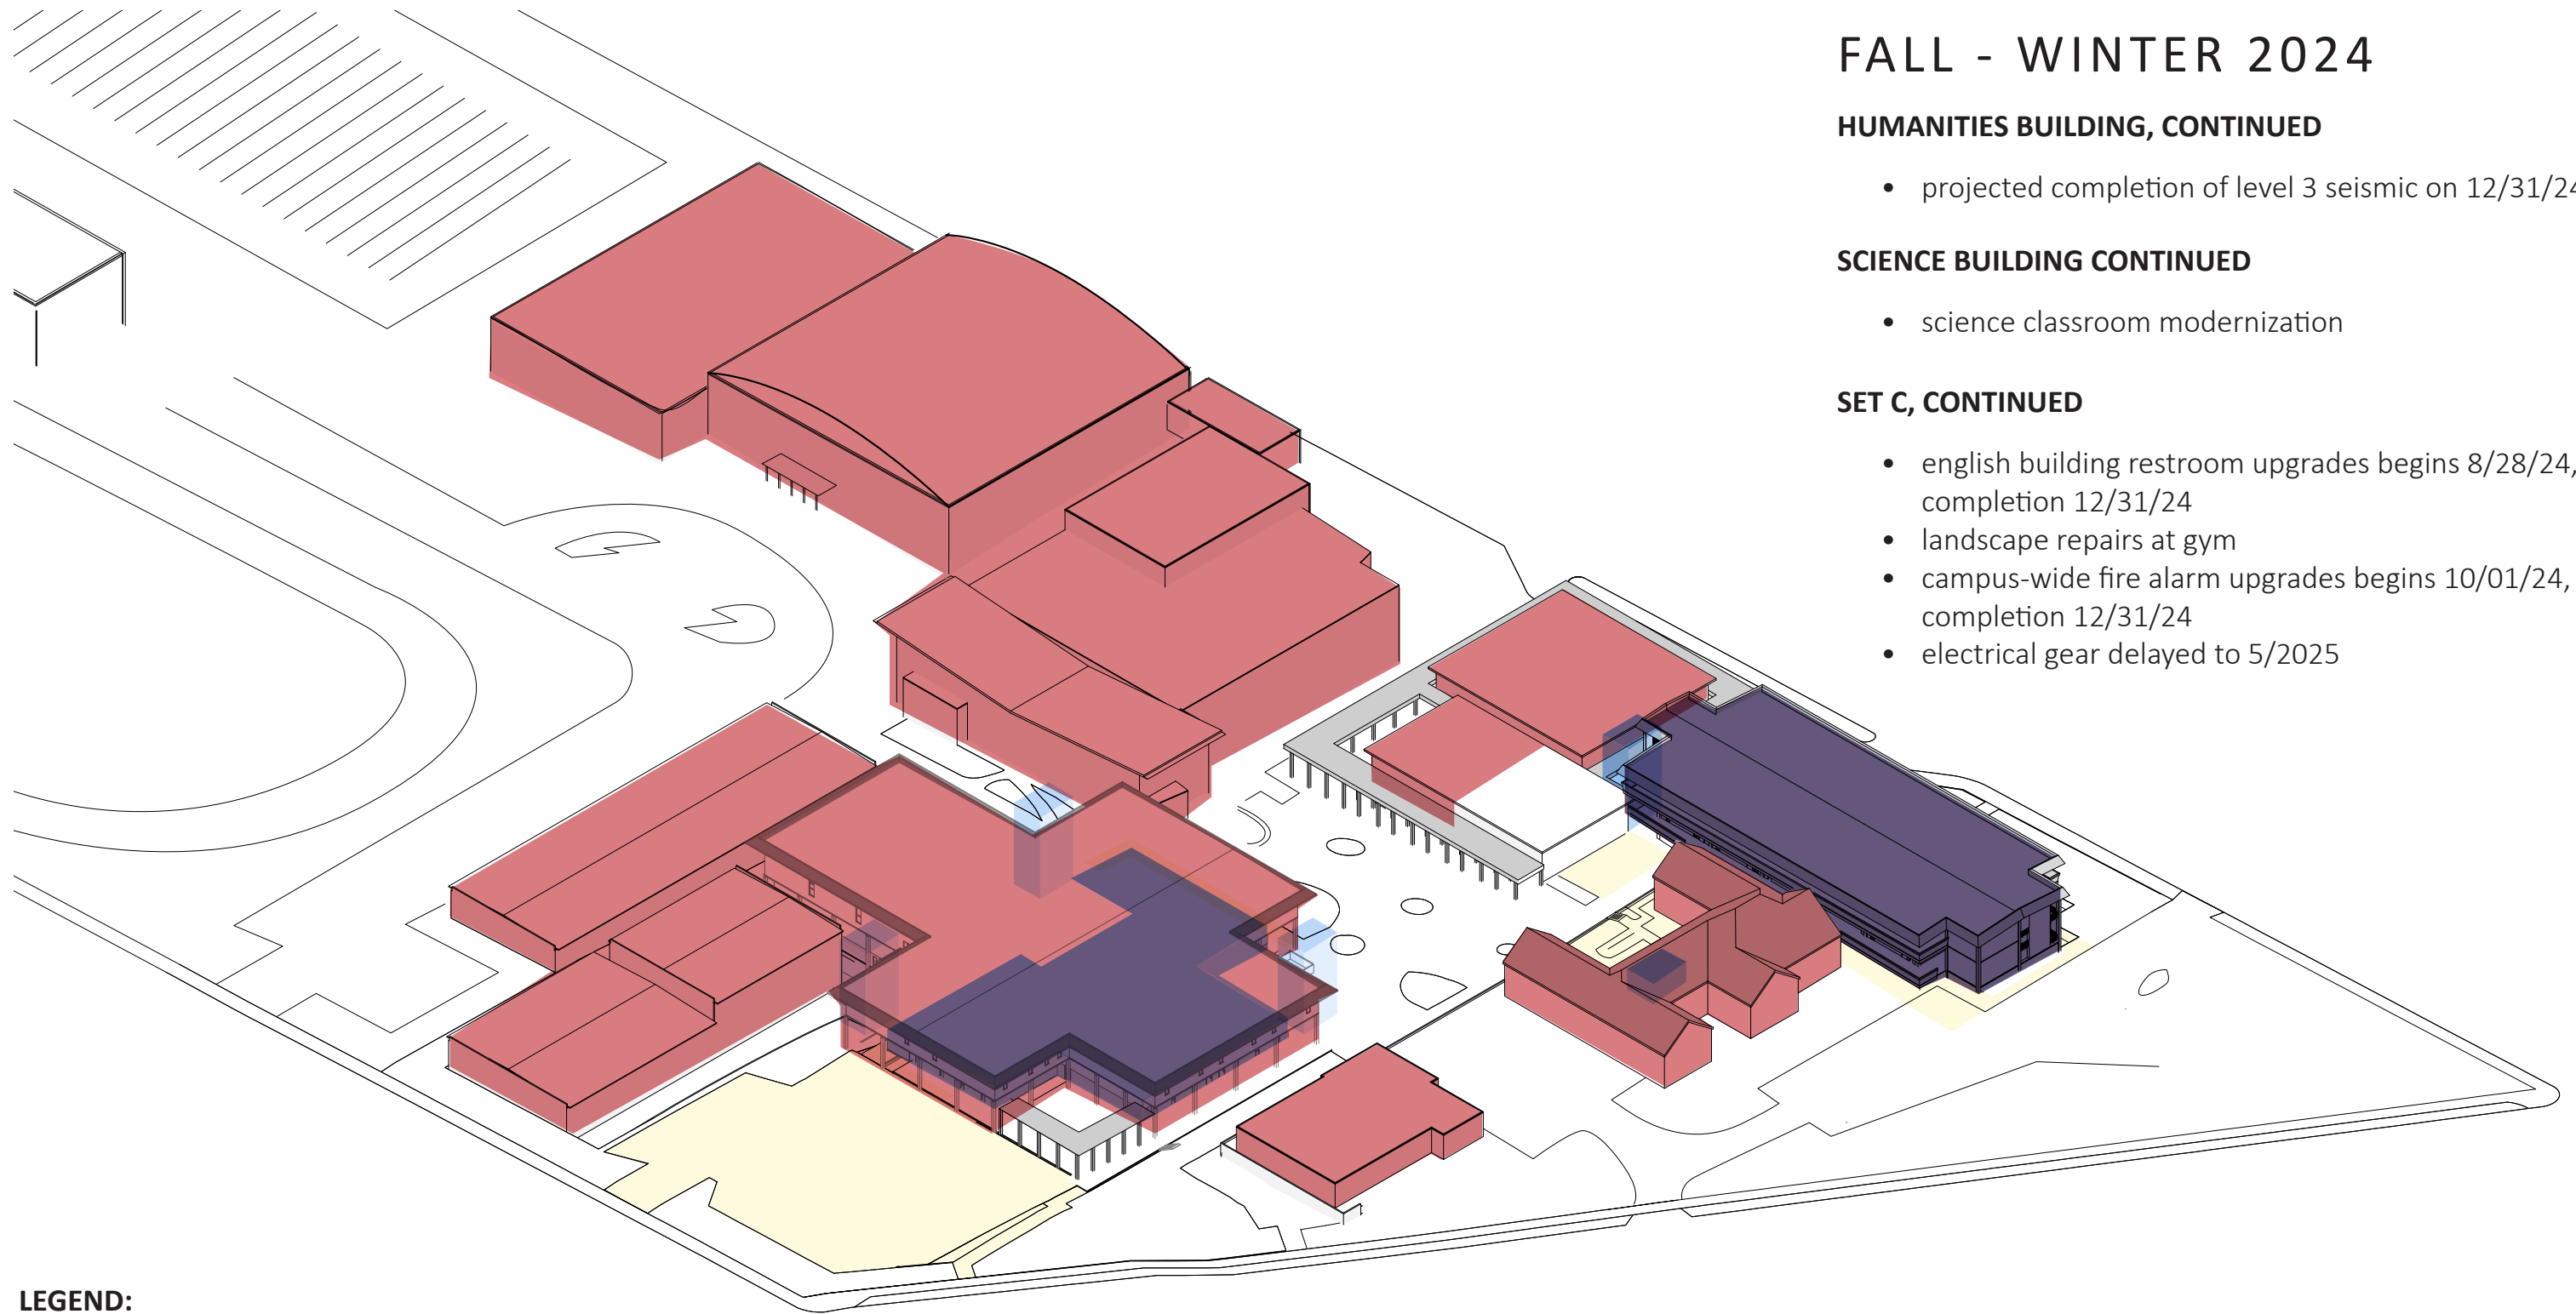

# FALL - WINTER 2024

## HUMANITIES BUILDING, CONTINUED

- projected completion of level 3 seismic on 12/31/24

## SCIENCE BUILDING CONTINUED

- science classroom modernization

## SET C, CONTINUED

- english building restroom upgrades begins 8/28/24, completion 12/31/24
- landscape repairs at gym
- campus-wide fire alarm upgrades begins 10/01/24, completion 12/31/24
- electrical gear delayed to 5/2025

### LEGEND:

- site work
- building structure & systems
- fire alarm



























EXIT







MEDIUM  
Speaker  
PLEASE  
FRAGILE  
Gullo  
Long Term

FRAGILE












# SPRING - SUMMER 2025

## SCIENCE BUILDING, CONTINUED




- CMGC selected
- seismic improvement construction

## QUAD LANDSCAPE UPGRADES

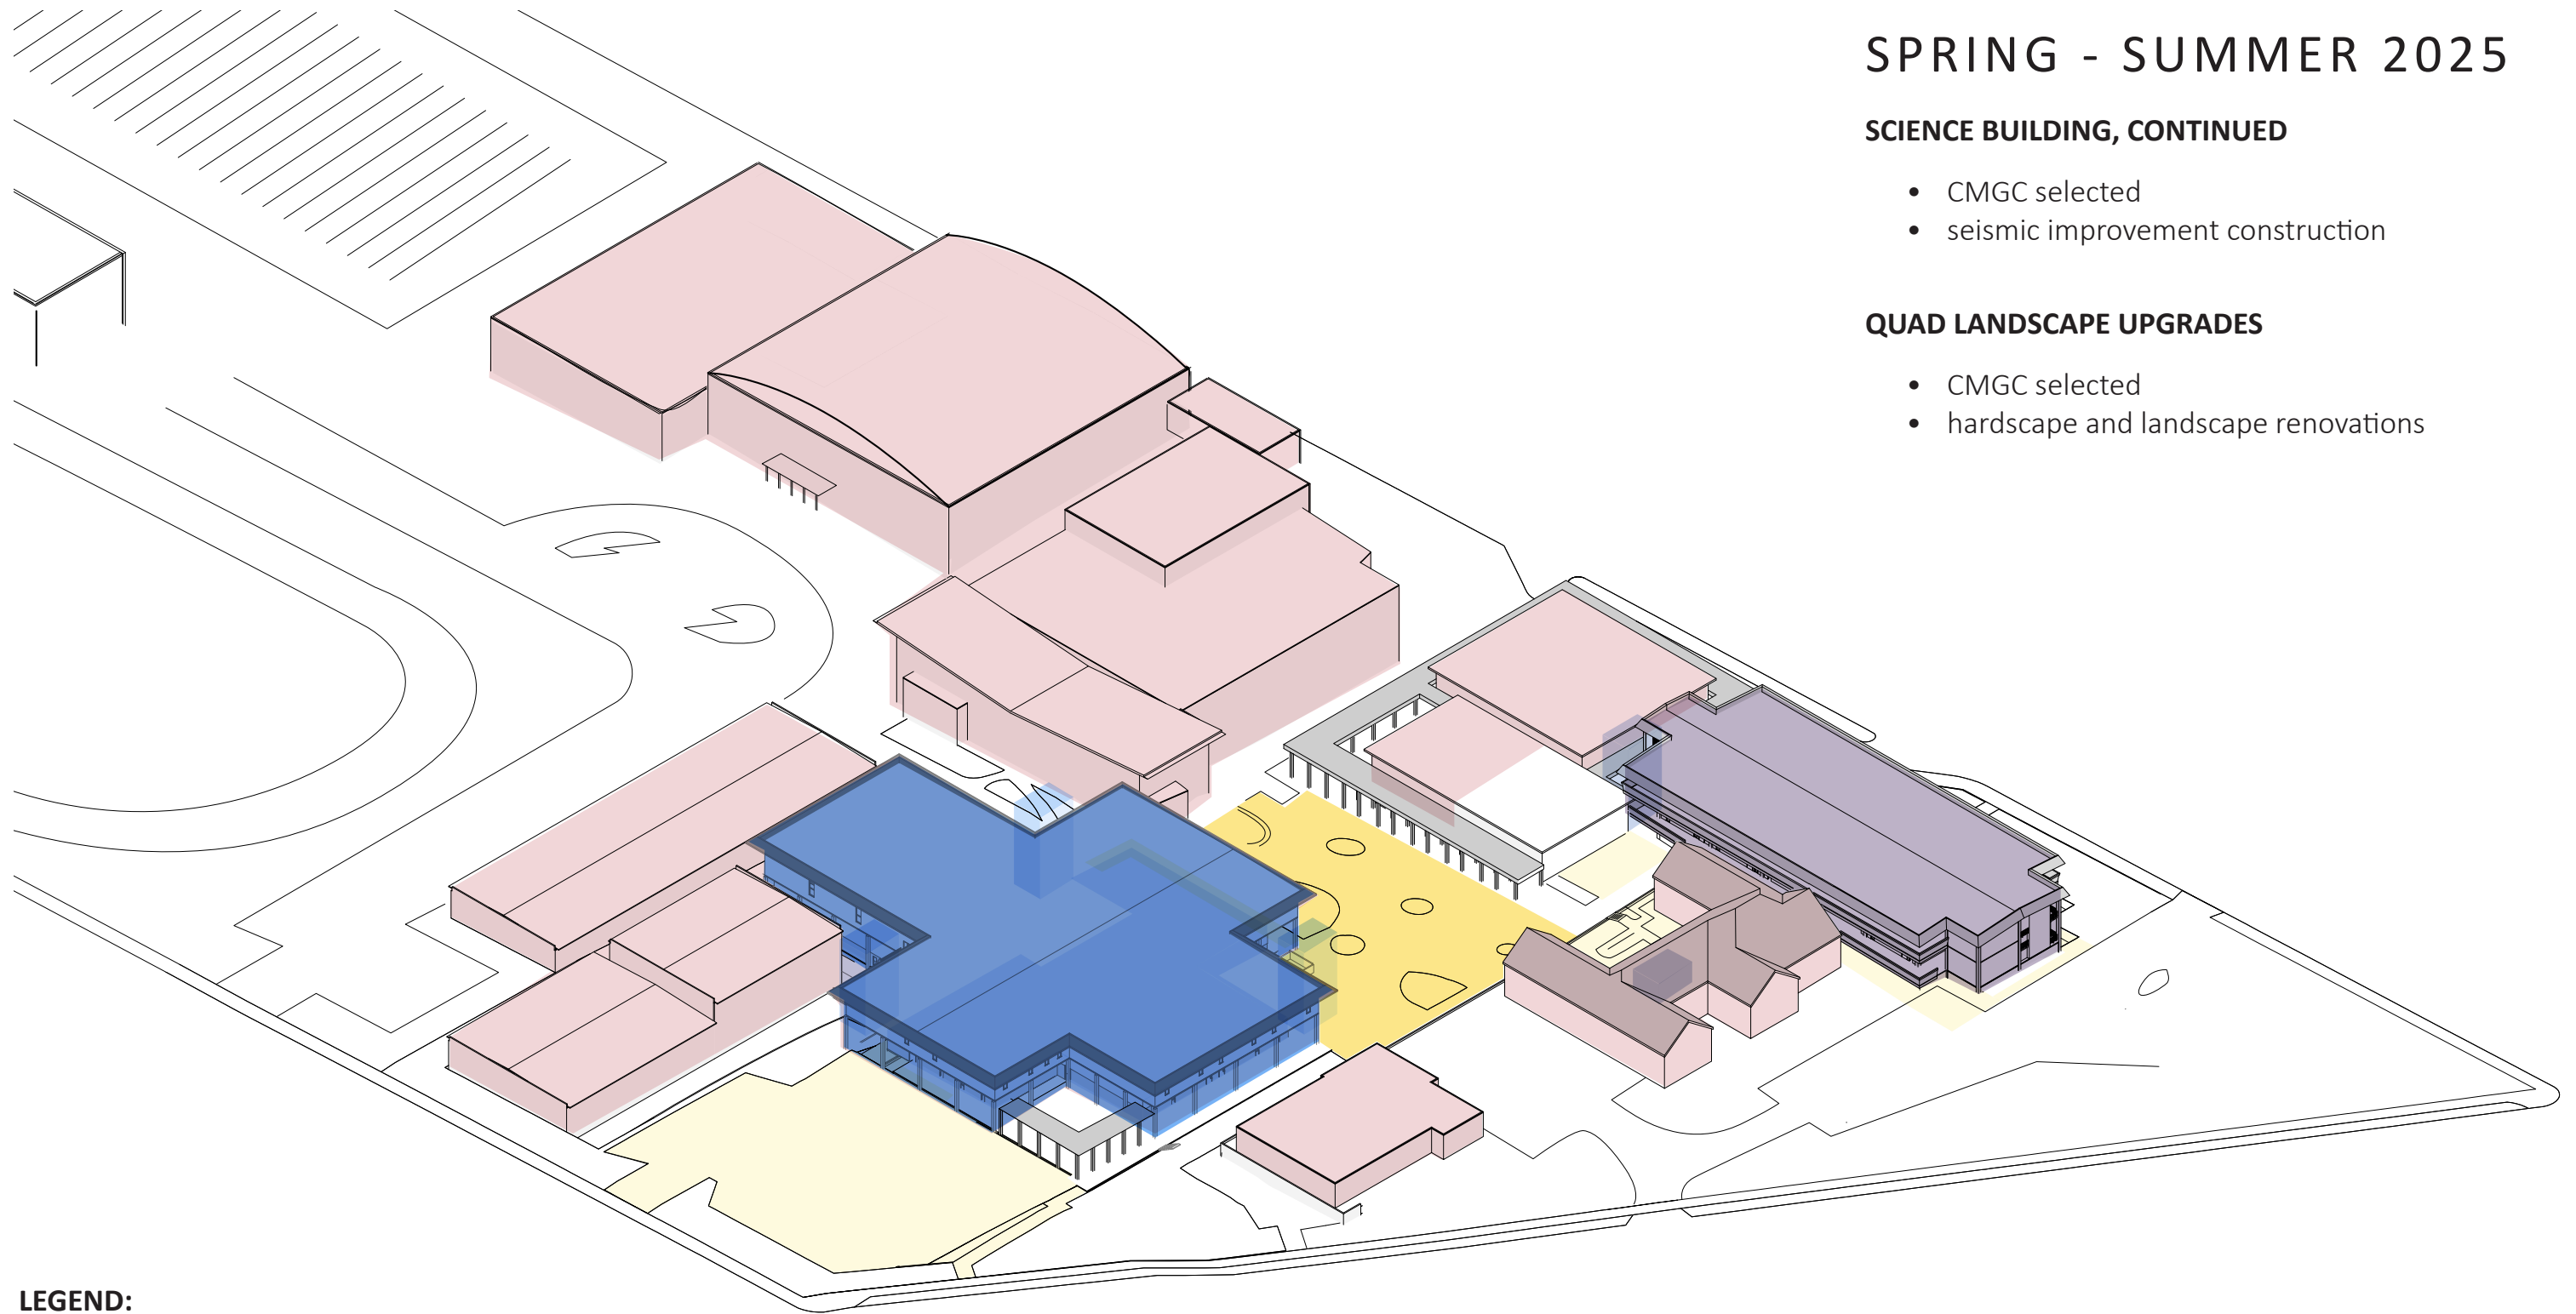- CMGC selected
- hardscape and landscape renovations




### LEGEND:

-  site work
-  building structure & systems
-  fire alarm




# AHS SCIENCE SOLAR CANOPY STUDY

## 201 S MOUNTAIN AVE

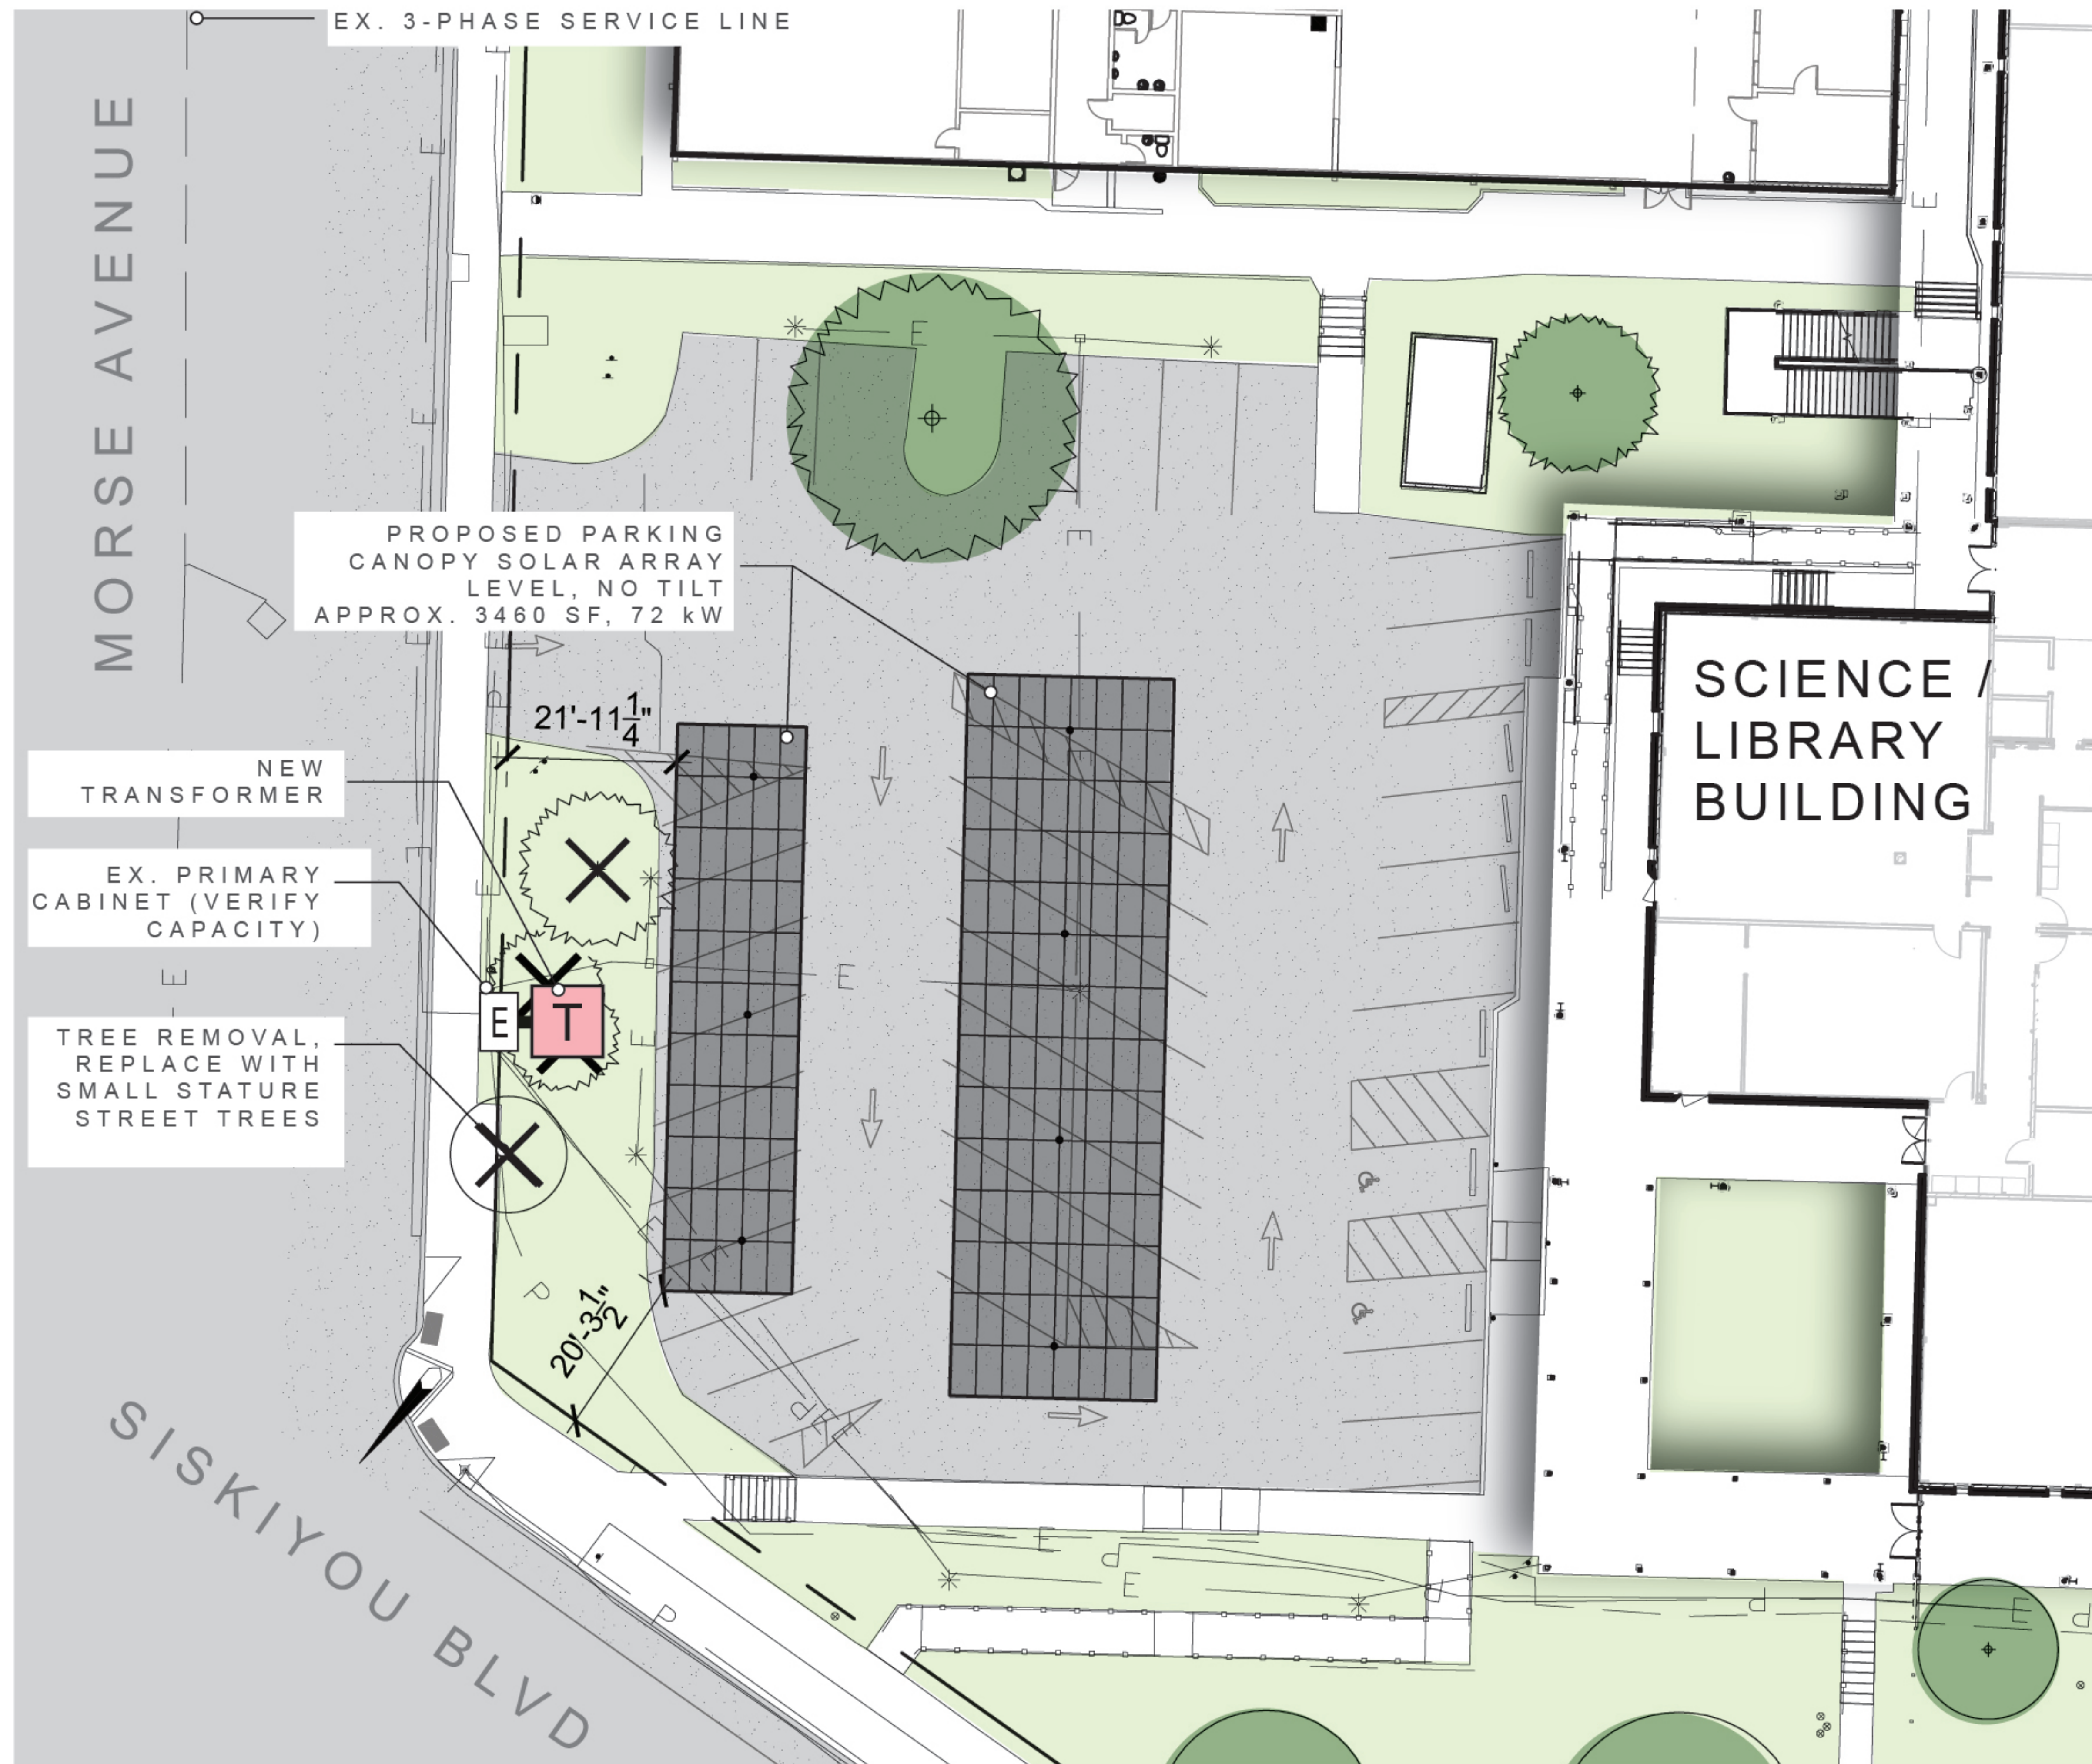

Conceptual Rendering

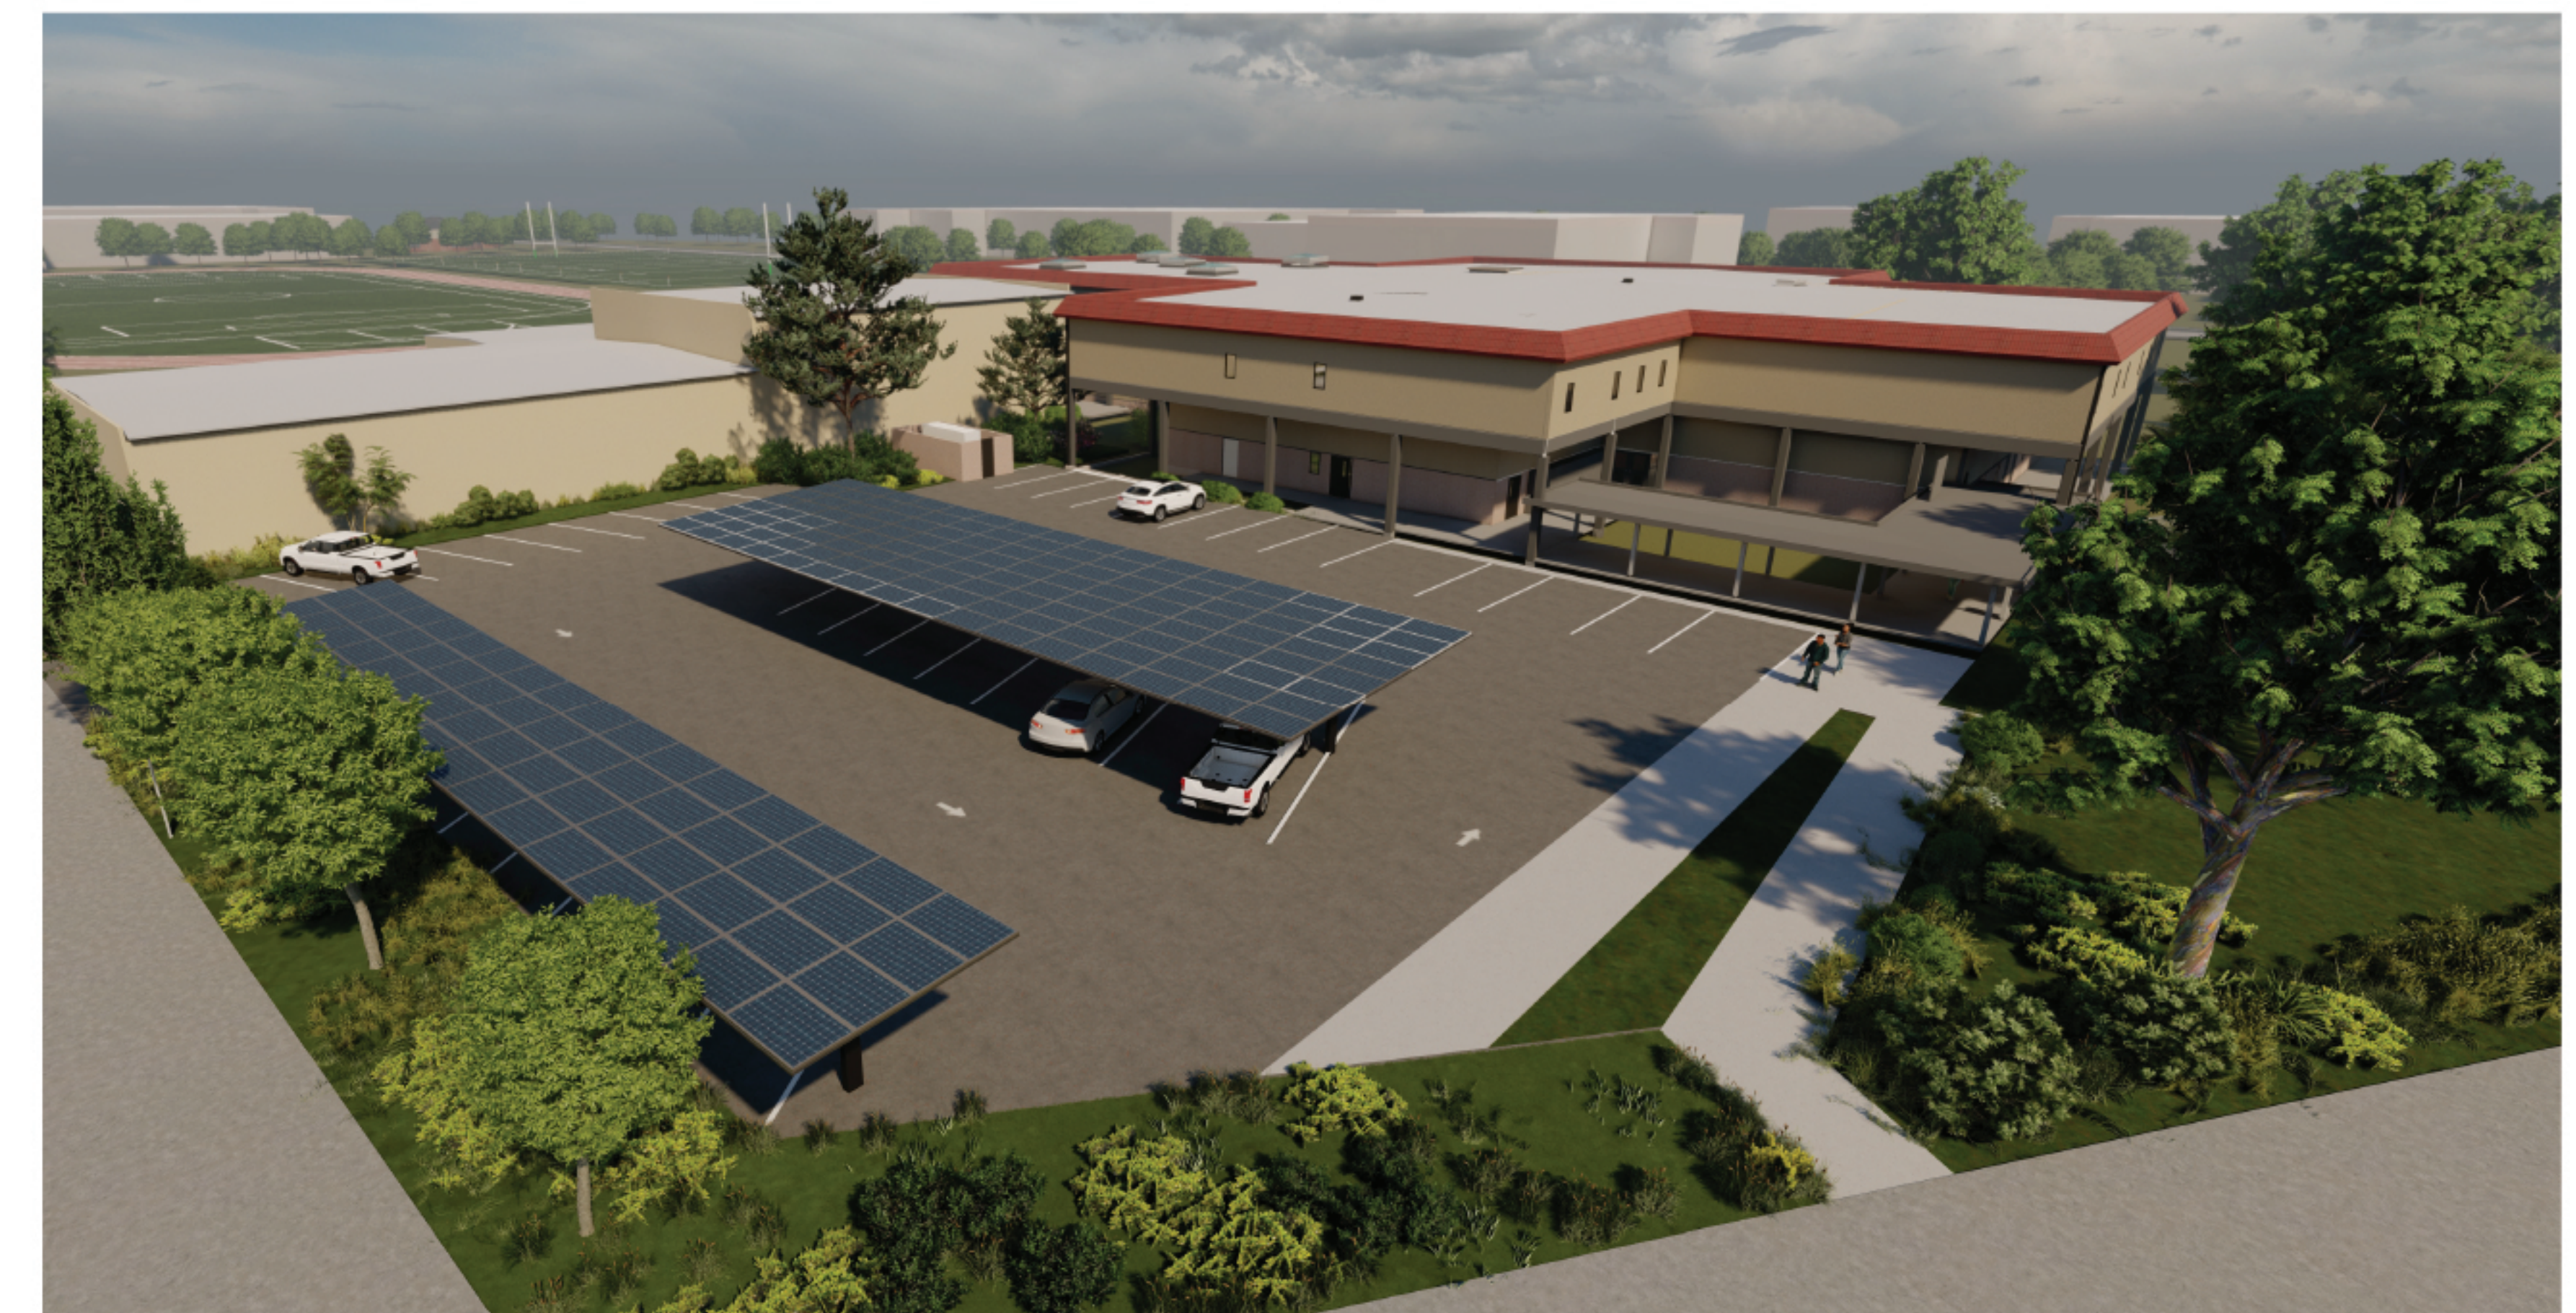

Conceptual Rendering

Conceptual Site Plan




### SUMMARY

- approximately 72 kW
- simple system, minimal trenching
- shade for cars
- new transformer
- parking lot lighting redesign
- educational
- historic commission approval needed




# ASD MAINTENANCE YARD SOLAR STUDY


## 212 WALKER AVE

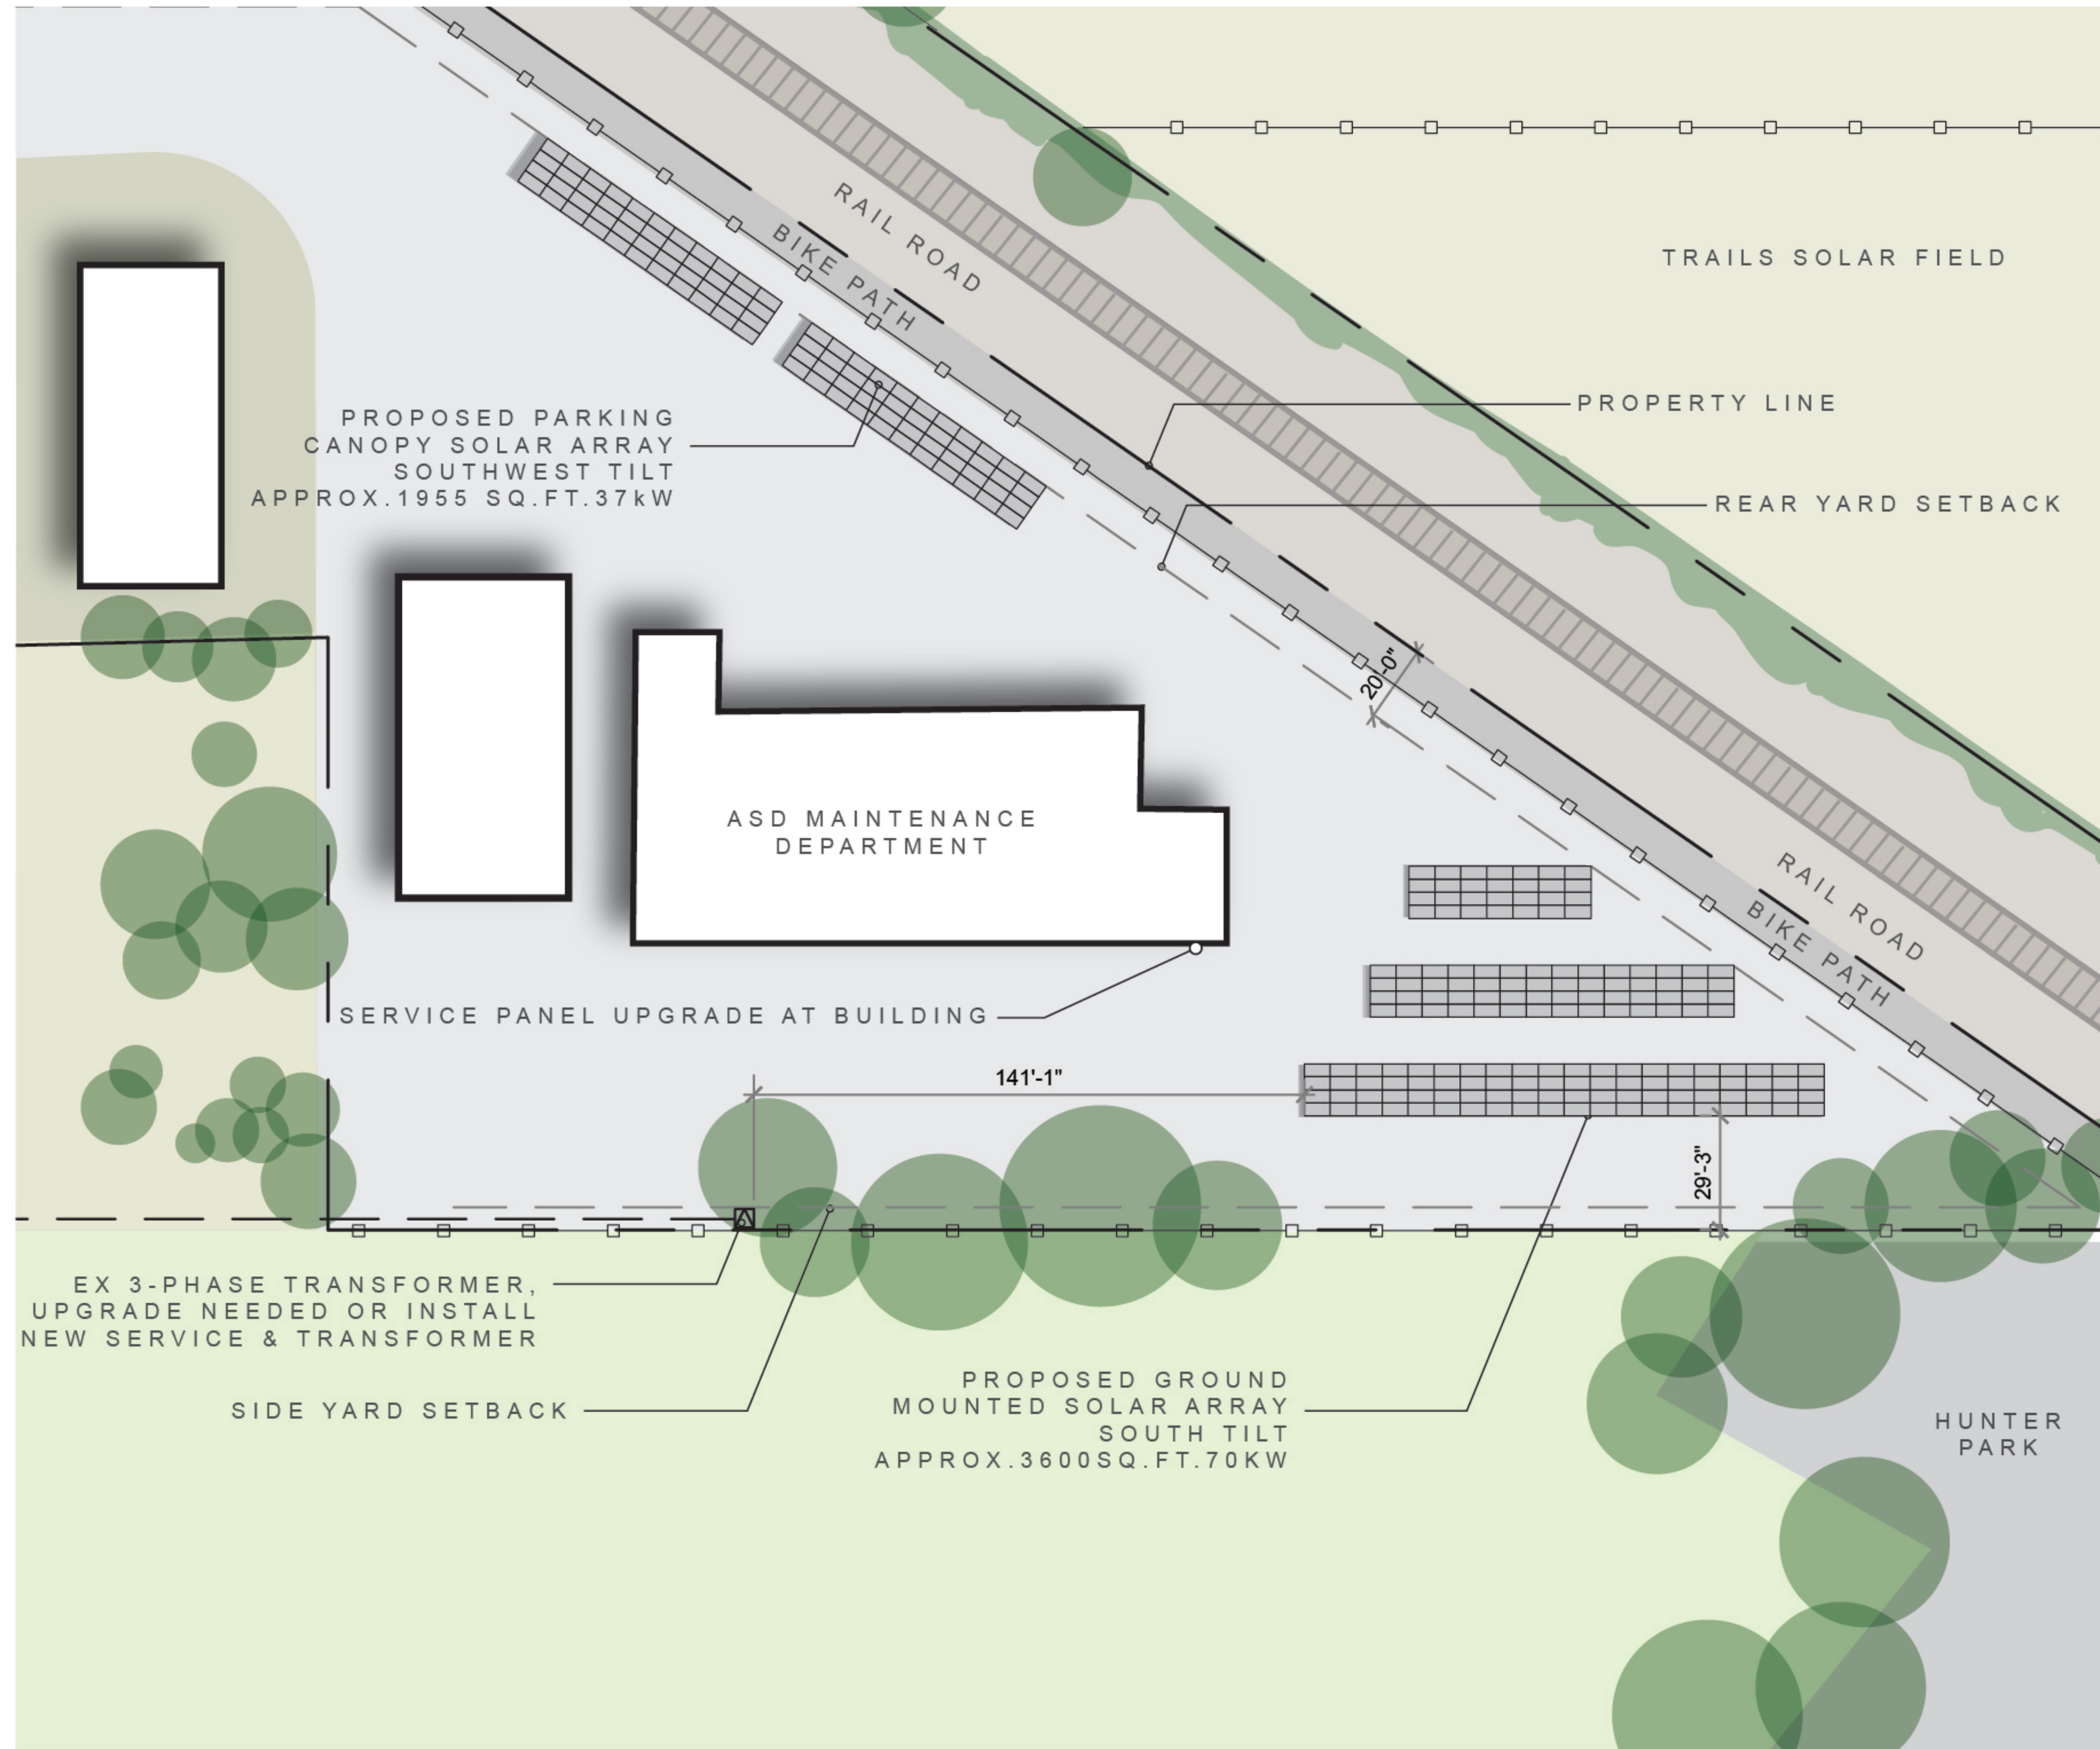

Conceptual Site Plan

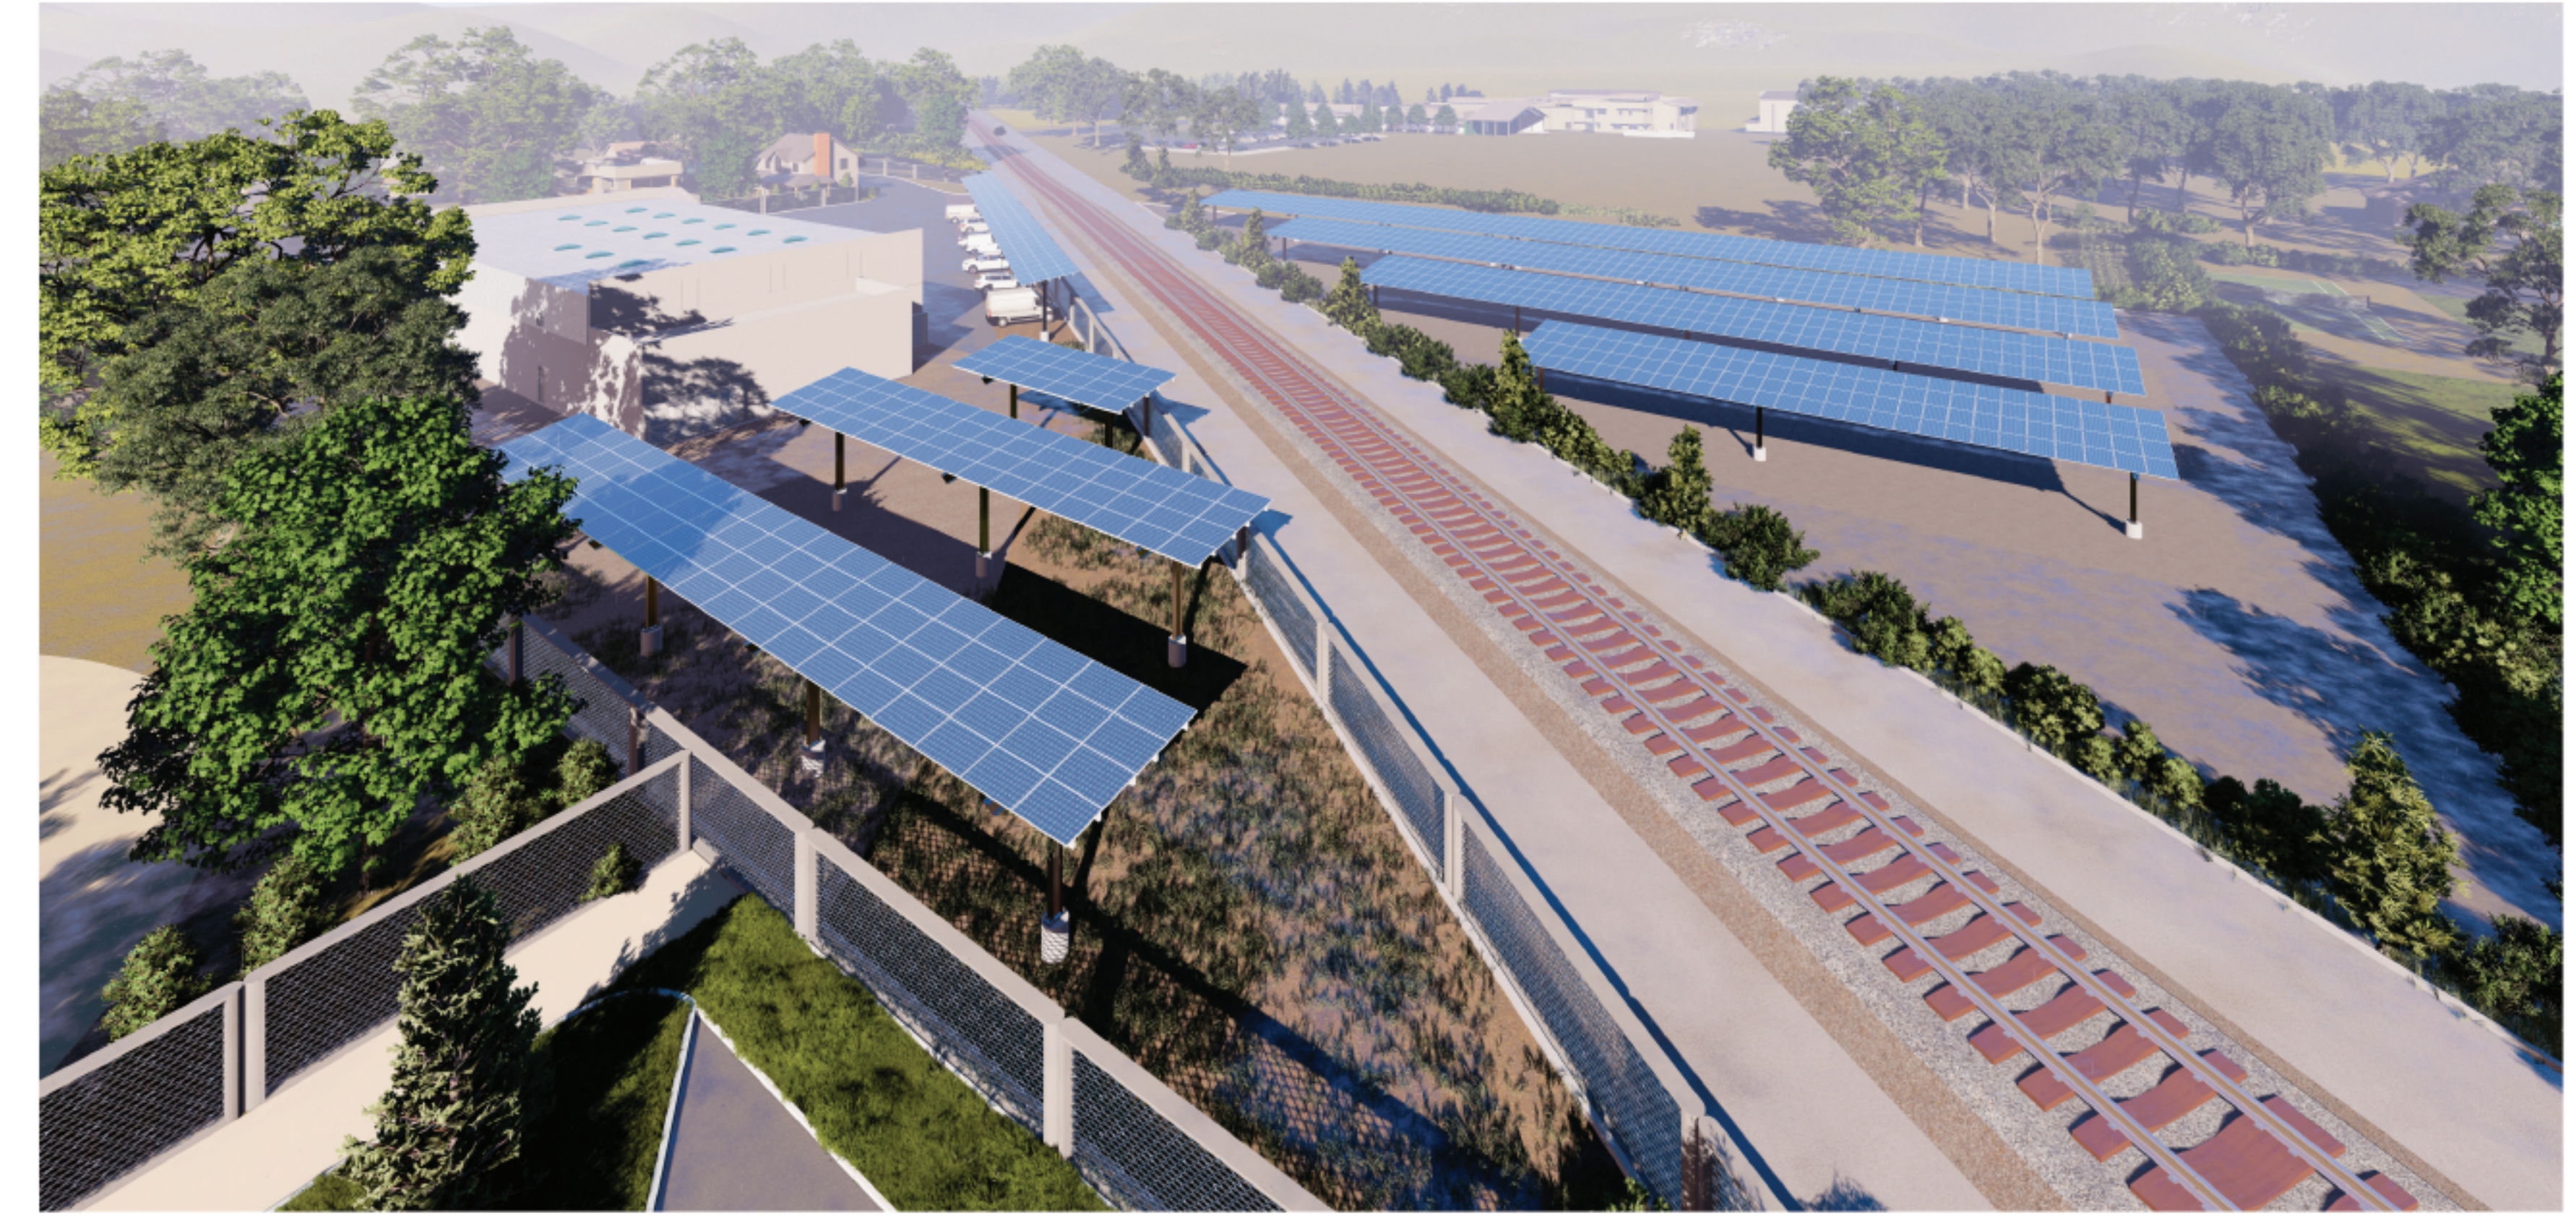

Conceptual Rendering

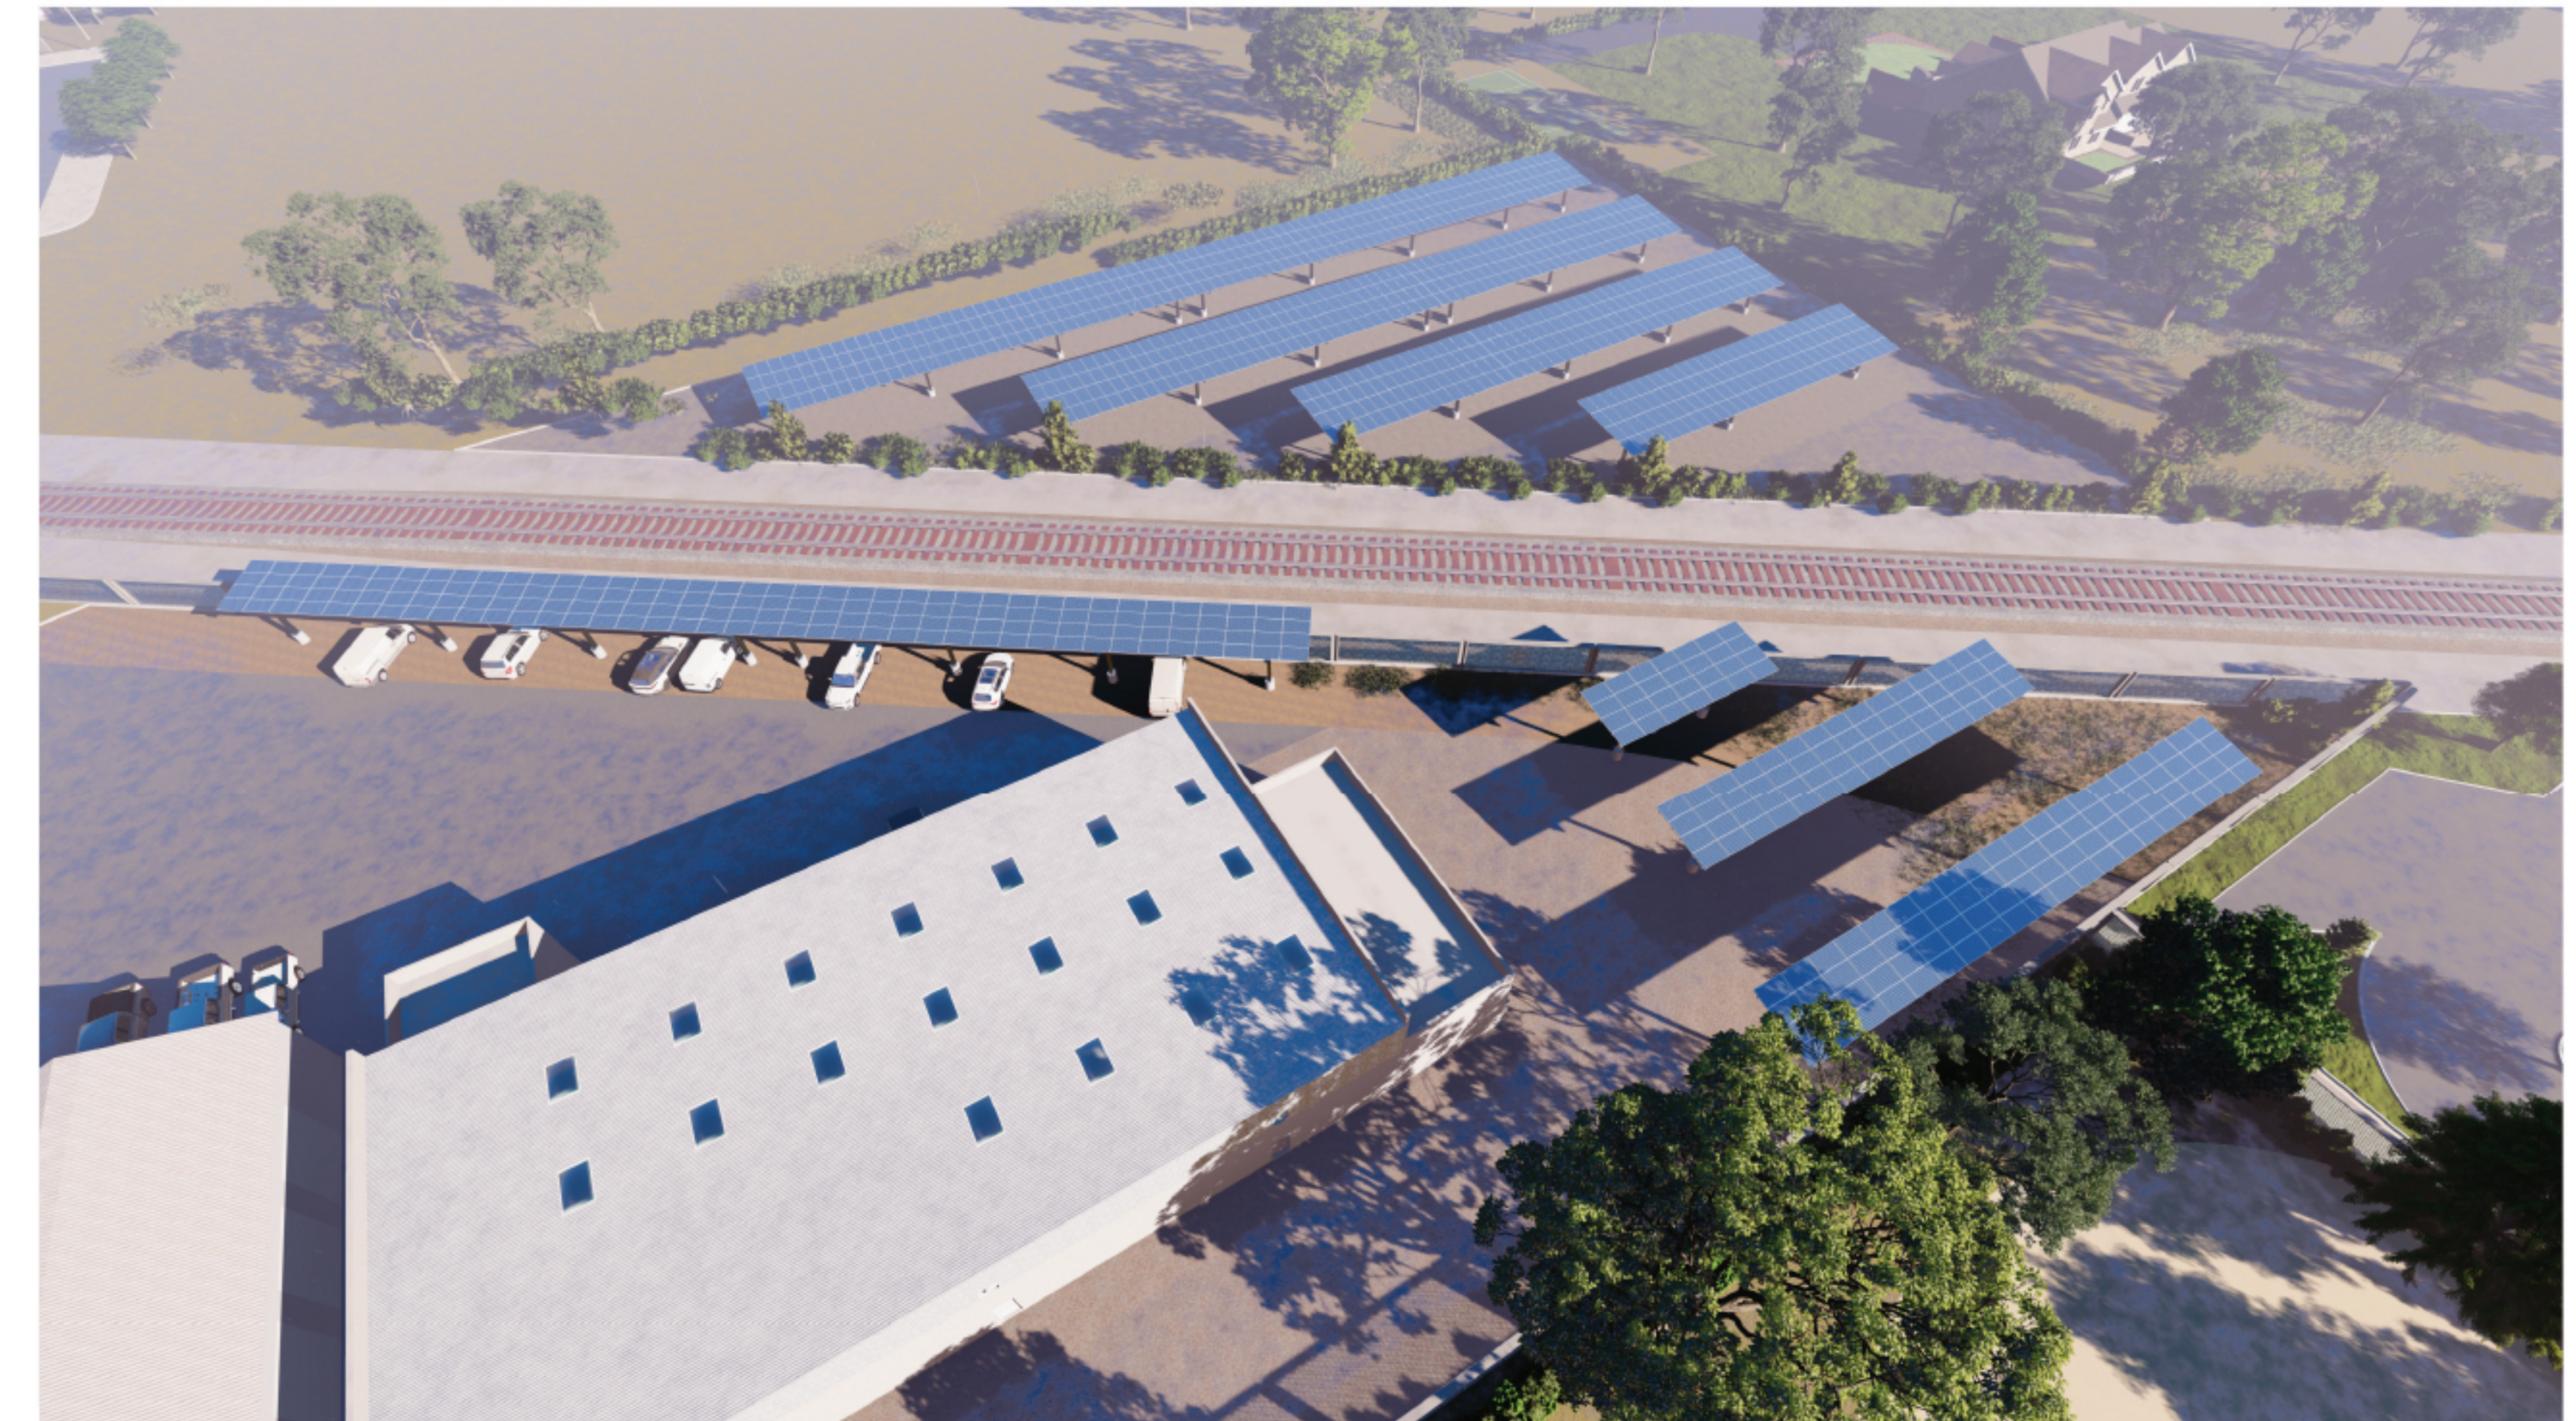

Conceptual Rendering



### SUMMARY

- approximately 107 kW
- new service & transformer recommended
- upgrade building service panel to handle PV size
- long trenching runs increases cost and reduces efficiency
