

Status of Bond Projects

6/9/2020 Governing Board Meeting

President Day, Vice President Cox Golder, Board Members and Superintendent Jaeger, it is my pleasure to provide you with an update of the projects currently under construction with bond and SFB funding.

AHS:

Bonds Projects

Asphalt repairs – parking lot & baseball field	\$18,624
- 80% complete	
- remainder to be completed 8/3 & 8/4	
Library renovation 100% complete	\$348,393

SFB Projects

300 wing – structural evaluation – assessment in progress	\$9,910
AHS main gym roof replacement	\$30,253
- supplemental design award received 7/1	

CDO:

Bond Projects

Main Switchgear Modernization – 100% complete	\$187,486
T Building – fan coil improvements – construction in progress	\$116,672
- will be complete week of July 6 th	
Replacement of east parking lot lights – awaiting materials	\$11,454
Addition of snack bar / air conditioner – contractor ordering materials	\$18,908
M & T Building underground pipe replacement	\$54,566
- excavation complete – installing new pipe	
- will be complete week of July 6 th	


SFB Projects

Campus roofing phase I

\$2,662,679

- Bldg E - 90% complete
- Bldg JE - 90% complete
- Bldg JW - 90% complete
- Bldg J - 90% complete
- Bldg K - 80% complete
- Bldg D - 85% complete
- Bldg S - 90% complete

Campus roofing phase II - bids due 7/7

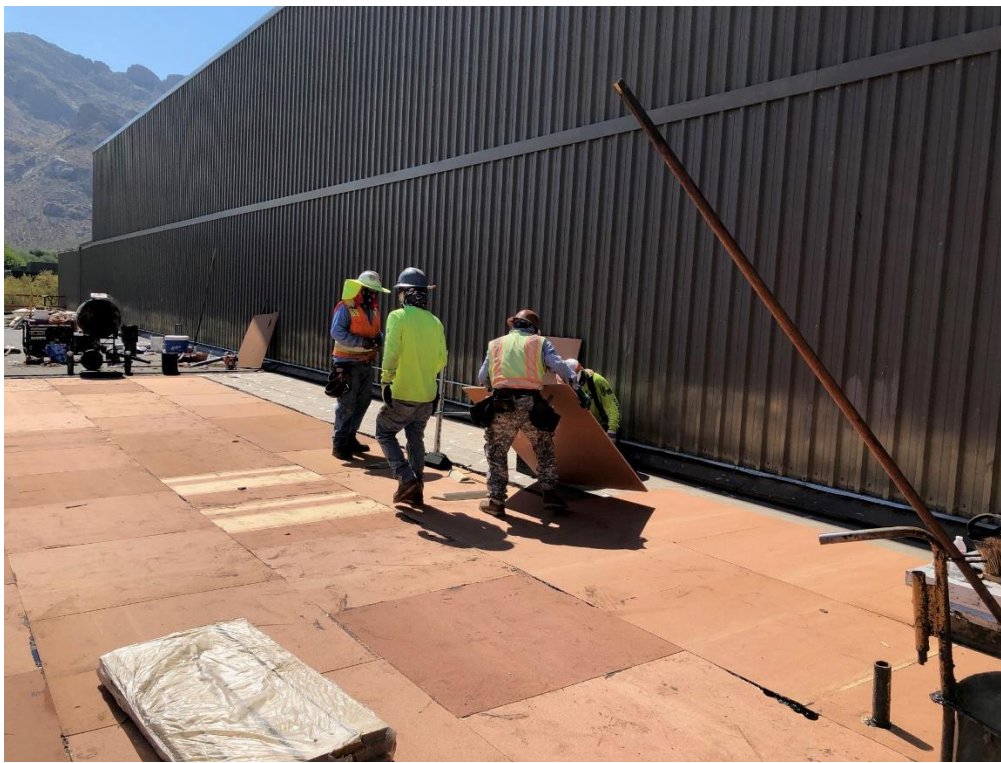

IRHS:

Bond Projects

ADA parking lot improvements – 100% complete	\$77,912
ADA shower faucets – locker rooms 100% complete	
OCR repairs for ADA science tables – 90% complete	\$29,544
OCR repairs for trainer's room – 100% complete	\$26,192

SFB Projects

Roofing – Bldg A – 85% complete	\$4,272,241
Bldg F – 10% complete	

AMS:

Bond Projects

PA System improvements – working on punch list items	\$109,382
Maker Space- room 806 B - 100% complete	\$25,877
Weight room to woodshop improvements – 100% complete	\$14,384
MPR restroom vent repair - in progress – 100% complete	\$6,128
MPR restroom wall repairs – 100% complete	\$6,968



Copper Creek:

Bond Projects

Central plant chiller replacement - construction- 100% complete	\$198,756
Design for staff RR remodel / special needs RR - design 95% complete	\$7,500
Administration boiler replacement – 100% complete	\$10,261
Nurses office water fountain / bottle filler – 100% complete	\$4,639



Coronado:

Bond Projects

Exterior lighting fixture replacement – materials on order	\$15,755
Exterior paint improvements - elementary bldgs. - 100% complete	\$31,530
Admin Bldg – (2) A/C unit replacements – installation date 7/3	\$20,991
Elementary Bldg A/C replacement – units ordered – start date 7/13	\$96,775
East side security fence re-painting – in progress – 80% complete	\$7,058
Retrofit electric panel – room 24 – P.O. received – materials on order	\$2,588

SFB Projects

SFB 4854 MPR building roof replacement – 90% complete - roof coating to start 7/9	\$403,519
--	-----------

Cross:

Bond Projects

Maker Space- room 403 – 100% complete

\$17,623



SFB Projects

MPR HVAC replacement – HVAC - units operating– 90% complete \$252,674

Roof replacement – assessment report received – punch list walk 7/7 \$8,205

T.E.P. Grant - LED lighting upgrades



Donaldson:

Bond Projects

Building E - HVAC controls – construction begins 7/6	\$9,708
Building E - interior ceiling repaint – P.O. issued	\$5,163
Roof restoration - E pod – 100% complete	\$6,673
Classroom lighting – Building E – materials on order	\$22,413
HVAC replacement – Building E – await scheduling	\$36,043

El Hogar:

Bond Projects

Exterior painting, add exterior sink / bottle filler – start date 7/6	\$24,455
---	----------

Harelson:

Bond Projects

Mechanical hot water replacement/ Phase I – 100% complete	\$3,120
Maker Space – room 7 B – 60% complete – completion date 7/6	\$18,962

SFB Projects

SFB 3508/5563 Funhouse roof & HVAC	\$577,230
- HVAC 75% complete	
- roof replacement in progress – 90% complete	



Holaway:

Bond Projects

Maker Space - room 19 – 100% complete	\$20,562
Admin - HVAC replace (4) units – construction week of 7/6	\$35,557
West side security fence improvements – 100% complete	\$39,204
West side security fence painting – start date 7/6	\$5,188
Hallway lighting improvements – 100% complete	\$6,200

Keeling:

Bond Projects

Access control improvements – new card readers, additional card readers, and new lock down button – awaiting schedule	\$32,281
Replace (3) A/C units on Bldg G – contractor ordering materials	\$39,675

La Cima:

Bond Projects

Exterior door replacement – 100% complete	\$3,533
Central plant chiller compressor replacements – 100% complete	\$132,293



Mesa Verde:

Bond Projects

MPR A/C replacement – Construction week of 7/6 \$28,835

SFB Projects

Roof replacement – design grant approved by SFB 6/24 \$42,450

T.E.P. Grant - LED lighting upgrade



Nash:**Bond Projects**

Access control improvements - new card readers, additional card readers
and new lockdown button – 100% complete \$36,775

Prince:**Bond Projects**

Maker Space – rooms 19-20 – 100% complete \$17,435
Classrooms 21-25 – flooring improvements - 100% complete \$32,610
room 25 – 100% complete room 22 100% complete
room 23 complete room 21 completed by 7/3
room 24 completed by 7/10
Access control improvements - new card readers, additional card
readers and new lockdown button – 100% complete \$39,588

Rillito	\$42,570	Balance	\$24,832
----------------	-----------------	----------------	-----------------

Bond Projects

Greenhouse improvements – 100% complete \$16,875
Sensory room improvements – 100% complete
- new sign in front of the school – 100% complete
New water fountain / bottle filler - 100% complete \$2,775

SFB Projects

SFB 4850 campus roofing – start date 7/13 \$250,124

Rio Vista	\$79,440	Balance	\$26,224
------------------	-----------------	----------------	-----------------

Bond Projects

Smoke detector replacement – Building C – 100% complete \$10,700
MPR A/C/ replacement – 100% complete \$35,994

Walker	\$115,431	Balance	\$21,574
---------------	------------------	----------------	-----------------

Bond Projects

Pre-K building AC replacement – 100% complete	\$41,261
Access control improvements –100% complete	\$6,010
A/C replacement – computer room – materials on order	\$31,169

SFB Projects

Classroom 14 HVAC replacement – grant request submitted 6/12	\$9,959
- structural report being prepared	

*SOMETHING NEW AT EVERY SCHOOL,
EVERY YEAR!*
