


# **Bond Program Update**

**Lee Raspberry**  
**Director of Construction & Planning**  
**May 13, 2025**



# Adelton Elementary

- Schedule: June 2024 – August 2025
- New 105,000 SF School
- Dry utilities complete
- Parking area final lift of asphalt early June
- HVAC units set
- Exterior curtain wall (glass) 60% complete
- Permanent address issued - 119 Blume Dr., Bastrop, TX 78602
- On Schedule

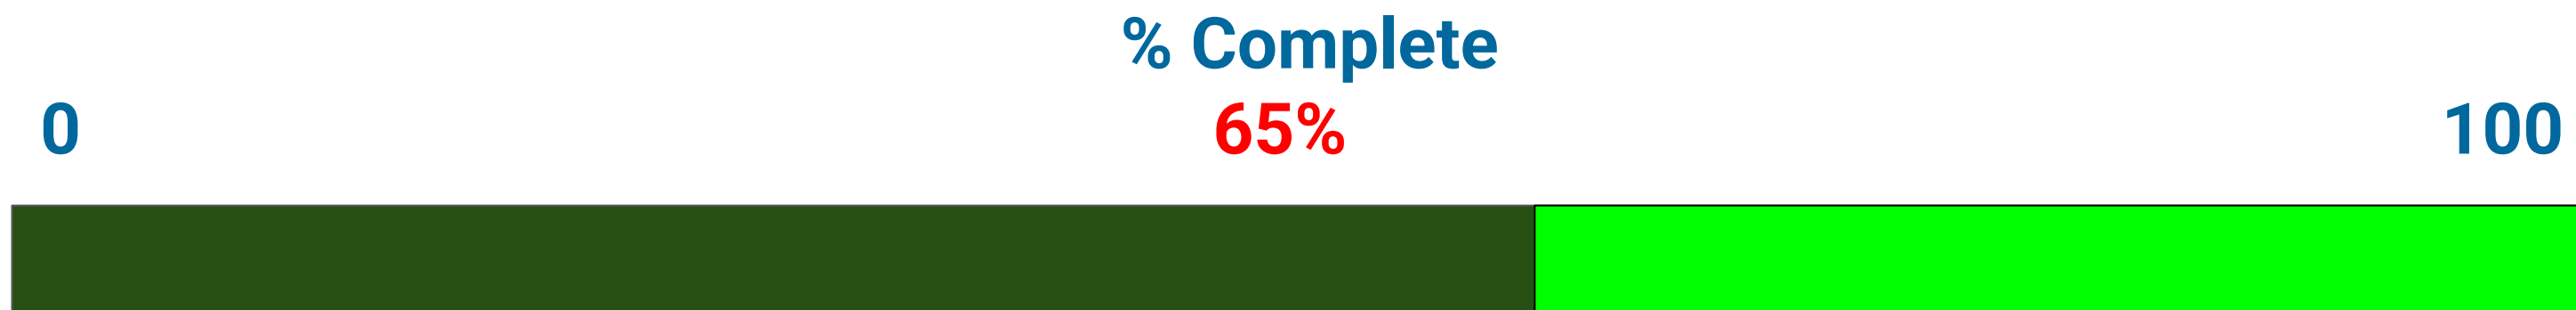
















# Mina Elementary Phase 2

- Schedule: Jan. 2025 – May 2026
- Approximately 35,500 SF Facility
- 1st phase demo complete
- Building pad complete
- Plumbing/electrical rough-in complete
- Concrete pour area “B” complete
- On Schedule

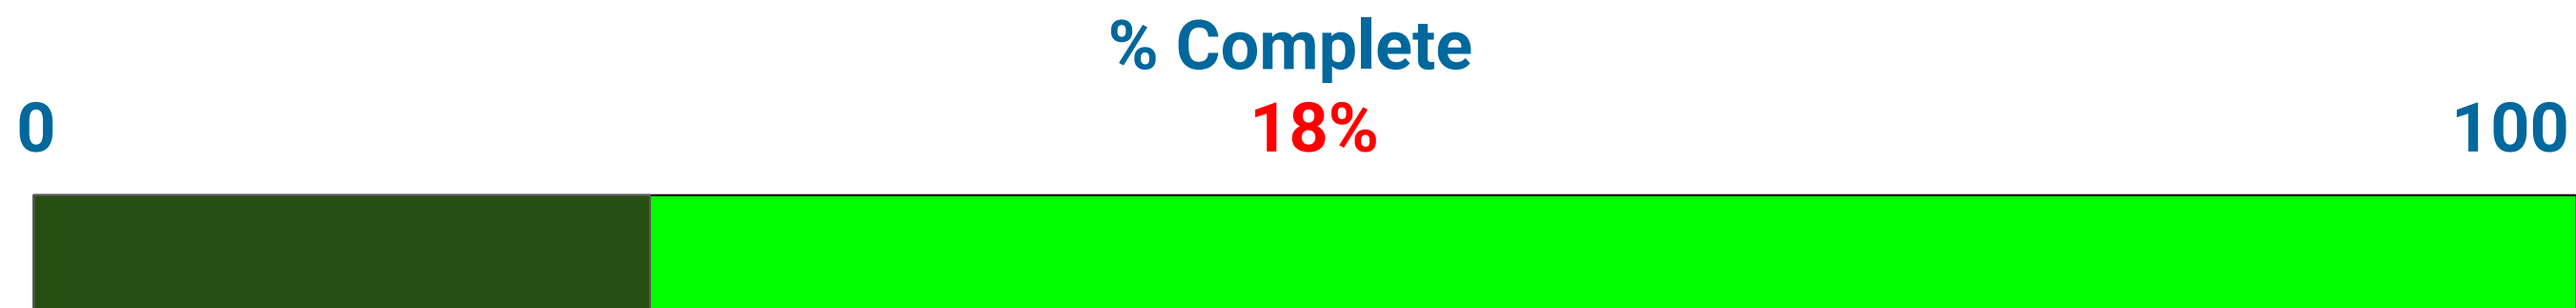







# Elementary Playgrounds & Furniture

- Schedule: May 2025 – Aug. 2025
- Lost Pines, Emile, Bluebonnet, Cedar Creek and Red Rock
- Remove Fibar mulch and replace with PIP (pour in place rubber) fall protection
- Upgraded ADA accessibility & inclusivity for all students
- New shade structures at some locations
- New classroom furniture and/or cafeteria furniture
- On Schedule








# Bastrop & Cedar Creek MS

- Schedule: Dec. 2024 – Dec. 2025
- Approximately 21,000 SF additions
- Steel erection complete
- Exterior CMU walls complete
- Athletic field work to begin 5/15
- On Schedule

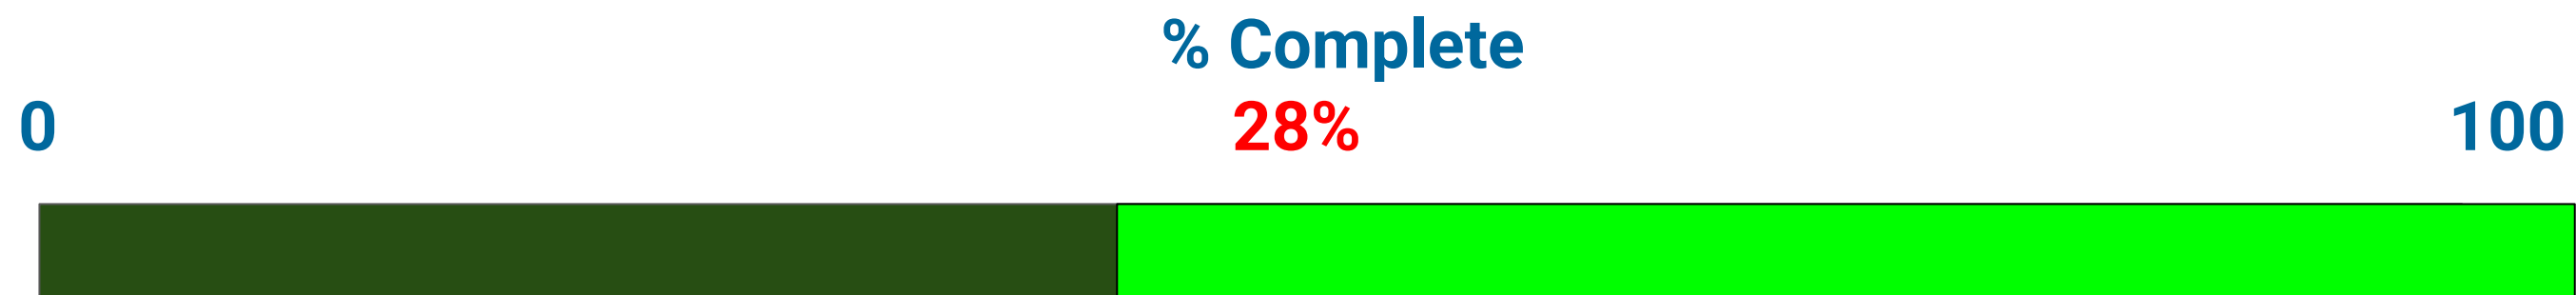



# Bastrop Middle School






# Cedar Creek Middle School





# Riverside Middle School

- Schedule: Oct. 2024 – Dec. 2025
- Approximately 60,000 SF addition
- 3rd phase of interior renovation complete
- New competition gym & Fine Arts addition underway
- On Schedule

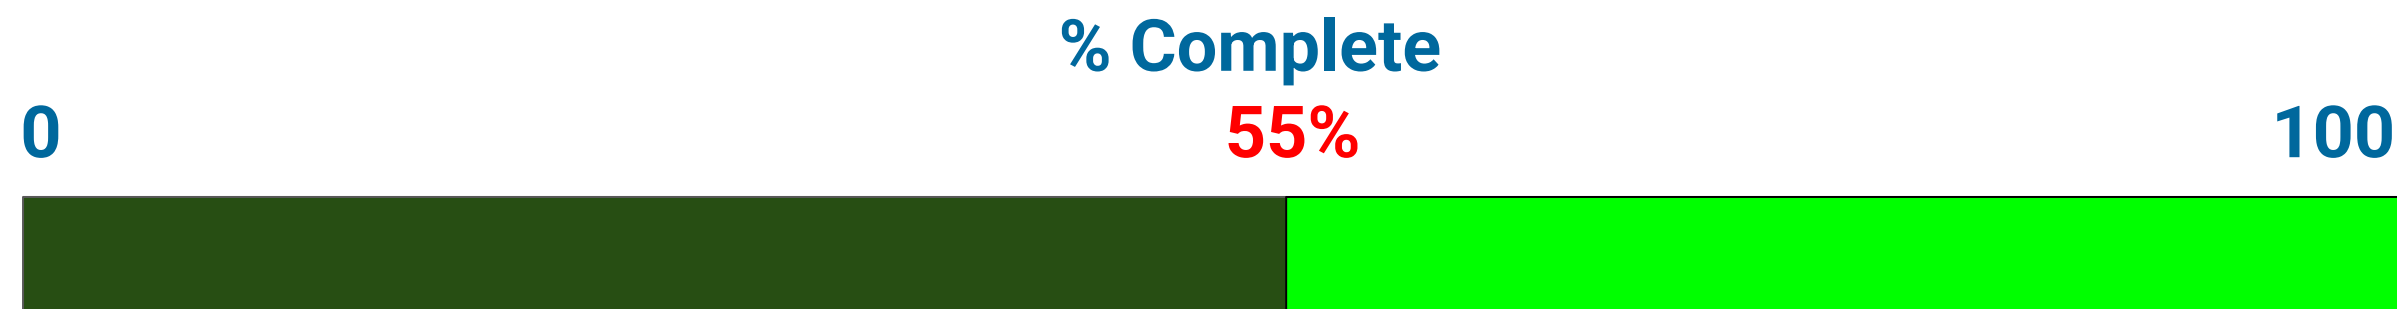












# Creekside Middle School

- Schedule: Oct. 2024 – Dec. 2025
- Approximately 60,000 SF addition
- 3rd phase of interior renovation complete
- New competition gym & Fine Arts addition underway
- On Schedule

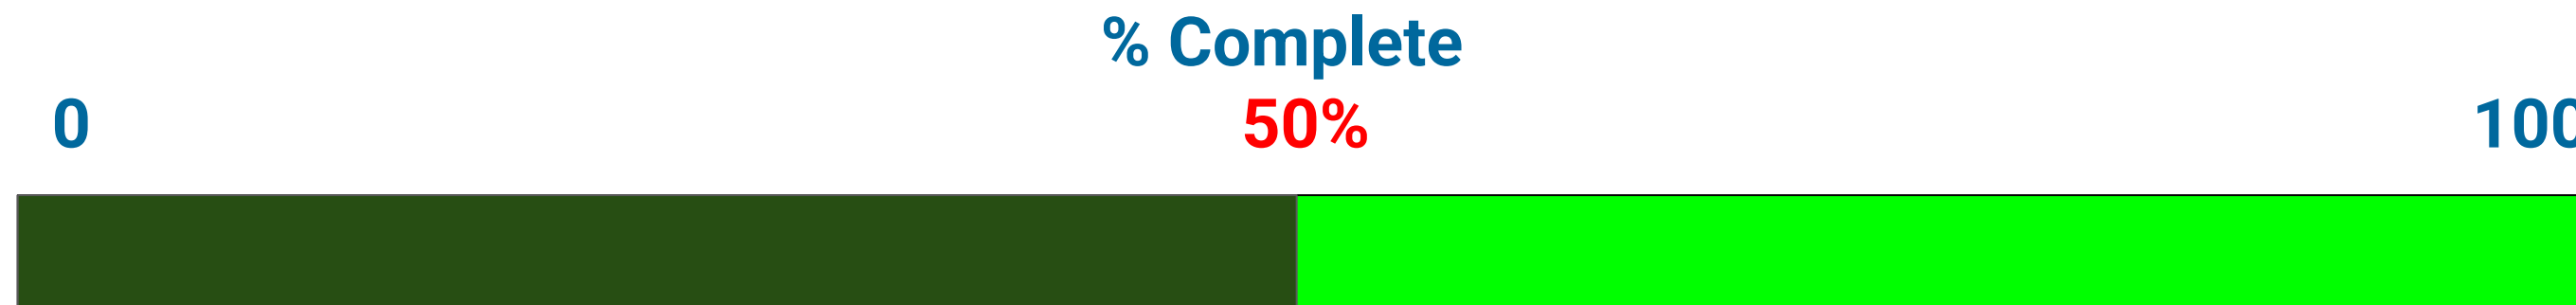










**Bastrop Independent School District | May 13, 2025**





# Bastrop High School

- Schedule: May 2025 - Dec. 2027
- Approximately 38,000 SF classroom addition in permitting phase
- New classroom wing & continued renovations
- Competition gym
- Dance studio
- Additional student parking
- Sitework permit issued 5/2/2025
- On Schedule

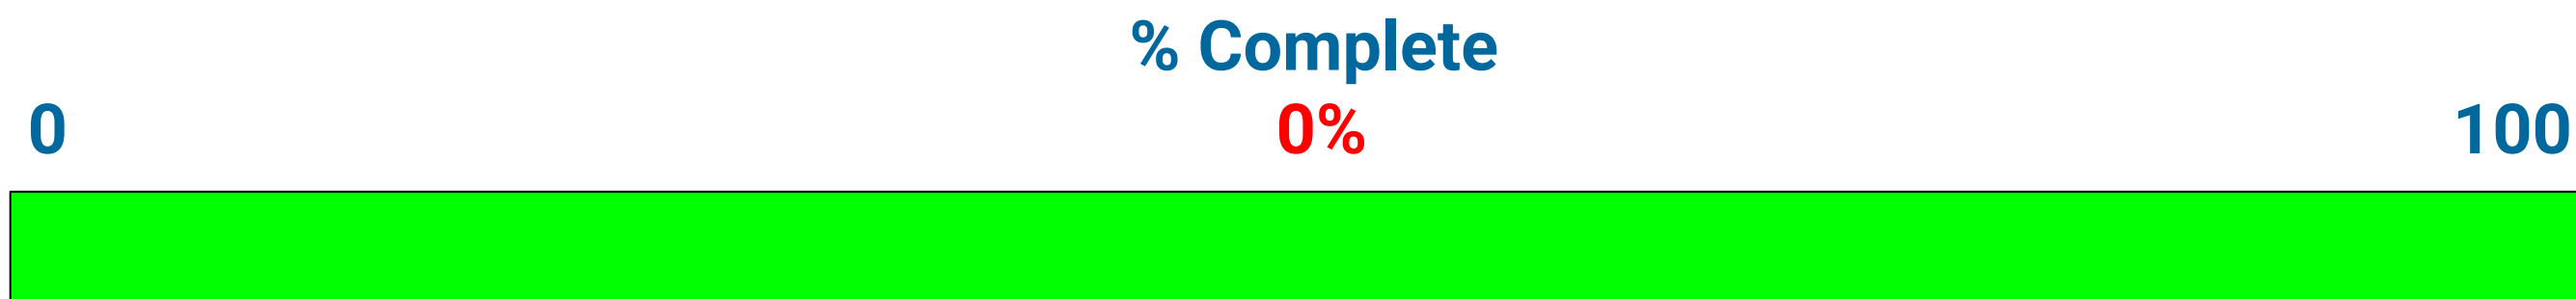












# Cedar Creek High School

- Schedule: Sept. 2024 – Dec. 2025
- Approximately 30,500 SF addition
- Structural steel complete
- 1st floor stud framing complete
- Sky Bridge connection complete
- 2nd floor decking complete
- On Schedule

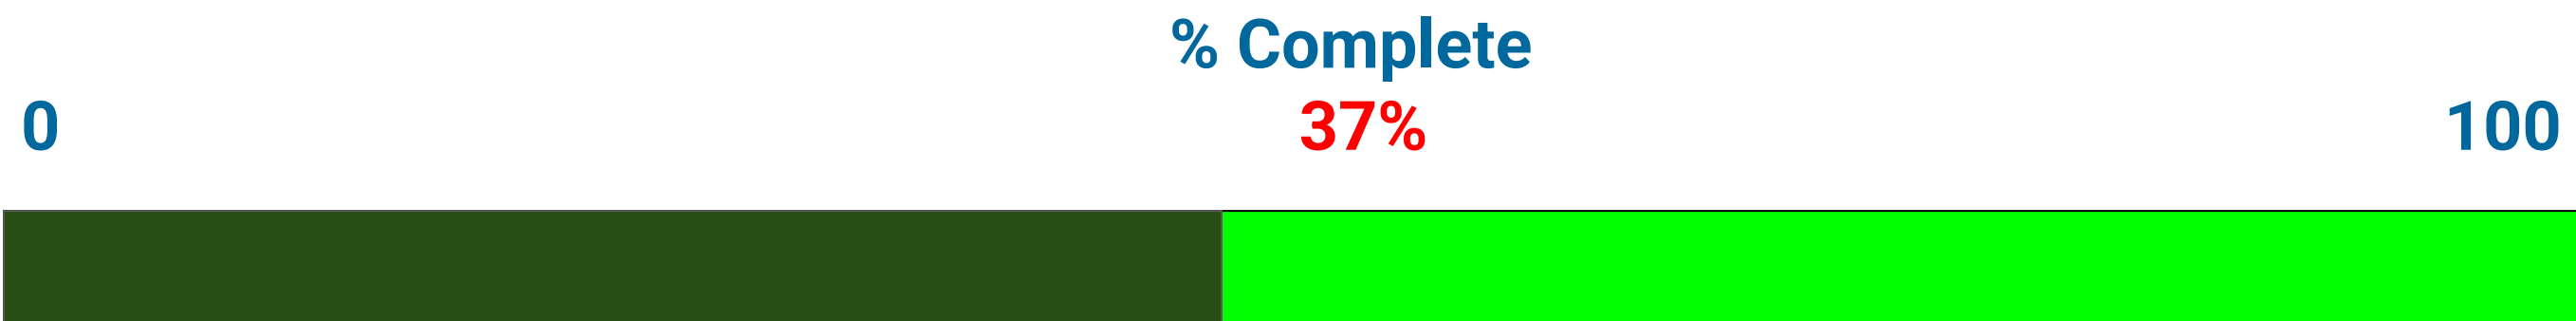









**Bastrop Independent School District | May 13, 2025**



# Gateway School

- **Schedule: Begin Fall 2025**
- **Addition of security vestibule**
- **Expansion of student/parent service area, food service area and nurses clinic**
- **Project currently in Design Development phase**
- **On Schedule**



# BISD Police & Operations

- Schedule: Jan. 2025 – Mar. 2026
- Approximately 55,000 SF Multi-Use Facility for maintenance, custodial, groundskeeping, warehouse, print shop, and police administration
- Permitting Complete - Construction underway
- Area “A” slab poured
- Area “B” grade beams & spread footings poured
- Ponds and parking areas rough graded
- Building steel erection to begin first week of June
- On Schedule

















**THANK YOU!**

**Are there any questions?**

