

Argyle Stadium

December 2025 Update

Site Photos



Site Photos



Site Photos



Interior Photos



Interior Photos




Site Photos



Interior Photos



Interior Photos

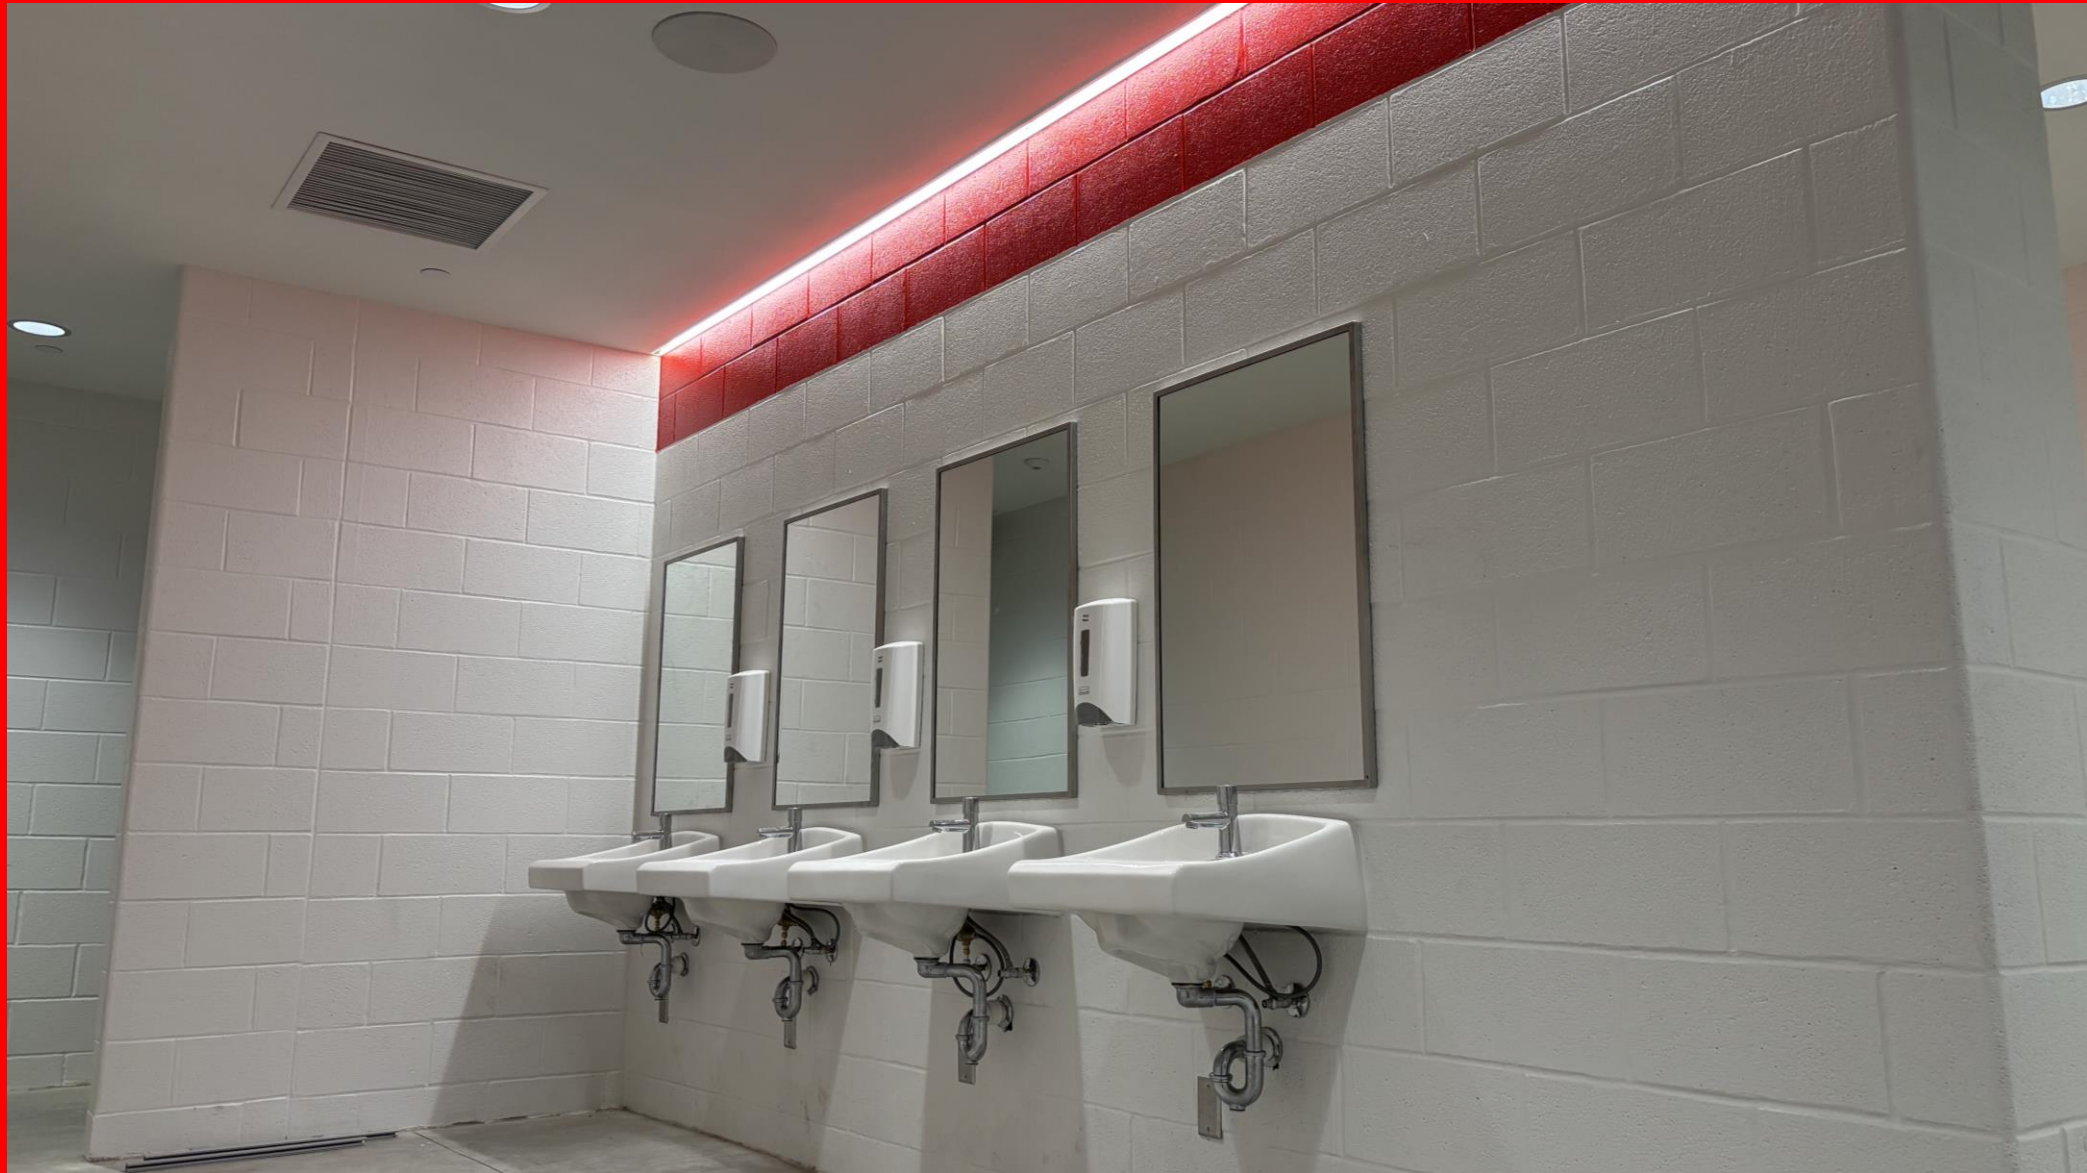

Interior Photos



Site Photos



Site Photos



Site Photos



Interior Photos



Look Ahead

- Testing Stadium Production System
- Press Box Interior Finishes
- Indoor Activity Center Turf
- Punch Walks



Key Milestones

Key Milestone Tracking

Town Permit Field Event Locations	September 5, 2024 January 1, 2025
Press Box Erection Begins IAC Erection Begins	March 2025 Spring 2025
Grandstand Install Interior Finishes	Fall 2025 Fall 2025
Substantial Completion	January 2025





Middle School #1

December 2025 Update

Site Photos



Site Photos



Site Photos




Site Photos



Interior Photos



Interior Photos

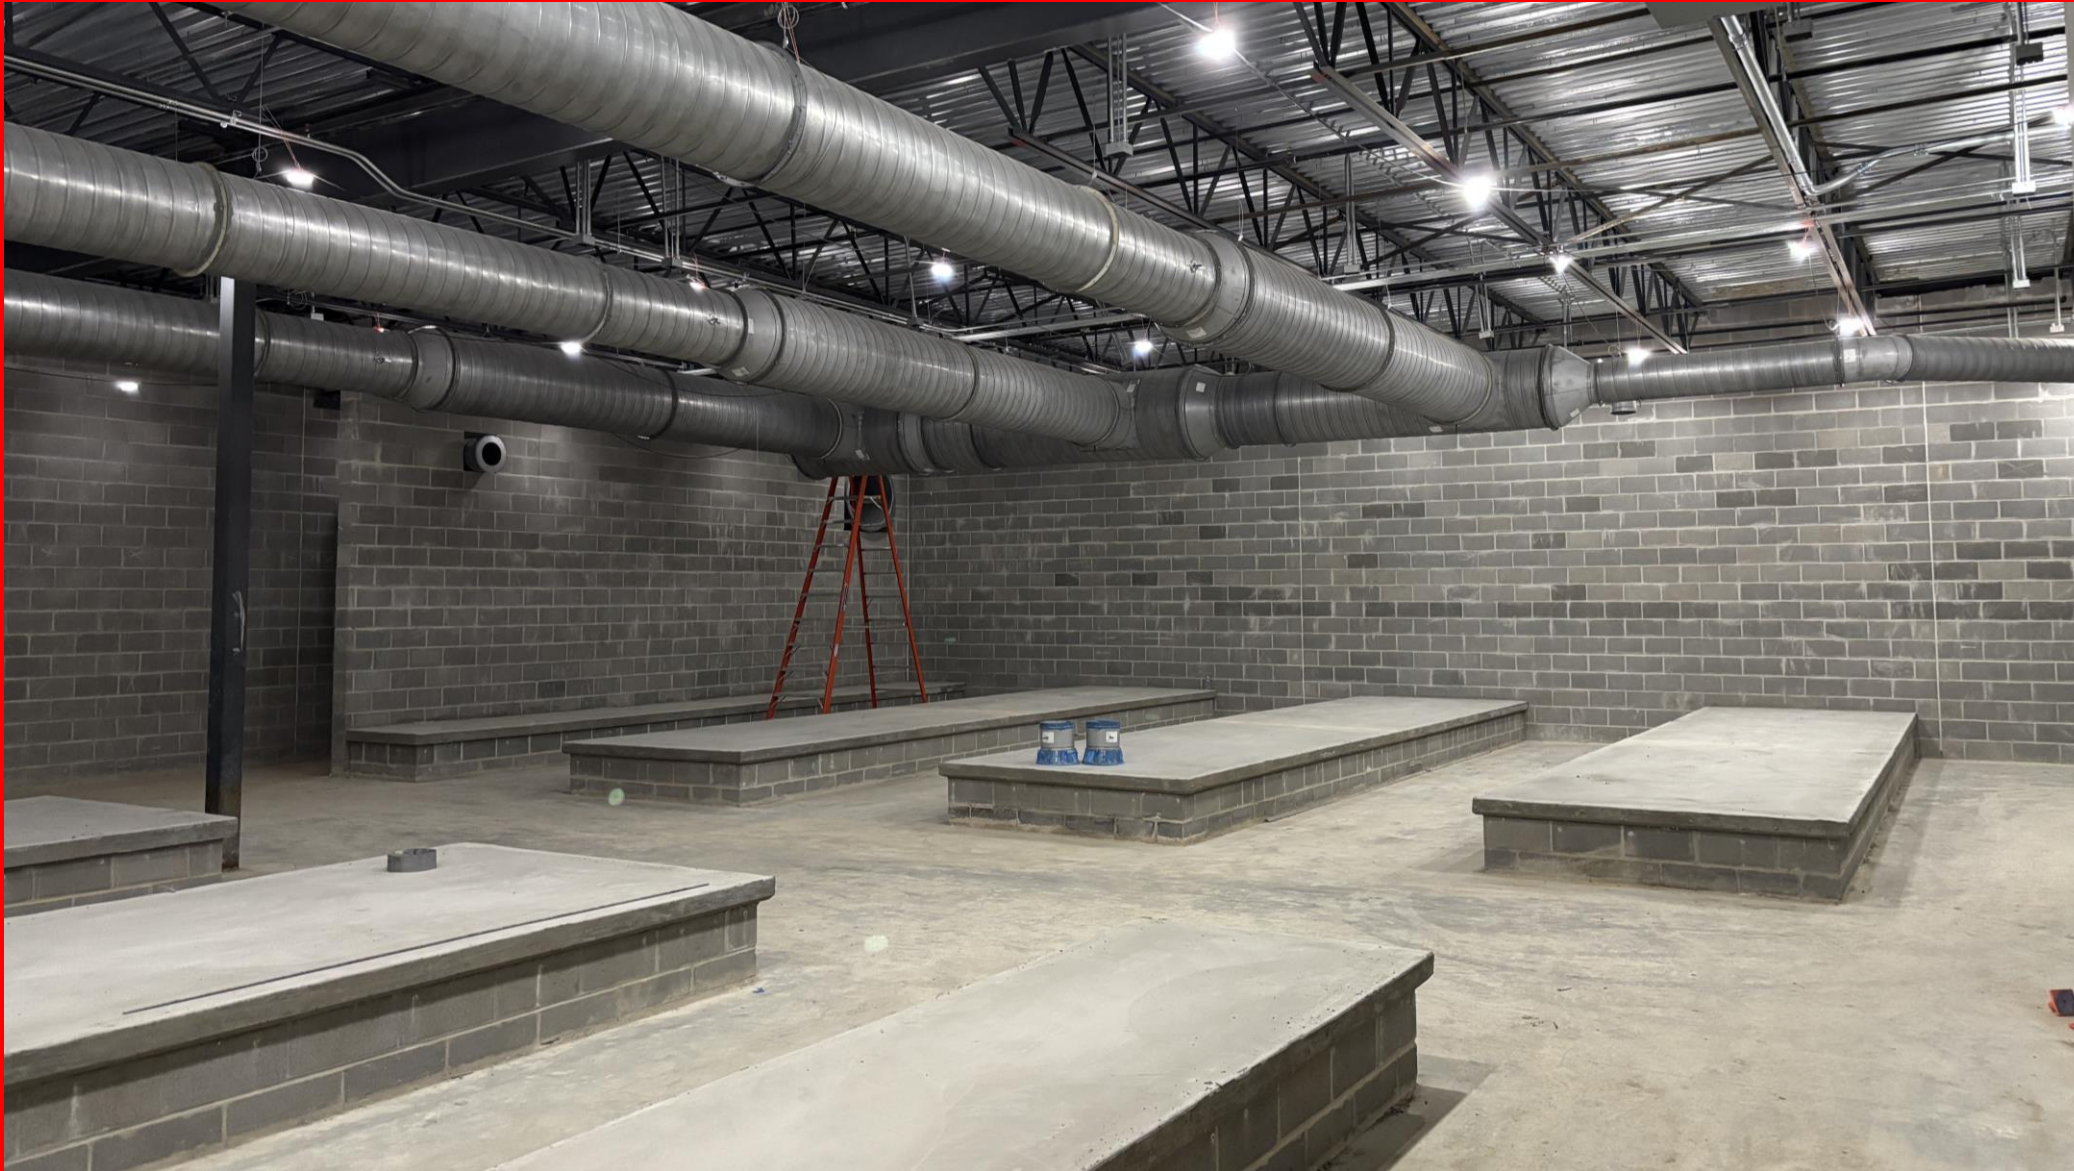

Interior Photos



Site Photos



Site Photos



Look Ahead

- Roof Complete at Classroom Wings
- Interior Finishes in Gyms and Fine Arts
- Permanent Power Connection
- Bleacher Install at Sports Field



Key Milestones

Key Milestone Tracking

Town Permit	December 20, 2024
Structural Steel Completion	October 2025
Entire Building Dried-In	December 2025
Substantial Completion	July 2026





Elementary School #5

December 2025 Update

Site Photos



Site Photos



Look Ahead

- Underground Utilities
- Underground Electrical
- Concrete Piers



Key Milestones

Key Milestone Tracking

Town Permit	October 8, 2025
Mobilization	November 2025
Steel Erection Complete	May 2026
Substantial Completion	February 2027

