

## ROOF PROGRESS REPORT: *Through 05-16-2025*

<b>Contact:</b>	Ryan Palmer (507) 402-6783 <a href="mailto:rpalmer@tremcoinc.com">rpalmer@tremcoinc.com</a>
<b>Inspector:</b>	Kevin Johnson (763) 458-0272 <a href="mailto:kjohnson@tremcoinc.com">kjohnson@tremcoinc.com</a>
<b>Contractor:</b>	Western Specialty Contractors
<b>Project Manager:</b>	David Grandbois (612) 685-7107 <a href="mailto:davidlg@westernspecialtycontractors.com">davidlg@westernspecialtycontractors.com</a>
<b>Foreman:</b>	Larry Hadley (612) 860-9347 <a href="mailto:larryh@westernspecialtycontractors.com">larryh@westernspecialtycontractors.com</a>

### Through Wall Flashing Complete (Light Green)

- Brick installation completed
- All repairs completed in light green area

### Through Wall Flashing Complete (Blue)

- Brick installation completed
- All repairs completed in blue area

### Through Wall Flashing Complete (Pink)

- Brick installation completed
- All repairs completed in pink area


### Lift delivered 5/12/25. Precast Sealant Replacement & Penetrating Sealer of Red & Orange areas

- Sealant (caulking) is complete
- Lightly grinded joint edges to remove loose residual sealant and replaced with new urethane sealant.
- Penetrating Sealer in this area is in progress
- Through Wall Flashing work to start 5/19 on the Library Area Green and Yellow with noise allowed 6am-8am and 3pm-6pm. Minimal noise 8am-2:30pm.

### Issues and Corrections

Kevin will make a site visit week of 5/19/25 to investigate/repair roof leak (last week was postponed)

### Project Map:

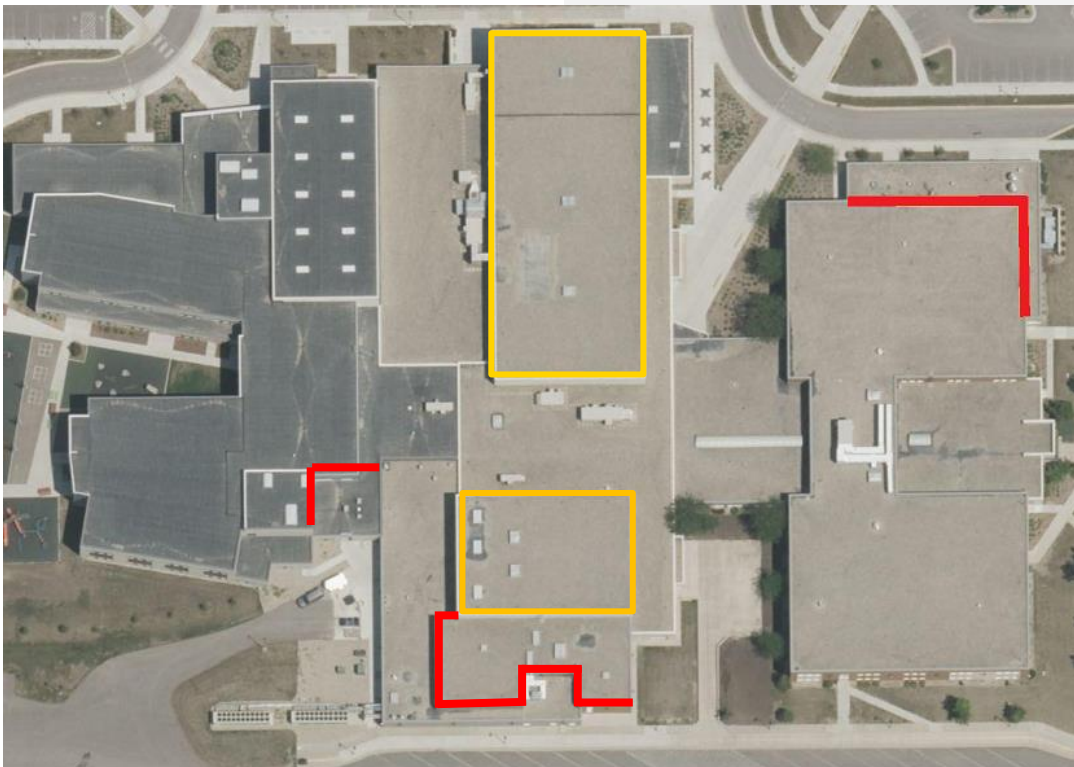

- Current Area of Work
- Areas Completed

## ROOF PROGRESS REPORT: *Through 05-16-2025*



Through Wall Flashing Repair in Progress - 2 Courses of Brick Removed to Install Through Wall Flashing System (Pink Area)

## ROOF PROGRESS REPORT: *Through 05-16-2025*



Through Wall Flashing Installation in Progress - New Weeps for Water to Exit the System



## ROOF PROGRESS REPORT: *Through 05-16-2025*



Plywood Protection noted on top of Existing Roofing Membrane

## ROOF PROGRESS REPORT: *Through 05-16-2025*



Completed through wall flashing. Bottom 3 courses of brick have been tuckpointed.  
New Weeps and Reglet.



## ROOF PROGRESS REPORT: *Through 05-16-2025*



Through Wall Flashing Complete Above Door. New Weeps & Regelet (Blue Area)



## ROOF PROGRESS REPORT: *Through 05-16-2025*



Precast Sealant Replacement in Progress (Orange)  
Loose residual sealant removed, Replaced with New Urethane Sealant
