

Aledo ISD Board Update 2023 Bond Progress

February 17, 2025





Elementary School #7

\$59,800,00



High School Addition/Repurpose

\$20,200,00



AHS/DNG Furniture

\$5,000,000



Transportation

\$4,500,000



Land (to include tracts for additional high school facilities)

\$17,800,000



Safety & Security

\$5,000,000



Technology

\$6,500,000



Facility Maintenance

\$5,000,000

TOTAL BOND PACKAGE:

\$123,800,000

McKinney Elementary School- ES#7

Grades: K-5

Capacity: 889

Budget: \$59,800,000.00

Amount Obligated To Date: \$54,114,153.10

Phase Completion: **planning, design, procurement, construction**, warranty

Square Footage: 106,180

Date To Open: August 2024

McKinney Elementary School- ES#7

- **Construction**
 - Substantially complete.
 - Punch list
 - HVAC balancing
 - Close out
 - March target

AHS Repurpose and Additions

Grades: 9-12

Capacity: 3,000

Budget: \$20,200,000.00

Amount Obligated To Date: \$19,193,201.89

Phase Completion: **planning, design, procurement**, construction, warranty

Date To Open: August 2024


AHS Repurpose and Additions

- Construction
 - AHS Reno
 - Substantially complete.
 - Punch list ongoing.
 - Steve Wood Complex
 - Ceiling inspections this month.
 - Wall rough inspections complete.
 - Paint and interior finishes complete.
 - AG Barn Addition
 - Final Trade inspections next week.
 - Move in by first of March.


Steve Wood Complex



Steve Wood Complex

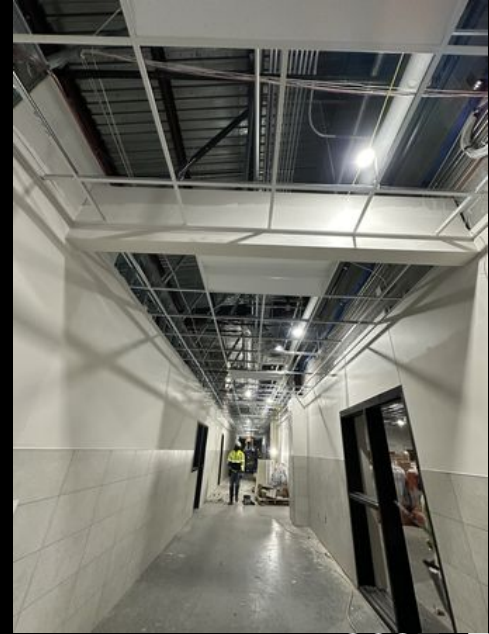

Steve Wood Complex

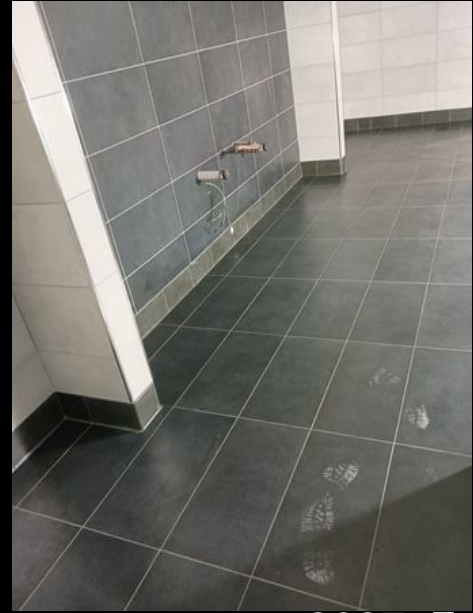

Ag Barn Addition

