

# DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

# Construction, Planning & Growth

# **Construction Report**

### Active Construction Timeline



Facility	Phase of Development	Move In Date	
Hill Elementary School	Under Construction	TBD	
Reeves Elementary School	Under Construction	Summer 2025	
Denton High School Multipurpose	Under Construction	Fall 2025	
Braswell High School Multipurpose & Additions	Under Construction	2025	
Guyer High School Multipurpose & Ag Facility	Under Construction	2025	
Ryan High Renovation & Multipurpose	Under Construction	2026	
High School #5	Under Construction	2027	
Harpool Middle School Track & Field	Under Construction	2025	
Navo Middle School Track & Field	Under Construction	2025	
Strickland Middle School Track & Field	Under Construction	2025	

## Active Project Timeline



Facility	Phase of Development	Construction Commencing	Move In Date
Borman Elementary School Replacement	Awaiting Permit	Spring 2025	August 2026
W.S. Ryan Elementary School Renovation	Awaiting Permit	Summer 2025	August 2025
Hodge Elementary School Renovation	Awaiting Permit	Summer 2025	August 2025
C.H. Collins Facility Upgrades	Awaiting Permit	Summer 2025	August 2025
Crownover Middle School Facility Upgrades	Awaiting Permit	Summer 2025	August 2025
Harpool Middle School Facility Upgrades	Awaiting Permit	Summer 2025	August 2025
McMath Middle School Facility Upgrades	Awaiting Permit	Summer 2025	August 2025
Providence Elementary School Facility Upgrades	Awaiting Permit	Summer 2025	August 2025
Stephens Elementary School Facility Upgrades	Awaiting Permit	Summer 2025	August 2025
E.P. Rayzor Roofing	Awaiting Permit	Summer 2025	August 2025
Stephens Administration Roofing	Awaiting Permit	Summer 2025	August 2025

# DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS


Construction, Planning & Growth

# Borman Elementary School

## Borman Elementary School



2023 Bond Authorization
Architects – Corgan
Contractor – Joeris
Move In – Summer 2026

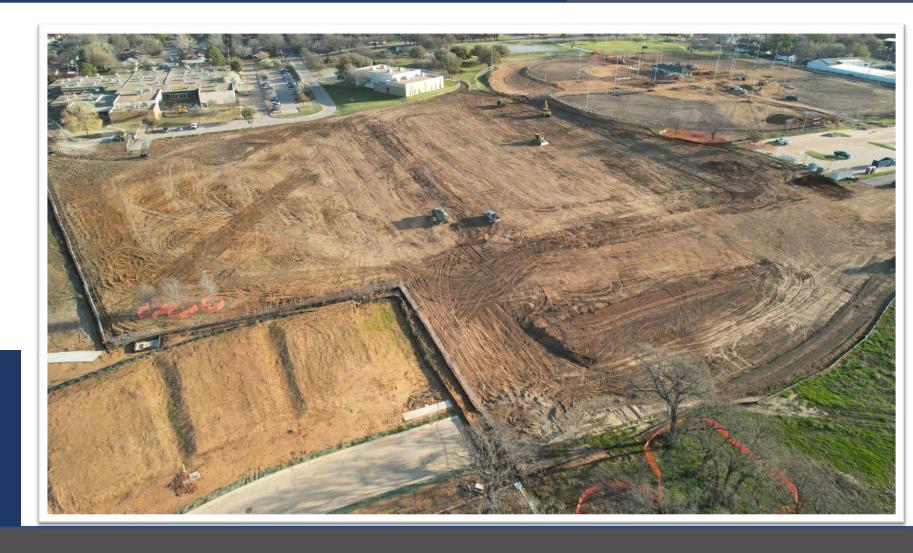

## Borman Elementary School



2023 Bond Authorization
Architects – Corgan
Contractor – Joeris
Move In – Summer 2026

#### **Upcoming tasks:**

- Grading of site to begin
- Building pad to begin mid April
- Site utilities to begin mid April
- Piers and grade beams to begin mid May



#### DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

# Construction, Planning & Growth

# High School #5







2023 Bond Authorization
Architects – VLK Architects
Contractor – CORE
Move In – 2027

#### Tasks completed previous 90 days:

- Site clearing and grading
- Construction trailers, laydown yard and site fencing
- Underground utilities began
- Installing geothermal wells
- Constructing building pads

#### **Upcoming tasks:**

- Rough grading to be completed
- Continue underground utilities
- Continue geothermal wells
- Construct building piers and grade beams
- Install fire lanes around building pad
- Concrete foundation and slab



















#### DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

# Reeves Elementary School









2023 Bond Authorization
Architects – Pfluger
Contractor – Balfour Beatty
Move In – Summer 2025

#### **Tasks Previous 90 Days:**

- Steel detailing and decking
- Brick installation at Gym
- Slab on metal deck in multiple areas
   to be completed
- Punch Windows
- Exterior Framing and Sheathing ongoing
- Storefronts and curtain walls will begin

#### **Upcoming Tasks:**

- Construction of Riney Road to begin
- Brick veneer to be completed
- Canopy columns being installed
- Interior finishes ongoing
- Millwork ongoing
- Mechanical/Electrical/Plumbing overhead ongoing

**Prepared by:** 















# DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

# Braswell High School Multipurpose Facility



2023 Bond Authorization
Architects – VLK
Contractor – Balfour Beatty
Move In – 2025







2023 Bond Authorization
Architects – VLK
Contractor – Balfour Beatty
Move In – 2025

#### **Tasks Previous 90 Days:**

- Prep of fire lanes ongoing
- Grade beams and piers ongoing
- Slab on grade to begin
- Erecting steel for indoor facility completed
- Batting cages for Baseball/Softball completed

#### **Upcoming Tasks:**

- Mechanical/Electric/Plumbing ongoing
- Sheathing on east side to begin
- Batting cages CMU and steel
- Construction of outdoor practice field ongoing
- Construction of discus area starting



2023 Bond Authorization
Architects – VLK
Contractor – Balfour Beatty
Move In – 2025








2023 Bond Authorization
Architects – VLK
Contractor – Balfour Beatty
Move In – 2025





# Questions?

**Prepared by:** 

Brandon Boyter Executive Director of Construction, Planning & Growth
