

ROOF PROGRESS REPORT: *Through 04-21-2025*

Contact:	Ryan Palmer (507) 402-6783 rpalmer@tremcoinc.com
Inspector:	Kevin Johnson (763) 458-0272 kjohnson@tremcoinc.com
Contractor:	Western Specialty Contractors
Project Manager:	David Grandbois (612) 685-7107 davidlg@westernspecialtycontractors.com
Foreman:	Larry Hadley (612) 860-9347 larryh@westernspecialtycontractors.com

Through Wall Flashing Installation

- 3 courses of brick above the existing TWF is removed and new stainless steel TWF is installed. The new system is comprised of stainless-steel flashing, stainless-steel termination bar, mastic, and weep rope
- After the flashing system is installed a water test will be completed to assure the area is watertight
- New brick is then installed to match existing brick size and color with mortar to match existing as well
- Brick installation estimated to be completed by end of the week


Sealant Replacement


- Existing sealant at windows and masonry walls removed with grinders and replaced with new sealant

Issues and Corrections

- Demolition time to be adjusted due to noise

Project Map:

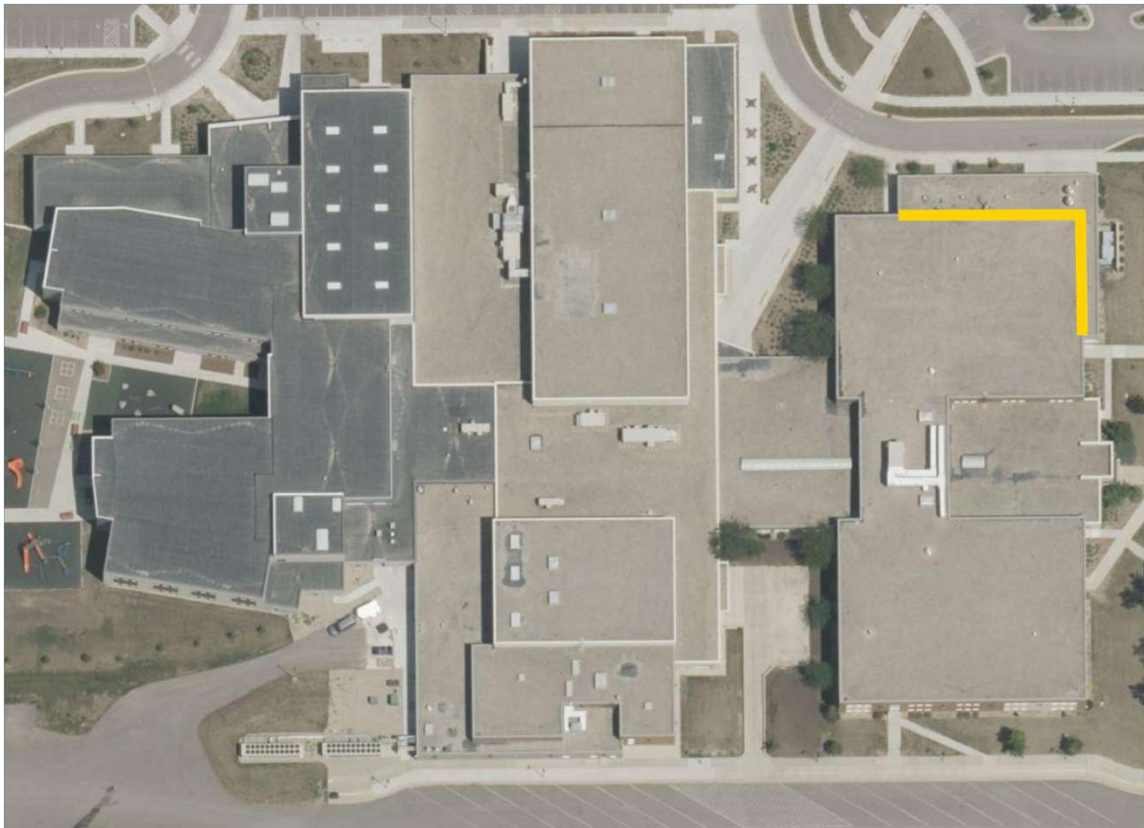

-  Current Area of Work
-  Areas Completed

ROOF PROGRESS REPORT: *Through 04-21-2025*



Through wall flashing installation in progress

ROOF PROGRESS REPORT: *Through 04-21-2025*



Completed through wall flashing detail ready for brick installation

ROOF PROGRESS REPORT: *Through 04-21-2025*



Completed through wall flashing detail ready for brick installation

ROOF PROGRESS REPORT: *Through 04-21-2025*



Completed through wall flashing detail ready for brick installation

ROOF PROGRESS REPORT: *Through 04-21-2025*



Original through wall flashing detail

ROOF PROGRESS REPORT: *Through 04-21-2025*



New through wall flashing detail

ROOF PROGRESS REPORT: *Through 04-21-2025*



Bricks are staged on plywood sheeting to protect roof membrane

ROOF PROGRESS REPORT: *Through 04-21-2025*



Removal of existing sealant around windows

ROOF PROGRESS REPORT: *Through 04-21-2025*



Installation of backer rod at windows prior to sealant application

ROOF PROGRESS REPORT: *Through 04-21-2025*



Completed sealant around window perimeter
