


Lincolnwood Capital Project News

Water Transmission Main

This week, the contractor pressure tested and chlorinated the piping and 20-inch water main at the valve house and the meter vault that serves the Village's underground reservoirs. The electricians installed new wiring and the electrical panel at the valve house. A second crew began excavation for new curb and pavement patching on Hamlin Avenue, north of Touhy Avenue. The concrete subcontractor installed new curb, sidewalk, and pavement patching on the west side of Hamlin Avenue. A third crew installed the 20-inch transmission main on Hamlin Avenue, north of Howard Street. The boring subcontractor will complete the 30-inch steel casing bore under the CTA tracks at Hamlin Avenue and Harvard Terrace. The asphalt subcontractor completed pavement grinding on Arthur, Springfield, and Hamlin Avenues as well as on East Prairie Road.

Next week, the contractor will continue excavation for new curb and pavement patching on Hamlin Avenue, north of Touhy Avenue. The concrete subcontractor will continue installing new curb and pavement patching on the west side of Hamlin Avenue. A second crew will install the 20-inch transmission main on Hamlin Avenue, north of Howard Street. The asphalt subcontractor will place the first lift of asphalt on Arthur, Springfield, Pratt, and Hamlin Avenues as well as East Prairie Road. Traffic on these streets will be impacted while the contractor is performing this work.

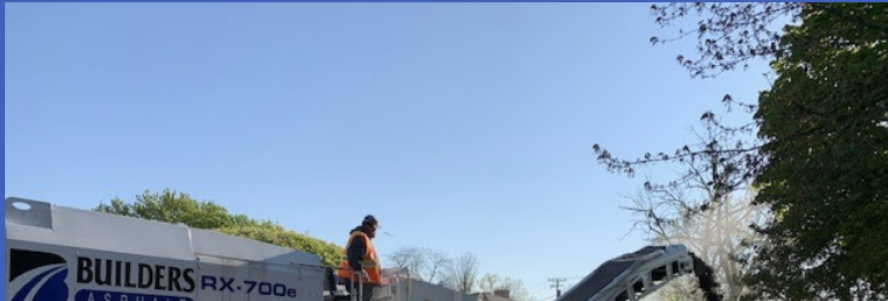

May 14, 2020
